

Semi-Annual Social Monitoring Report

Project number: 42173-013

Period: January – June 2020
Submission Date: November 2020

BAN: Dhaka Environmentally Sustainable Water Supply Project – PART A


This report was prepared by Management, Design and Supervision Consultant, Government of Bangladesh for the Asian Development Bank. This document is made publicly available in accordance with ADB's Access to Information Policy and does not necessarily reflect the views of ADB.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature. Your attention is directed to the "terms of use" section of this website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



**Dhaka Environmentally
Sustainable Water Supply
Project
Loan No. 3051 BAN**



Management, Design & Supervision Consultant
(MDSC)
Semi-Annual Social Safeguard Monitoring Report
January to June 2020

1 November 2020

Mott MacDonald
Plot 77, Level 6 Block-M
Road 11
Banani
Dhaka 1213
Bangladesh

T +880 (2) 986 1194
mottmac.com/international-development

Dhaka Water Supply and
Sewerage Authority

Funded by:

Asian Development Bank
Agence Française de
Développement
European Investment Bank
Government of Bangladesh

Dhaka Environmentally Sustainable Water Supply Project Loan No. 3051 BAN

Management, Design & Supervision Consultant
(MDSC)
Semi-Annual Social Safeguard Monitoring Report
January to June 2020

1 November 2020

Issue and Revision Record

Revision	Date	Originator	Checker	Approver	Description
A	30.07.20	Dr. Rafeza Akter	AYM. Imtiazul Haque	Nigel Osmaston	Issue to DWASA
B	01.11.20	Dr. Rafeza Akter	AYM. Imtiazul Haque	Nigel Osmaston	ADB Comments incorporated

Document reference: MMD-346152-RS-RP-PX-XX-060

Information class: Standard

This document is issued for the party which commissioned it and for specific purposes connected with the above-captioned project only. It should not be relied upon by any other party or used for any other purpose.

We accept no responsibility for the consequences of this document being relied upon by any other party, or being used for any other purpose, or containing any error or omission which is due to an error or omission in data supplied to us by other parties.

This document contains confidential information and proprietary intellectual property. It should not be shown to other parties without consent from us and from the party which commissioned it.

Contents

Executive summary	1
1 Background of the Monitoring Report	4
1.1 Project Description	4
1.2 Purpose of the Report	6
1.3 Category of Resettlement Plan	7
1.4 Resettlement Plan Update and Public Consultation	7
2 Scope of Impacts	8
3 Status of Resettlement Plan Implementation	10
3.1 Institutional Arrangement and Capacity	10
3.2 Update of the Resettlement Plans	10
3.3 Compensation and Rehabilitation	12
3.3.1 Land Acquisition Progress	12
3.3.2 Progress in Livelihood Restoration	24
3.3.3 Overall Progress	25
3.4 Disclosure and Public Consultation	29
3.5 Grievance Redress Mechanism	31
4 Summary Monitoring Results and Key Findings	32
5 Compliance Status	36
6 Follow up Actions and Recommendation	37
A. Changed alignment in Section 5	42
B. Leaflet on Dedicated Account	43
B.1 Leaflet on Dedicated Account in English	43
B.2 Leaflet on Dedicated Account in Bangla	45
C. List of Leaflet Recipient on Dedicated Account	47
D. FGD on Dedicated Account Meeting Minutes	51
E. Public Consultation on Dedicated Account Meeting Minutes	55

F.	DD Record for unpaid Aps	62
G.	Graveyard Signed MoU	77
H.	Map of arranged Graveyard	79
I.	Photos on Temple and Graveyard	80
J.	Additional Payment in Section 2 up to June 2020	82
K.	Comparative Pictures of Structures	157
L.	Structures to be relocated in Section 2	166
M.	CCL non paid affected persons in non-priority mouzas up to 30.06.2020	173
N.	Signed JVC Meeting minutes	188
	N.1 Signed JVC Meeting minutes (Bangla)	188
	N.2 JVC Meeting Minutes (English)	193
O.	List of Wage Earners	198
P.	List of LIRP Participants in Section 1	201
Q.	Summary of Consultation	206
R.	GRC 2nd Meeting (English)	213
S.	GRC Summary Report	220
T.	Meeting Minutes	227
	T.1 Zoom Meeting on Resettlement Progress held on 3 June 2020	227
	T.2 Meeting on Affected Persons Counting and Payment held on 17 June 2020	235
	T.3 Zoom Meeting on Resettlement Progress held on 1 July 2020	246
U.	List of Encroacher in Section 3	251
V.	Received copies of notices to the encroacher	252

Tables

Table 1.1: Length of Pipelines in Each Section	6
Table 2.1: Land Acquisition and Resettlement Impacts	8
Table 3.1: Progress of Land Acquisition (LA) and Compensation Payment	14
Table 3.2: Taskwise Land Acquisition Progress of Resettlement Plan (RP) Sections 1, 2 and 4	16
Table 3.3: Land Acquisition Progress of Resettlement Plan (RP) Sections 3, 5 and 6	20
Table 3.4: Details of Training on LIRP	25
Table 3.5: Status of IGA Engagement of the Trained Affected Persons	25
Table 3.6: Cumulative Progress up to 30 June 2020	26
Table 4.1: Summary of Project Impacts as per Resettlement Plans for Section 1, 2, 3, 4, 5 and 6 (up to June 2020)	32
Table 6.1: Required Actions	37
Table 6.2: Monitoring of Activities during Implementation	39

Figures

Figure 1.1: Project location map	5
Figure 3.1: Resettlement Plan Approval Status	11
Figure 3.2: Payment Status in all Sections	14
Figure 3.3: Land Acquisition Progress for Resettlement Plan Section 1, 2 and 4	23
Figure 3.4: Land Acquisition Progress for Resettlement Plan Section 3, 5 and 6	23
Figure 3.5: GRC Decisions Taken	31

Executive summary

This is the 10th Semi-annual Social Safeguard Monitoring Report (SSMR) prepared for project implementation under Dhaka Environmentally Sustainable Water Supply Project (DESWSP) of the Dhaka Water Supply and Sewerage Authority (DWASA) for submission to the Asian Development Bank (ADB).

The report is prepared by Mott MacDonald, the Consultant of the project, to assist the DWASA Project Management Unit (PMU) in updating the ADB on implementation of the Social Safeguard Plans (Resettlement Plans) of the project.

The objective of this project is to provide a reliable water supply for the Dhaka city by developing a surface water intake, raw water pipeline, water treatment plant, treated water pipeline and distribution network to improve quality water supply, water pressure in the pipelines, cost recovery, reduce water loss and gradual groundwater depleting in Dhaka city.

The DESWSP is being and to be delivered through several contract packages by several consultants, contractors and NGOs under DWASA's project management unit (PMU). Mott MacDonald is responsible for the three main construction contracts through their management, design and supervision consultancy (MDSC) contract. Under MDSC, Mott MacDonald is acting as the Employer's designer for Packages 2 and 3 and as the supervision consultant for Packages 1, 2 and 3. Package 1 or P1 (water intake, raw water pipeline and water treatment plant) is as a Design, Build & Operate (DBO) contract. Length of the raw water pipeline is 22 km. Package 2 (P2) comprises of 14 km. treated water pipeline from water treatment plant to Madani Avenue. Package 3 (P3) includes 66 km distribution reinforcement pipeline in north Dhaka City.

The total length of the alignment (except P3) is 36 kilometres. This starts from the Meghna River and passes through Arahazar and Rupganj upazila and reaches Madani Avenue in Dhaka after crossing Sitalakshya and Balu rivers. This project will use 308.32 acres of land of which Dhaka WASA owns 81.5 acres (in Gandharbpur) and Bangladesh Water Development Board (BWDB) with Roads and Highways own another 37.82 acres. The rest of the land (189.00 acres) is privately owned.

Issues of involuntary resettlement have been being implementing following National (GoB) Legislations such as Acquisition and Requisition of immovable Property Ordinance (ARIPO), 1982 and Acquisition and Requisition of Immovable Property Act (ARIPA), 2017. In addition, ADB Safeguard Policy Statement (SPS), 2009 have been being followed. A Resettlement Framework (RF) has been developed for DESWSP in 2013 to provide guidance to the Executing Agency (EA) in making and updating resettlement plans and implementation.

The scope of land acquisition and resettlement impacts have already been identified based on the design. The project will impact private and government land of different organizations including structures, assets, crops, fishes, trees, etc. As per the design, a total area of 189.00 acres of private land will be acquired for the construction of the water pump at the intake and for the required pipelines.

DWASA is the executing agency. PMU has established Safeguard Implementation Unit (SIU) for monitoring safeguard activities implementation. It also involves a Supervising Officer (SO), designated as Safeguard Officer (Social & Gender). The SO is responsible for monitoring overall safeguard implementation including resettlement. An independent External Monitoring Agency (EMA) has been engaged as a third-party monitor for Resettlement Plan (RP) implementation. Evaluation of the resettlement activities will be undertaken during and after implementation of the Resettlement Plan.

To carry out the resettlement activities, PMU has contracted DORP, a local NGO in February 2015. For the convenient implementation of the Resettlement Plans, P1 and P2 area has been divided into 6

sections. ADB has approved four resettlement plans for sections 1, 2, 3 and 4. Resettlement plans for Section 5 and Section 6 need updating. Some pending documents and COVID-19 pandemic delayed required survey for changed alignment. DORP is updating those and will be submitted to ADB by July 2020. P3 has been divided into two; P3.1 and P3.2. DDR for P3.1 and Resettlement Plan for P3.2 receipt ADB approval.

The land acquisition is in progress in four sections; 1, 2, 3 and 5. About 99% of the affected persons have been fully paid (CCL and other resettlement assistance) in Section 1. About 97% of CCL payment has been completed in Section 2. Payments for the remaining affected persons are still pending due to reasons such as delay in submission of necessary papers, legal issues with the land, conflict with co-sharers, procedural delays, etc. Among the CCL recipients 98% received full payment. PMU has opened a dedicated account for the unpaid affected persons, in which money for additional payment will be kept intact. DORP is motivating affected persons by personal contacts, community meetings, announcement, leaflet distribution, etc. Following government rule, Deputy Commissioner has handed over required land for Section 1 and Section 2 to DWASA though CCL payment is still continuing. Contractor has started civil works in Section 1 and Section 4.

In this reporting period, DORP has imparted livelihood and income restoration training program to 46 eligible affected persons of Section 1 on chicken and duck rearing as well as cows and goat rearing. About 92% of total training recipients are engaged in income generating activities.

One Grievance Redress Committee (GRC) meeting has been held. The meeting dealt with 17 cases; 9 cases were forwarded to Deputy Commissioner, 3 cases were advised to DWASA for paying compensation and 4 5 cases were rejected.

To facilitate land acquisition some actions have been recommended by the MDSC to PMU and DORP. Handing over RWP to the contractor by September 2020 is a must. So, update and upload of resettlement plan for section 1 and 2 is urgent. Based on approval of these and depositing money in the dedicated account, ADB may allow relocation of the unpaid affected persons. PMU needs to follow up Deputy Commissioner's office to consider affected persons' problems and to facilitate payment. Deploying full-time man-power in Deputy Commissioner's office from PMU and DORP is advised to collect data on actual number of affected persons in section 1 and 2. PMU should give due attention to ensure data is available faster for updating the web-based database and error free reporting. PMU should pay due top up and other resettlement benefits by August 2020. It should finalize MoU with BWDB by August 2020. Appointment of a Land & Resettlement Officer has been advised to support affected persons and SIU, PMU to facilitate resolution of the legal problems and CCL receipt. For dismantling structures in the raw water pipeline, PMU may seek help from the Deputy Commissioner for legal action. PMU needs to check with Deputy Commissioner's office for completion of award book for Section 3, issue new LA case for Section 5 and request for the feasibility study of section 6. PMU may coordinate regularly with the concerned Ministry, Deputy Commissioner Office and DORP.

DORP should help affected persons more in processing legal papers for getting CCL. They should inspire affected persons in submitting CCL papers for additional payment. Supervision of all DORP activities should be increased by PMU as they planned. DORP management, TL and DTL should be more careful in deploying competent staffs and should be more proactive in monitoring their field staffs' activities.

Abbreviation

ADB	Asian Development Bank
BDT	Bangladeshi Taka
DBO	Design-Build-Operate or Design-Build-Operation
Dec	Decimal
DORP	Development Organization for the Rural Poor
DDR	Detailed Design Reports
DED	Detailed Engineering Designs
DESWSP	Dhaka Environmentally Sustainable Water Supply Project
DWASA	Dhaka Water Supply and Sewerage Authority
EIA	Environmental Impact Assessment
GEM	General Entitlement Matrix
FGD	Focus Group Discussion
GRC	Grievance Redresses Committee
JVC	Joint Verification Committee
MLGRDC	Ministry of Local Government Rural Development Cooperatives
MDSC	Management, Design and Supervision Consultant
MLD	Millions of Liters Per Day
MML	Mott MacDonald Limited
MODS	Maintenance Operations and Distribution Services
MoU	Memorandum of Understanding
PMC	Project Management Consultant
PPMS	Project Performance Management System
PMU	Project Management Unit
PVAC	Property Valuation Advisory Committee
RAC	Resettlement Advisory Committee
RWP	Raw Water Pipeline
SIU	Safeguard Implementation Unit
SPS	Safeguard Policy Statement
ToR	Terms of Reference
WIA	Water Intake Area
WTP	Water Treatment Plant

1 Background of the Monitoring Report

1.1 Project Description

The DESWSP of the DWASA is funded by the Government of Bangladesh (GoB), ADB, AFD and EIB. The project comprises of water intake, water treatment plant, raw and treated water mains. It is to be delivered through several contract packages by several consultants, contractors and NGOs under DWASA's project management unit (PMU). Mott MacDonald is responsible for the three main construction contracts through their management, design and supervision consultancy (MDSC) contract. Under MDSC, Mott MacDonald is acting as the Employer's designer for Packages 2 and 3 and as the supervision consultant for Packages 1, 2 and 3. Package 1 or P1 ((water intake, raw water pipeline and water treatment plant) is a Design, Build & Operate (DBO) contract. Length of raw water pipeline is 22 km. Package 2 or P2 comprises of 14 km. treated water pipeline from water treatment plant to Madani Avenue near to American Embassy in Dhaka. Packages 3 or P3 includes distribution reinforcement pipeline in Dhaka North City. P3 has been divided into two parts; P3.1 and P3.2. The start of the primary distribution network for P3.1 shall be at the interface with the Package 2 transmission mains. This is the injection point of the Phase 1 treated water pipeline (500 MLD) and shall be located at Notun Bazar in Vatara, at the junction of Madani Avenue and Progati Sharani. The package P3.2 pipelines connect to the package P3.1 pipeline in various places and to the District Metered Areas (DMAs) i.e., comparative small-dia feeder pipelines (branch lines) will be connected with each large pipeline. Package 1 and 2 has been divided into six (6) sections and Package 3 in two (2) for convenient resettlement plan implementation. Sections are as follows:

Package 1 and 2

Section 1: Water Intake Area

Section 2: Water Intake to Baliapara (End of Arahazar)/raw water pipeline

Section 3: Darikhandi Chak (start of Rugganj) to Murapara via Gandharbpur WTP

Section 4: Water Treatment Plant in Gandharbpur Area

Section 5: Rugganj (West bank of Sitalakshya River) to Balu River (East bank)/treated

Section 6: Balu River (West bank) to Vatara along Madani Avenue up to Baridhara

It is to be mentioned here that Section 2 includes raw water pipeline. Section 3 falls under two packages; P1 and P2, which includes part of raw water and part of treated water pipeline. Section 5 and 6 are for treated water pipeline.


Package 3

P3.1: Primary Distribution Pipelines

P3.2: Feeder Pipelines

Project location map showing sections of resettlement plans is given below as Figure 1.1.

Figure 1.1: Project location map

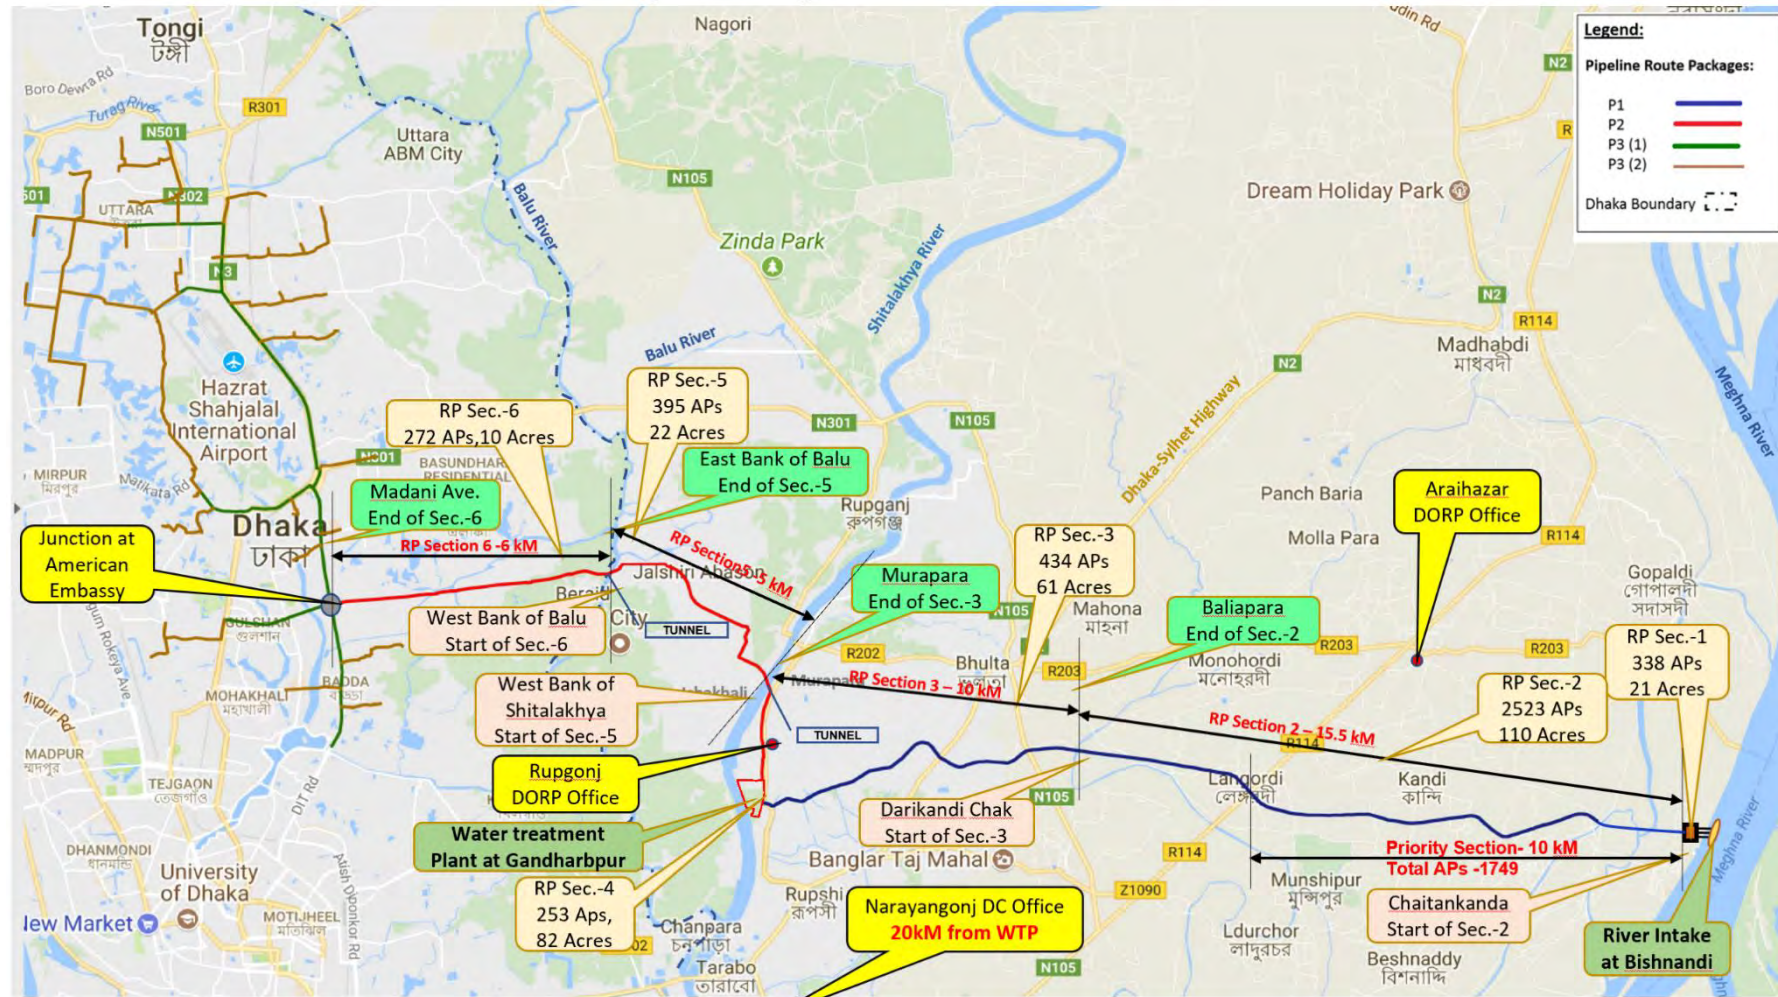

Section-wise length of the pipelines is given below:

Table 1.1: Length of Pipelines in Each Section

Name of Section	Type of Pipeline	Length
Section 2	Raw Water Pipeline	14.25 km.
Section 3	Raw Water Pipeline+Treated Water Pipeline	7.75 km. + 2 km
Section 5	Treated Water Pipeline	5 km.
Section 6	Treated Water Pipeline	7 km.
P3.1	Primary Distribution Pipelines	24 km,
P3.2	Feeder Pipelines	42 km.
Total		102 km.

This project will provide a reliable water supply for the Dhaka city by developing a surface water treatment and distribution network. This starts from the Meghna River and passes through Arai hazar and Rugganj upazila and reaches Madani Avenue in Dhaka after crossing Sitalakshya and Balu River. This P1 and P2 area requires 308.32 acres of land. Of total lands, Dhaka WASA's own land is 81.50 acres. Bangladesh Water Development Board (BWDB) and Roads and Highways Department (RHD) own 37.82 acres. The rest 189.00 acres are privately owned, which will need to be acquired. Dhaka WASA's land is in Gandharbpur, which will be used for construction of WTP. No land acquisition is required for Package 3. Existing roads under Roads & Highways and Dhaka City Corporation will be used with due permission.

A Resettlement Framework (RF) has been developed for DESWSP in 2013 to provide guidance to prepare and implement Resettlement Plans. Involuntary resettlement follows project Resettlement Framework, 2013, ADB Safeguard Policy Statement (SPS), 2009 and national legislations of GoB, which includes Acquisition of Immovable Property Ordinance (ARIPO), 1982 as well as Acquisition and Requisition of Immovable Property Act (ARIPA), 2017. Resettlement plans for section 1, 2, and 4 has been updated based on the then ARIPO, 1982 because land acquisition processes were started before ARIPA, 2017 was enacted. This Act is applicable for updating and implementing resettlement plans for Section 3, Section 5 and Section 6, P3.1 and P3.2.

This is a SSMR, which has been prepared following the outline given in the Resettlement Framework, 2013. This monitoring report covers package 1 and package 2. Package 3 activities have not been started yet. It has been prepared by the MDSC for the PMU for onward submission to ADB. DORP (a resettlement plan implementing NGO) provided necessary inputs to prepare this report. It describes the progress made during the months of January to July 2020.

1.2 Purpose of the Report

According to the Resettlement Policy Framework (Appendix C), the Project Director has to submit to ADB, a semi-annual report on status of implementation of safeguard plans and progress made towards the desired outcomes of the project in compliance with the ADB Safeguard Policy Statement (2009) and the Operations Manual section on Safeguard Policy (OM F1).

The purpose of this report is to assist the Project Director in reporting to the ADB on status of implementation of 'Social Safeguard Plans' which are here termed as 'Resettlement Plans' for the project in compliance with the Clause no. 18 (iii) of the Terms of Reference for the Management, Design and Supervision consultant (MDSC), in here Mott MacDonald. MDSC is hereby submitting the 10th SSMR.

1.3 Category of Resettlement Plan

Considering the extent of significance of impacts, ADB has classified projects into four categories: A, B, C and F. The involuntary resettlement impacts of an ADB-supported project are considered significant if 200 or more persons are physically displaced from home or lose 10% or more of their productive or income-generating assets. The project, which has significant involuntary resettlement impacts, falls under category A. Thus, the DESWSP is classified as Category A. No indigenous household has been found during the surveys; therefore, the project falls under category C with regard to indigenous people categorization.

1.4 Resettlement Plan Update and Public Consultation

The INGO, DORP is assisting DWASA in updating the Resettlement Plans and implementation of the resettlement activities. DORP has updated five (5) draft resettlement plans (1-5). The Resettlement Plan for Section 6 is yet to be done.

Regular consultations with the affected persons (APs) and other stakeholders are being conducted by DORP to ensure that they are fully aware of the project interventions and about their entitlements in case of involuntary land acquisition and resettlement benefits for affected persons (titled or non-titled holders).

No land acquisition is required for P3.1 and P3.2. Due Diligence Report (DDR) for P3.1 has been approved by ADB in February 2020. MDSC prepared Resettlement Plan for P3.2 because temporary relocation impact was found in one of the pipe routes. ADB has provided no objection on 15 May 2020 to this draft resettlement plan for bidding purpose with the condition of confirming all the edits made by ADB in track changes and have the document formatted. In addition, prior to loan processing for additional financing this might have been needed to polish further. Resettlement Plan implementing NGO is yet to be appointed under P3. ToR for selecting INGO has been revised by the MDSC based on ADB comments given in May 2020.

2 Scope of Impacts

The project has impact on private and public lands. It also impacts other assets such as structures, livelihoods, crops and trees. A single Resettlement Plan for the project was prepared in 2013, which identified major impacts on lands, scope of land acquisition and other resettlement impacts based on the design of the project. This was subsequently divided into 6 sections under P1 and P2 and two parts (P3.1 and P3.2) to facilitate Resettlement Plan implementation.

The project requires total 308.32 acres of land for the construction of water intake, raw water pipeline, water treatment plant and treated water pipeline under P1 and P2. Of the total land, 189.00 acres are privately owned, which is needed for the construction of water intake and pipelines. DWASA owns required land for water treatment plant.

Section 1 (water intake area) requires private land only. Other sections need acquisition of both private and public land. No land acquisition is required for Section 4. Here, DWASA acquired 81.50 acres of land in 1982-83. DWASA had given 4.67 acres land to Bangladesh Water Development Board (BWDB) for excavation of a canal for irrigation purpose. Now they have drafted a Memorandum of Understanding (MoU) to get this land back. Hopefully it will be done by the end of the August 2020. Other remaining public land is being acquired following government legislations.

The Table 2.1 presents the summary of the land requirements with areas and types of impacts identified so far.

Table 2.1: Land Acquisition and Resettlement Impacts

Section of RPs	Locations	Land Requirement for Acquisition (in acre)			Structure and other impacts	Comments / Status
		Total	Public	Private		
1	Water Intake Area (WIA)	21.38	2.53	18.85	Agriculture and fish livelihood	338 affected persons have been identified by the Deputy Commissioner.
2	Intake to Balia Para	110.15	4.07	106.08	Agriculture, livelihood, and structure	2523 affected persons have been identified by the Deputy Commissioner. These numbers may increase after actual submission of documents for CCL.
3	Darikandi Chak (start of Rupganj) to Murapara via Gandharbpur WTP	66.85	29.61	37.24	Agriculture, structure and livelihood	Approximately 434 affected persons have been estimated by the Deputy Commissioner after Joint verification survey. Deputy Commissioner has prepared Award Book for the part of the alignment LA case 5. Award Book for another LA case is not completed yet.
4	Water Treatment Plant (WTP)	81.50	DWASA land	No private land	Structure, agriculture and livelihood	253 affected persons have been identified as non-titleholders.
5	Rupganj (West bank of Sitalakhya river) to Balu river (East bank)	21.48	0.07	21.41	Structure, pond, agriculture and livelihood	Socioeconomic survey identified 116 affected persons. Joint verification survey had been completed. But it will need to do again because Deputy Commissioner's office cancelled previous LA case due to alignment change. New one will be issued after CLAC approval. PMU submitted proposal.

Section of RPs	Locations	Land Requirement for Acquisition (in acre)			Structure and other impacts	Comments / Status
		Nos.	Total	Public		
6	Balu river to Bhatara	6.96	6.5 km long RAJUK road and 1.54 acres of public land	5.42	Permanent and temporary business structures and livelihood	136 affected persons have been identified during the socioeconomic survey. RAJUK roads will be used for installation of pipes.
Total land		308.32	119.32	189.00		

Source: Plot Schedule provided by PMU as of June 2020

3 Status of Resettlement Plan Implementation

3.1 Institutional Arrangement and Capacity

DWASA is the Executing Agency of the project. A project management unit (PMU) has been established with a safeguard implementation unit (SIU), which includes Safeguard Officer (Social and Gender) and Safeguard Officer (Environment). DWASA has established its own SIU to assist PMU for managing social and resettlement issues. Safeguard Officer (Social and Gender) of the SIU assisted by the Resettlement Experts and Social Development and Gender Specialist of MDSC, who oversee the implementation of Resettlement Plans/DDR with support of the resettlement implementing NGO, DORP. The other staffs, who are responsible for looking the safeguard issue of the project include: one Executive Engineer and two Assistant Engineers. The Project Director and two Deputy Project Directors and one Senior Water Supply Engineer is responsible for administering overall activities. Senior Water Supply Engineer's post is vacant now.

DESWSP is being implemented through several contract packages by several consultants, contractors and NGOs under DWASA's PMU. Mott MacDonald is responsible for three main construction contracts, through their MDSC contract. Under MDSC, Mott MacDonald is acting as the Employer's designer for Packages 2 and 3 and will act as the supervision consultant for Packages 1, 2, 3.1 and 3.2.

MDSC is being led by the Mott MacDonald Limited (UK) in association with Fichtner GmbH & Co. KG (GER), Euroconsult Mott MacDonald (Netherland) and Yooshin Engineering Corporation (KOR), BCL Associates Limited (Bangladesh), SARM Associates Limited (Bangladesh), Associates for Development Services Limited (Bangladesh). The goal of the MDSC is to provide all necessary consulting services requirements to implement the DESWSP. MDSC resettlement consultants are specifically monitoring the resettlement plan implementation program. International and national Resettlement Experts have been assigned to review and assist the resettlement plan implementation process.

DWASA has an NGO, DORP for implementing resettlement plans. DORP is working in close coordination with DWASA PMU and MDSC. The major tasks of DORP are: updating resettlement plans, public consultations and FGDs with the affected persons and communities for awareness campaign, assessing resettlement impacts, collecting the market price of the loss of the properties, activities for making top up payment and other resettlement assistance, skill training for livelihood restoration to the affected persons, livelihood monitoring, etc.

3.2 Update of the Resettlement Plans

Four resettlement plans for section 1, 2, 3 and 4 received ADB approval. Two updated resettlement plans (section 5 and 6) are yet to be submitted to ADB. Section-wise Resettlement Plan status is presented below:

Section 1: Water Intake Area

Resettlement Plan received ADB approval on 19 November 2018. This is being updated further to include payment data and dedicated account details. Expected date of submission to ADB is 31 July 2020.

Section 2: Water Intake to Baliapara (End of Araihasar)/Raw Water Pipeline

ADB has approved Resettlement Plan on 4 April 2019. This is also being updated further to include payment data and dedicated account details. Expected date of submission to ADB is 31 July 2020.

Section 3: Darikhandi Chak (start of Rugganj) to Murapara via Gandharbpur WTP

Resettlement Plan got ADB approval on 28 November 2019.

Section 4: Water Treatment Plant in Gandharbpur Area

ADB approved this resettlement plan on 19 November 2018. This is being updated further to include payment data and graveyard shifting details. Expected date of submission to ADB is 31 July 2020.

Section 5: Rugganj (West bank of Sitalakhya River) to Balu River (East bank)/treated

Resettlement Plan is being updated based on changed alignment. DORP is surveying new alignment. A map showing new and old alignment is attached as **Appendix A**

This updating delayed due to late collection of land details (alignment maps, plot index, etc) from PMU. COVID-19 pandemic was also a major constraint, which is still continuing. Expected date of submission is 31 October 2020.


Deputy Commissioner had served land acquisition notice and conducted the joint verification survey in this area in May 2019. PMU has informed the Deputy Commissioner about the change. Based on the change, Deputy Commissioner has cancelled previous LA case to issue a new LA case. LA notice will be served again. JVS will also be conducted by the next reporting period.

Section 6: Balu River (West bank) to Vatara along Madani Avenue up to Baridhara

No further development has been found regarding the update of the Resettlement Plan during this reporting period. PMU is still awaiting to get Central Land Acquisition Committee (CLAC) approval against their land acquisition proposal. DORP received land details (proposed alignment maps, plot index, etc.) from PMU in May 2020. COVID-19 hindered them in doing the survey. Considering the COVID-19 situation, they have planned to submit the resettlement plan by November 2020.

Land acquisition is taking time in this section. Due to this ADB suggested¹ that the resettlement plan will present land acquisition plan in two separate sections; private and government so that land can be handed over for construction by part. If there are delays in paying compensation to the affected persons, government land can be given to the contractors for the smooth operation of the project.

Figure 3.1: Resettlement Plan Approval Status

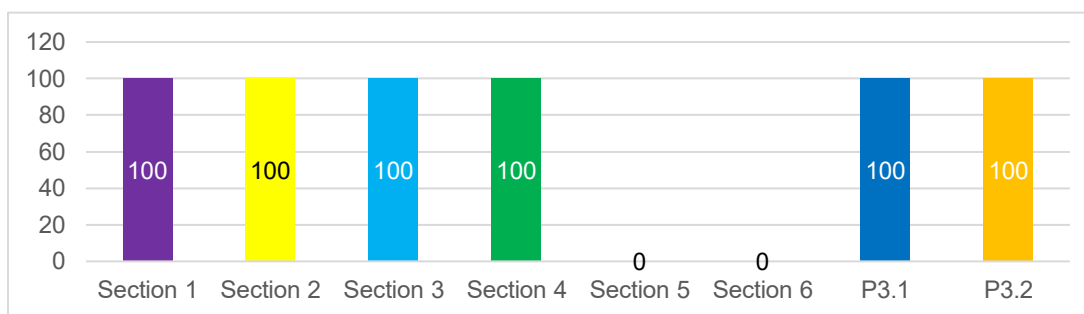

¹ Skype meeting with donors, PMU, MDSC and DORP on 19 May 2020

3.3 Compensation and Rehabilitation

3.3.1 Land Acquisition Progress

Land acquisition work is in progress for Section 1 (water intake area), Section 2 (raw water pipeline), Section 3 (part of raw and part of treated water pipeline) and Section 5 (treated water pipeline). DWASA has its own land for water treatment plan in Section 4. Deputy Commissioner has handed over required land for Section 1 and Section 2 to DWASA though 3.6% (0.6% in Section 1 and 3% in Section 2) compensation payment is still pending due to some reasons such as delay in affected persons' submitting necessary papers for CCL, legal issues with the land, conflict with co-sharers, expatriate affected persons, etc. Resolution of these cases may take time, which will delay implementation. To facilitate availability of encumbrance free land for civil works. DWASA has deposited the required CCL money with the Deputy Commissioner for payment, to be made available to the affected persons on the submission of the relevant land related papers.

ADB visited alignment in February 2020. Based on discussion on the way forward DWASA prepared an action plan for opening a dedicated account so that PMU can keep affected persons' receivable money (for top up and other resettlement benefits payment) intact. DWASA opened the account in the corporate branch of Janata Bank Ltd., Karwan Bazar on 12 February 2020. The account/customer ID is 0100210340372. This account will be operated by the joint signature of Project Director and Senior Finance and Accounts Officer of the project. This will only be used for the payment of resettlement assistance/benefits, not for any other purpose. After getting CCL, affected persons will contact INGO for getting top up and other resettlement benefits. This account will remain active and operational with the requisite balance due for the affected persons till the last unpaid affected persons even if project activities complete. A leaflet has been distributed amongst affected persons to disseminate information regarding purpose of the bank account, bank information, operation procedure, money keeping duration, etc. Copies of Bangla and English leaflet are attached as **Appendix B.1 and Appendix B.2**. A list of unpaid affected persons, who received leaflet on dedicated account has been attached with their due signature as **Appendix C**. In addition to the leaflet, DWASA with the assistance of INGO disseminated this information to the eligible affected persons through FGD and public consultation in presence of local government representatives. Minutes of the FGD and public consultation are attached as **Appendix D and Appendix E**. Through these meetings and leaflet affected persons have been requested to vacate the lands. DWASA needs to handover the land for civil works by September 2020. Otherwise, as per contract, DBO contractors will claim money for the delay. Affected persons, who participated in the meetings were agreed with DWASA's payment arrangement and gave consent for freeing the acquired land. DWASA is waiting for ADB approval for depositing money in this dedicated account. Before giving approval ADB needs to disclose respective updated resettlement plans. DWASA has prepared a due diligence record (DDR) on these activities and in the process of updating the resettlement plans for section 1 and 2 based on DDR findings and on payment (CCL+ resettlements benefits) data. DORP is working on resettlement plans and will submit by the end of the July 2020. The report has been delayed as DORP's Data Manager was affected by COVID-19. A copy of DD Record is attached as **Appendix F**.

In Section 1, all CCL recipient affected persons got additional payment (top up and other resettlement assistance) while about 96% of them received full payment in Section 2.

There was a temple in Section 2, which was constructed after cut-off-date. Several motivational meetings were held with the affected person (Ajit Mohan Das) for years. Eventually, he relocated that temple in February 2020, with his own initiatives. PMU helped him in the relocation.

Resettlement Plan for Section 3 covers 12 mouzas such as Darikandi Chak, Darikandi, Datterkandi, Golakandail, Tetlabo, Bhulta, Karnagop, Deboi, Noagaon, Gandharbpur, Brahmnagaon, and Shibganj. To facilitate land acquisition these mouzas have been divided into two LA cases; LA case 5 and LA case 10. Though LA case 10 also covers very small part of two mouzas (Harina and Rupanjan) under Resettlement

Plan Section 5. Deputy Commissioner has prepared Award Book for LA Case 5. The Deputy Commissioner sent an estimate to Project Director in June 2020 for depositing money in Deputy Commissioner's account for CCL payment. DWASA has deposited 50% of the previously estimated CCL amount. At this moment Project Director does not have money to deposit the remaining because the ministry cannot allocate money in this month due to new fiscal year. But he expected to deposit the money by the end of the July 2020. Deputy Commissioner's office has served LA notice under section 7 to the affected persons of this area. Award Book and estimate under LA Case 10 are yet to be prepared.

DWASA has completed payment to the affected persons of the Resettlement Plan Section 4.

PMU has resolved the graveyard issue with the community in Section 4. An MoU was signed on 27 January 2020 with the graveyard committee in presence of the Mayor of the Tarabo Municipality. Copy of the MoU is given in the **Appendix G**. Summary of the MoU is below:

- Community will leave the northern part of the graveyard for the sake of the water reservoir construction in the WTP. The same quantity of the land will be adjusted in the east and the west part of the graveyard. DWASA will give this land outside the WTP but adjacent to the graveyard.
- DWASA will construct 5 feet high boundary wall after joint inspection and finalization by the Graveyard Committee and DWASA representatives. Graveyard committee will cooperate with DWASA.
- All graves from the northern part land will be relocated. Graves will be counted and listed by the joint effort of Atani Samaj Graveyard Committee, INGO, Atani Samaj Masjid Committee, local elites, imam of local mosques and DWASA representatives.


Graveyard Committee will relocate all graves following religious rituals. DWASA will bear expenses of relocation. As per the agreement, all graves have been relocated in the agreed graveyard in presence of the Graveyard Committee. DWASA paid BDT. 500,000 to the graveyard committee as relocation expenses. The committee representatives cooperated with DWASA representatives in relocation of the graves and the reservoir construction on the land adjacent to the graveyard. DWASA constructed boundary wall for three sides. About 70% of the earthwork has been completed. After completion of the earthwork, construction of the other side of the boundary wall and main gate will be started. In addition to the MoU, DWASA will also install lighting and water facilities inside the graveyard.

A map of the newly arranged graveyard is presented under **Appendix H**.

Some photos of temple relocation of Section 2, signing ceremony of MoU, graves relocation religious ritual, dug graves and construction inception of boundary walls in Section 4 are shown in **Appendix I**.

Resettlement Plan for Section 5 covers 3 mouzas; Naora, Harinagram and Ruppangj. These were under LA case 11. However, Deputy Commissioner will launch a new LA case here subject to CLAC approval of changed alignment.

Compensation and rehabilitation process could not be started in the Resettlement Plan Section 6 since CLAC has not approved land acquisition proposal yet.

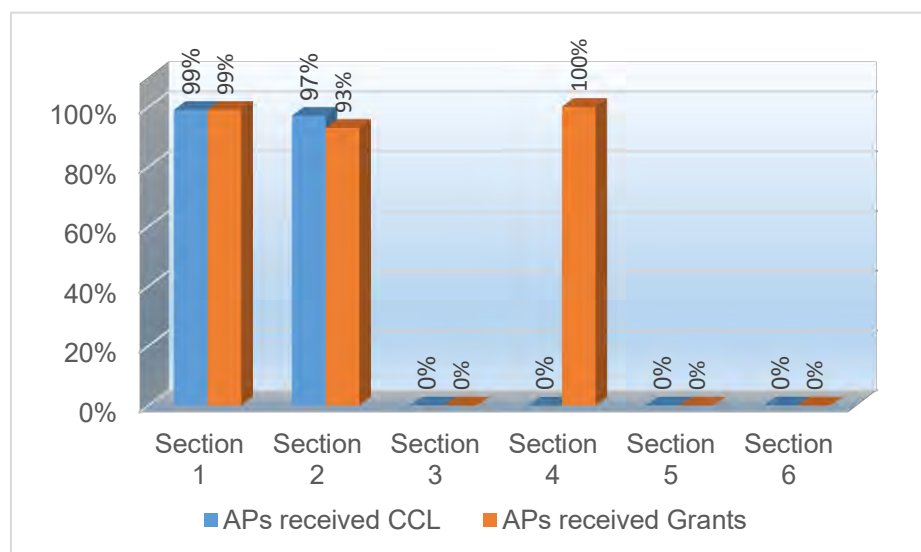Figure 3.2: Payment Status in all Sections

The Table 3.1 below summarizes section-wise progress of land acquisition and compensation payment.

Table 3.1: Progress of Land Acquisition (LA) and Compensation Payment

Sections	Project Locations	Land Acquisition	Compensation (CCL+Other Resettlement Assurances)
Section1 (Water Intake)	Water Intake area	DC office has handed over land to DWASA under LA case 3/2015-16 by March 2019.	Out of 338 ² affected persons, 336 (99.4%) have received CCL along with top up and other resettlement benefits. The remaining could not be paid because of unresolved legal problem with their land ownership document. No new payment has been made in this reporting period. Land has been vacated by the affected persons.
Section2 (Raw water pipeline)	Intake to Baliapara (End of Araihasar)	DC office has handed over land to DWASA under LA case 3/2015-16, 4/2015-16, 5/2015-16 and 6/2015-16 by March 2019.	<p>PMU collected affected persons list from the Deputy Commissioner office. In total 2523 affected persons have been identified. Of them, 2447³ (97%) got CCL up to June 2020. Additional resettlement assistance has been paid 2338 (93%) up to June 2020. INGO has submitted estimate to PMU for the rest 59 affected persons, who could not be paid due to COVID-19 outbreak. They will be paid by July 2020 maintaining health and safety. List of paid affected persons is given as Appendix J</p> <p>In this section, 17 business person (including 13 tenants) and 83 wage labors will be paid compensation for temporary relocation, decided by the Joint Verification Committee (JVC).</p> <p>Out of 290 structures 205 has already been relocated up to June</p>

² List of total numbers of CCL recipient affected persons sometimes may not match with the total number of resettlement assistance recipients because in some cases Deputy Commissioner counts a single affected person more than once in case of having ownership of more than one plots i.e., as many times as he/she receives CCL against each plot but INGO counts the affected person once irrespective of the number of times the affected person receives CCL. INGO prepares payment voucher based on one identity card, not on plot numbers. However, database is being updated. This discrepancy will be adjusted with the Deputy Commissioner's list in the next SSMR. Though it was expected to be completed by this reporting period but that could not be done due to the COVID-19 pandemic since March 2020. PMU has deployed one PMU staff and one DORP staff to check and match both data. It is expected to be rectified by the next SSMR.

³ Here, 1329 individual affected persons received 2447 payments. Numbers include payment for land+structures+trees. Some affected persons have been double counted as they own more than one plots.

Sections	Project Locations	Land Acquisition	Compensation (CCL+Other Resettlement Assurances)
			<p>2020. Some photos of newly built structures⁴ has been given in the Appendix K</p> <p>A list of structures⁵, which are yet to be relocated is appended as Appendix L. DWASA with the help of INGO is following up the timely relocation of the affected persons. Project Director will seek Deputy Commissioner's authoritative help in this regard.</p> <p>DWASA paid shifting allowance for one graveyard and one private grave in this reporting period.⁶</p>
Section 3 (Part of raw and part of treated water pipeline)	Darikandi Chak (start of Rupganj) to Murapara via Gandharbpur WTP	DC submitted estimate to Project Director for CCL payment. Award Book for the rest part is yet to be prepared.	Payment is yet to be started.
Section 4 (Water treatment plant)	Water Treatment Plant in Gandharbpur	DWASA owned land.	All affected persons (100%) have been paid compensation as non-titleholders. Land is free and civil works is going on. Graveyard has been relocated by the DWASA.
Section 5 (Treated water pipeline)	Rupganj (West bank of Sitalakhya River) to Balu River (East bank)	DC has cancelled previous LA case. Deputy Commissioner will launch a new case after getting CLAC approval.	Payment is yet to be started.
Section 6 (Treated water pipeline)	Balu River to Vatara Baridhara.	DWASA yet to get CLAC approval against acquisition proposal.	Payment is yet to be started.

Source: DORP and DWASA

The above table shows that land acquisition process of Package 1 (Resettlement Plan Section 1, 2 and 4) is in a progress except part of Section 3. Compensation payment of Package 2 (Resettlement Plan Section 3, 5 and 6) has not started yet.

Deputy Commissioner is paying CCL for Resettlement Plan Section 1 and 2. DWASA is also disbursing resettlement assistance efficiently in these two sections. Lands under Resettlement Plans for Section 1 and 2 area are being acquired following ARIPO, 1982. WTP land acquisition also followed this ordinance. However, Lands under Resettlement Plan for Section 3, 5 and 6 are being acquired following ARIPA, 2017. A detailed status of the land acquisition process of six sections is presented in two separate tables below. Table 3.2 presents status for Section 1, 2 and 4 while Table 3.3 describes Section 3, 5 and 6. Figure 3.1 and Figure 3.2 also follow the same sequence.

⁴ There are 24 mouzas in the Section 2. Out of those, 9 mouzas do not have any affected structures. In another 15 mouzas have affected structures, of which one mouza has only one structure, which is yet to be relocated and another has a small part of a structure. Due to this reason photos have been given from 11 mouzas.

⁵ There are 85 (primary+secondary) structures are still to be relocated in the raw water pipeline out of which 46 have been fully paid. To vacate land, relocation notice has been issued to the affected persons at the date of their resettlement benefits payment. In addition, announcements were made 4 times throughout the area.

⁶ The total area of the graveyard is 26 decimals. Large part (21.14 dec.) of it was inside the project alignment. Graveyard Committee received CCL from the Deputy Commissioner's office. In January 2020, DWASA has paid assistance for the relocation of the graves. Graveyard Committee had claimed BDT 2.75 lac as allowance for the shifting of the human remains from the project alignment. DWASA has given them BDT. 3 lacs. Graveyard committee has shifted all human remains on their own initiatives using this money. In Kamaldi Mouza, one private grave has also been shifted by the affected person. In February 2020, DWASA paid BDT 10,000 as shifting allowance as per affected person's claim.

Table 3.2: Taskwise Land Acquisition Progress of Resettlement Plan (RP) Sections 1, 2 and 4

	Task	Complete for RP Sections			Action by	Remarks	
		RP Sections:	1	2			4
			Araihazar				Rupganj
1	Submission of LA Proposal to Deputy Commissioner (DC)					Time needed: 6 months	
1	Administrative approval from the ministry (MLGRDC)	100	100	NA ^[1]	DWASA responsible	Done	
2	Layout Plan, LA Plan including plot schedule, Cadastral Maps and <i>Khatiyans</i>	100	100	NA	DWASA responsible	Done	
3	Maximum Land Requirement Certificate from MLGRDC	100	100	NA	DWASA responsible	Done	
4	Fund Allocation Assurance	100	100	NA	DWASA responsible	Done	
2	Administrative Approval from LGD Ministry (It took 6 months for RP Section 1 and 2)						
1	Feasibility Study done by Deputy Commissioner + given to CLAC	100%	100%	NA	DC responsible (after receipt of proposal from DWASA/ Mo land, Deputy Commissioner has max 21 day)	Actual time taken:4 months	
2	Upon CLAC approval Deputy Commissioner starts LA case and issues notice under section 3 of the LA Ordinance.	Jan-Mar 2017 100 %	Jan-Mar 2017 100 %	NA	DC responsible	Actual time taken:3 months	
3	Joint verification by Deputy Commissioner and DWASA.	Jan-Mar 2017 100%	Jan-Mar 2017 100%	NA	DC (Legal time: 3 days)	Actual time taken:3 months	
4	Objection (u/s 5) against acquisition proposal. ⁷	Jan-May 2017 100%	Jan-May 2017 100%	NA	affected persons (AP)	Actual time taken:5 months	

⁷ Objection may be made by affected persons (AP) within 15 days after LA notice section 4.

	Task	Complete for RP Sections			Action by	Remarks	
		RP Sections:	1	2			4
			Araihazar				Ruganj
5	Objection hearing and reporting by DC.	May 2017 100%	May 2017 100%	NA	DC responsible (After expiry of objection period within 30 days)	Actual time taken: 1 day	
6	Approval by Deputy Commissioner. ⁸	NA	NA	NA	Deputy Commissioner/DvC responsible.	No objection	
7	Return the proposal to Deputy Commissioner with decision of the MoL.	NA	NA	NA	Deputy Commissioner/DvC (from submission of the report by Deputy Commissioner. Time limit: 15 days and 90 days respectively)	No hearing	
3	Notice served and invite claim from persons interested under section 7	NA	NA	NA	Deputy Commissioner responsible [After approval by Deputy Commissioner/DvC /MoL]	No claim received	
1	Hearing on claims (if there is)	NA	NA	NA	DC responsible (Legal time: 15 days after notice u/s 7)	No hearing	
4	Collection of rates/price of assets to be acquired from different agencies	100	100	100	-	-	
1	Sub-Registrar's Office for Land	Jan-Feb 2017 100%	Jan-Feb 2017 100%	NA	Deputy Commissioner responsible (Legal time: 2 months)	Actual time needed: 1 month	
2	Public Works Department for Structure	May 2017 100%	May 2017 100%	100%	DC responsible (Legal time: 1 month)	Actual time needed: 1 month	
3	Department of Forest for Trees	May 2017 100%	May 2017 100%	100%	DC responsible (Legal time: 1 month)	Actual time needed: 1 month	
4	Dep Agriculture + Marketing for Crops	May 2017 100%	May 2017 100%	100%	DC responsible (Legal time: 1 month)	Actual time needed: 1 month	
5	Department of Fisheries for Fish Stock	May 2017 100%	May 2017 100%	100%	DC responsible (Legal time: 1 month)	Actual time needed: 1 month	
5	Make award and estimate for compensation by Deputy Commissioner. Claim fund from DWASA	100%	100%	NA	DC: After notice u/s 7/8 (Legal Time: 30 days)	Actual time needed: 7 days	
6	Deposit of compensation money to Deputy Commissioner by (DWASA)	100%	100%	NA	DWASA responsible (From date of estimate from Deputy	Actual time: 10 days	

⁸ If quantity of land below 7 ha and if no objection. If there is objection, DC sends record with report to the Govt. or to Divisional Commissioner (DvC). If land quantity is less than 7 ha should take 10 days. If more land, can take 30 days after objection period.

	Task		Complete for RP Sections			Action by	Remarks
	RP Sections:		1	2	4		
			Araihazar		Rugpanj		
						Commissioner. Legal Time limit: 120 days)	
7	Notice to persons interested (u/s 7) for updating Record of Rights and receiving cash compensation (CCL)		100%	100%	NA	DC responsible (From the date of award of compensation, Legal Time: 7 days)	Actual time: 1 month
8	Payment of compensation (CCL) (u/s 10) by Treasury cheque					DC: From deposit of compensation money by DWASA Time limit: 60 days	
	1	affected persons (AP) receive CCL	Start Jul 2017 336 (99%)	Start Jun 2017 2447 (97%)	NA	Entitled Persons responsible to receive (Legal Time: Max 15 days after issue of notice under section 7)	On-going; PMU collected from the Deputy Commissioner's office the list of total awardees and awarded for RP Section 1 and 2.
9	Compensation deemed to have been paid		Yes	Yes	0	DC responsible (After expiry of above 60 days u/s 10)	Though CCL payment still pending, following ARIPO 1982, Deputy Commissioner has handed over acquired lands for RP Section 1 and 2 to DWASA.
10	Application to Arbitrator (u/s) 28					AP/DC/DvC: From the date of serving notice of award, Legal Time limit: 45 days	
	1	Complain to the Deputy Commissioner	Yes	Yes	NA	DC: can add 10% of entitled CCL after positive verdict.	Settled by Deputy Commissioner's office
	2	If unsatisfactory verdict, arbitration to DvC	Yes	Yes	NA	DvC: can add another 10%	Settled by Deputy Commissioner's office
11	Copies of CCL Cheque Submitted to INGO		6/1/2017 (cheque received 336)	6/1/2017 (cheque received 1027)	NA	DORP/DWASA responsible	DC office provided a list showing that they have paid CCL to 2306 APs out of 2447 awardees.
12	Additional Payment/Top up pay as per PVAC recommendations; DWASA/INGO after Resettlement Plan Approval						
	(Time needed: 2 months after RP approval)						

	Task	Complete for RP Sections			Action by	Remarks	
		RP Sections:	1	2			4
			Araihazar				Ruganj
1	CCL Statement Prepared by INGO	100% of the documents received	100% of the documents received	NA	DORP Responsible	Continuous process subject to CCL receipt.	
2	Prepare ID Card with Photo	100% of CCL recipient APs	100% of CCL recipient APs	100% of total squatter APs	DORP: after Copies of CCL Cheque received	Do	
3	Prepare affected person file and EC	100% of CCL recipient affected person files and entitlement card ready	100% of CCL recipient affected person files and entitlement card prepared	100%	DORP responsible	Do	
4	Prepare Estimate	100% of CCL documents received	100% of CCL documents received	100%	DORP responsible	Do	
5	Prepare payment voucher by INGO and Submit to DWASA.	100% of CCL documents received	100% of documents received	100%	Compared to DORP could manage CCL papers so far	Do	
6	Other Resettlement Benefits as per RP Policy	100% of CCL documents received	98% of CCL recipients	100%	DWASA/DORP	Do	
7	Payment of all grants	100% of CCL documents received	98% of CCL recipients	100%	DWASA/ DORP	Do	
13	Compensation/Benefits/Grants as per GRC Decision				DWASA/DORP/GR C responsible upon RP approval	RPs for Section 1, 2 and 4 have been approved by ADB. These are now being further updated to include information on the dedicated account.	
1	Propose + Approve GRC	100%	100%	100%	DWASA + LGD responsible	GRC has been approved by LGD.	

	Task RP Sections:	Complete for RP Sections			Action by	Remarks
		1	2	4		
		Araihazar		Rugganj		
2	GRC is functioning Y or N?	Yes	Yes	Yes	DWASA responsible	Eighty-eight (88) GRC complaints have been filed in three sections. Two hearings held up to June 2020 for 32 cases dealt with in Section 1 and 2. More hearing required for Section 4.

[1] Section 4 is WTP. DWASA's own Land

* Section #1 = Intake, #2 = RW pipeline, #4 = WTP

KEY Action required

Table 3.3: Land Acquisition Progress of Resettlement Plan (RP) Sections 3, 5 and 6

Sl. No.	Task	Complete for RP Sections			Action by	Remarks	
		RP Sections:	3	5			6
		Upazila	Rugganj				
1	Submission of LA Proposal to Deputy Commissioner (DC) by DWASA					It took 6 months	
1	Obtaining administrative approval from the concerned ministry (MLGRDC)	100	100	100	DWASA	Done	
2	Layout Plan, LA Plan including plot schedule, Cadastral Maps and <i>Khatiyans</i>	100	100	100	DWASA	Done	
3	Maximum Land Requirement Certificate from MLGRDC	100	100	100	DWASA	Done	
4	Fund Allocation Assurance	100	100	100	DWASA	Done	
2	Administrative Approval from LGD Ministry						
1	Feasibility Study done by Deputy Commissioner + given to CLAC	100%	0 (Previous LA case cancelled)	0	DC (after receipt of proposal from DWASA/ MoL) Legal Time:21 days	Actual time needed: 4 months for previous one but CLAC approval need again due to alignment change in RP Section 5.	
2	Upon CLAC approval Deputy Commissioner starts LA case and issues notice under Section 4(1) of the LA Act 2017.	100%	0 (Previous LA case cancelled)	0	DC	Actual time needed: 6 months for previous one but CLAC approval need again.	
3	Joint verification by Deputy Commissioner and DWASA should be 3 days after issuance of notice under Section 4	100%	0 (Previous LA case cancelled)	0	DC, Legal time: 3 days	Actual time needed: 6 months for previous one. New JVS needed in RP Section 5.	

Sl. No.	Task		Complete for RP Sections			Action by	Remarks
	RP Sections:		3	5	6		
	Upazila	Rupganj					
4	Objection (u/s 5) against acquisition proposal.	100%	NA	0	Affected Persons, Legal time: 15 days	Objection has been registered by one affected person in RP Section 3 under LA case 5/2018-19. No objection reported in RP Section 5. No LA notice has been served yet in RP Section 6.	
5	Hearing of Objection by Deputy Commissioner and preparing report	100%	NA	0	DC: After expiry of objection period within 30 days	Do	
6	Approval by Deputy Commissioner if quantity of land below 7 ha and if no objection. If there is objection, Deputy Commissioner sends record with report to the Govt. or to Divisional Commissioner (DvC)	0	NA	0	DC/DvC: if land quantity is less than 7 ha should take 10 days. If more land, can take 30 days after objection period	Decision pending against objection for RP Section 3 under LA case 5/2018-19. No LA notice has been served yet in RP Section 6.	
7	Return the proposal to Deputy Commissioner with decision of the Ministry of Land.	0	NA	0	Deputy Commissioner/DvC: from submission of the report by Deputy Commissioner. Time limit: 15 days and 90 days respectively; (No hearing)	Do	
3	Notice served and invite claim from persons interested under Section 8	0	0	0	Deputy Commissioner: After approval by Deputy Commissioner/DvC/MoL; (No claim received)	This LA notice yet to be served.	
1	Hearing on claims (if there is)	0	0	0	Deputy Commissioner: 15 days after notice u/s 7/8; (No hearing)	Do	
4	Collection of rates/price of assets to be acquired from different agencies					On-going by Deputy Commissioner's office	
1	Sub-Registrar's Office for Land	100	0	0	DC, Legal Time: 2 months	Do	
2	Public Works Department for Structure	100	0	0	DC, Legal Time: 1 month	Do	
3	Department of Forest for Trees	100	0	0	DC, Legal Time: 1 month	Do	
4	Dep Agriculture + Marketing for Crops	100	0	0	DC, Legal Time: 1 month	Do	
5	Department of Fisheries for Fish Stock	100	0	0	DC, Legal Time: 1 month	Do	
5	Make award and estimate for compensation by Deputy Commissioner. Claim fund from DWASA	50	0	0	DC: After notice u/s 8.; Legal Time: 30 days	Notice served to the affected persons under LA case 5.	
6	Deposit of compensation money to Deputy Commissioner by DWASA	50	0	0	DWASA: From date of estimate from Deputy Commissioner. Legal Time limit: 120 days)	Actual time: 10 days	

Sl. No.	Task		Complete for RP Sections			Action by	Remarks
	RP Sections:		3	5	6		
	Upazila		Rupganj				
7	Notice to persons interested (u/s 8) for updating Record of Rights and receiving cash compensation (CCL)		0	0	0	DC: From date of award of compensation.; Legal Time limit: 7 days	LA notice has been served to LA case 5
8	Payment of compensation (CCL) (u/s 10) by Treasury cheque					DC: From deposit of compensation money by DWASA Time limit: 60 days	No notice has been served
	1	Affected Persons (AP) receive CCL	0	0	0	Entitled Persons: Max 15 days after issue of notice under section 4	Do
9	Compensation deemed to have been paid		0	0	0	DC: After expiry of above 60 days u/s 10.	Compensation not started
10	Application to Arbitrator (u/s) 28					AP/DC/DvC: From date of serving notice of award.; Time limit: 45 days	Not applicable
	1	Complain to the Deputy Commissioner	0	0	0	DC: can add 10% of entitled CCL after positive verdict.	Do
	2	If unsatisfactory verdict, arbitration to DvC	0	0	0	DvC: can add another 10% Settled by Deputy Commissioner's office	Do
11	Copies of CCL Document Submitted to INGO		0	0	0	DC	Not applicable
12	Additional Payment/Top up pay as per PVAC recommendations; DWASA/INGO after Resettlement plan (RP) Approval (Time needed: 2 months after RP approval)						
	1	CCL Statement Prepared by INGO	0	0	0	DORP	Not applicable
	2	Prepare ID Card with Photo	0	0	0	DORP: after Copies of CCL Cheque received	Do
	3	Prepare affected person file and EC	0	0	0	DORP	Do
	4	Prepare Indent subject to RP Approval	0	0	0	DORP: after RP Approval by ADB+ LGD ministry	Do
	5	Prepare necessary papers and documents by INGO and Submit to DWASA for payment	0	0	0	DWASA/DORP	Do
	6	Other Resettlement Benefits as per RP Policy	0	0	0	DWASA/DORP	Do
	7	Payment of all grants	0	0	0	DWASA/ DORP	Do
13	Compensation/Benefits/Grants as per GRC Decision					DWASA/DORP/GRC	Not applicable
	1	Propose + Approve GRC.	100%	100%	100%	DWASA + LGD: GRC has been approved by LGD.	Do
	2	GRC is functioning Y or N?	N	N	N	GRC cannot function until RP approved by ADB + LGD.	RP for Section 3 has been approved in November 2019. GRC yet to be declared here.

* Section #3 = RW+TW Pipeline in Rupganj, #5 = TW Transmission to Dhaka, #6 = TW Pipelines inside Dhaka.

KEY Action required

Figure 3.3: Land Acquisition Progress for Resettlement Plan Section 1, 2 and 4


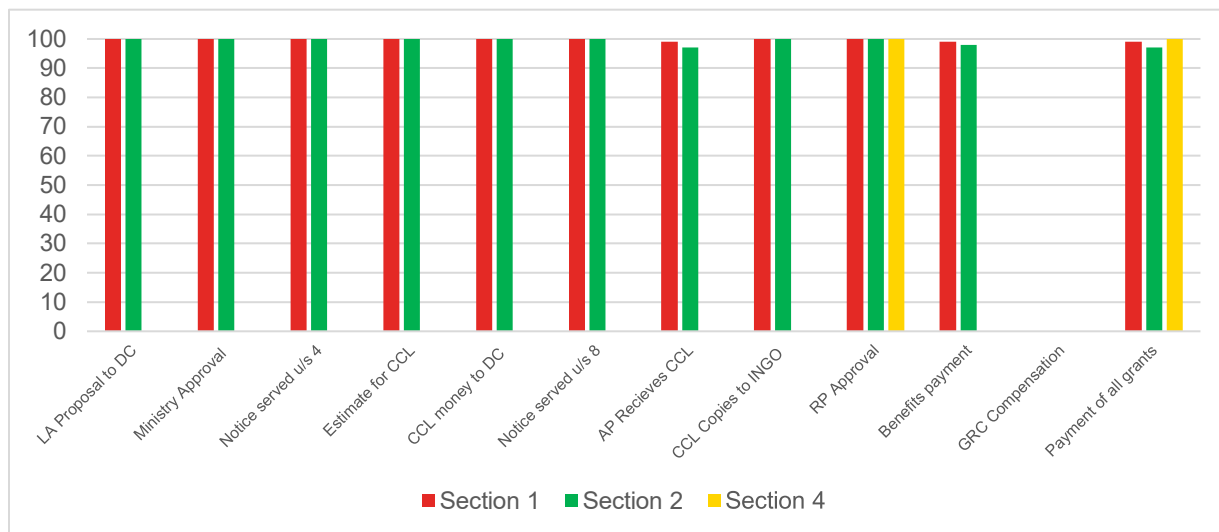


Figure 3.4: Land Acquisition Progress for Resettlement Plan Section 3, 5 and 6

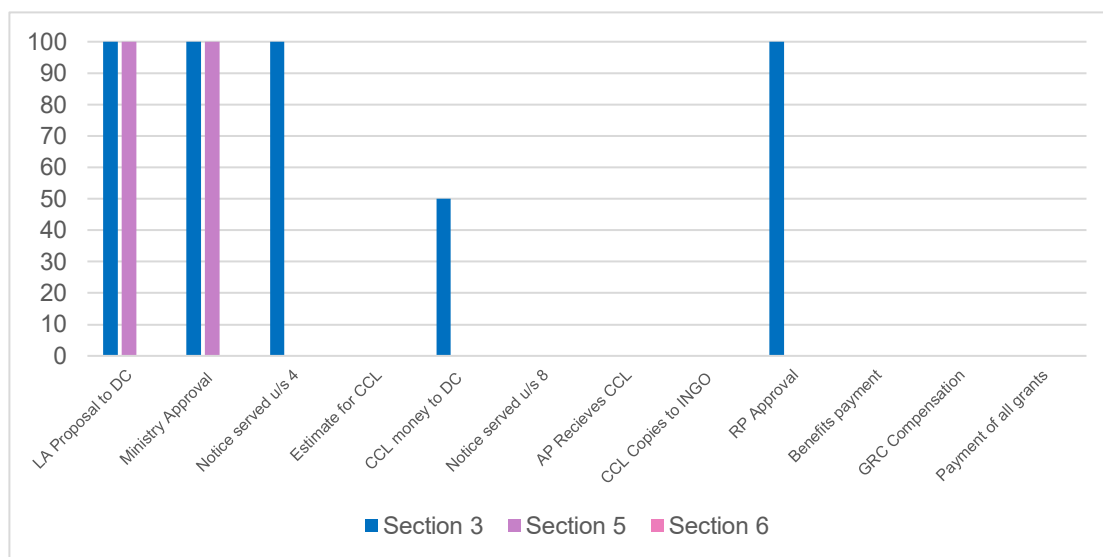

In section 1 and 2, according to the data provided by the Deputy Commissioner’s office there should be only 78 affected persons who are yet to receive CCL. However, INGO identified 180 affected persons from the field who have problem in establishing their land ownership to the Deputy Commissioner. List of 106⁹ affected persons from 21 priority mouzas was attached with the last SSMR. List of remaining 74 affected persons from the non-priority 3 mouzas is given as **Appendix M** To resolve aforesaid data discrepancy, PMU is working in Deputy Commissioner’s office to recheck and find out actual numbers of affected persons. DORP’s data management team is assisting PMU in this regard.

DORP is assisting entitled persons in receiving CCL by preparing legal papers and introducing them to the Deputy Commissioner’s office. In addition, they are conducting awareness campaigns informing that fair compensation will be paid, and the project authority will ensure all payments are made directly to

⁹ List had been appended in the last SSMR.

the affected persons. Community meetings, personal contacts, leaflet distribution, announcement all over the area using mike, etc. have been conducted to motivate affected persons with regard to receive CCL papers and top up plus other resettlement assistance by submitting proper documents in a timely manner.

Encumbrance free land under raw water pipeline must be given to the DBO contractor for civil works by September 2020. However, the above mentioned CCL unpaid affected persons have legal problems in submitting papers required for compensation. Types of problems found are conflict with co-sharers, mutation not done for the land, on-going court case, vested property, wrong name inclusion in the Deputy Commissioner's provided land acquisition notice, etc. Despite INGO's cooperation, resolution of the cases is likely to take a long time. As mentioned earlier, PMU opened a dedicated account for these affected persons in which their receivable compensation will be intact. Thus, affected persons will cooperate in vacating their land for construction works.

PMU has given notice several times to the affected persons for dismantling 46 fully paid structures. Moreover, in January and February 2020 PMU announced last dates of structures relocation using mike throughout the raw water pipelines area. Despite all the efforts, the affected persons did not vacate the land. PMU will seek help from the Deputy Commissioner to take legal action in dismantling by July 2020. Compensation money for the structures, which are facing legal problems, deposited in the dedicated account so that the affected persons can get their money at the time of their CCL receipt.

Payment to non-titled affected persons

There are 111 affected households identified in the resettlement plan section 2. Out of them 18 are business persons, 5 are textile mill owners, 2 are dairy farm owners, 1 poultry farm owner and 83 are wage labourers who have been working these employment sector. A joint verification survey was conducted in February 2020. After verification, Joint Verification Committee (JVC) found 17 business persons (including 13 tenants), and 83 wage laborers as eligible for getting resettlement assistance according to entitlement matrix of resettlement framework. According to Resettlement Framework tenant business persons will get cash compensation, calculated at the amount of income lost during the period of disruption. Compensation will be paid regardless of whether or not the business closes during the construction period. These business persons and their employees have been waiting for getting eviction notice and entitled compensation by the DWASA for about 4 years, as there was no decision taken on this. The JVC considered and decided that these business persons and their 83 wage employees should get compensation money equivalent to their 3 months' average monthly income. In case, any of them earn monthly income more than national tax payable amount per month but cannot show income tax identification number (TIN), they will get compensation at par non-tax payable amount of monthly income. Bangla and English version of the minutes of JVC meetings are attached as **Appendix N.1 and N.2 respectively**, where list of payable business persons provided. A list of payable wage labours is attached as **Appendix O**.

3.3.2 Progress in Livelihood Restoration

In total 119 (46 in Section 1 and 83 in Section 2) affected persons received training on Livelihood and Income Restoration Program (LIRP). In this reporting period, 46 affected persons (there are 43 vulnerable persons and 3 persons are incurring full loss to agriculture-based livelihood) of Section 1 have been imparted this training. Half of them received training on cow and goat rearing and another half on chicken and duck rearing. Trade wise disaggregation of total and male-female participants are given below:

Table 3.4: Details of Training on LIRP

Category of training	Total participants				
	Female			Male	Total
	Female headed HHs	Male headed HHs	Total		
Cow & goat rearing	3	2	5	18	23
Chicken & duck rearing	11	2	13	10	23
Total	14	4	18	28	46

After

successful completion of the training each of them received BDT. 20,000 as investment allowance upon submission of investment plan. A list of the trained affected persons is given in **Appendix P**.

In Section 2, 289 eligible affected persons (vulnerable:212 and full loss of agriculture-based livelihood:77) have been identified for Livelihood and Income Restoration Program on different trades such as poultry, cattle rearing, fish culture, vegetable cultivation, small trading, tailoring and seasonal crops etc. Out of 289 eligible affected persons, 218 are from male headed households and 71 are from female headed households. Field staff completed training needs assessment for 252 eligible affected persons for identification of specific trade for training. The training need assessment for remaining 37 identified eligible affected persons will be completed by the next quarter. LIRP training was scheduled from 22 March 2020. DORP has planned to impart training to the remaining 6 affected persons in Section 4 at the same time. However, due to COVID-19 outbreak, the training program has been postponed. It will happen after COVID-19 situation improves.

In Section 4, Out of trained 83 vulnerable affected persons, 77 (93%) are engaged in income generating activities. In Section 1 out of the 46 trained vulnerable affected persons and 42 (91%) are engaged in income generation activities. In total 119 (92%) trained affected persons started IGA and the rest could not do due to insufficient space for cow and goat rearing, shortage of funds, sickness, untold personal reasons and COVID-19 situation, etc. Status of engagement in income generation activities is as follows.

Table 3.5: Status of IGA Engagement of the Trained Affected Persons

Category of training	Total trained			Engaged in IGA			Reason for not started IGA
	Section 1	Section 4	Total	Section 1	Section 4	Total	
Tailoring	None	12	12	N/A	10 (83%)	10 (83%)	<ul style="list-style-type: none"> • Insufficient place for Cow & Goat rearing • Shortage of fund • Sickness • COVID-19 outbreak
Small Business	None	14	14	N/A	12 (86%)	12 (86%)	
Cow and Goat rearing	23	44	67	21(91%)	43 (98%)	64(96%)	
Chicken and Duck Rearing	23	13	36	21(91%)	12 (92%)	33(54%)	
Total	46	83	129	42(91%)	77 (93%)	119(92%)	

Resettlement Plan Section 3, 5 and 6 could not start payment and so to LIRP.

3.3.3 Overall Progress

MDSC social safeguard team reviewed DORP's monthly and quarterly progress reports. In this reporting period, MDSC reviewed six (6) Monthly Progress Reports and two (2) Quarterly Progress Reports and one (1) Livelihood Monitoring Report which have been received in this period (January to June 2020). MDSC provided feedback with specific comments to DORP for improving their quality of documentation and other

works to focus on the critical issues. With reference to those reports, the progress made so far by the DORP up to June 2020 is presented in the Table 3.6 as follows:

Table 3.6: Cumulative Progress up to 30 June 2020

Tasks as per Work Plan	Section 1		Section 2		Section 3		Section 4		Section 5		Section 6		Causes of delay
	Total	%	Total	%	Total	%	Total	%	Total	%	Total	%	
Resettlement Plan Updating													
SES data collection from Affected Household Heads	87	100	1178	100	434 (Resurvey May-June 2019)	100	253	100	116	100	136	100	Completed
RP updating/Preparation	ADB approved on 19 November 2018	100	ADB approved on 05 April 2019	100	ADB approved on 28 November 2019	100	ADB approved on 19 November 2018	100	Draft submitted to ADB (29 September 2019)	100	Zero Draft submitted to ADB (24 September 2018)	100	Updating RP delayed. ¹⁰
Conducted Consultation meeting with AHs	6	100	12	100	8	100	8	100	6	100	5	100	No consultation meeting held from January to June 2020
Implementation of RP													
Personal contact established with AHs and other Stakeholders	1995	103	5067	105	5538	103	1816	102	2171	100	1613	>100	Percent calculated on monthly cumulative average number of target and achievement.
Community meetings held with AHs and other Stakeholders	79	100	126	100	217	100	56	100	72	100	49	100	It is continuous process. As per month wise target achievement it is more

¹⁰ Section-5 delayed due to change of alignment. Section 6 delayed for finalization of alignment. Moreover, COVID-19 hindered updating of both.

Tasks as per Work Plan	Section 1		Section 2		Section 3		Section 4		Section 5		Section 6		Causes of delay
	Intake		Total	%	Total	%	Total	%	Total	%	Total	%	
													than 100 percent.
Distributed Leaflets to AHs and other Stakeholders	1,010	100	2140	100	531	100	345	100	262	90	280	100	Almost completed for all sections.
Distributed Booklets to AHs and other Stakeholders	300	100	700	100	950	100	251	100	210	90	100	100	Almost completed for all sections
Joint verification survey completed by DWASA /DC assisted by DORP	21.38 Acre	100	110.15 Acre	100	66.85 Acre	100	DWASA land; JVS done by DWASA	-	21.48 Acre	100	Proposed 6.96 Acre (Not done)	-	Section 6 awaiting for CLAC approval
Video Filming done	21.38 Acre	100	110.15 acre	100	66.85 Acre	100	81.53 acre	-	21.48 Acre	100	do	-	do
Assisted Deputy Commissioner office to disburse the notice under section 3 or 4 (1) to Affected Persons	260	100	2660	100	2056	100	Not applicable (DWASA land)	-	1428	100	do	-	do
Distributed the Notice under section 6 or 7 (1) (ka) to affected persons	180	100	2985	100	Served partially	-	do	-	Yet to be served	-	do	-	do
Distributed the Notice under section 7 or 8 (3) (ka) to affected persons	87	100	1933	100	Yet to be served	-	do	-	Not Yet served	-	do	-	do
Affected persons received CCL	336	99	2447	97	Not applicable	-	Not applicable	-	Not applicable	-	do	-	do
CCL Statement Preparation	336	99	2447	97	Not applicable	-	do	-	Not applicable	-	do	-	-
CCL related	336	99	2447	97	Not	-	do	-	do	-	do	-	-

Tasks as per Work Plan	Section 1 Intake		Section 2		Section 3		Section 4		Section 5		Section 6		Causes of delay
	Total	%	Total	%	Total	%	Total	%	Total	%	Total	%	
papers collection					applic able								
Top up payment / resettlement benefit made	336	99	2447	97	do	-	253	100	Not applic able	-	Not applic able	-	Subject to approval of RP and CCL payment made
Conducted Focus Group Discussion with eligible AHs to develop livelihood plan	6	100	18 As per MPR June 2020	100	9	100	11	100	7	100	2 (Planned to cover more 2 FGD meetings	50	
Developing LIRP training module	2	100	7	100	5 As per RP	100	4 As per RP	100	2 As per RP	100	2 As per RP	100	Developed 7 modules for the project and submitted to PMU for approval
LIRP training to APs (Vulnerable and fully loss of Agriculture based livelihoods)	46	100	Planned to start from mid-August 2020	-	Subject to completion of payment	-	83 vulnerable APs receive IGA training under LIRP	93	Subject to approval of RP	-	Subject to approval of RP	-	A total of 547 affected persons identified for LIRP training (as per MPR June 2020)
Database													
Developed software for data entry – This software to be updated to accommodate supplementary	1	100	1	100	1	100	1	100	1	100	1	100	Completed
Completed data entry using in "excel" sheet	87	100	1178	100	434	100	253	100	116	100	136	100	Completed
Submitted ID card sample to PMU, DESWSP for approval	1 (Approved)	100	1 (Approved)	100	1 (Approved)	100	1 (Approved)	100	1 (Approved)	100	1 (Approved)	100	Completed
Submitted	1	100	1	100	1	100	1	100	1	100	1	100	Completed

Tasks as per Work Plan	Section 1 Intake		Section 2		Section 3		Section 4		Section 5		Section 6		Causes of delay
	Total	%	Total	%	Total	%	Total	%	Total	%	Total	%	
Payment Voucher sample to PMU, DESWSP for approval	(Approved)		(Approved)		(Approved)		(Approved)		(Approved)		(Approved)		

3.4 Disclosure and Public Consultation

DORP adopts different techniques for information disclosure and consultation such as public consultation, community meeting, focus group discussion (FGD), personal contact, etc. In addition to regular personal contacts, in this reporting period they have conducted 42 community meetings, 1 large public consultation and 1 FGDs to develop resettlement and livelihood restoration plan in the Section 1, 2, 3, 4, 5 and 6. Total numbers of participants were 656 (308 male and 348 female). Eleven (11) DORP staff were present for conducting meetings in the two field areas of Arahazar and Rugganj. The summary minutes of the consultations is provided in **Appendix Q**. Main discussion issues were on papers required in receiving CCL and other resettlement benefits from DWASA, serving notice under section-7(1) and 8(3) (ka); per decimal payment rate for the affected land; of compensation and resettlement benefits in rehabilitation and income generating activities to make lives better, taking away or removal of the structures from the project acquired land; construction of new structures; changing of alignment; affected persons entitlements; explain dedicated account to the affected persons, assist to the project construction work; receiving IGA training under LIRP; Involvement in income generating activities; grievance redress mechanism; etc. Affected persons were very keen to know about above mentioned issues. Information on these matters were disseminated to them. INGO also motivated them to cooperate with resettlement implementation.

Key issues of information dissemination are mentioned below: The participants need papers for receiving compensation from Deputy Commissioner's office which include ownership document of the land, updated mutation and land tax receipt, national identity (ID) card, bank account number They will be paid by account payee cheque. DORP will try to ensure that payments are made fair and transparent. The INGO staffs will support them and will guide them in collecting papers accordingly.

- Unpaid affected persons, who were reluctant to give access to their land for civil works have been informed that their payment have been delayed mostly due to legal problem and lack of mutation according to RS record etc. So, as long as their problems will remain unsettled the compensation money will be kept safe in a separate dedicated account opened for them. As soon as the legal issues are solved, they would be able to receive their payments. The participants agreed to cooperate with the contractors during project construction work and vacate the land required by the project.
- As for additional payment, they will receive additional payment according to the current market value and according to the project entitlement matrix. INGO DORP will assist/guide them in preparing/collecting necessary papers to be submitted to DWASA for receiving additional payment and other resettlement benefits. Similar to CCL, this payment will be made by account payee cheque. Affected persons, who have already received CCL from Deputy Commissioner's office, will need to submit all those papers along with affected persons' identity card, photocopy of NID/SMART card, citizenship certificate from Union/Pauroshava Chairman, account number, share sheet etc. to DORP local office to get additional/resettlement benefits.
- Unpaid affected persons will get CCL from the Deputy Commissioner's office as soon as they submit required document. Till then their money will be safely kept in Deputy Commissioner's account for CCL and also in the DESWSP's separate dedicated account for resettlement assistance opened in Janata Bank by the PMU. Based on the circumstances, even after the project is over, the money will be kept safe in this exclusive account. After resolution of the ownership problems and subject to submission of

the necessary proper documents, the payment will be made to them from Deputy Commissioner's office and from the project office's dedicated account as well.

- Affected persons before dismantling of their structures will be fully paid, and they will get one- month time after making all payments meet up to dismantle their structures. Being assured from the project side they agreed to shift their structures and to make the project area free for project construction work. They requested to notify them before dismantling and allow them a reasonable time for shifting, otherwise they will not hand over their land or remove their structures etc.
- The alignment of section 5 has been changed. The pipeline in this section was passing through a housing complex named Jalshiri, which is owned by the Bangladesh military. Military authority has recently rearranged their plots and roads. Due to Jalshiri's rearrangements, DWASA found that resettlement impact would be more than before. So, to minimize the resettlement impact DWASA has changed the pipeline route in this section. Survey for the new plots will need to be carried out for updating of the resettlement plan. New LA case will be issued again after the CLAC approval.
- Notice will be served again. The participants were informed that serving notice under section 7(1) has been stopped due to the alignment change. Serving notice under section 7 (1) and 8 (3) (ka) will start again soon. After serving notice under section 8(3) (ka) they will be instructed to submit necessary papers to Deputy Commissioner's office for receiving compensation. After issue of notice under section 8 (3) (ka) is completed it will not take much time to receive compensation. The affected persons will get 200% premium on land loss and 100% premium on structures, trees, crops and fish stock from Deputy Commissioner's office. In addition, they will receive other resettlement benefits according to eligibility and entitlement matrix of resettlement framework.
- Affected persons, those have constructed structures or filled land after cut-off date i.e. after issue of notice under section 4(1), which was on 16 April 2019. will not be eligible to receive any compensation. These persons will have to remove any construction at their own cost, otherwise legal action will be taken against them by the government.
- The participants were interested to know the per decimal land value they will be paid. In response they have been informed that Deputy Commissioner's office collected land value *mouza* and land classification wise for the preceding one-year sale. The purchase rate of the land was averaged according to mouza and land classification. While the INGO has collected current actual sale and purchase price through interviewing local persons engaged in the different occupations according to mouza and land classification. Affected persons received the difference in value between the Deputy Commissioner's office's rate and INGO calculated current actual rate as additional/top up payment in addition to the Deputy Commissioner's office's CCL payment.
- DWASA will arrange several trainings for affected persons who are vulnerable and who lose full of their agriculture-based livelihood.
- The IGA training will be provided to them with an aim to re-establish or restart the loss of livelihood-based activities for enhancing households' income particularly giving emphasis to vulnerable women.
- They will be given an investment allowance after training receipt and on the submission of an investment plan. The money which they will receive as compensation and resettlement benefits will have to be used to rebuild the lost structures and restart their livelihood so that they can bring a positive change in their lives or at least at the level of pre project condition. Affected persons were advised not to use the compensation money/ resettlement benefits in unproductive ways.
- Training grant recipient affected persons will be monitored and advised regularly by the DESWSP's INGO, MDSC and PMU.
- The INGO will assist them in involving them with the local level credit institution and NGOs which can provide them technical and financial support.
- In response to the affected person's query of their grievances they were informed that at first, they will share their complaint to the INGO. The implementing NGO will assist the affected households in drafting


the grievances.. Complaints and grievances will be heard by the INGO and focus group discussions will be held at the village level. The grievance will need to be resolved within 1 day. If the grievance cannot be addressed by the INGO and the Social Safeguard Officer, PMU, the complainant can lodge complaint related to compensation or delay of payment to the GRC committee. DORP will arrange GRC meeting for resolving the complaint.

In addition to public consultations, approved resettlement plans for P1, P2 and P3.2, SSMRs, DDR for P3.1 have been disclosed on ADB and DWASA website though these are yet to be disclosed in the locality. Resettlement plans for Sections 1, 2, 3 and 4 are being translated by DORP and Safeguard Officer (Social and Gender), PMU. Expected date of completion is 31 July 2020.

3.5 Grievance Redress Mechanism

Grievance Redress Committees (GRCs) are functioning in the resettlement plan sections 1, 2 and 4. In total 88 number of complaints have been filed in three sections (1 case in Section 1, 30 cases in Section 2 and 57 in Section 4). Up to June 2020, two hearings have been conducted to address 31 grievances in the Section 1 and 2. Out of which, 4 have been advised for DWASA payment, 18 cases have been forwarded to the Deputy Commissioner and 9 are cases have been rejected, 2 received compensation before hearing was conducted. One GRC meeting was held during this period (27.01.2020) where 17 cases have been heard. Out of these 3 cases have been resolved and suggested for making payment (eligible for vulnerable grants) by the DWASA; 9 cases have been forwarded to Deputy Commissioner's office as those were found as legal cases and 5 cases have been rejected. Out of these five, one claimant's structure was proven to be not within the project alignment, one's poultry farm was found as non-existent, two could not be considered as vulnerable as per their claims and one has already received CCL. Minutes of this meeting is attached as **Appendix R**. In previous meeting, held in October 2019, 14 cases were heard. In total 31 cases have been addressed. All recommendations of first meeting could not be implemented due to COVOD-19 outbreak. Summary of the cases/GRC meeting minutes is attached as **Appendix S**.

Figure 3.5: GRC Decisions Taken

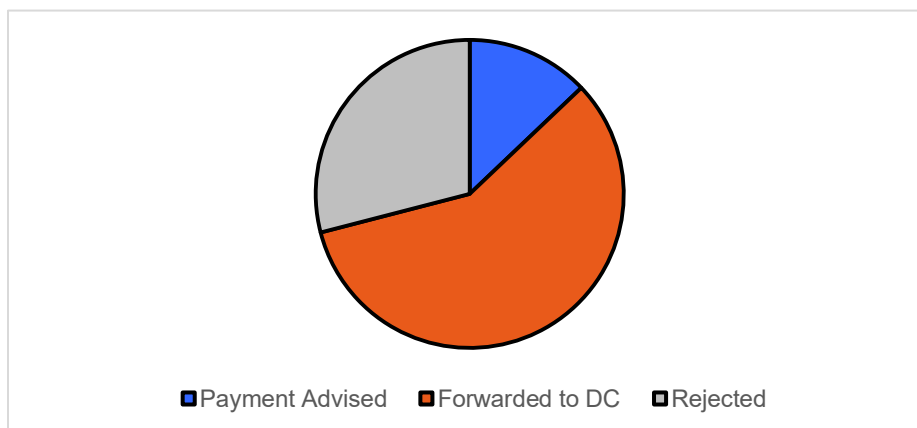

GRC hearing for Section 4 has been planned for August 2020.

GRC is needed to be declared in Section 3. Resettlement plan of it has been approved in last reporting period. MDSC reminded Project Director in this regard.

GRC will be declared in the section 5 and 6 after resettlement plan receipt approval.

A training on Grievance Redress Mechanism has been imparted to the GRC members of Section 1,2 and 4 on 14 March 2020. Training has been organized in the DWASA conference room. Members came from Araihasar and Rupanj. DWASA paid them honorariums and training completion certificates.

4 Summary Monitoring Results and Key Findings

Out of 6 resettlement plans under P1 and P2, 4 (section 1, 2,3 and 4) receipt ADB approval. In total 4 resettlement plans got approval so far. Two are remaining to be approved. Resettlement plan 5 is being updated to comply with the changed alignment. Resettlement plan 6 is being updated based on the final alignment provided by the PMU. In P3.1 there was no impact found. DDR has been prepared and approved for this. In P3.2 impact has been found in one pipe route, where only 95 vendors and 113 employees will be affected. Resettlement plan has been prepared for this section and the same has been approved. As per Resettlement Plans of P1 and P2, as of June 2020, in total 2204 affected households will have impacts on their livelihood, agricultural production, small businesses, and structures (both dwellings and businesses) due project implementation. Summary of impacts in all sections is given in Table 4.1 below:

Table 4.1: Summary of Project Impacts¹¹ as per Resettlement Plans for Section 1, 2, 3, 4, 5 and 6 (up to June 2020)

Sl. No.	Impacts/Types of losses	Total (Nos./quantity)					
		Section1	Section 2	Section 3	Section 4	Section 5	Section 6
A	Total land required	21.38 acres	110.15 acres	66.85 acre	81.5 acres	21.48 acres	6.96 acres
	i. Private land to be acquired	18.85 acres	106.08 acres	37.24 acres	No private land required	21.41 acres	5.60 acres
	ii. Government land to be acquired/transferred	2.53 acres	4.07 acres	29.61 acres belongs to BWDB and Govt.	74.96 acres DWASA owned land and the rest 6.99 acres owned by BWDB	0.08 acres	1.36 acres and 6.5 km. RAJUK road.
	iii. Total affected households	87	1178	434	253	116 (Number reduced because DORP could not survey in actual alignment before due to non-cooperation of the local people in 3 mouzas)	136
B	Total affected population	535	5784 (Included-83 wage earners & 18 tenants)	2113 (Included-53 wage earners & 33 tenants)	1197 (Included-15 wage earners)	600 (Included-52 wage earners & 3 tenants)	518
C	Total vulnerable Households (C1+C2)	46	384	74	89	14	15
C1	Female headed AHs (income below poverty line)	15	60	24	8	8	13
C2	Male headed AHs (income below poverty line)	31	324	50	81	6	2
D	Total affected primary and secondary Structures (D1+D2)	0	534	512	60	225	14

¹¹ It varies during compensation payment

Sl. No.	Impacts/Types of losses	Total (Nos./quantity)					
		Section1	Section 2	Section 3	Section 4	Section 5	Section 6
D1	Affected primary structures (i+ii+iii)	0	398	246	51	55	11
	i: Affected residential Structures	-	242	206 + (9 more structure 6 are under construction and 3 are CPRs)	12	43	-
	ii: Affected business structures	0	20	31	38	12	11
	iii. Affected residential-cum-business structure	0	136	0	01	-	-
D2	Affected secondary structures (i+ii)	0	136	266	9	170	3 (Fountain, cooker & safety tank)
	i. Total nos. of Sanitary Latrine affected	0	45	26	6	12	0
	ii. Tube wells, Deep Tub Wells and Water Pump affected	0	91	52 (Tub-well-15, Deep tubwell-7, and water pump-29, water compressor-1 & pillar-188)	3	158 (Tubewell-5, water pump-12 and pillar-141)	0
E	Affected business persons	0	13	23	31	7	0
F	Wage Laborers in business houses	0	83	53	12	52	0
G	Affected CPR (Graveyard and Mosque)	0	0	3	1 (Newly affected after DBO design)	0	0
H	Numbers of affected trees (including banana and bamboo)	09	6352	3794	561	1264	3 (Trees on island in middle of the road was not counted)

Source: RPs of Section 1 (WIA), Section 2 (Intake to Baliapara Raw Water Pipeline), Section 3 (Darikandi Chak to Murapara via Gandharbpur WTP), Section 4 (WTP), Section 5 (Rugganj to Balu River and Section 6 (Balu River to Vatara along Madani Avenue up to Baridhara.

MDSC is monitoring the activities of the INGO, DORP. MDSC carried out field visits and regular meetings between PMU and DORP to share the progress. In this reporting period, field activities were impeded due to COVID-19, which started in Bangladesh from 8 March 2020. DORP field offices were closed for more than 2 months (Mid-March to end May 2020) following government instruction. DORP resumed its field activities from June 2020. MDSC is still doing office from home due to safety policy of Mott MacDonald. Thus, field activities could not be carried out by physical inspection. However, several meetings were held over the apps such as Zoom, Skype and WhatsApp. Since May 2020 fortnightly meetings have been being conducted with PMU, DORP and MDSC. The Project Director presided over the meeting. It has been scheduled for each month till completion of the resettlement activities. These meetings were to monitor the progress of resettlement activities. It focused on expediting payment, vacating land in RWP, dealing with unpaid affected persons, who have legal problems, ensuring the process of dedicated account is explained to the affected persons, graveyard relocation, quicker payment to the non-titled affected persons in the RWP, finalization of updating web based database for resettlement, progress presentation in ADB mission

meeting, etc. Minutes of some meetings have been attached as **Appendix T**. During this monitoring period, 7 field visits have been carried out: 3 in January 3 in February and 1 in March. Field visits were carried out to observe top up and other resettlement assistance payments to the affected persons in water intake and raw water pipeline area, attend GRC meeting, attend JVC meeting, observe MoU signing ceremony on graveyard issue in WTP area, visit structures in raw water pipeline area and plan with DORP field staff in expediting dismantling, information dissemination on dedicated or dedicated account.

Key findings of field visits and consultations with the affected persons and other stakeholders (DWASA, contractor, DORP, etc.) in this reporting period are as follows:

- Additional payment has been expediated. About 98% of the CCL recipient affected persons have been paid resettlement assistance. Though 59 affected persons in Section 2 still remain to get that due to COVID-19 outbreak. Their payment voucher is ready and submitted to PMU. Expected date of payment is 26 July 2020.
- Joint verification survey (JVS) has been completed for non-titled affected persons identified in the Resettlement Plan for section 2. Based on JVS, JVC suggested payment to the eligible affected persons (17 business persons and 83 wage employees) by July 2020.
- GRC resolved cases within their jurisdiction and advised others to contact Deputy Commissioner. There are no pending cases in section 1 and section 2. MDSC suggested to PMU to hold GRC hearing in Section 4 by August 2020.
- Graveyard issues have been resolved by holding several meetings with graveyard committee and other stakeholders.
- Strip plan has been prepared in the alignment mouza maps for water intake and raw water pipeline area. There are 180¹² affected persons still due for CCL in here. In this period, no mouza is considered as priority. All mouzas are given same importance. In view of vacating land an action plan has been set. PMU staff have been deployed to assist DORP in helping affected persons in the collection of compensation.
- Some unavoidable reasons hindered affected persons in getting CCL and other resettlement assistance. Remaining 180 unpaid affected persons have been informed that DWASA has deposited required CCL money with the Deputy Commissioner's office. DWASA also opened a dedicated account for depositing required money for top up and other resettlement assistance. Affected persons have agreed with DWASA's arrangement.
- MDSC advised DORP to conduct awareness campaign amongst affected persons to submit CCL papers for getting additional payment. It was suggested to carry out miking and distributing leaflets in the area, carrying out personal contact, community meeting, etc. to make people understand the importance of CCL papers submission.
- Graveyard shifting has been negotiated. Sixty (60) graves have been relocated from the water reservoir area. Boundary wall and gate is under construction.
- MDSC guided DORP to prepare a leaflet and give notice to the encroachers, who have constructed structures, filled land with sand, etc. after cut-off-date 16 April 2019 in Section 3 of the project alignment. The list of encroachers and types of encroachment is attached as **Appendix U**. Following MDSC advice, DORP has served notice to those illegal structure owners to make them aware that such encroachments are illegal and they will not be able to claim compensation since these structures have been constructed after the cut-off-date. Notice received copies with the signatures of the stakeholders are attached herewith as **Appendix V**.
- There are 85 primary and secondary structures (of which 46 are fully paid) yet to be relocated. Upon MDSC advice, Project Director decided to announce dismantling of these structures. In January, INGO

¹² Previously mouzas under raw water pipeline had been divided based on land clearing priority. Out of 180, 103 is from the then priority mouzas and 77 from non-priority mouzas.

did the announcement using mike. Besides, INGO and PMU staff paid a fortnightly visit to the area for motivating affected persons.

- Some structures were missing during JVS. MDSC reviewed scope of GRC and guided Project Director in the payment process for those structures. GRC made a list of valid complaints and sent them to the Deputy Commissioner's office for getting compensation.
- DORP conducted livelihood restoration training program for 46 affected persons of Section 1 in January 2020. Training has been imparted in two batches on cow and goat rearing and chicken and duck rearing. MDSC supervised the training provided. About 93% of the earlier training recipient are found to be using their training knowledge and investment grant money.
- One GRC hearing conducted in this reporting period, in which 17 cases addressed; 3 suggested to pay vulnerable grant, 9 forwarded to Deputy Commissioner and 5 rejected.
- JVS has been conducted. JVC suggested quick payment to 17 business persons and 83 wage laborers.
- In Resettlement Plan Section 3, CPR include one mosque in Noagaon, Rupganj. A small part of the main structure of the mosque and Imam's residence will be affected. PMU has been notified to look into modifying the alignment, if possible, to avoid impacting any part of the mosque. MDSC reminded PMU on this matter and PMU is working on that. Deputy Commissioner's office was closed about 2 months due to COVID-19 lockdown.
- Resettlement Plan for P3.2 has been complied with ADB comments and PMU has receipt approval.
- ToR for INGO selection for Package 3 has been revised based on ADB comments received in March 2020.
- Though participation of female affected persons in the consultation process is not yet up to the expected level. Progress is good. Against 40% target it is 37% now, which was 35% in the last reporting period. In this period (January-June 2020) it was 59% which was less than before. Impeded field activities have influence on this. Initiatives have been taken for increasing female participation. MDSC advised DORP to hold separate meetings, exclusively with the female. MDSC is regularly following up on this issue and will be guiding DORP to increase female participation.
- Total 344 vulnerable affected persons (section 1: 43, Section 2: 212, Section 4: 89) have received resettlement assistance) among which 95 were from female headed households.
- MDSC advised DORP to finalize the web-based database and reporting format.
- MDSC ensured that the contractors provided safe drinking water for all staff and labours within the intake and WTP construction site. Proper water supply is to be made available in all washroom including those for labors with toilet tissue, soap, water supply, flashing system, bucket etc. GWT ensured separate toilet facilities for male & female including labors in the intake and WTP area.
- Till 30 June 2020, total 22071 person days of unskilled laborers have been employed by the GWT but no female labors was employed. It outsourced security guards from various Bangladeshi companies. Those companies deployed 14% unskilled and 18% skilled female guards up to June 2020.
- Area Manager, Rupganj was not sufficiently diligent in this reporting period. Submission of daily activity reports were not done to the DORP head office and to MDSC.
- Overall resettlement progress was presented by the MDSC to the ADB Mission through a PowerPoint presentation during their project visit in February 2020.

5 Compliance Status

The compliance as per loan agreement a list of covenants is described, and some are related to land acquisition and resettlement activities has been given. The status of progress and compliance including all covenants are provided in the monitoring and evaluation section of the project's Quarterly Progress Report and will not be repeated here.

ADB has given comments on 9th SSSMR on 23 April 2020 and MDSC has complied with those. Revised one has been submitted to ADB on 26 April 2020 and receipt approval on 27 April 2020.

6 Follow up Actions and Recommendation

As mentioned, the section-wise resettlement plans updating, and compensation payment are going on simultaneously. However, there are some outstanding issues that need to be resolved and compensation and implementation expedited to maintain the timelines. MDSC has held several meetings with DORP and PMU to expedite resettlement progress and finalization of resettlement plans. Therefore, following actions have been recommended.

Table 6.1: Required Actions

Outstanding Issues	Recommendation/Required Actions
Updating of Resettlement Plan for Section 1, 2 & 4	Resettlement Plan for Section 1 and 2 essentially needed to be updated and uploaded on ADB website for giving approval for depositing money in the dedicated account by the PMU.
	Resettlement Plan for Section 4 also needs faster update with payment and graveyard data
	PMU may strongly follow up the completion of the tasks.
ADB approval of Resettlement Plans	Finalization of Resettlement Plan for section 5 is delayed due to changes in alignment. RP 6 awaiting CLAC approval of final alignment.
	PMU should follow up with the DORP for sooner submission of these resettlement plans with updated data to obtain ADB approval. These two plans are required to be approved before payment can be made.
CCL payment to all affected persons	DORP should help affected persons more in processing legal papers for getting CCL. In addition, with the assistance of respective Union Parishad (UP) representatives, they will provide support to those affected persons who have conflicts to resolve.
	PMU to follow up with the Deputy Commissioner's office to consider affected persons' problems and to facilitate payment.
Non-submission of necessary documents to Deputy Commissioner's Office by 180 individual affected persons (other than government) in all Mouzas	INGO to take proactive measures in convincing the affected persons, who are delaying in submission of their land papers, since land handover is urgent in this section.
	PMU to deposit money in the dedicated account soon for 103 affected persons in 21 priority mouzas
Collection of CCL data and correct number of Affected Persons from Deputy Commissioner's Office, which are affecting real-time updating of Web-based database and authenticate reporting.	Further negotiation with Deputy Commissioner's Office and deployment of full-time personnel from PMU and DORP.
Payment of top up /non-titleholders' compensation	PMU to pay top up and other resettlement benefits by July 2020 in Section 2 because encumbrance free land to be handed over to the DBO contractor by September 2020.
	DORP Area Managers should be more proactive in helping affected persons in solving legal problems and submitting necessary papers for getting compensation.

Outstanding Issues	Recommendation/Required Actions
Land Acquisition	<p>Every 15 days PMU shall monitor DORP to see their progress on payment.</p>
	<p>Land handover from government and private sources are essential now for part of section 3 (Raw water pipeline towards WTP) because DBO contractor needs encumbrance free land as a part of their contract with DWASA.</p>
	<p>PMU to check with Deputy Commissioner in completing Award Book and faster compensation payment.</p>
	<p>Bangladesh Water Development Board (BWDB) has 29 acres of land in Section 3 to be handed over to DWASA. Still it is pending. Drafted an MoU but not finalized yet. DWASA expected to get the land by the end of August 2020.</p>
	<p>PMU should follow up this issue with BWDB.</p>
	<p>PMU to check with Deputy Commissioner's office for completion of award book for Section 3, issue new LA case for Section 5 and request for the feasibility study of section 6.</p>
	<p>DWASA to discuss with Deputy Commissioner's office to expedite land acquisition (public and private land both). DWASA to arrange multiple meetings with the Ministry of Land and Deputy Commissioner to expedite land acquisition and handing over land in all sections of resettlement plans.</p>
	<p>PMU to appoint a Land & Resettlement Officer to support affected persons and Safeguard Implementation Unit to facilitate resolution of the legal problems and CCL receipt.</p>
	<p>PMU to deploy one soon.</p>
Structure relocation from the raw water pipeline	<p>To vacate raw water pipeline by September 2020, structures dismantling needed. Structures owners have been notified 4 times during preceding 2 reporting period. Only motivation seemed to be ineffective.</p>
	<p>PMU may seek help from the Deputy Commissioner for legal action.</p>
Livelihood Restoration	<p>DORP should complete remaining training in Section 4. Subsequently, they need to monitor livelihood restoration activities of the training and grant money recipient affected persons.</p>
	<p>DORP should start skilled development training soon in Section 1 and 2 as a part of LIRP rehabilitation activities.</p>
Grievance Redress	<p>Decisions taken by the GRC for Section 1 and 2 to be implemented as soon as possible to facilitate land vacating. Hearing should be conducted for resolving pending cases in Section 4.</p>
	<p>PMU to follow up GRC for expediting GRC sitting and for facilitating decisions taken as per Resettlement Plans. PMU to follow up with the Deputy Commissioner's office for checking and payment to those affected persons who have been referred by the GRC as eligible.</p>
	<p>More GRC meetings should be conducted to resolve the rest of the complaints lodged in Section 4.</p>
	<p>DORP has been advised to put up GRC members' list with their names and contacts in their offices and in other important public places of the area.</p>
	<p>GRC should be declared in Resettlement Plan Section 3.</p>

Outstanding Issues	Recommendation/Required Actions
Performance of DORP	<p>Web based database for resettlement completion is a challenge for DORP at this stage. MDSC has assisted DORP much even beyond their ToR requirements. DORP should complete the database and give training to PMU on operating of this database.</p> <p>PMU to follow up with DORP regarding the completion of database and providing training.</p> <p>Health and safety of the field staffs is a major concern for DORP due to COVID-19. Field activities slowed down due to restricted movement in the project area. DORP should develop a strategic plan with careful deployment of manpower to maximize time on the field effectively. .</p> <p>Data given by DORP is sometimes ambiguous. DORP should be careful in giving data with the consensus of the all concerned member.</p> <p>DORP management, TL and DTL should be more careful in deploying competent staffs and should be more proactive in monitoring their field staffs' activities. They should visit the field more often to ensure regular monitoring of the field activities related to implementation of land acquisition and resettlement.</p> <p>DORP to prepare a weekly action list at the start of each week and to prepare a report on actual field progress achieved by the end of that week and send to PMU and MDSC.</p> <p>Supervision of all DORP activities will be done by PMU. Executive Engineer, Mr. Mustafizur Rahman and Assistant Engineer, Mahrin Binte Islam has been assigned for this task.</p>

Below is the monitoring format for activities to be done during implementation of the land acquisition and resettlement as provided in the resettlement framework.


Table 6.2: Monitoring of Activities during Implementation

Sl. No.	Resettlement Plan Activities	Completed Y/N	Remarks
A. Pre-Construction Activities and Resettlement Plan Activities			
1	Approval of Draft Resettlement Plan by ADB prior to contract award	Y	Resettlement Plan for Section 1, 2, 3, 4, P3.2 and DDR for P3.1 received ADB approval. Resettlement Plans for Section 5 and 6 are yet to be approved.
2	Disclosure of Draft Resettlement Plan on ADB and Executive Agency (EA) websites	Y	Final Resettlement Plans 1, 2, 3, 4 and P3.2. DDR for P3.1 also uploaded.
3	Circulation of Summary Resettlement Plan in two languages i.e., English and Bangla to all stakeholders	N	Translation is being done by DORP and PMU but not completed.
4	Establishment of GRC and other committees for the resettlement plans finalization/ implementation	Y	For Resettlement Plan Sections 1, 2, and 4. Section 3 is pending.
5	Recruitment/Appointment of External Monitoring Agency	Y	

SI. No.	Resettlement Plan Activities	Completed Y/N	Remarks
B. Resettlement Plan Implementation			
1	Grievance Redress Committee and telephone hotlines established	Y	GRC established in Resettlement Plan Section 1, 2 and 4 areas but telephone hotlines not available in easily accessible places for the affected persons. However, the phone number of Member Secretary, GRC has been distributed to the affected persons.
2	Entitlements and grievance redress procedure disclosed	Y	On ADB and DWASA website.
3	Finalization of list of affected persons, vulnerable affected persons and compensation/ assistance/ allowances	Y	Done for resettlement plan Section 1, 2 and 4.
4	Finalization of list of affected common facilities and roads for closure; mitigation measures proposed	Y	Ditto
5	Affected persons received entitlements as per amounts and program specified in resettlement plans	Y	For RP Section 1, 2 and 4
6	Payment of compensation, allowances and assistance (Nos. of affected persons)	Y	CCL paid to 2783 affected persons in Section 1 and 2. Top up and other resettlement benefits given to 2724 affected persons. In Section 4, 253 affected persons received resettlement assistance.
7	Additional assistance for vulnerable households given (Nos. of vulnerable affected persons)	Y	344 vulnerable affected persons (M-249, F-95) [Section 1= 43 APs (M-27, F-16), Section 2=212 (M-141, F-71), Section 4= 89 APs (M-81, F-8)] received resettlement assistance.
8	Livelihood arrangements provided to vulnerable affected persons	N	Livelihood training and grant has been provided to 119 vulnerable affected persons in Section 1 and 4.

SI. No.	Resettlement Plan Activities	Completed Y/N	Remarks
9	Reinstallation of affected common facilities	N	
10	Grievances		
	No. of grievances registered	Y	88 in Section 1, 2 and 4
	No. of grievances redressed	Y	31 in Section 1 and 2
	Outstanding complaints	Y	57
	Disclosure of grievance redress statistics	N	
11	Consultation, participation and disclosure as per resettlement plans	Y	On-going
12	Livelihood and Income Restoration activities:		
	1. Nos. of affected households resettled	Y	119 business affected households have been resettled in Section 1, and 4.
	2. Nos. of affected households attend the retraining program	N	
	3. Nos. of affected households replaced their agricultural land	N	34 as of now in Section 1 and 2
	4. Nos. of affected households join the micro finance program	N	Not joined yet
	5. Nos. of affected households reconstruct the lost business	N	31 households started to reconstruct business
C. Monitoring			
1	Survey on socio-economic status of affected persons (including vulnerable) completed and compared with baseline survey results	Y	Census on socioeconomic status done but not compared with baseline survey.
2	Survey on satisfaction levels of affected persons with resettlement plan implementation completed	N	Survey not done
D. Labour			
1	Implementation of all statutory provisions on labour like health, safety, welfare, sanitation, and working conditions by Contractors	Y	Civil works is going on in the intake and WTP. Water and sanitation facilities was satisfactory.
2	Equal pay for equal work for men and women	Y	

A. Changed alignment in Section 5

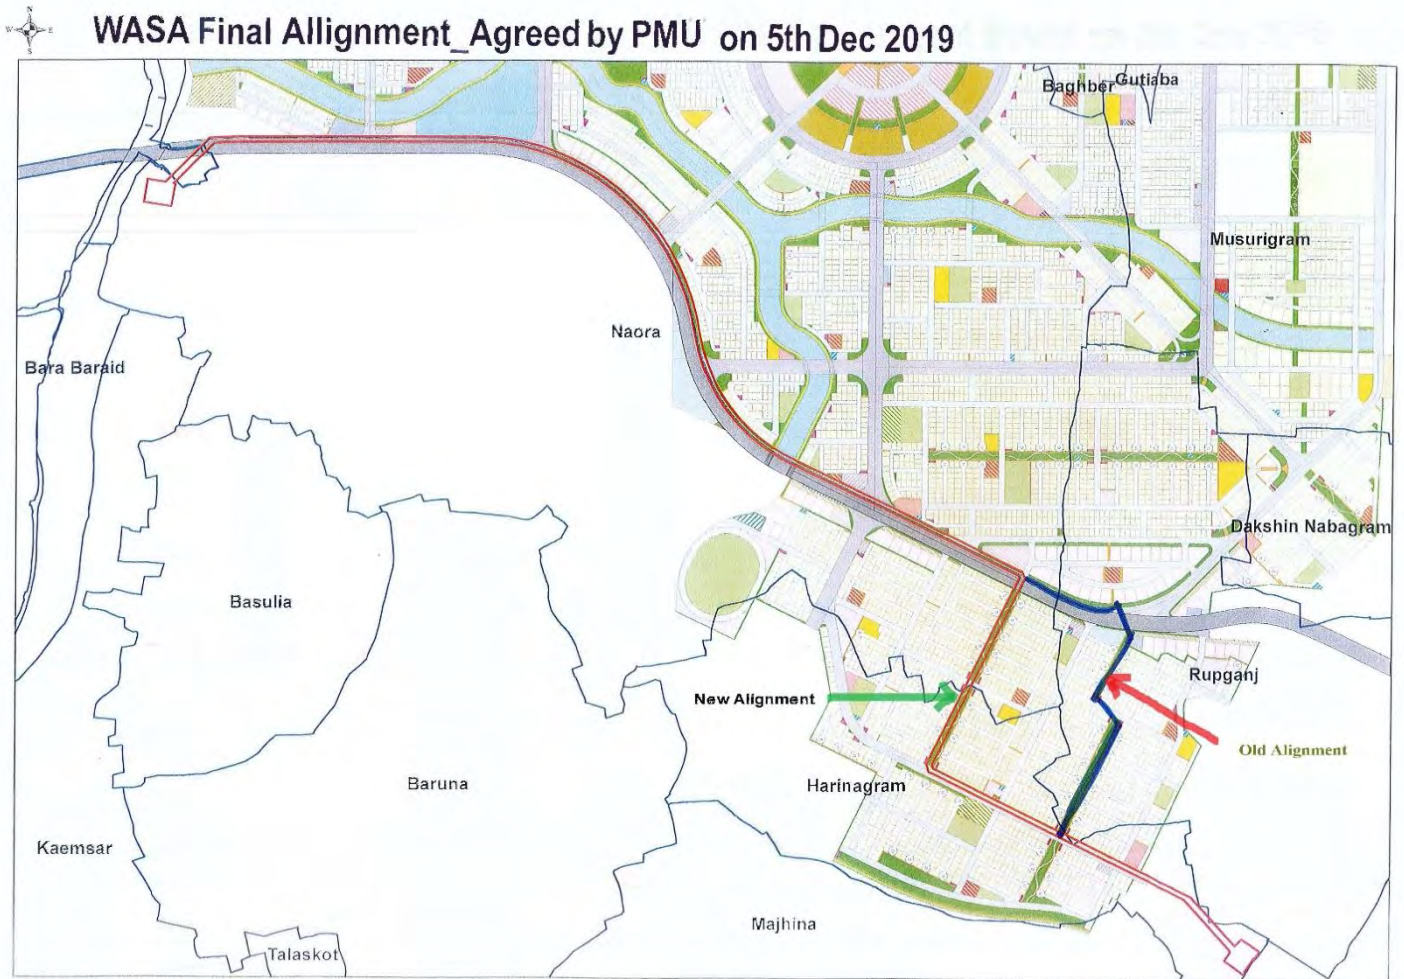

B. Leaflet on Dedicated Account

B.1 Leaflet on Dedicated Account in English



Dhaka WASA

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Some Important Information Related to the Resettlement Activities

Dhaka WASA is implementing an important project called Dhaka Environmental Sustainable water Supply Project to meet the demand of pure/hygienic water for the city dwellers. Wasa, Narayanganj. For implementing the project, Dhaka WASA is constructing a 36 km water pipeline from Bishnandi, Arihazar Upazila, Narayanganj to Beridhara, Dhaka, for constructing of the project an area of 200 acres of private land (as per the resettlement and rehabilitation plan) will be acquired. Due to acquiring the land those who will lose their own land, houses, businesses, crops, income, and livelihood all of the affected persons and families will be entitled to receive compensation and resettlement benefits as per the resettlement plan and entitlement matrix. It is to be noted that due to the complexity of ownership problem on land or due to legal process in the court of law, yet some affected families did not receive any additional payment and resettlement benefits from DWASA and compensation from the office of the District Commissioner, Narayanganj. For the sake of their due payment, the following processes and activities have been undertaken by the project authority.

1. According to the SPS (2009) of ADB, the funding agency of the project, those socially and legally recognized as affected persons by the project intervention, will be eligible for additional and resettlement benefits from DWASA. At that time, they are requested to communicate with INGO- DORP and DWASA office at the given address in the leaflet.
2. After finishing/completion of the legal process regarding land-related disputes by the court, the APs to be applied and submitted the necessary relevant papers to the DC office with judgment copy from court in favor of APs for a compensation payment. At this time, the APS is also requested to communicate to the office of INGO-DORP and DWASA as mentioned in the leaflet.
3. Those APs did not receive CCL on affected land from DC office due to the dispute over ownership claim in the court, their land value has already been deposited in the account of DC office. In the same way, those APs could not receive additional payment/resettlement benefits due to the legal problems in the court, the estimated amount they will be supposed to be received has been kept safely by opening a separate account (escrow/dedicated account) at Janata Bank Limited, corporate branch, Karwan Bazar, Dhaka. The account will be operated by the joint signature of Project Director and Senior Finance & Accounts Officer of the project.
4. This account will be used only for payment of resettlement benefits to the CCL non-paid APs not for any other purposes.
5. After the settlement of the disputes on ownership claim over the land by the court, sooner the decree or judgment copy from court along with other relevant papers to be submitted and applied to the DC office and to be informed and applied to DWASA appointed INGO for necessary payments.
6. The District Commissioner (DC) will give CCL on affected land to the APs and the WASA project office will pay all other (additional and other resettlement) benefits to the APs from the escrow/dedicated account.
7. This account will remain active and operational with the requisite balance due for APs, till the last unpaid man (AP) and even after the completion of the project activities.
8. The interest that will be incurred on the balance of the account over time will be distributed proportionately to the APs payment amount.
9. If any AP is unpaid by DWASA after the completion of implementation activities of the project, in that case, the AP is instructed to apply to the Director, Management, Maintenance, and Operation Department of Water Treatment Plant at Gandharbpur. Payment of necessary additional /resettlement benefits will be arranged from this office. Time to time the CCL non-paid APs will be updated by the project.
10. To implement the resettlement activities smoothly a 6 (six) members Grievance Redress Committee (GRC) has been formed at each of the local level Union Parishad according to Government Gazette Notification. This committee will deal with resolving the compensation-related complaints.

It is to be mentioned here that already the possession of the acquired land has been handed over to Dhaka Wasa by the Deputy Commissioner, Narayanganj. For the sake of water pipeline construction work, several notices have been issued at several times to clear the land and to stop all types of activities, including cultivating the land and removing the houses and other structures from the land acquired and by the Dhaka WASA, and also the INGO (DORP) has served notice to remove all structures from the acquired land and forbidden to stop cultivation newly in the acquired land. So, finally, through this present leaflet, you have been allowed two weeks' time from receipt of this leaflet to remove all sorts of structures and to make the land quite free for the commencement of the project construction work. You are thus requested to cooperate in the implementation of the project activities.

Dhaka WASA hopes that local people, dignitaries, government non-governmental organizations will extend their hand in implementing this government project for the greater interest of the development of the water management system in Dhaka city.

Area Office DESWSP
Team Leader / Area Manager
Development Organization of the Rural Poor
Arihazar, Narayanganj.
Mobile No: 01716-104604, 01714-091216

Project Director
Dhaka Environmentally Sustainable Water
Supply Project (DESWSP)
WASA Building, 1 Kazi Nazrul Islam Avenue
(9th Floor)
Karwan Bazar, Dhaka- 1215

B.2 Leaflet on Dedicated Account in Bangla



ঢাকা ওয়াসার ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্ট (DESWS) এর পুনর্বাসন কার্যক্রম সম্পর্কে কিছু জরুরি তথ্য

ঢাকা ওয়াসা ঢাকা শহরবাসীর জন্য বিতঞ্চ/বাহ্যাসম্মত পানির চাহিদা পূরণের লক্ষ্যে ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্ট নামে একটি গুরুত্বপূর্ণ প্রকল্প বাস্তবায়ন করছে। উক্ত প্রকল্প বাস্তবায়নে ঢাকা ওয়াসা, নারায়ণগঞ্জ জেলার আড়াইহাজার উপজেলার বিশদদি থেকে বারিধারা, ঢাকা পর্বত মোট ৩৬ কি.মি. পানির লাইন নির্মাণ করছে যাতে ২০০ একর (পুনর্বাসন পরিকল্পনা অনুযায়ী) ব্যক্তি মালিকানাধীন জমি অধিগ্রহণ করা হবে। উক্ত অধিগ্রহণের ফলে বাসের জমি, ঘরবাড়ী, ব্যবসা প্রতিষ্ঠান কল, আর ও জীবন জীবিকা ক্ষতিগ্রস্ত হবে সেই সমস্ত ক্ষতিগ্রস্ত ব্যক্তি ও পরিবারবর্গের জন্য প্রকল্পের পুনর্বাসন পরিকল্পনা অনুযায়ী ক্ষতিপূরণ প্রদান করা হচ্ছে। উল্লেখ্য যে, কিছু ক্ষতিগ্রস্ত পরিবারবর্গ তাদের জমির মালিকানা বিষয়ে জটিলতা থাকায় বা আইনী প্রক্রিয়া সম্পাদন করে জেলা প্রশাসক, নারায়ণগঞ্জ হতে জমির ক্ষতিপূরণ মূল্য বা ওয়াসা হতে অতিরিক্ত পুনর্বাসন ক্ষতিপূরণ অদাব্যধি পান নাই, সেই সকল ক্ষতিপূরণ বিল প্রদান বিষয়ে নিম্নে বর্ণিত প্রক্রিয়া/কার্যক্রম হাতে নেয়া হয়েছে।

১. প্রকল্পের দাতা সংস্থা এশিয়ান উন্নয়ন ব্যাংকের পুনর্বাসন নীতিমালা অনুযায়ী আইন সংগত ও সামাজিকভাবে স্বীকৃত ক্ষতিগ্রস্ত (APs) মালিকগণ ঢাকা ওয়াসা হতে অতিরিক্ত প্রকল্প সহায়তা পাবেন। সহযোগী সংস্থা এনজিও “ডব্লুপ” আবেদনের বিষয়ে সার্বিক সহযোগিতা প্রদান করবে।
২. জমি সংক্রান্ত আইনি প্রক্রিয়া শেষ হওয়ার পর রায়ে রকি বা প্রয়োজনীয় কাগজপত্রসহ জিসি অফিসে বসবাস জমির ক্ষতিপূরণের ঢাকা পাওয়ার জন্য আবেদন করতে হবে। উক্ত সময়েই পুনর্বাসন সহযোগী সংস্থা এনজিও “ডব্লুপ” ও ঢাকা ওয়াসার নিম্নে উল্লিখিত টিকানায় বা অফিসে যোগাযোগ করার জন্য অনুরোধ করা হলো।
৩. যে সকল ক্ষতিগ্রস্ত ব্যক্তিবর্গ তাদের জমির মালিকানা সংক্রান্ত জটিলতা থাকায় ক্ষতিপূরণ পান নাই তাদের জমির মূল্য জেলা প্রশাসক, নারায়ণগঞ্জ অফিসে জমা রাখা হয়েছে। আইনি জটিলতা থাকায় যে সকল ক্ষতিগ্রস্ত ব্যক্তি ক্ষতিপূরণ গ্রহণ করতে সক্ষম হননি, ঢাকা ওয়াসা কর্তৃক প্রদেয় তাদের আনুমানিক প্রাপ্য অর্থ সহায়তা হিসেবে করে সঞ্চিত রাখার উদ্দেশ্যে জনতা ব্যাংক লিঃ, কাওরানবাজার কর্পোরেট শাখায় একটি পৃথক একাউন্ট খোলা হয়েছে। উক্ত একাউন্ট প্রকল্প পরিচালক এবং প্রকল্পের সিনিয়র কাউন্সিলর ও একাউন্টস অফিসারের যৌথ স্বাক্ষরে পরিচালিত হবে।
৪. আলোচ্য হিসাবটি শুধুমাত্র পুনর্বাসন ক্ষতিপূরণ প্রদানের জন্যই পরিচালিত হবে। অন্য কোন কাজে বা উদ্দেশ্যে এই হিসাব ব্যবহার করা হবে না।
৫. জমির আইনি জটিলতা নিরাসনের সাথে সাথে এ সংক্রান্ত ঘোষিত রায়/নিউটেশন বা জমির তথ্য/কাগজপত্রসহ জেলা প্রশাসক ও ঢাকা ওয়াসা কর্তৃক নিয়োজিত এনজিও ডব্লুপকে অবহিত করণসহ আবেদন করতে হবে।
৬. জেলা প্রশাসন জমির সিসিএল (জমির মূল্য) ক্ষতিগ্রস্তদের প্রদান করবে এবং ওয়াসার প্রকল্প অফিস কর্তৃক আলোচ্য হিসাব হতে অন্যান্য অতিরিক্ত পুনর্বাসন সহায়তা বিল পরিশোধ করা হবে।
৭. ক্ষতিপূরণ বিল প্রদানের জন্য খোলা আলোচ্য হিসাব সর্বশেষ ক্ষতিগ্রস্ত ব্যক্তি ক্ষতিপূরণ বিল পরিশোধ হওয়া পর্যন্ত এমনকি প্রকল্পের মেয়াদ উত্তীর্ণ হবার পরও চালু থাকবে।
৮. আলোচ্য হিসাবে জন্মকৃত টাকার উপর অর্জিত মত্যাংশ/সুদ আনুপাতিক হারে সকল ক্ষতিগ্রস্ত ব্যক্তিকে প্রদান করা হবে।
৯. প্রকল্প বাস্তবায়ন মেয়াদ শেষ হওয়ার পর যদি কোন ক্ষতিগ্রস্ত ব্যক্তি তাদের ক্ষতিপূরণ ওয়াসা হতে না পেয়ে থাকে তবে তিনি গুরুত্বপূর্ণ পানি শোধনাগারের অপারেশন ও মেইন্টেন্যান্স বিভাগে আবেদন করবেন (আবেদনের কপি ব্যবস্থাপনা পরিচালক বরাবর প্রদান করতে হবে)। ঢাকা ওয়াসার উল্লিখিত সংশ্লিষ্ট বিভাগ হতে ঐ ক্ষতিপূরণ বিল প্রদানের ব্যবস্থা করা হবে। সময়ে সময়ে আলোচ্য হিসাবের হালনাগাদ (Update) ক্ষতিগ্রস্ত ব্যক্তিদের অবহিত করা হবে।
১০. পুনর্বাসন কর্মসূচি বাস্তবায়ন করার জ্ঞানে সবকারি প্রজ্ঞাপন মোতাবেক ছয় সদস্য বিশিষ্ট অভিযোগ নিরসন কমিটি (জিআরসি) প্রকল্প এলাকার প্রতি ইউনিয়নে গঠন করা হয়েছে। এই কমিটি ক্ষতিগ্রস্ত ব্যক্তির ক্ষতিপূরণ সংক্রান্ত কোন অভিযোগ থাকলে তা নিরসনে প্রয়োজনীয় পদক্ষেপ গ্রহণ করবে।

উল্লেখ্য যে, ইতোমধ্যে আপনার জমি অধিগ্রহণপূর্বক জেলা প্রশাসক, নারায়ণগঞ্জ কর্তৃক ঢাকা ওয়াসাকে পরামর্শ বুঝিয়ে দেয়া হয়েছে। প্রকল্পের পানির পাইপ স্থাপন কাজ শুরু করার স্বার্থে ঢাকা ওয়াসা কর্তৃক অধিগ্রহণকৃত জমিতে চাষাবাদসহ এ জাতীয় সকল কার্যক্রম বন্ধ করে জমিতে বিদ্যমান ঘর বাড়ি ও অন্যান্য স্থাপনা নিজ দায়িত্বে সরিয়ে নিয়ে জমি খালি করে দেওয়ার জন্য ইতোপূর্বে বেশ কয়েকবার নোটিশ প্রদান করা হয়েছে এবং প্রকল্প ও প্রকল্পের এনজিও (ডব্লুপ) কর্তৃকও নিয়মিত তপাদ প্রদান করা হচ্ছে। প্রকল্পে নিয়োজিত টিকানার কর্তৃক জনস্বার্থে জমিতে কাজ শুরু করার স্বার্থে অধিগ্রহণকৃত জমি হতে আগামী ২ (দুই) সপ্তাহের মধ্যে আপনার স্থাপনা সরিয়ে নিয়ে বা চাষাবাদসহ এ জাতীয় সকল কার্যক্রম বন্ধ করে প্রকল্প কাজ বাস্তবায়নে সহযোগিতা করার জন্য পুনরায় অনুরোধ করা হলো। ঢাকা ওয়াসা আশা করে যে, ঢাকা শহরে পানি ব্যবস্থাপনা উন্নয়নের বৃহত্তর স্বার্থে স্থানীয় জনগণ, সম্মানিত ব্যক্তিবর্গ, সবকারি বেসরকারি প্রতিষ্ঠানসমূহ আলোচ্য সবকারী প্রকল্প বাস্তবায়ন কাজে সহযোগিতা হাত প্রস্তুত করবেন।

এরিয়া অফিস DESWS
টিন সিআর/এরিয়া নাসেমলার
ভেতলগানেশি অর্গানাইজেশন অব দি রকাল পুর
আড়াইহাজার, নারায়ণগঞ্জ।
সেফটিক নং- ০১৭১০-১০৪০০৪, ০১৭১৪-০১১২১৪

প্রকল্প পরিচালক
ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্ট (DESWS)
ওয়াসা ভবন, ১৮ কালী মন্ডলপ ইসলাম এডমিটি (১০০ ফলা)
কারওয়াল বাজার, ঢাকা-১২১০

C. List of Leaflet Recipient on Dedicated Account

List of unpaid affected persons, who received leaflet on dedicated/dedicated account

Dhaka environmentally sustainable water supply project (DESWSP)
Development Organization of the rural Poor (DORP)
Distribution Leaflet

Name of Area office: Arai hazar . Mouza : Section- 1 & 2 Date : 06-03-2020

SI No	Aps Name	Aps F/H Name	Mouza	Upazila	District	Plot No.	Receive Leaflet
1	Mosle Uddin	Late Ismail Munshi	Chaitonkanda	Arai hazar	Narayanganj	2815	স্বাক্ষরিত 01731690595
2	Motaleb	Late Ismail Munshi	Chaitonkanda	Arai hazar	Narayanganj	2815	স্বাক্ষরিত 0178101642
3	Shohel	Late Abdul Berek (Ismail)	Chaitonkanda	Arai hazar	Narayanganj	2818	স্বাক্ষরিত 01726107209
4	Asis Kumar Dey	Late Shopon Chandra Day	Bijoy Nagar	Arai hazar	Narayanganj	2	স্বাক্ষরিত 01993925392
5	Sharafat	Late Jobed Ali	Bijoy Nagar	Arai hazar	Narayanganj	57	স্বাক্ষরিত 0167499982
6	Begum Samsunnahar Khondokar	H/ Doctor Rejaul Karim Khondoker	Parashilmandi	Arai hazar	Narayanganj	314	স্বাক্ষরিত
7	Md. Bakul	Late Seraj Uddin	Bazinaband	Arai hazar	Narayanganj	14	স্বাক্ষরিত
8	Siddikur Rahman	Late Md. Nayeab Ali Master	Bazinaband	Arai hazar	Narayanganj	15	স্বাক্ষরিত 01778224 0177675445
9	Parul Mia	HUS: HAYDER ALI	Lengurdi	Arai hazar	Narayanganj	100	স্বাক্ষরিত
10	Mohsin	LATE ALMAS ALI	Lengurdi	Arai hazar	Narayanganj	104	স্বাক্ষরিত 01922245061
11	EID Ga- Adv. OmorFaruk	Late Rafiz Uddin	Lengurdi	Arai hazar	Narayanganj	111	স্বাক্ষরিত 01922245061
12	High School- Adv. Rashid		Lengurdi	Arai hazar	Narayanganj	237	স্বাক্ষরিত
13	High School		Lengurdi	Arai hazar	Narayanganj	330	স্বাক্ষরিত 0193078313
14	High School- Adv. Rashid		Lengurdi	Arai hazar	Narayanganj	331	স্বাক্ষরিত
15	Komol Mia	Late Abul Kashem	Lengurdi	Arai hazar	Narayanganj	350	স্বাক্ষরিত 01914007716

Aps Name	Aps F/H Name	Mouza	Upazila	District	Plot No.	Receive Leaflet	
16	Faruk	Late Abul Kashem	Lengurdi	Arai hazar	Narayanganj	350	স্বাক্ষরিত
17	Laybu	Late Abul Kashem	Lengurdi	Arai hazar	Narayanganj	350	স্বাক্ষরিত
18	Raja Mia	Late Abul Kashem	Lengurdi	Arai hazar	Narayanganj	350	স্বাক্ষরিত 01558092523
19	Moulovi Abu Hanifa	Late Abdur Quddus	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত 01914365288
20	Abu Taleb	Late Taher Ali Munshi	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত 0176660109
21	Abdul Awal	Late Abdur Quddus	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত
22	Kamrunnesa	Late Abdur Quddus	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত
23	Biithi	Late Abdur Quddus	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত
24	Fahim	Late Abdur Quddus	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত
25	Feroza	Late Abdur Quddus	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত
26	Most. Hosneara Begum	MD. WALI ULLAH	Lengurdi	Arai hazar	Narayanganj	351	স্বাক্ষরিত
27	Safaz Uddin	Late Mohiz Uddin	Laxmipura	Arai hazar	Narayanganj	416	স্বাক্ষরিত 01679365231
28	Abul Bashar	Late Rahmat Ali	Laxmipura	Arai hazar	Narayanganj	19	স্বাক্ষরিত 01871756864
29	Md. Hossain	Late Rahmat Ali	Laxmipura	Arai hazar	Narayanganj	19	স্বাক্ষরিত 01730169045
30	Mizan	Yanus	Laxmipura	Arai hazar	Narayanganj	19	স্বাক্ষরিত 0184965974
31	Md. Asad Ullah	Yanus	Laxmipura	Arai hazar	Narayanganj	24	স্বাক্ষরিত
32	Razu	Yanus	Laxmipura	Arai hazar	Narayanganj	24	স্বাক্ষরিত 0199931286
33	Rasel	Yanus	Laxmipura	Arai hazar	Narayanganj	24	স্বাক্ষরিত
34	Poly	Yanus	Laxmipura	Arai hazar	Narayanganj	24	স্বাক্ষরিত
35	Fahima	Yanus	Laxmipura	Arai hazar	Narayanganj	24	স্বাক্ষরিত 01957057617
36	Md. Kamal Uddin	Late Abdul Majid	Aguandi	Arai hazar	Narayanganj	24	স্বাক্ষরিত
37	Md. Fazlul Haque gong	Late Sayedali Master	Aguandi	Arai hazar	Narayanganj	150	স্বাক্ষরিত 01813-585830
38	Abdul B...		Aguandi	Arai hazar	Narayanganj	195	স্বাক্ষরিত

**Dhaka environmentally sustainable water supply project (DESWSP)
Development Organization of the rural Poor (DGRP)
Distribution Leaflet**

Name of Area office: Arai hazar, Mouza :

Section- 2

Date :

SI No	Aps Name	Aps F/H Name	Mouza	Upazila	District	Plot No.	Receive Leaflet
✓ 59 +	Md. Shamsul Haque Vuia	ABU SIDDIQUE	Atabdi	Arai hazar	Narayanganj	45	৭৭৯!
						46	
✓ 60 →	Jahirul Haque Vuia	ABU SIDDIQUE	Atabdi	Arai hazar	Narayanganj	45	২১৫৯২০ ০১৭১১৬১৩৪৬৪
						46	
✓ 61 ৪	Fazlul Haque Vuia	ABU SIDDIQUE	Atabdi	Arai hazar	Narayanganj	45	২১৫৯২০ ৭৭৯!
						46	
✓ 62 ০	Jaidul Haque Vuia	ABU SIDDIQUE	Atabdi	Arai hazar	Narayanganj	45	৩২৭৭২০ ৭৭৯!
						46	
63 ৪	Hazrat Ali	Late Abu Sayed	Atabdi	Arai hazar	Narayanganj	162	২২০৬০৭৭৭ ০১৯৪১৪৭২৬৪৪
✓ 64 ৭	Md. Helal Uddin	Late Sofur Uddin	Atabdi	Arai hazar	Narayanganj	176	০১৯২৩২১৩২৭২৪
✓ 65 ৭	Md. Sana	Late Shofi Ullah Mollah	Atabdi	Arai hazar	Narayanganj	215	২১৫৯২০ ০১৯২৭৬০১২৭২
✓ 66 ৪	Mostafa	Late Shofi Ullah Mollah	Atabdi	Arai hazar	Narayanganj	215	০১৯২৭৭৭ ০১৯৪৩০২৪৫৯৯
✓ 67 ৪	Md. Dillur Rahman	LATESAYD MOKLESUR RAHMAN	Ranidi	Arai hazar	Narayanganj	20	০১৭৯৫৬২২৯৩৫
68 ৪	Md. Babul Mollah	Late Nazim Uddin	Ranidi	Arai hazar	Narayanganj	22	
✓ 69 ৪	Md. Parul Mia	Late Nazim Uddin	Ranidi	Arai hazar	Narayanganj	22	২১৫৯২০ ০১৪৪৫৪৩৪৬৬৫
✓ 70 ৪	Md. Dillur Rahman	Late Alhaz Moklesur Rahman	Ranidi	Arai hazar	Narayanganj	22	u

SI No	Aps Name	Aps F/H Name	Mouza	Upazila	District	Plot No.	Receive Leaflet
71	Most. Selina Begum	M/ Md. Babul Mia	Ranidi	Arai hazar	Narayanganj	22	
72	Gias Uddin Master	LATE OLI ULLAH MIA	Ranidi	Arai hazar	Narayanganj	345	০১৯৬৭৭২০০৭৬৫০৬
73	Md. Shahaj Uddin	LATE, ALI BOX PRODHAN	Ranidi	Arai hazar	Narayanganj	587	০১৭২০০৭১৪ ০১৭২০০৭৪১৪০
74	Ayesh Begum	SHAHAJ UDDIN	Ranidi	Arai hazar	Narayanganj	587	০১৬২০০৭১
75	Tomiz Uddin	LATE ELAHI BHUYAN	Ranidi	Arai hazar	Narayanganj	593	০১৯২৭৭৭ ০১৯২৭৭০৬৫৪৭
76	Tota Mia	LATE ALAHI BHUYAN	Ranidi	Arai hazar	Narayanganj	593	
77	Samoddi	LATE SHAMSUDDIN	Ranidi	Arai hazar	Narayanganj	593	
78	Jahatun	LATE HAZROT ALI	Ranidi	Arai hazar	Narayanganj	593	
79	Laily	LATE ALAHI	Ranidi	Arai hazar	Narayanganj	593	
80	Suruj Mia	Late Abdus Samad	Verarkur	Arai hazar	Narayanganj	120	
						121	০১৯৪০২০৬৩৯৫
81	Md. Mostafijur Rahman	Md. Abdul Ali	Verarkur	Arai hazar	Narayanganj	166	
						168	
82	Farzana Boby	Late Abdul Baten Bhuiyan	Verarkur	Arai hazar	Narayanganj	166	০১৯১১০৩৩৫৩৩
83	Amzad Hossain	Late Md. Ali	Hazishahadi	Arai hazar	Narayanganj	297	
84	Ainal Hossain	Late Md. Ali	Hazishahadi	Arai hazar	Narayanganj	297	০১৯৩৩৫০০০৪৪
85	Mozibor	Late Md. Ali	Hazishahadi	Arai hazar	Narayanganj	297	
86	Shahid Ullah	Late Kamaj Uddin	Hazishahadi	Arai hazar	Narayanganj	310	
						312	০১৯৪১৩৯৯১৪ ০১৯৪১৩৯৪১৪
87	Nazmul					310	
87		Late Kamaj Uddin	Hazishahadi	Arai hazar	Narayanganj	312	11 11

No	Aps Name	Aps F/H Name	Mouza	Upazila	District	Plot No.	Receive Leaflet	
88	30	Jakir Hossain Late Kamaj Uddin	Hazishahadi	Araihazar	Narayanganj	310	11	11
						312	কোঃ আব্দুল হক	
89	31	Md. Lutfur Rahman Vuia	Hazishahadi	Araihazar	Narayanganj	313	01925814516	7
90	32	Tara Mia	Hazishahadi	Araihazar	Narayanganj	314	01917407423	
91	33	Bokul Mia	Hazishahadi	Araihazar	Narayanganj	314	কোঃ আব্দুল হক	
92	34	Md. Kashem	Hazishahadi	Araihazar	Narayanganj	315	2161	01794700636
93	35	Md. Hashem	Hazishahadi	Araihazar	Narayanganj	315	216	01993260611
94	36	Md. Selim	Hazishahadi	Araihazar	Narayanganj	315	216	01794700636
95	37	Mozibor	Hazishahadi	Araihazar	Narayanganj	315	কোঃ আব্দুল হক	01794700636
96	38	Md. Monir	Hazishahadi	Araihazar	Narayanganj	316	01817508799	
97	39	Abdur Rahman	Hazishahadi	Araihazar	Narayanganj	350	বিদ্য	01911709701
98	40	Md. Akbor Ali	Hazishahadi	Araihazar	Narayanganj	350	কোঃ আব্দুল হক	01981179961
99	41	Abdul Kadir	Hazishahadi	Araihazar	Narayanganj	357	কোঃ আব্দুল হক	01998764580
100	42	Abdur Rahim Late Miznur Rahman	Hazishahadi	Araihazar	Narayanganj	367	কোঃ আব্দুল হক	0177553407
						369	u	
						371	u	
101	43	Abdusamad Late Miznur Rahman	Hazishahadi	Araihazar	Narayanganj	367	কোঃ আব্দুল হক	01741667388
						369	u	
						371	u	
102	44	Abdul Kadir Late Miznur Rahman	Hazishahadi	Araihazar	Narayanganj	367	কোঃ আব্দুল হক	01998764580
						369	11	11
						371	u	11

No	Aps Name	Aps F/H Name	Mouza	Upazila	District	Plot No.	Receive Leaflet	
103	45	Dulal Late Md. Abdul Majid	Hazishahadi	Araihazar	Narayanganj	409	কোঃ আব্দুল হক	01789292143
						410	11	11
104	46	Lal Mia	Hazishahadi	Araihazar	Narayanganj	427	01927383433	কোঃ আব্দুল হক
105	47	Sona Mia	Hazishahadi	Araihazar	Narayanganj	427	কোঃ আব্দুল হক	01992442527
106	48	Golesha Begum	Hazishahadi	Araihazar	Narayanganj	427	কোঃ আব্দুল হক	01838922790
107	49	Abul Bashar	Hazishahadi	Araihazar	Narayanganj	444	কোঃ আব্দুল হক	
108	50	Abul Kalam	Hazishahadi	Araihazar	Narayanganj	444	কোঃ আব্দুল হক	
109	51	Abul Basar Mia	Hazishahadi	Araihazar	Narayanganj	445	কোঃ আব্দুল হক	
110	52	Abdul Wahid	Hazishahadi	Araihazar	Narayanganj	445	কোঃ আব্দুল হক	01726144578
111	53	Monir	Hazishahadi	Araihazar	Narayanganj	445	কোঃ আব্দুল হক	01726144578

D. FGD on Dedicated Account Meeting Minutes

Dhaka Environmentally sustainable Water Supply Project (DESWSP)

Development Organisation of the Rural Poor (DORP)

Meeting Minutes on Dedicated account with CCL non-paid Affected Persons

Subject: Meeting related to Dedicated account with CCL non-paid Affected Persons of section-1 and 2

Venue: Araihasar Area office

Date: 01 March 2020

Time of Meeting: 10.00 AM to 1.30 PM

Commencement of the Meeting: The meeting was presided over by the Team Leader, DORP. The Team Leader welcomed the participants and introductions were carried out after which he briefed the participants regarding project before starting on the agenda discussions. In the meeting the following agenda was discussed:

1. Present status of problems related to receiving CCL from Deputy Commissioner's office;
2. Dedicated account and its operation procedure;
3. Assistance to the Affected Persons;
4. Affected persons' opinion on cooperating with the project construction work;
5. Conclusion;

1. Present status of problems related to receiving CCL from Deputy Commissioner's office: The DORP Team Leader was concerned about their present stand with regard to receiving CCL from Deputy Commissioner's office. Based on the analysis of the situation and the documentation the affected persons brought with them to the meeting. The problems can be categorized as three types: i) few cases are intrinsically within the family and shareholders itself which they can solved easily, ii) Some are related to updating records which needs pursuing to the local land office and to the office of Assistant Commissioner, land, iii) Some have suit case ongoing in the court, which will need a long time to resolve and will require effort by legal adviser.

2. Dedicated account and its operation procedure: The team leader explained the definition of dedicated account. It was explained that the account was opened for the CCL non paid APs, where their payable amount from DWASA will be kept deposited till their case is resolved. He added that compensation payment from Deputy Commissioner's office will remain deposited to the account of Deputy Commissioner's office. The operation procedures of dedicated account was narrated before the affected persons in a simple and explicit manner, so that all the meeting participants can easily understand the theme and concept of each, and every point of the leaflet prepared for CCL non-paid APs. The discussed points from leaflet was as below:

a. According to the SPS (2009) of ADB, the funding agency of the project, those socially and legally recognized as affected persons by the project intervention, will be eligible for additional and resettlement

benefits from DWASA. At that time, they are requested to communicate with INGO- DORP and DWASA office at the given address in the leaflet.

b. After finishing/completion of the legal process regarding land related disputes by the court, the affected persons to apply and submit the relevant papers to the Deputy Commissioner's office with judgment copy from court in favour of affected persons for compensation payment. At this time, the affected persons are also requested to communicate to the office of INGO-DORP and DWASA as mentioned in the leaflet.

c. Those affected persons who did not receive CCL for the affected land from the Deputy Commissioner's office due to the dispute over ownership claim in the court, their land value has already been deposited in the account of Deputy Commissioner's office. In the same way, those affected persons who could not receive additional payment/resettlement benefits due to the legal problems in the court, the estimated amount which they are supposed to receive will be kept safely in a separate account (dedicated account) at Janata Bank Limited, corporate branch, Kawran Bazar, Dhaka. The account will be operated by the joint signature of Project Director and Senior Finance & Accounts Officer of the project.

d. This account will be used only for payment of resettlement benefits to the CCL non-paid affected persons not for any other purposes.

e. After settlement of the disputes on ownership claim over the land by the court, along with the decree or judgment copy from court and other relevant papers to be submitted with an application to Deputy Commissioner's office. And application information to be given to INGO for necessary payments.

f. The District Commissioner (DC) will give CCL on affected land to the affected persons and the DWASA project office will pay all other (additional and other resettlement) benefits to the affected persons from the dedicated account.

g. This account will remain active and operational with the requisite balance due for affected persons, till last unpaid affected persons is paid and even after the completion of the project activities.

h. The interest that will be incurred on the balance of the account over the time will be distributed proportionately to the affected persons payment amount.

i. In case any affected person is unpaid by DWASA after the completion of implementation activities of the project, the affected person is instructed to apply to the Director, Management, Maintenance and Operation Department of Water 'Treatment Plant' at Gandharbpur. Payment of necessary additional /resettlement benefits will be arranged from this office. Time to time the CCL non-paid affected persons will be updated by the project.

j. To implement the resettlement activities smoothly a 6 (six) members Grievance Redress Committee (GRC) has been formed at each of local level Union *Parishad* according to Government Gazette Notification. This committee will deal with resolving the compensation related complaints.

3. Assistance to the APs: In the meeting almost all the affected persons appealed to DORP to help them in getting CCL from Deputy Commissioner's office and other benefits from DWASA. They told that they do

not understand the papers properly and some of them have legal problems in the court of law and it is a lengthy process, and they have no ability to bear the case related expenses for long time in this regard the requested PMU and DORP to help them to expedite t resolution of their problems.

4. Affected persons opinion to cooperate in project construction work: All the meeting participants (CCL non-paid APs) expressed their support for the project and agreed to cooperate with the project construction work for a success to the greater interest of Dhaka city dwellers to access pure water supply by DWASA.

5. Recommendations: A majority number of affected persons have problem with cases which are in court and local land office for updating the land records. Few had title suit in the court of law. Providing legal support to these affected persons will be effective and fruitful for them as well for the smooth implementation of the project.

6. Conclusion: Having no other matter for discussion the chair of the meeting closed the meeting. He thanked all the participants for attending the meeting.

S M Alamgir Hossain
Team Leader, DORP
DESWSP

Development Organisation of the Rural Poor (DORP)
Dhaka Environmentally Sustainable Water Supply Project
Araihazar ,Narayanganj

Subject : CCL Non paid APs Consultation Meeting,

Date : 01.03.2020

Location : DORP Area Office,Araihazar,Narayanganj

Time of Meeting : 10 AM

SL No	Name	Mouza & Plot No	Mobile No	Signature	Remarks
১	শ্রী: মহম্মদ হোসেন	আড়াইদা, ২০৪	০১৭২২২৪৫০৬১	শ্রী: মহম্মদ হোসেন	
২	শ্রী: মোস্তাফিজ	আড়াইদা, ২০৫	০১৭২৬০১২৭২	শ্রী: মোস্তাফিজ	
৩	শ্রী: হোসেন	আড়াইদা, ২১৫	০১৭২৩-২১৩২৭২	শ্রী: হোসেন	
৪	শ্রী: সানাউল্লাহ	আড়াইদা, ২১৫	০১৭২৬০১২৭২	শ্রী: সানাউল্লাহ	
৫	শ্রী: অরশাদুল হক	আড়াইদা, ২১৬	০১৭১৫ ৩২৭২৩২	শ্রী: অরশাদুল হক	
৬	শ্রী: সানাউল্লাহ	আড়াইদা, ২১৬	০১৮৭০১৭৩৫০৪	শ্রী: সানাউল্লাহ	
৭	শ্রী: মিজবান	আড়াইদা, ২১৮		শ্রী: মিজবান	
৮	শ্রী: মোস্তাফিজ হোসেন	TL, DORP, Dhaka	০১৭১৪০৭১২১৬	শ্রী: মোস্তাফিজ হোসেন	
৯	শ্রী: মোস্তাফিজ হোসেন	DM- DORP - Dhaka	০১৭০০৭০৮১৫৭	শ্রী: মোস্তাফিজ হোসেন	
১০	শ্রী: আবদুল হান্নান	আড়াইদা, ২১৯	০১৭৩৬৬৪৫৩৭	শ্রী: আবদুল হান্নান	
১১	শ্রী: মোস্তাফিজ হোসেন	আড়াইদা, ২২০	০১৭১১৬১৩৫৬৮	শ্রী: মোস্তাফিজ হোসেন	
১২	শ্রী: মোস্তাফিজ হোসেন	আড়াইদা, ২২১	০১৭৭১৬২৩৬১২	শ্রী: মোস্তাফিজ হোসেন	
১৩	শ্রী: মোস্তাফিজ হোসেন	আড়াইদা, ২০২৬	০১৭৭৩৫৩৭২২০	শ্রী: মোস্তাফিজ হোসেন	
১৪	শ্রী: মোস্তাফিজ হোসেন	Area manager, DORP	০১৭১৬১০৫৬০৫	শ্রী: মোস্তাফিজ হোসেন	
১৫	শ্রী: মোস্তাফিজ হোসেন	R.O, DORP	০১৭৬১৫৭৩৮৫৫	শ্রী: মোস্তাফিজ হোসেন	
১৬	শ্রী: মোস্তাফিজ হোসেন	R.O DORP	০১৭৫৪৮৫৭৩০৮	শ্রী: মোস্তাফিজ হোসেন	
১৭	শ্রী: মোস্তাফিজ হোসেন	R.O DORP	০১৭৩২-৭১৬২২৬	শ্রী: মোস্তাফিজ হোসেন	
১৮	শ্রী: মোস্তাফিজ হোসেন	L.F DORP	০১৭২৫৪০০৭৭৫	শ্রী: মোস্তাফিজ হোসেন	

E. Public Consultation on Dedicated Account Meeting Minutes

Dhaka Environmentally sustainable Water Supply Project (DESWSP) Development Organisation of the Rural Poor (DORP) Meeting Minutes on Dedicated account with CCL non-paid Affected Persons Araihazar, Narayanganj

Subject: Meeting related to Dedicated account with CCL non-paid Affected Persons of section-1 and 2

Venue: Haizadi Union Parishad complex, Araihazar, Narayanganj

Date: 08 March 2020

Time of Meeting: 10.00 AM to 1.00 PM

Discussing Agenda:

- a. Present status of problems related to receiving CCL from Deputy Commissioner's office;
- b. Dedicated account and its operation procedure;
- c. Assistance to the APs;
- d. Conclusion;

The meeting was held at Haizadi union parishad complex with the CCL non-paid affected persons of section-1 and section-2. In the meeting the following personnel were present from executing authority and from supporting agencies.

1. Md. Mahmudul Islam (Project Director, DESWSP, DWASA),
2. Dr. Rafeza Akter (National Resettlement Expert, MDSC),
3. Md. Tofazzal Hossen, Social Safeguard Officer (Social & Gender),
4. Md. Wahid Alam, External Monitoring Agency (EMA),
5. Md. Ali Hossain, Chairman Haizadi Union Parishad,
6. Md. Iqbal Hossain, Area Manager, DORP.

At the start of the meeting Md. Iqbal Hossain, Area Manager (DORP), Araihazar told to the meeting participants that the honorable Project Director will discuss about the payment related issues of CCL non-paid affected persons along with other relevant issues. After that the Chair of the meeting welcomed the participants and introduction of the participants was done. The participants were given a background on the project. It was explained that land has been acquired for the project construction work under the land acquisition and requisition ordinance of 1982 and Act 2017. According to this, the affected person is supposed to receive compensation from the Deputy Commissioner's office for their affected land and properties besides other resettlement benefits from DWASA. It was explained that by implementing this project the untreated water from Meghna River at Bishnandi point will be pumped through the raw water pipeline and will be sent to water treatment plant at Gandharbpur, Rupganj point. After treating, the treated water will send to injection point at Baridhara through the treated pipeline and will supplied to the city dwellers of Dhaka north city corporation. For this project an amount of 131.52 and 60.55 acres of land is needed to be acquired and the length will be 35 km. The project is being done with the financial support of ADB, so there are some resettlement conditions which need to be fulfilled. The Project Director added that the contractors have started construction activities at the intake point at *Shamvupura Mouza*, and they will start work in other places very soon. He told that DORP staff have visited house to house and distributed the leaflet related to dedicated account. He asked the participants whether they read the leaflet, in reply the participants told that they have read the leaflet. After that he started agenda-based discussions.

The Project Director wanted to know the present status of their papers needed related to CCL and he requested all of them to update their papers and to submit those to Deputy Commissioner's office immediately for receiving CCL.

The Project Director explained that those with land ownership problem have not received CCL from Deputy Commissioner's office, the amount of compensation for their loss property will remain deposited to the account of Deputy Commissioner's office. Other payable resettlement benefit amount which is due from DWASA will be kept deposited in a separate dedicated account. until For this purpose a separate account has been opened by DWASA at Janata Bank Limited, Kawran Bazar, Dhaka. The account will be operated with joint signature of Project Director and Senior Finance and Accounts officer of DWASA. The detailed operational procedures of the dedicated account were explained to the affected persons by the Project Director. This money will not be spent in any other purposes. In case their problems are not resolved during the project period, the resettlement assistance amount will be remain in this account even after the completion of the project. and they will be able to receive resettlement benefits from DWASA. He added that the bank interest will be distributed among the affected persons proportionately. The participants queries related to compensation are given below:

1. Affected person Sohel told to the project director that it is taking time to get mutation of their land from land office. Affected person requested Project Director they should not be deprived from compensation.
2. Affected person Mujibar Rahman assured that they will cooperate in implementing the project construction work. He added by no means the project activity can be stopped, he suggested to carry on the project construction work.
3. Affected person Md. Abdul Aziz, president of A. AM Bodruzzaman high school told one behalf of the high school that land office did not want to give mutation of the land of high school with an excuse that the land has already been acquired, so, it is taking time to get the land mutated. He also suggested to carry on project activities.
4. Affected person Md. Safazuddin has a court case on his land, after resolution of the case he wanted to know whether they will receive compensation? In reply Project Director told him that after disposal of the case he must submit necessary papers to Deputy Commissioner's office for compensation payment. Subject to receiving compensation from Deputy Commissioner's office he must submit papers to DORP Araihaazar Area office for additional payment.
5. The Chairman of Haizadi union parishad Mr. Ali Hossain Miah expressed that due to the complex paper work it may take time to resolve problems. However, and for this reason by no means project activities can be hampered. He suggested to continue the project construction work with the the consent of the chairman all participants gave consent in continuing the project construction work.




The Project Director told the participants that the land has already been acquired by the government for the purpose of the project construction work. He the participants clear that Deputy Commissioner Narayananj has already handed over the land to DWASA. The contractors will start their construction work soon, so, they must remove all their structures from the project acquired land within two weeks and make the land free of encumbrance for project construction work.

Conclusion: Project Director requested the participants to support to the project construction work by removing structures from the project land. In response all the participants including the Union Parishad Chairman of Haizadi Union Parishad agreed upon with the Project Director's request and expressed their support to cooperate with the construction work for a successful completion. Having no further matter of discussions, the chair of the meeting closed the meeting by thanking all the participants.

Md. Mahmudul Islam
 Superintending Engineer & Project Director
 DESWSP, Dhaka WASA

Attached: 1. Attendance Sheet

SL No	Name	Mouza & Plot No	Mobile No	Agreed with the DWASA and signed
40	আব্দুল আজিজান নেংদুয়া			Saiful 08/03/20
41	কাজিমুর রহমান	হালীমাখালী, ৩২৩	01794700636	কাজিমুর
42	আ. রহমান	হালীমাখালী, ৩২০০		আ. রহমান
43	আব্দুর স্বপ্ন	আব্দুলখালী,		✓
44	কাজিমুর রহমান	হালীমাখালী,		কাজিমুর
45	শামস	হালীমাখালী-	01993260611	✓ ২।২।০৮
46	কারওয়ানী ববি	হালীমাখালী	01715832525	✓
47	ইমানুস			✓ ইমানুস
48	শ্রী: মাহমুদ	চন্দ্রাবতী খুলনা	01716054788	✓
49	আব্দুল কালাম	কামালী		✓ আব্দুল
50	কামাল	চন্দ্রাবতী -		কামাল
51	শ্রী: মুহাম্মদ শামস	DORP, R.O	0761593845	✓
52	আব্দুল হাফিজ	হালীমাখালী	-	আঃ হাফিজ
53	শ্রী: মোহাম্মদ শামস	কামালী	01715849723	মোহাম্মদ
54	আব্দুল কামাল	কামালীখালী-		✓
55	কামাল	আব্দুলখালী,		✓ কামাল
56	মোহাম্মদ হাফিজ	চন্দ্রাবতী	01781011692	মোহাম্মদ
57	মুহাম্মদ হাফিজ	কামালী-		✓
58	আব্দুল হাফিজ	কামালীখালী		আব্দুল হাফিজ
59	আব্দুল হাফিজ	কামালীখালী		আব্দুল
60	আব্দুল হাফিজ	কামালীখালী-		আব্দুল
61	কাজিমুর রহমান	আব্দুলখালী	01711613468	কাজিমুর
62	আব্দুল হাফিজ	আব্দুলখালী		আব্দুল

SL No	Name	Mouza & Plot No	Mobile No	Agreed with the DWASA and signed
63	আমজাদ (শমস)	শাকী কাশনী	01938500048	 আমজাদ
64	নাজমুল	শাকী কাশনী	01941394924	 নাজমুল
65	আঃ মনির	শাকী কাশনী	-	মনির
66	আবুল হামিদ	শাকী কাশনী	01775534077	আঃ হামিদ
67	লাল মিয়া	শাকী কাশনী		
68	আনা মিয়া	শাকী কাশনী		আনা
69	আবুল হামিদ	শাকী কাশনী		আবুল হামিদ
70	আবু জাফর	কাশনী		আবু জাফর
71	বাবু	নকলীপুরা	01957057617	বাবু
72	আবুল হামিদ	নকলীপুরা		আবুল হামিদ

F. DD Record for unpaid Aps

Due Diligence Record

Project Loan Number: 3051
May 2020

Project Loan

Bangladesh: Dhaka Environmentally Sustainable Water Supply Project

ABBREVIATIONS

ADB:	Asian development Bank
CCL:	Cash Compensation under Law
DESWSP:	Dhaka Environmentally Sustainable Water Supply Project
DORP:	Development Organization of the Rural Poor
DWASA:	Dhaka Water Supply and Sewerage Authority
NGO:	Non-governmental Organization
PMU:	Project Management Unit

Introduction

1. The Dhaka Environmentally Sustainable Water Supply Project (DESWSP) will provide reliable and sustainable water supply for Dhaka City dwellers by developing a new surface water supply scheme for supply augmentation, which includes development of a water intake at Meghna River, twin raw water transmission pipelines, a water treatment plant (WTP) at Gandharbpur with capacity of 500 million liters per day, twin treated water transmission pipelines to the existing water supply network, and distribution reinforcements. The project also includes distribution network improvements to reduce non-revenue water and will promote household and community access to safe water, including support to low-income communities. Dhaka Water Supply and Sewerage Authority (DWASA) is the executing and implementing agency of the project.
2. A Resettlement Framework was developed for DESWSP to provide guidance to prepare and implement Resettlement Plans. Issues of involuntary resettlement are being addressed based on the Project Resettlement Framework, 2013, National Legislations of Government of Bangladesh, which includes Acquisition of Immovable Property Ordinance (ARIPO), 1982, Acquisition and Requisition of Immovable Property Act (ARIPA), 2017 and the ADB Safeguard Policy Statement (SPS), 2009.
3. The Resettlement Plans for DESWSP cover 6 Sections. Sections 1 and 4 are already under construction. For Sections 2 and a part of 3, the raw water pipeline section, the contractors are mobilized and ready to start. However, the project has not been able to pay compensation to all the affected persons, hence, based on the Resettlement Framework, cannot start work unless all affected persons have been paid.

Resettlement Plans for the Project

Sections	Description
Section 1	Water Intake Area
Section 2	Water Intake to Baliapara (End of Araihasar)
Section 3	Darikandichak (Start of Rupganj) to Murapara via Gandharbpur WTP
Section 4	Water Treatment of Plant Gandharbpur
Section 5	Rupganj (West bank of Sitalakhya River) to Balu River (East Bank)
Section 6	Balu River (West Bank) to Vatara along Madani Avenue up to Baridhara

4. This report is a due diligence of the all the activities and measures carried out by Dhaka Water Supply and Sewerage Authority (DWASA) to facilitate payments to meet ADB safeguards requirements.

DWASAs Actions to Facilitate Payments.

5. Between 30th May and 2nd June 2019, DWASA had reported to ADB its inability to pay compensation for 100 percent affected persons in Section1 and Section 2 Resettlement Plans.
6. As on 1 April 2020, 21 cases (of 130 which was reported during the Mission in Oct-Nov 2019) were resolved through DWASA's efforts to support affected persons in receiving compensation payments, bringing the total down to 109.
7. As on 1 April 2020, due to further facilitation by DWASA, 3 affected persons received cash compensation under law (CCL) payments and have received remaining compensation due to

them as well, bringing down the total number of affected persons with unpaid compensation to 106.

8. As on 1 April 2020, another 8 affected persons' CCL payments are ready due to pursuing of the matter by DWASA with the concerned Deputy Commissioner's Office; the affected persons have been informed about the same by the project NGO, Development Organisation of the Rural Poor (DORP) and are being encouraged and facilitated to collect the compensation payments.

The Table below provides the summary status as on 1 April 2020.

	Summary of Cases as on 1st April 2020	No. Affected Persons	Remarks
1	No. of cases resolved with DWASA and implementing NGO facilitation	11	3 affected persons have already received CCL and CCL is ready at Deputy Commissioners office for 8 affected persons.
2	Affected persons who are the actual owners of the land but the notice under section 4(1) was served to the wrong persons	17	DORP and PMU to initiate correction by Deputy Commissioner's Office. The persons who are rightful owners of these properties will have to submit their papers to the land office for correction. The persons who have been wrongfully served notice, are aware that there has been a mistake on the issue of notification.
3	No. of mutation cases where papers have been submitted to land office.	18	PMU and DORP are pursuing regularly with land office.
4	No. of mutation cases where papers are not yet submitted to land office.	28	PMU and DORP are pursuing this regularly with the affected persons.
5	No. of cases pending in the Court of law	25	20 affected persons have filed title-suite cases and 5 affected persons applied for clearance for allotment of vested property.
6	No. of cases where there is conflict among shareholders	8	8 cases. DORP and PMU are motivating and pursuing affected persons to process papers to submit to land office for record correction.
7	No. of cases where affected persons are not willing to receive CCL as they perceive the amount as too small.	2	PMU and DORP are motivating the affected persons to receive the same.
	Total	109	

9. From the above table, it is evident that 11 cases have either been resolved/ are close to resolution; 17 affected persons are wrongly identified, the same number of rightful owners now have to submit their papers; the Court's intervention will be required to reach resolution of

ownership disputes for 25 affected persons; and 56 affected persons are under process of being facilitated by DORP and PMU to receive compensation.

10. The following actions are/ have been taken by DWASA to facilitate payment of unpaid compensation:

Step 1: List of affected persons with unpaid compensation prepared, to enable follow up, facilitation and monitoring

11. The list of affected persons with unpaid compensation and the reason for non-payment is prepared and is being monitored on weekly basis by PMU and updates reported to ADB on fortnightly basis (until COVID 19 outbreak).

12. Verification of severity of Impact on affected persons with unpaid compensation was carried out by DORP. None of these affected persons are losing any structures residential, commercial or other assets. There is no physical displacement anticipated. There is no loss of trees either. However, loss of strips of land ranging from less than 1% - 80% is anticipated, for which compensation will be paid according to the Resettlement Framework of the project.

Step 2: Reasons for Non-Payment Identified for each affected person with unpaid compensation. The following major issues were identified:

1. Mutation of land records to present owner's name not done.
2. Vested (government) lands occupied by affected persons and are being claimed by them. The ownership of these properties needs to be resolved only by the Court.
3. Ownership disputes. These cases are pending in the Court.

Step 3: Preparation of information leaflet on dedicated account

14. An information leaflet has been prepared in Bengali and distributed to all affected persons with unpaid compensation/pending issues.

Step 4: Series of consultations held with affected persons who have not received compensation and specific actions taken for facilitation of payments

1. The implementing NGO, DORP, and the project management unit (PMU) have been following up and supporting affected persons who do not have their papers in order, for submission to the Upazila land office. They are assisting affected persons to obtain their required land ownership documents and papers. There have been repeated consultations, individual meetings and focus group discussions with the affected persons who are yet to receive CCL payment, to explain the process of CCL payments and the requirements. All the meetings are documented.
2. For pending mutation cases, DORP and PMU have met and requested the owners on an individual basis, to go to the Upazila land office and apply for correction and updating of land records. DORP and PMU are engaging with the affected persons to motivate them to initiate the mutation process. It has been explained to the affected persons that Deputy Commissioner's office can pay compensation for land only after the land records are in order and mutation is undertaken.

3. The implementing NGO DORP is counselling affected persons who have expressed a lack of interest in taking their CCL payments, citing the small amount budgeted towards compensation for their lack of interest. The NGO is explaining the process of computation of CCL payment, the provision for top up payments to meet replacement cost requirements, and other resettlement assistances and benefits that are available.
4. In case of ownership disputes and legal cases DORP and PMU are requesting the affected persons to seek legal help to pursue the matter in court and resolve the issue at the earliest.
5. In a few cases, ownership issues are being discussed with the claimants/shareholders in the presence of respected members of the communities, who have been identified by DORP and PMU, to facilitate resolution of minor issues.

Step 7: Dedicated account opened

15. A dedicated account has been opened at Janata Bank Limited, Kawran Bazar Corporate Branch, on 12th February 2020, account no. 0100210340372, which is meant exclusively for depositing of compensation that cannot be paid due to Court cases and disputes. The dedicated account will be maintained until the last affected person is paid and interest earned on the deposited compensation amount will be shared proportionately by the concerned affected persons (in proportion to their respective compensation amounts).

Next Steps

Step 6: Payment of all resettlement assistances to affected persons - other than those with court cases, disputes and unwilling affected persons.

Step 7: Proposed appointment of Land and Resettlement Officer at DWASA, to support affected persons

16. Appointment of Land Officer status/action taken/deadline to be mentioned

Step 8: Further facilitation of pending mutation and pending compensation cases and actions taken for avoidance of impact to persons wrongly served with acquisition notices

17. As per DWASA's estimates, mutation cases can be resolved within a year, with support from PMU and DORP to get individuals' papers (28 cases) in order for submission to Upazila office.

Step 9: Update and disclose Resettlement Plans with details of dedicated account

Step 10: Deposit unpaid compensation for affected persons with court cases (25 affected persons), conflict among shareholders (8 affected persons), where the acquisition notification has been sent to wrong person (17 affected persons), mutation cases where papers have been submitted to land office (18 affected persons), mutation cases where papers are not yet submitted to land office (28 affected persons) and affected persons unwilling to receive compensation despite best efforts of DWASA and NGO (2 affected persons).

Conclusion

18. The following actions sum up the actions and measures taken by DWASA to exhaust all means of payment of unpaid compensation to affected persons:

(i) **Payment of compensation due:** 24 cases (of 130 affected persons with unpaid compensation) were resolved through DWASA's efforts to pay compensation payments.

(ii) **Follow up with Deputy Commissioner's office to expedite cash compensation under law (CCL) payments.** Another 8 affected persons' CCL payments are ready due to pursuing of the matter by DWASA with the concerned Deputy Commissioner's Office; the affected persons have been informed about the same by the project NGO and are being encouraged and facilitated to collect the compensation payments.

(iii) **Facilitation of submission of mutation papers by affected persons (completed):** the NGO has facilitated submission of mutation papers for 18 affected persons to Deputy Commissioner's office.

(iv) **Facilitation of submission of mutation papers by affected persons (under progress):** the NGO is in the process of facilitating submission of mutation papers for 28 affected persons to Deputy Commissioner's office.

(v) **Facilitation of resolution of conflict among shareholders:** NGO and PMU are engaging closely with affected persons related to 8 cases of disputes/conflicts, to facilitate dispute resolution.

(vi) **Court cases.** There are 25 court cases, for which CCL payments have been deposited by DWASA with Deputy Commissioner's office.

(vii) **Addressing lack of willingness to receive compensation:** There are 2 affected persons who have indicated lack of willingness to receive compensation as they find it too low. They are being motivated by NGO and PMU to accept their compensation.

(viii) **Facilitation of submission of papers of rightful owners to Deputy Commissioner's office:** There are 17 affected persons whose records of ownership is in the process of getting rectified in the Deputy Commissioner's office. Once all the papers are submitted, notification for acquisition will be sent to them.

21. The list of affected persons and the compensation amount due to them is given in the Attachment 1. (Please note that the attachment has been given plot wise, which is why there are 114 entries. There are 5 affected persons who have two plots).

Dhaka Environmentally Sustainable Water Supply Project
Approximate Estimate of Resettlement Grant for Titled APs
Raw Water Transmission Line (Section-1)
Upazila: Araihasar, District: Narayanganj

SI No	Aps Name	Aps F/H Name	Mouza	Upazila	District	Plot No.	Land Type	Total Land owned by AP (in decimal)	Affected Land (in decimal)	CCL Amount to be paid by Deputy Commissioner	Amount to be paid by DWASA																											Remarks				
											Additional Grant For Land (AGL)	AL	HL	WB	CFS	GT	SC	TP	CGSLL	RS	BS	SS	CPRMF	AEE	BR	LIP	VH	RA	RRC	STG	SRG	Additional Grant	Resettlement Grant	Total Amount	Payable Amount							
Col 0	Col 1	Col 2	Col 3	Col 4	Col 5	Col 6	Col 7	Col 8	Col 9	Col 10	Col 11	Col 12	Col 13	Col 14	Col 15	Col 16	Col 17	Col 18	Col 19	Col 20	Col 21	Col 22	Col 23	Col 24	Col 25	Col 26	Col 27	Col 28	Col 29	Col 30	Col 31	Col 32	Col 33	Col 34	Col 35	Col 36	Col 37	Col 38				
1	Shahin Ahmed	Abdul Baten	Sumbupura	Araihasar	Narayanganj	131	Nall	230	6.5000	423872	34379	34379					4225																		45825			34379	50050	84429	84429	
2	Anowara	Late Munhag	Sumbupura	Araihasar	Narayanganj	131	Nall	48	6.5000	423872	34379	34379					4225																		45825			34379	50050	84429	84429	
3	Md. Javed Ali	Late Sona Miah	Sumbupura	Araihasar	Narayanganj	127	Nall	41	26.0000	1695486	137514	137514					16900										20000	58500							183300			137514	278700	416214	416214	
Total								319	39.0000	2543229.00	206271.00	206271.00	0.0					25350.00																		274950			206271.00	#####	585074	585074

29	Md. Dillur Rahman	LATESAYD MOKLESUR RAHMAN	Ranidi	Araihazar	Narayanganj	20	Nall	19.2500	1455647	0	0	12513	145565	0	158077	158077	158077			
30	Md. Babul Mollah		Ranidi	Araihazar	Narayanganj	22	Nall	0.5000	37809	0	0	325	3781	0	4106	4106	4106			
31	Md. Parul Mia		Ranidi	Araihazar	Narayanganj	22	Nall	0.2500	18905	0	0	163	1890	0	2053	2053	2053			
32	Md. Dillur Rahman		Ranidi	Araihazar	Narayanganj	22	Nall	0.2500	18905	0	0	163	1890	0	2053	2053	2053			
33	Most. Selina Begum		Ranidi	Araihazar	Narayanganj	22	Nall	0.2500	18905	0	0	163	1890	0	2053	2053	2053			
34	Gias Uddin Master	LATE OLI ULLAH MIA	Ranidi	Araihazar	Narayanganj	345	Nall	135	6.2500	472613	0	0	4063	47261	0	51324	51324	51324		
35	Md. Shahaj Uddin	LATE,ALI BOX PRODHAN	Ranidi	Araihazar	Narayanganj	587	Nall	8.0000	604944	0	0	5200	60494	0	65694	65694	65694			
36	Ayesh Begum	SHAHAJ UDDIN	Ranidi	Araihazar	Narayanganj	587	Nall	8.0000	604944	0	0	5200	60494	0	65694	65694	65694			
37	Tomiz Uddin	LATE ELAHI BHUYAN	Ranidi	Araihazar	Narayanganj	593	Nall	45	5.0000	378090	0	0	3250	20000	78000	37809	0	139059	139059	139059
38	Tota Mia	LATE ALAHI BHUYAN	Ranidi	Araihazar	Narayanganj	593	Nall	50	5.0000	378090	0	0	3250	20000	97500	37809	0	158559	158559	158559
39	Samoddi	LATE SHAMSUDDIN	Ranidi	Araihazar	Narayanganj	593	Nall	60	5.0000	378090	0	0	3250	20000	58500	37809	0	119559	119559	119559
40	Jahatun	LATE HAZROT ALI	Ranidi	Araihazar	Narayanganj	593	Nall	34	5.0000	378090	0	0	3250	20000	78000	37809	0	139059	139059	139059
41	Laily	LATE ALAHI	Ranidi	Araihazar	Narayanganj	593	Nall	55	5.0000	378090	0	0	3250	20000	97500	37809	0	158559	158559	158559
	Suruj Mia					120	Nall	0.2500	9304											

Code Sheet

SI No	Entitlement	Code
	LAND	
1	Agricultural Land	AL
2	Homestead Land	HL
3	Water Bodies (Cultivated & Non-cultivated)	WB
4	Current fish stock	CFS
5	Grant for Trees	GT
6	Standing Crops	SC
7	Tree Plantation	TP
8	Cash Grant Titled and non-Titled Share croppers, Licensees and Lessees of agricultural land and pond	CGSLL
	STRUCTURES	
9	Residential structures	RS
10	Business structures	BS
11	Secondary structures	SS
12	Physical Cultural Resources (PCR) / Common Property Resources(CPR) Management Fund	CPRMF
	LIVELIHOOD ALLOWANCES	
13	Affected Employees/ Wage Earners	AEE
14	Business Restoration	BR
15	Livelihood Improvement Program	LIP
16	Vulnerable households	VH
	OTHER ALLOWANCES	
17	Relocation allowance	RA
18	Refund of Registration Cost (Stamp Duty)	RRC
19	Structure Transfer Grant	STG
20	Structure Reconstruction Grant	SRG
21	New Utilities Connection	CGNUC
22	Shifting Grant for Tenant	SGT
23	Rental assistance for both residential and commercial structures of the Rented-Out AP	RARO
24	Unforeseen Adverse Impact	UAI

G. Graveyard Signed MoU

বিষয়ঃ ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রকল্পের অধীনে গছবর্পুর রূপগঞ্জের ঢাকা ওয়াসার নির্মাণাধীন পানি শোধনাগার নির্মাণের জায়গায় আটানি সমাজের কবরস্থান থাকার কারণে সূত্র জটিলতা নিরসনের বিষয়ে কবরস্থান কমিটি/মসজিদ কমিটি ও ঢাকা ওয়াসার মধ্যে সমঝোতার জমির সীমানা নির্ধারণ ও বাউন্ডারী ওয়াল নির্মাণ প্রসঙ্গে।

ঢাকা ওয়াসার ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রকল্পের অধীনে গছবর্পুর রূপগঞ্জের ঢাকা ওয়াসার নিজস্ব জায়গায় সৈনিক ৫০ কোটি লিটার ক্ষমতা সম্পন্ন পানি শোধনাগার নির্মিত হচ্ছে। পানি শোধনাগার সাইটের একাংশে স্থানীয় আটানি সমাজের অদা হইতে প্রায় ৬০ বৎসরের ব্যবহৃত একটি কবরস্থান থাকায় উহা স্থানান্তরের বিষয়টি নিয়ে স্থানীয়/এলাকাবাসী ও ঢাকা ওয়াসার সাথে অনাকাঙ্ক্ষিত ঘটনা ঘটে ফলে উভয় পক্ষের মধ্যে একটা টানা-পোড়ন চলেছে যা কোন পক্ষের কাম্য নয়। এখানে উল্লেখ্য যে, সরকার কর্তৃক আলোচ্য জমি অধিগ্রহণের পূর্বেই কবরস্থান বিদ্যমান ছিল এবং এলাকাবাসী কর্তৃক উক্ত জমি ওয়াকক করা হয়েছিল। একপর্যায়ে কবরস্থান বিষয়ক জটিলতার কারণে প্রকল্পের পানি শোধনাগার নির্মাণ কাজ বর্তমানে বন্ধ আছে। বিষয়টি জরুরী ভিত্তিতে সমাধানপূর্বক প্রকল্পের কাজ পুনরায় আরম্ভ করা প্রয়োজন এবং সূত্র সমাধানকল্পে নিম্নোক্ত শর্তে বর্তমান কবরস্থানের জমির আকার ও পরিমাণ পূর্ব ও পশ্চিমাংশে সমন্বয়পূর্বক তা কবরস্থান হিসাবে আটানি সমাজকে ব্যবহার করার জন্য উভয় পক্ষের সম্মতি এবং ঢাকা ওয়াসার কর্তৃপক্ষ বিগত ১৫/০১/২০২০ ইংরেজী তারিখে 46.113.618.00.00.G-(V-1)/DESWSW/১৮৮৩ নং সমঝোতা সমন্বয়পূর্বক স্মারকলিপির পেশের মাধ্যমে একমত পোষন করা হলোঃ

- প্রকল্পের কাজের সার্থে বর্তমান কবরস্থানের উত্তর পার্শ্বের কিছু অংশ থাকার কারণে উত্তর পার্শ্বের যে অংশটুকু প্রকল্পের প্রয়োজনে প্রকল্পের আওতায় আনা হবে সেই অংশটুকু সমন্বয় করা হবে। ঢাকা ওয়াসার কর্তৃক সরঞ্জামে সাইট পরিদর্শন করে নির্মাণাধীন পানি শোধনাগার ডিজাইনের বাইরে বিদ্যমান (সংযুক্ত নকশা মোতাবেক) জমি কবরস্থান হিসেবে ব্যবহার করার জন্য ঢাকা ওয়াসার হতে সম্মতি দেয়া হল।
- কবরস্থান কমিটি ও ঢাকা ওয়াসার প্রতিনিধি কর্তৃক সমন্বয়কৃত কবরস্থানের সীমানা চিহ্নিত করবে এবং ঢাকা ওয়াসার কর্তৃক ৫ ফুট উচ্চতার বাউন্ডারী ওয়াল ও একটি মেইন গেইট নির্মাণ করা হবে। এতদ্বিধয়ে সংশ্লিষ্ট আটানি সমাজের কবরস্থান কমিটি/মসজিদ কমিটি প্রতিনিধি ঢাকা ওয়াসার বিভাগকে সহযোগিতা করবে।
- প্রস্তাবিত সীমানা প্রসারের বাইরে উত্তর পার্শ্বের যে অংশটুকু প্রকল্পের আওতায় ছেড়ে দেয়া হবে উক্ত অংশে (সংযুক্ত নক্সায় প্রদর্শিত) দৃশ্যমান কবরসমূহ আটানি সমাজের কবরস্থান কমিটির প্রতিনিধি ঢাকা ওয়াসার নিয়োজিত এনজিও, স্থানীয় আটানি সমাজের মসজিদ কমিটির প্রতিনিধি, স্থানীয় সমাজের উপদেষ্টা প্রতিনিধি, স্থানীয় মসজিদের ইমাম সাহেব, ওয়াসার প্রকল্প উপদেষ্টা প্রতিনিধি এবং প্রকল্প দপ্তরের প্রতিনিধিবর্গ সৌখন্ডাবে কবর সমূহের তালিকা প্রস্তুত করবে। উক্ত কমিটির পরামর্শ মোতাবেক তালিকাভুক্ত কবরগুলো ধর্মীয় নিয়ম, আচার ও রীতি অনুসরণ করে আটানি সমাজের কবরস্থান কমিটি/মসজিদ কমিটি কর্তৃকই তালিকাভুক্ত কবরসমূহ প্রতিস্থাপনের ব্যবস্থা করবে। কবরসমূহ প্রতিস্থাপনের জন্য ঢাকা ওয়াসার কর্তৃক প্রয়োজনীয় ব্যয়ভার বহন করবে। কবরস্থানে চলাচলের জন্য তালতলা হতে কবরস্থানের গেইট পর্যন্ত চলাচলের রাস্তা উন্মুক্ত থাকবে।
- কবরস্থানের অবকাঠামোর ভিতরে চলাচলের রাস্তা, পানি নিষ্কাশন ব্যবস্থা, সেড ও আলোর ব্যবস্থা ঢাকা ওয়াসার কর্তৃক করা হবে।

এমতাবস্থায়, প্রস্তাবিত সীমানা প্রসারের বাইরের কবরসমূহ সীমানা প্রসারের অভ্যন্তরে ধর্মীয় নিয়ম, আচার ও রীতি অনুসরণ করে প্রতিস্থাপন করাসহ বাউন্ডারী ওয়াল নির্মাণ কাজে সহযোগিতা প্রদানের লক্ষে সম্মানিত এলাকাবাসী ও কমিটির প্রতিনিধিবর্গকে সরকার কর্তৃক গৃহীত এবং ঢাকা ওয়াসার কর্তৃক বাস্তবায়নাধীন ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রকল্পের পানি শোধনাগার নির্মাণ, কবরস্থানের উন্নয়নকল্পের কাজ এবং উপরে উল্লেখিত সমঝোতার সকল বিষয়াদি মানিয়া উন্নয়নমূলক সকল কাজ এগিয়ে নেওয়ার ব্যাপারে সকলে আন্তরিক সহযোগিতা প্রদান করবে এ মর্মে একমত পোষন করে সমঝোতা স্মারকে স্বাক্ষর করা হলো।

স্বাক্ষরিত
সভাপতি
২৭-১-২০২০

স্বাক্ষরিত
সাধারণ সম্পাদক
আটানি সমাজ কবরস্থান কমিটি
গছবর্পুর, রূপগঞ্জ, নারায়ণগঞ্জ

ঢাকা ওয়াসার প্রতিনিধি

১। মোঃ মোস্তাফিজ
নিঃ সঃ ঢাকা ওয়াসার

স্বাক্ষরিত
সভাপতি
আটানি সমাজ মসজিদ কমিটি
গছবর্পুর, রূপগঞ্জ, নারায়ণগঞ্জ

স্বাক্ষরিত
সাধারণ সম্পাদক
আটানি সমাজ মসজিদ কমিটি
গছবর্পুর, রূপগঞ্জ, নারায়ণগঞ্জ

২। ২৭/০১/২০২০
১৫/০১/২০২০

৩। (মোঃ মাহমুদুল ইসলাম)
তত্ত্বাবধায়ক প্রকৌশলী ও
প্রকল্প পরিচালক
DESWSW, ঢাকা ওয়াসার।

১। মোঃ হাবিবুল হক
২। ২৭/১/২০২০

১।
Mayor
Tarabo Municipality
Rupganj, Narayanganj

২।
২।
৩।

৪। মোঃ মিজানুজ্জামান
৫। মোঃ হাবিবুল হক

