

Social Monitoring Report

Project No. 42173-013
Semi-Annual Report (January-June 2023)
August 2023

Bangladesh: Dhaka Environmentally Sustainable
Water Supply Project

Packages P1, P2, P3.1 and P3.2

Prepared by the Ministry of Local Government Rural Development and Cooperatives Dhaka
Water Supply and Sewerage Authority for the Asian Development Bank.

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, the Asian Development Bank does not intend to make any judgments as to the legal or other status of any territory or area.



People's Republic of Bangladesh

Ministry of Local Government Rural Development and Cooperatives

Dhaka Water Supply and Sewerage Authority

9th-floor DWASA Bhaban, 98 Kazi Nazrul Islam Avenue, Kawran Bazar, Dhaka 1215



Dhaka Environmentally Sustainable Water Supply Project (DESWSP)

ADB Loan No. 3051-BAN (SF)

SEMI-ANNUAL SOCIAL SAFEGUARD MONITORING REPORT

(COVERS PACKAGES P1, P2, P3.1 AND P3.2)

JANUARY — JUNE 2023

August 2023

Funded by:



AFD
AGENCE FRANÇAISE
DE DÉVELOPPEMENT



European
Investment
Bank

The EIB bank

EXECUTIVE SUMMARY

This is the 16th Semi-annual Social Safeguard Monitoring Report (SSMR) prepared for project implementation under Dhaka Environmentally Sustainable Water Supply Project (DESWSP) of the Dhaka Water Supply and Sewerage Authority (DWASA) for submission to the Asian Development Bank (ADB).

The project is funded by Asian Development Bank (ADB), Agence Francaise de Development (AFD), and European Investment Bank (EIB). The total project cost is 1104.9 million USD of which ADB contributes 390 million, AFD 204.90 million, EIB 136million, and Bangladesh government 374 million. The cost of resettlement (social safeguard) has been borne by the government.

The DESWSP has a target impact (Goal) of “Improved access to and quality of sustainable water supply services in Dhaka (City)”. The project aims to achieve an outcome of “More reliable and improved security of water supply and sanitation in Dhaka” and to achieve the target ‘impact’ through these defined outputs:

- (i) Output 1: New surface water supply system developed comprises of 1,000 MLD river intake, 500 MLD water treatment works (phase 1), 22 km raw water pipeline, 14 km treated water transmission, 24 km primary distribution pipelines, and 44 km feeder pipelines (Figure 2.1). [Completion target: December 2024]
- (ii) Output 2: Distribution network strengthened comprises rehabilitating 376 km of distribution networks and 32,000 household and community connections, and legalization of 3700 household and community connections at MODS Zone 6 (Figure 2.2). [Completed]
- (iii) Output 3: Project management and administration adequately supported. [Completion target: December 2024]
- (iv) Output 4: Empowerment of women and vulnerable groups supported (new scope) along with the construction of at least 1,000 community toilets and bathing chambers with separate units for males/females in low-income communities in Dhaka city.¹ [Completion target: December 2023]

Package 3.2 and Output 4 have been added as a new scope under the additional financing.

Output 1 is divided into four contract packages, such as P1 (water intake, raw water pipelines, and water treatment plant), P2 (treated water transmission pipelines), P3.1 (primary distribution pipelines), and P3.2 (feeder pipelines).

The report is prepared on Output 1 by the DWASA Project Management Unit (PMU). Mott MacDonald, the Consultant of the project assisted PMU in this regard.

The DESWSP’s output 1 is delivered through several contract packages by several consultants, contractors, and NGOs under DWASA’s PMU. Mott MacDonald is responsible for the four main construction contracts through their management, design, and supervision consultancy (MDSC) contract. Under MDSC, Mott MacDonald is acting as the Employer’s designer for Packages 2 and P3.1 and P3.2 and as the supervision consultant for Packages 1, 2, P3.1, and P3.2. Contractors have been appointed for P1, P2, and P3.1. The construction

¹ For output 4, it will be supported by an ADF grant to strengthen access of women and vulnerable groups in underserved low-income communities (slums) of Dhaka to basic infrastructure and social services and to promote their legal empowerment.

contract for P3.2 has been awarded to Chi na Geo-Engineering Corporation (CGC) on 28 December 2022. P1 is a Design, Build and Operate (DBO) contract.

The bulk water supply system runs 36 km from the Meghna River to Dhaka, passing through Araihasar and Rugganj Upazila and Madani Avenue after crossing Sitalakshya and Balu rivers. This project will use 310.71 acres of land of which Dhaka WASA owns 81.53 acres (in Gandharbpur). Public land is another 46.03 acres. The rest of the land (183.15 acres) is privately owned. The project will impact private and government land of different organizations including structures, assets, crops, fish, trees, etc.

The DESWSP falls under Category 'A' according to ADB classification based on involuntary resettlement impacts of projects. It falls under Indigenous Peoples' Category 'C' according to ADB Indigenous People's Categorization of projects. No indigenous people's households have been found during the surveys.

Issues of involuntary resettlement are being implemented following two national (GoB) legislations such as Acquisition and Requisition of immovable Property Ordinance (ARIPO) 1982 – for land acquisition initiated before the 2017 Act came into force, and Acquisition and Requisition of Immovable Property Act (ARIPA), 2017, for subsequent land acquisition. In addition, ADB Safeguard Policy Statement (SPS), 2009 is being followed. Land under resettlement plan Section 1 and Section 2 is being acquired following ARIPO, 1982. After repealing ARIPO, 1982, land under resettlement plans 3, 5, and 6 is being acquired following newly enacted ARIPA, 2017.

DWASA is the executive agency. PMU has a Safeguard Implementation Unit (SIU) for monitoring safeguard activities implementation. An independent External Monitoring Agency (EMA) has been engaged as a third-party monitor for Resettlement Plan (RP) implementation. To carry out the resettlement activities in P1 and P2, PMU contracted DORP, a local NGO in February 2015. Another NGO has been appointed in December 2021 for carrying out resettlement activities for P3.1 and P3.2.

For the convenient implementation of the Resettlement Plans, P1 and P2 areas were divided into 6 separate Resettlement Plan Sections (1-6). Five resettlement plans for Sections 1, 2, 3, 4, 5 and 6 in P1 and P2 received approval and disclosed on ADB and DWASA websites. Due Diligence Reports (DDR) for P3.1 and Resettlement Plan for P3.2 received approval and are disclosed on ADB and DWASA websites.

The Deputy Commissioner has completed land acquisition for P1 and P2 and handed over the land to DWASA. However, CCL and other resettlement assistance is still ongoing in five sections such as section 1, 2, 3, 5, and 6. Land under Resettlement Plan 4 is owned by DWASA. In Section 1, 99.6% of the affected persons have been fully paid (CCL and other resettlement assistance). About 94.2% of CCL payment has been completed in Section 2. In Section 3 it is 85.1%. The percentages of CCL payment are 87.0% and 82.2% in Section 5 and Section 6 respectively. All non-titled (100%) affected persons (9 in Section 1; 73 in Section 2; 63 in Section 3; 260 in Section 4 and 36 in Section 6) have been paid. The affected persons who received CCL payment, all of them received applicable top up and resettlement assistance.

During this reporting period, Deputy Commissioner has handed over land to DWASA under LA Case 10/2020-21 in a part of Resettlement Plan Section 5 on 2 January 2023. Payments for the remaining affected persons here are still pending due to legal issues and other unavoidable reasons. The CCL unpaid affected persons will receive CCL as soon as they submit required land documents to Deputy Commissioner's office.

DORP is motivating affected persons by personal contacts, community meetings, announcements, leaflet distribution, etc. to resolve CCL unpaid affected persons' problems and receive compensation.

DWASA had submitted a DDR on 4 October 2022 for the part of land under LA case 10/2018-19 in Resettlement Plan Section 3 and part of Resettlement Plan Section 5 to start civil works. DWASA received ADB concurrence to this DDR on 23 January 2023. Another DDR had been submitted to ADB on 28-12-2022 to get concurrence to start civil works in RAJUK's Major Road-5ka2 Project (3.4 km). This DDR also received ADB concurrence on 26 April 2023. The contractors are carrying out civil works in all sections except 280m of land under Resettlement Plan Section 6. Though the Deputy Commissioner handed over this portion of land to DWASA also, but PMU is waiting to hand over this land to contractor since the affected persons have not received CCL yet.

All affected persons who received CCL also received full resettlement assistance which they are entitled to from DWASA. Affected persons who are yet to receive CCL will also receive other applicable resettlement assistance according to the entitlement matrix. PMU has deposited full estimated CCL amount into the Deputy Commissioner's Public Account of Republic and estimated compensation for payment of resettlement assistance in a dedicated account. The required amount for paying resettlement assistance will be kept intact until the last affected person has been paid CCL.

No vulnerable affected persons have been paid during this reporting period. No LIRP training was imparted to the affected persons in this reporting period.

In addition to regular personal contact, in this reporting period, DORP has conducted 102 community meetings. The total number of participants were 1325 (518 male and 807 female). Key discussion points were: wrong issuance of CCL notice, papers required in receiving compensation from Deputy Commissioner's office and additional payment/other resettlement benefits from DWASA, Affected Persons' entitlements payment for loss of business, trees, etc., determination of the present market value of lands, payment for affected persons with land disputes, livelihood training, unpaid CCL issues, job opportunities in project's civil works, seeking support from the affected persons in ongoing/ensuing project construction works, etc.

One (1) Grievance Redress Committee (GRC) meeting has been held during this reporting period for Resettlement Plan Section 3. In this meeting, 1 case from 1 affected person was heard regarding grave shifting compensation. The GRC advised that the affected person be paid, and the payment has been made.

Major tasks that need to be accomplished over the next SSMR period:

- (i) Following up with Deputy Commissioner's office to facilitate remaining unpaid CCL payment in all the Sections, except Section 4.

² The project titled Widening of Madani Avenue to Balu River (Major Road-5) and Road Construction (Phase 1) from Balu River to Shitalakshya River (Major Road-5ka) is being implemented by the Rajdhani Unnayan Kortripakshya (RAJUK). According to a draft agreement between Dhaka WASA and RAJUK, decision was taken that Dhaka WASA will use 3.4 km of alignment of the RAJUK's project portion of Construction of Road from Balu River to Shitalakshya River (Major Road-5ka) (Phase 1) for laying the pipeline of treated water (Package-2).

ABBREVIATIONS

ADB	Asian Development Bank
AFD	Agence Française de Développement
BDT	Bangladeshi Taka
CCGP	Cabinet Committee for Government Purchase
CLAC	Central Land Acquisition Committee
COVID-19	Coronavirus disease of 2019
DBO	Design-Build-Operate or Design-Build-Operation
DLAC	District Land Acquisition Committee
DORP	Development Organization for the Rural Poor
DDR	Due Diligence Record
DESWSP	Dhaka Environmentally Sustainable Water Supply Project
DWASA	Dhaka Water Supply and Sewerage Authority
EIA	Environmental Impact Assessment
EIB	European Investment Bank
FGD	Focus Group Discussion
GRC	Grievance Redresses Committee
GRM	Grievance Redresses Mechanism
JVC	Joint Verification Committee
JVS	Joint Verification Survey
MLGRDC	Ministry of Local Government Rural Development Cooperatives
MDSC	Management, Design and Supervision Consultant
MLD	Millions of Litres Per Day
MML	Mott MacDonald Limited
MODS	Maintenance, Operations and Distribution Services
MoU	Memorandum of Understanding
MSC	Management and Supervision Consultant
PMC	Project Management Consultant
PPMS	Project Performance Management System
PMU	Project Management Unit
PVAC	Property Valuation Advisory Committee
RAC	Resettlement Advisory Committee
RWP	Raw Water Pipeline
SIU	Safeguard Implementation Unit
SPS	Safeguard Policy Statement
ToR	Terms of Reference
WIA	Water Intake Area
WTP	Water Treatment Plant

CONTENTS

EXECUTIVE SUMMARY	1
ABBREVIATIONS	4
CONTENTS	5
TABLES	7
FIGURES	7
1. PREAMBLE	9
2. BACKGROUND OF THE REPORT AND PROJECT DESCRIPTION	10
2.1 BACKGROUND (/CONTEXT) OF THE REPORT	10
2.2 DESWSP COMPONENTS.....	11
2.3 PROJECT DESCRIPTION	12
2.3.1 <i>Output 1: New surface water supply system developed.</i>	12
2.3.2 <i>Project Cost</i>	14
2.3.3 <i>Project Completion Targets</i>	14
2.3.4 <i>Output 1 Implementation Progress</i>	14
2.4 SOCIAL SAFEGUARDS CATEGORIZATION OF THE PROJECT	15
2.4.1 <i>Involuntary Resettlement Categorization</i>	15
2.4.2 <i>Indigenous People’s Categorization</i>	15
3. SCOPE OF THE SOCIAL SAFEGUARDS IMPACTS BY THE PROJECT	16
3.1 SUMMARY OF IDENTIFIED IMPACTS AND MITIGATION	19
3.1.1 <i>Resettlement Plan Update and Public Consultation</i>	22
4. COMPENSATION AND REHABILITATION	23
4.1 FRAMEWORK, POLICIES, AND ACTS FOR RESETTLEMENT PLAN IMPLEMENTATION ..	23
4.2 PROCESS OF RESETTLEMENT PLAN IMPLEMENTATION.....	23
4.3 PROGRESS OF RESETTLEMENT PLAN IMPLEMENTATION.....	25
4.3.1 <i>Updating Resettlement Plans</i>	25
4.3.2 <i>Progress in Lands Acquisition and handing over to Contractor</i>	27
4.3.3 <i>Progress in Payment of CCL and Other Resettlement Assistances</i>	29
4.3.4 <i>Progress in Livelihood and Income Restoration Program</i>	32
5. PUBLIC PARTICIPATION AND CONSULTATION	37
5.1 PUBLIC CONSULTATION	37
5.1.1 <i>Public Participation and Information Dissemination on Key Aspects</i>	37
5.1.2 <i>Gender mainstreaming</i>	39
5.2 DISCLOSURE OF RESETTLEMENT PLANS.....	40
6. GRIEVANCE REDRESS MECHANISM (GRM)	41
6.1 GRIEVANCE REDRESS COMMITTEES (GRC).....	42
6.2 SCOPE AND JURISDICTION OF GRC.....	42
7. INSTITUTIONAL ARRANGEMENT	44
7.1 PROJECT IMPLEMENTATION PARTNERS	44
8. MONITORING RESULTS – FINDINGS	47
9. COMPLIANCE STATUS	50
9.1 COMPLIANCE TO RELEVANT LOAN COVENANT	50
10. FOLLOW UP ACTIONS, RECOMMENDATIONS, AND DISCLOSURE	53

11. APPENDIX	54
11.1 APPENDIX: LIST OF AFFECTED PERSONS PAID DURING JANUARY TO JUNE 2023 IN SECTION 2	54
11.2 APPENDIX: LIST OF AFFECTED PERSONS PAID DURING JANUARY TO JUNE 2023 IN SECTION 3	56
11.3 APPENDIX: LIST OF AFFECTED PERSONS PAID DURING JANUARY TO JUNE 2023 IN SECTION 5	66
11.4 APPENDIX: LIST OF AFFECTED PERSONS PAID DURING JANUARY TO JUNE 2023 IN SECTION 6	68
11.5 APPENDIX: MONITORING RESULT OF CCL UNPAID AFFECTED PERSONS IN SECTION 1 AND 2	71
11.6 APPENDIX: MONITORING RESULT OF CCL UNPAID AFFECTED PERSONS IN PART OF SECTION 3 (LA CASE 5/2018-19)	80
11.7 APPENDIX: MONITORING RESULT OF CCL UNPAID AFFECTED PERSONS IN PART OF SECTION 3 AND PART OF SECTION5 (LA CASE 10/2018-19)	82
11.8 APPENDIX: MICROFINANCE ACCESS BY TRAINED AFFECTED PERSONS IN SECTION 1	88
11.9 APPENDIX: MICROFINANCE ACCESS BY TRAINED AFFECTED PERSONS IN SECTION 2	91
11.10 APPENDIX: MICROFINANCE ACCESS BY TRAINED AFFECTED PERSONS IN SECTION 4	99
11.11 APPENDIX: SUMMARY OF COMMUNITY MEETINGS HELD DURING JANUARY TO JUNE 2023	101
11.12 APPENDIX: MINUTES OF 13TH GRC MEETING IN BANGLA (SIGNED).....	109
11.13 APPENDIX: MINUTES OF 13TH GRC MEETING IN ENGLISH	112

TABLES

Table 2.1: Funding of project	14
Table 2.2: Project completion target dates	14
Table 3.1: Land Acquisition and Resettlement Impacts	19
Table 3.2: Length of Pipelines in each Section of Resettlement Plan and DDR	21
Table 4.1: Section-wise Resettlement Plan Implementation Status	25
Table 4.2: Availability of Work Front	28
Table 4.3: Progress of CCL payment and other assistances	30
Table 4.4.1: Distribution of Eligible (received compensation+ specially advised) Affected Persons who are Vulnerable and incur significant loss of Agriculture-based Livelihood	32
Table 4.5: Distribution of Affected Persons who received Training and Engaged in IGA	34
Table 4.6: Distribution of Affected Persons who received Training and Linked with NGOs/microfinance institutions for financial involvement.	35
Table 4.7: Distribution of Vulnerable Affected Persons	35
Table 8.1: Semi-Annual Social Safeguards Progress Checklist for P1, P2, P3.1, and P3.2	48
Table 9.1: Progress in training and income generation engagement	50
Table 10.1: Follow up actions, recommendations, and disclosure	53

FIGURES

Figure 2.1: Source- Surface water treatment and transmission	11
Figure 2.2: Services – distribution network strengthened	11
Figure 2.3: 3D view of Water Treatment plant	12
Figure 2.4: 3D view of Meghna River Intake	12
Figure 2.5: 3D view of a River Crossing	13
Figure 2.6: 3D view of a large diameter Pipeline	13
Figure 3.1: Location Map of Pipeline Route for Packages 1, 2, 3.1, and 3.2	18
Figure 4.1: Process of Resettlement Plan Implementation and site handover to Contractor	23
Figure 4.2 : Progress on Land Acquisition	28
Figure 4.3: Female participation in LIRP training	36
Figure 5.1: Trend of female participation in the social consultation meetings during the immediate last 12 months	39
Figure 5.2: Trend of female participation in the social consultation meetings during this reporting period	40
Figure 6.1: Grievance Redress Mechanism Flow Chart	41
Figure 7.1: Social Safeguards Plans Implementation partners relationship and information flow	44

1. Preamble

1. The Asian Development Bank approved a loan amounting to \$250 million equivalent from its Special Funds resources for Dhaka Environmentally Sustainable Water Supply Project on 22 October 2013. Subsequently, Loan Agreements between the Government of Bangladesh and each of Asian Development Bank, Agence Française de Développement, and European Investment Bank were signed on 24 April 2014, 29 January 2015, and 30 June 2014, respectively.

2. Dhaka Water Supply and Sewerage Authority, on behalf of the Government of Bangladesh, is the executing Authority of the project.

3. DWASA presents this 16th Semi-annual Social Safeguards Monitoring Report (January – June 2023) in compliance with the requirement of paragraph 91 of item B. Monitoring under Section IX. Performance Monitoring, Evaluation, Reporting, and Communication of the Project Administration Manual (PAM) (December 2020).

4. The contents of this report, as outlined in Appendix 13 of the PAM, are:

- (i) Executive Summary
- (ii) Background of the Report and Project Description
- (iii) Scope of Impacts
- (iv) Compensation and Rehabilitation
- (v) Public participation and consultation
- (vi) Grievance Redress Mechanism (GRM)
- (vii) Institutional Arrangement
- (viii) Monitoring Results – Findings
- (ix) Compliance Status

2. Background of the Report and Project Description

2.1 Background /context of the Report

5. According to the Project Administration Manual (refer to Appendix C - copy of Appendix 13 of the PAM), the Project Director has to submit to ADB, a semi-annual report on the status of implementation of safeguard plans and progress made towards the desired outcomes of the project in compliance with the ADB Safeguard Policy Statement (2009).

6. PMU has prepared this report as a deliverable to ADB. MDSC assisted PMU in compliance with the Clause no. 18 (iii) of the Terms of Reference for the Management, Design and Supervision Consultant (MDSC) - Mott MacDonald to assist the Project Director in reporting to ADB on the status of implementation of 'Social Safeguard Plans', which are termed as 'Resettlement Plans' for DESWSP.

2.2 DESWSP Components

7. The DESWSP comprises,
- (i) (Source/Intake) development, water treatment, and distribution pipelines, comprising: 1,050 MLD river intake with the pumping capacity 525 MLD, 500 MLD water treatment plant (phase -1), 22 km raw water pipeline and 14 km treated water transmission pipeline, 24 km primary distribution pipelines, and 42 km of feeder pipelines to northern Dhaka;
 - (ii) (Services) distribution network strengthened, comprising: rehabilitating 376 km of distribution networks and 32,000 household and community connections, and legalization of 3700 households and community connections at MODS Zone – 6;
 - (iii) Construction of at least 1,000 community toilets and bathing chambers with separate units for males/females in low-income communities in Dhaka city (added in 2020).

Figure 2.1: Source- Surface water treatment and transmission


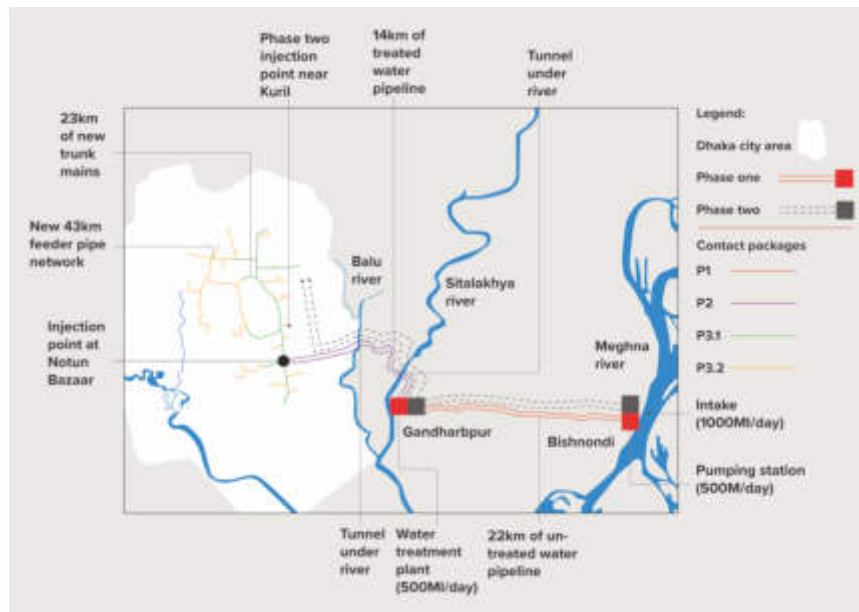


Figure 2.2: Services – distribution network strengthened

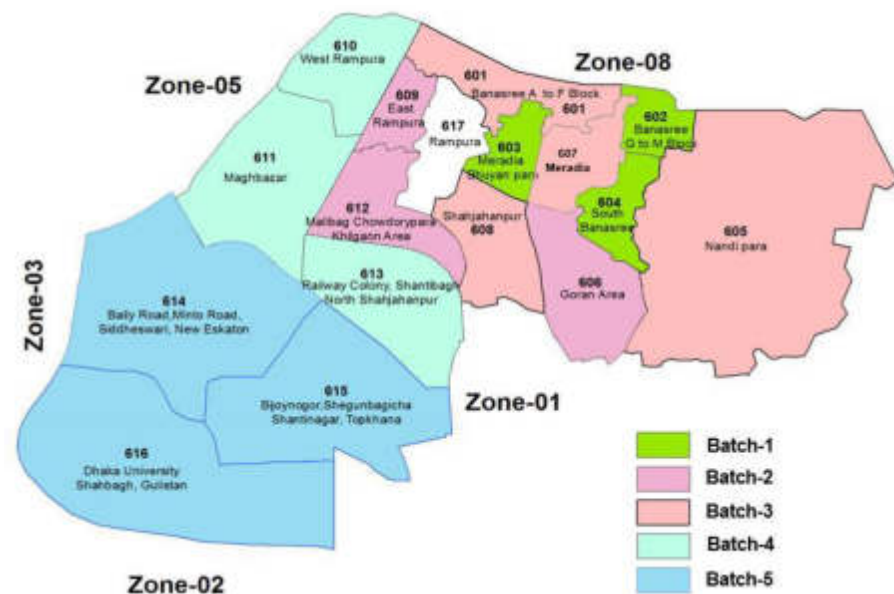

8. This report covers implementation progress of the ‘Social Safeguard Plans; for Output 1: New surface water supply system developed (ref: **Figure 2.1**) out of 4 defined outputs (detailed below) of the DESWSP.

2.3 Project Description

9. The Dhaka Environmentally Sustainable Water Supply Project (DESWSP) has a target impact (Goal) of “Improved access to and quality of sustainable water supply services in Dhaka (City)”.

10. The Project’s Design Monitoring Framework defined an outcome of “More reliable and improved security of water supply and sanitation in Dhaka” resulting from the project achieving the targeted ‘impact’. The DMF defined the following additional outputs to achieve the ‘outcome’:

- Output 1: New surface water supply system developed (Figure 2.1);
- Output 2: Distribution network strengthened (Figure 2.2);
- Output 3: Project management and administration adequately supported; and
- Output 4: Empowerment of women and vulnerable groups supported.

11. Output 4 was added with the proposal for additional funding in 2020. The loan has been effective on 08 April 2022. Implementation has started on January 2023.

2.3.1 Output 1: New surface water supply system developed.

12. The report covers, for the components (indicators) of the ‘new surface water supply system developed’ are described hereunder.

Package 1: River intake, raw water pipeline, and Gandharbpur treatment plant

- 1050 MLD river intake in the Meghna River at Bishnandi, Araihasar Upazila, with a 525MLD raw water pumping station, stand-by power supply station, workshops, offices, and accommodation for DWASA staff.

Figure 2.3: 3D view of Water Treatment plant



Figure 2.4: 3D view of Meghna River Intake



- 22 km raw water transmission pipeline (twin 1600 mm pipes sized for 500MLD) through rural areas with an access road beside the river intake to the water treatment plant (Figure 2.1). and
- 500 MLD surface water treatment plant (WTP) at Gandharbpur, Rupganj Upazila, with storage reservoir, treated water pumping station, standby power supply, workshop, chemical storage, offices, and accommodation for DWASA staff (Figure 2.1).

Package 2: Treated water transmission pipeline to Dhaka

13. Construction activities of P2 will take 36 months. The construction will include:
- 14 km treated water transmission pipeline (twin 1600 mm pipes) from Gandharbpur WTP to Dhaka (Vatara junction on Madani Avenue, at Natun Bazar near the American Embassy), where it connects to the P3.1 pipeline (Figure 2.1).
 - Two under-river tunnels for the pipeline: one at Murapara - Isakhali under the Sitalakhya river, and one at Beraid under the Balu River (Figure 2.1)

Figure 2.5: 3D view of a River Crossing

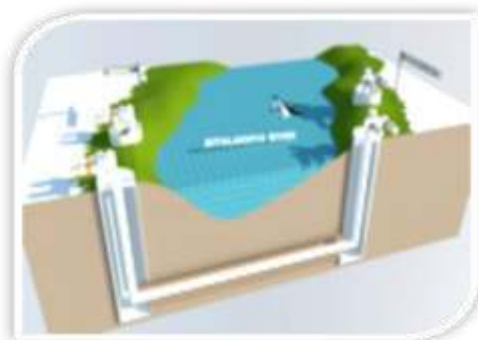


Figure 2.6: 3D view of a large diameter Pipeline



Package 3.1: Primary distribution pipelines in Dhaka

14. Construction activities of P3.1 will take 36 months. The construction will include:
15. 24 km of large diameter pipes of 0.8m to 1.6m diameter, all under major Dhaka highways to transfer the potable water to the P3.2 feeder pipelines (Figure 2.1).

Package 3.2: Feeder pipelines distribution in Dhaka

16. Construction activities of P3.2 will take 30 months. The construction will include: 42 km of feeder pipes from 350 to 800mm diameter, all under Dhaka roads, to deliver water to the District Metering Areas (DMAs) that feed individual water supply zones of Dhaka City (Figure 2.1).

2.3.2 Project Cost

17. The overall cost including additional funding of the DESWSP stated in the 1st December 2020 Aide Memoire is US\$ 1 104.9 million as summarized in Table 2.1. Additional funding is still being finalized between GoB and Financiers.

Table 2.1: Funding of project

Source of Funding	Original	Additional	Total
ADB	250.00	140.00	390.00
<i>Regular loan (OCR)</i>	-	85.00	85.00
<i>Concessional Loan (OCR)</i>	250.00	50.00	300.00
<i>Special Funds Resources (AFD)</i>	-	5.00	5.00
AFD	64.00	140.90	204.90
EIB	136.00	-	136.00
Government	224.90	149.10	374.00
Total	674.90	430.00	1 104.90

2.3.3 Project Completion Targets

18. The revised project completion target, as agreed during November 2020 ADB Mission, is September 2025. The target dates to achieve the project outcome and outputs are given below.

Table 2.2: Project completion target dates

Outcome: More reliable and improved security of water supply and sanitation in Dhaka	December 2025
Output 1: New surface water supply system developed	December 2024
Output 2: Distribution network strengthened	Completed
Output 3: Project management and administration adequately supported	December 2024
Output 4: Empowerment of women and vulnerable groups supported	December 2023

2.3.4 Output 1 Implementation Progress

19. At the end of the reporting period, the engineering works progress of various components of the Output 1: New surface water supply system developed are as below:

Package 1: River intake, raw water pipeline, and Gandharbpur treatment plant

Construction Component	Progress	Time elapsed ³	Comments
Construction (Overall)	87.14%	85.25%	Ahead of schedule
Intake (River)	72.63%	93.40%	Behind schedule
Water Treatment Plant	86.02%	93.33%	Behind schedule
Raw Water Pipeline	66.28%	76.26%	Behind schedule

Source: MDSC QPR Q2 2023

Package 2: Treated water transmission pipeline to Dhaka

Construction Component	Progress	Time elapsed	Comments
Pipeline Construction (Section-C)	40.13%	42.46%	Behind schedule
Pipeline Construction (Section-B)	11.89	29.11%	Behind schedule

³As per April 2021 revised schedule of works

Pipeline Construction (Section-A)	45.11%	52.23%	Behind schedule
-----------------------------------	--------	--------	-----------------

Source: MDSC QPR Q2 2023

Package 3.1: Primary distribution pipelines in Dhaka

Project Stage	Signing of Contract	Commencement	March 2023 (scheduled) Work yet to commence
Progress	Contract Signed on 9 September 2021		

Source: MDSC QPR Q2 2023

Package 3.2: Feeder pipelines distribution in Dhaka

Project Stage	Signing of Contract	Commencement	March 2023(scheduled) Work yet to commence
Progress	Contract signed on 28 December 2022		

Source: MDSC QPR Q2 2023

2.4 Social Safeguards Categorization of the Project

2.4.1 Involuntary Resettlement Categorization

20. Considering the extent of the significance of involuntary resettlement impacts, ADB has classified projects into four categories: A, B, C, and FI. The DESWSP falls under Category A as there would be 200 or more persons physically displaced from home and/or lose 10% or more of their productive and/or income-generating assets.

2.4.2 Indigenous People's Categorization

21. The DESWSP falls under Indigenous People's Category C as there is no Indigenous People's household has been found during the socioeconomic household surveys.

3. Scope of the Social Safeguards Impacts by the Project

22. A single Resettlement Plan for the project was prepared in 2013 covering the then identified three packages P1: River intake, raw water pipeline, and Gandharbpur water treatment plant, P2: Treated water transmission pipeline to Dhaka, and P3: Distribution Reinforcement Pipeline. At a later stage, during detailed design, package P3 was divided into two, namely, P3.1: Primary distribution pipelines in Dhaka and P3.2: Feeder pipelines distribution in Dhaka.

23. The Resettlement Plan identified that the project has major impacts on both private and public lands, and other assets such as structures, livelihoods, crops, and trees.

24. A single Resettlement Plan for the DESWSP, covering areas required for Output 1 (P1, P2, P3) and ICB 2.7 under Output 2, was prepared in 2013, which identified major impacts on lands, the scope of land acquisition, and other resettlement impacts based on the design of the project. The areas of P1 and P2 were subsequently divided into 6 sections to facilitate the Resettlement Plan implementation. The packages P1 and P2 require a total of 310.71 acres of land where a total of 183.15 acres of privately owned lands and 46.03 acres of public-owned except water treatment plant. DWASA owns the required land (81.53 acres) for the water treatment plant.

25. P3.1 and P3.2 run through the developed lands (roads) of Dhaka North City Corporation. No land acquisition is required for these packages. Necessary permission to work on the road alignment would need to be sought from the City Corporations.

26. The Due Diligence Report (DDR) for P3.1 has been approved and disclosed by ADB in February 2020 and also disclosed on DWASA website. PMU, with the assistance of MDSC prepared Resettlement Plan for P3.2. Temporary impacts (temporary income losses to shop owners/vendors and employees) were identified due to laying of the feeder pipelines for an estimated period of 14 days in one of the pipe routes. ADB has provided no objection on 15 May 2020. This Resettlement Plan has been prepared during loan processing for additional financing.

27. According to the design for the implementation of P1 and P2, water intake is located on private lands that needed land acquisition; the Water treatment plant is situated on DWASA's own lands (81.50 acres). Some squatters were identified on this land. All the squatters have been compensated. DWASA has received permission from the Bangladesh Water Development Board (BWDB) to use the required 24.8750 acres of land of the alignment. DWASA has also received permission from RAJUK⁴ to use 5.5 km land for installation of treated water pipelines. Bangladesh Inland Water Transport Authority (BIWTA) has renewed the authorization letter in favor of DWASA to use the for shaft locations in Shitalaksya and Balu River. The remaining required public lands require the acquisition and/or securing permissions from various government and semi-government/autonomous organizations.

28. To facilitate easy management and implementation of Resettlement Plans, the whole area, required by the packages P1 and P2, is divided into 6 sections as detailed below:

- Resettlement Plan Section 1: Water Intake Area
- Resettlement Plan Section 2: Intake to Baliapara (Raw Water Pipeline)
- Resettlement Plan Section 3: Darikandi Chak to Murapara via Gandharbpur WTP (Part of Raw Water Pipeline+part of Treated Water Pipeline)
- Resettlement Plan Section 4: Water Treatment Plant (WTP) at Gandharbpur


⁴ Rajdhani Unnayan Kartripakkha, or RAJUK – the Capital Development Authority of the Government of Bangladesh. It is a Bangladeshi public agency responsible for coordinating urban development in Dhaka, Bangladesh.

- Resettlement Plan Section 5: Rugganj (Shitalkhya West bank) to Balu River (East bank) (Treated Water Pipeline) and
- Resettlement Plan Section 6: West Bank of Balu River to Vatara along Madani Avenue up to Baridhara⁵ (Treated Water Pipeline).

⁵ Resettlement Plan mentioned at Vatara but later, during detailed designing, the location has been identified as Balu River (West bank) to the junction of Pragati Sarani and Madani Avenue at Natun Bazar. Location is same. Resettlement impact is not different. Engineers termed this section as “Balu River (West bank) to the junction of Pragati Sarani and Madani Avenue at Natun Bazar” instead of “West Bank of Balu River to Vatara along Madani Avenue up to Baridhara”.

29. The spread of each Resettlement Plan section is shown in **Figure 3.1** below.

Figure 3.1: Location Map of Pipeline Route for Packages 1, 2, 3.1, and 3.2

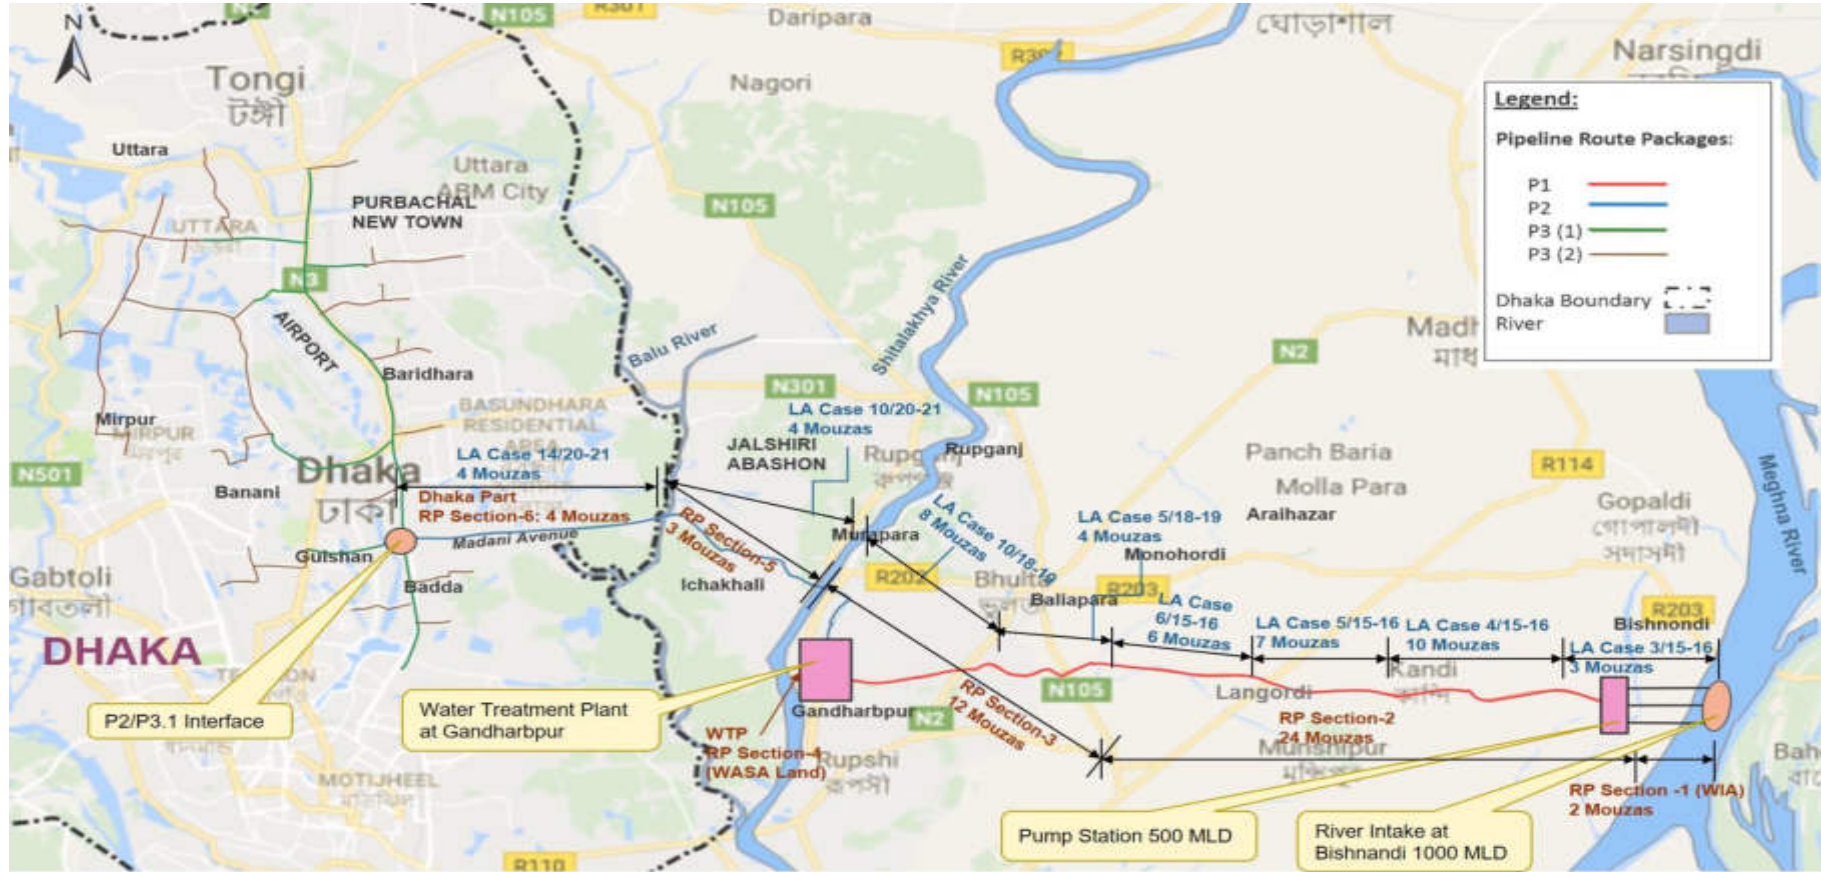

Source: Prepared by PMU

3.1 Summary of identified Impacts and Mitigation

30. The below table presents a summary of the land requirements with areas and types of impacts identified so far within the areas of packages P1 and P2.

Table 3.1: Land Acquisition and Resettlement Impacts

RP Section	Locations	Land Requirement for Acquisition (in acre)			Structure and other impacts	Comments / Status
		Total	Public	Private		
1 (P1)	Water Intake Area (WIA)	21.37	7.15	14.22	Agriculture and fish livelihood	According to the resettlement plan, there are 87 affected households. However, 232 ⁶ affected persons have been identified by the Deputy Commissioner's office and by the executing agency (DWASA) including non-titleholders. These numbers may vary after the completion of compensation payment (CCL and other resettlement assistances). Three (3) households significantly lose their agriculture-based livelihood. Compensation was paid to 231 affected persons. The remaining 1 person submitted papers to Deputy Commissioner's office for getting CCL.
2 (P1)	Intake to Balia Para	109.32	4.59	104.73	Agriculture, livelihood, and structure	According to the resettlement plan, there are 1165 affected households. 1620 ⁷ affected persons have been identified by the Deputy Commissioner's office and by the executing agency (DWASA) including tenants and wage laborers. These numbers may vary after the completion of all payments (CCL and other resettlement assistances). There were 290 structures also affected. All of the structures are relocated. 157 households significantly lost their agriculture-based livelihood. In total 1530 affected persons received CCL and other resettlement assistance. The remaining 90 ⁸ affected persons have legal issues.
3 (P1+P2)	Darikandi Chak (start of Rupganj) to Murapara via Gandharbur WTP	62.74	25.04	37.70	Agriculture, structure and livelihood	According to resettlement plan 434 are affected households. Approximately 610 ⁹ affected persons have been estimated by the Deputy Commissioner's office. These numbers may vary after the completion of all payments (CCL and other

⁶ In total 232 (223 titled+9 non-titled) affected persons.

⁷ In total 1620 (1547 titled+73 non-titled affected persons of which 1530 received payment. Numbers of non-title affected persons have been corrected in this report. Total numbers of non-title affected persons are 79 (tenant 13+wage labour 52+standing crops 10+irrigation pump 4) but total number has been counted as 73 APs because out of these 79 APs, 6 APs are same persons business tenants+wage employees. Double counting has been avoided. 3 affected persons were paid before the reporting period, but data entry has been done during this reporting period.

⁸ There were 158 CCL unpaid affected persons reported. Out of them 68 affected persons received CCL.

⁹ The Deputy Commissioner has identified 69 more affected persons and paid CCL.

RP Section	Locations	Land Requirement for Acquisition (in acre)			Structure and other impacts	Comments / Status
		Total	Public	Private		
						resettlement assistances). In addition, 63 non-titleholders affected persons have been identified and compensated. There are 141 structures affected – consisting of 119 residential structures and 22 commercial structures. and all of those are relocated. Out of those 610 affected persons, 519 affected persons received CCL and all 63 non-titled affected persons received resettlement assistances. 20 households significantly lose their agriculture-based livelihood.
4 (P1)	Water Treatment Plant (WTP)	81.53	DWASA land	No private land	Structure, agriculture, and livelihood	This land is DWASA's own land. 260 affected persons have been identified as non-titleholders. It also impacted 60 structures. All affected persons and all structures have been paid for.
5 (P2)	Rupganj (West bank of Sitalakhya river) to Balu River (East bank)	21.52	0.45	21.07	Structure, pond, agriculture, and livelihood	According to the revised resettlement plan, 110 households are affected. However, the Deputy Commissioner identified 54 as affected persons. These numbers may vary after the completion of all payments (CCL and other resettlement assistances). Out of those, 47 affected persons received CCL. In addition, according to the revised Resettlement Plan (for 1.9 km) 31 structures were affected. Out of them, all of those have been paid and relocated. Resettlement plan shows 12 households face significant loss of their agriculture base livelihood.
6 (P2)	Balu river to the junction of Pragati Sharani and Madani Avenue at Natun Bazar	14.23	8.79 [6.5 km (RAJUK road) =7.88 acres + 0.92acres (Public lands)]	5.43	Agriculture, Structures, and livelihood	According to the resettlement plan there are 191 households affected. The Deputy Commissioner's office identified 65 affected persons through 44 notices. These numbers may vary after the completion of all payments (CCL and other resettlement assistances). It also impacts 36 non-titleholder affected persons (29 businesspersons and 7 wage laborers). All of these 36 affected persons have been paid. There are 6 affected structures identified. 4 of those were paid. According to resettlement plan 79 ¹⁰ households are facing significant loss of their agriculture-based livelihood. Out of 6.5 km long pipelines,

¹⁰ According to Resettlement plan, total number was 91. Out of 91, 12 are common in vulnerable category also.

RP Section	Locations	Land Requirement for Acquisition (in acre)			Structure and other impacts	Comments / Status
		Total	Public	Private		
						about 5.5km RAJUK ¹¹ roads are being used for the installation of pipes.
P3.1	Primary Distribution Pipelines	0	0	0	No resettlement impact found	24 km pipelines. Due Diligence Report (DDR) has been approved and disclosed. The pipeline will be laid along roads/land which belong to different organizations such as Dhaka North City Corporation (DNCC), Roads and Highways Department (RHD), Dhaka Cantonment Board (DCB) and Bangladesh Railways (BR). No objection certificates (NOC) will be obtained for use of the land before project implementation.
P3.2	Feeder Pipelines				Temporary impact on livelihood and temporary structures.	42 km pipelines. There are 28 pipeline routes covering 42 km. Involuntary resettlement impacts have been identified in one pipeline route, named Matikata Bazar (other pipeline routes do not have any impact). In this route, there are 95 temporary shop owners/vendors and 113 employees who will be affected due to the laying of the feeder pipelines for an estimated period of 7 days. The entire civil works under this component for the feeder pipeline network are proposed on the land owned by different government organizations, Dhaka North City Corporation (DNCC), Roads and Highway Department (RHD), Dhaka Cantonment Board (DCB), and Bangladesh Railways (BR), etc. No objection certificates (NOC) will be obtained for use of the land before project implementation.
Total land		310.71	127.56	183.15		

Source: PMU provided plot schedule as of June 2020. No change occurred during this reporting period.

31. The section-wise length of the pipelines is given below:

Table 3.2: Length of Pipelines in each Section of Resettlement Plan and DDR

Name of Section	Type of Pipeline	Length
Section 2	Raw Water Pipeline	14.25 km
Section 3	Raw Water Pipeline +Treated Water Pipeline	7.75 km + 2 km
Section 5	Treated Water Pipeline	5 km.
Section 6	Treated Water Pipeline	7 km.
P3.1	Primary Distribution Pipelines	24 km.

¹¹ Rajdhani Unnayan Karttripakkha, or RAJUK – the Capital Development Authority of the Government of Bangladesh. It is a Bangladeshi public agency responsible for coordinating urban development in Dhaka, Bangladesh.

Name of Section	Type of Pipeline	Length
P3.2	Feeder Pipelines	42 km.
Total		102 km.

3.1.1 Resettlement Plan Update and Public Consultation

32. The INGO, DORP under the guidance of MDSC is assisting DWASA in updating the Resettlement Plans and implementation of the resettlement activities for the Resettlement Plan Sections 1 to 6 covering Packages P1 and P2. DORP has updated six (6) draft resettlement plans (1-6). All of the Resettlement Plans received ADB approval.

33. Regular consultations with the affected persons and other stakeholders are being conducted by DORP to ensure that affected persons are fully aware of the project interventions and about their entitlements in case of involuntary land acquisition and resettlement assistances for affected persons (titled and non-titled holders).

34. PMU with the assistance of MDSC has prepared DDR for P3.1 which is approved by ADB and disclosed on ADB and DWASA website. Resettlement Plan has been prepared for P3.2 which received no objection from ADB, which has also been disclosed on ADB and DWASA websites. This will be updated before the start of civil works. The contractors for P3.1 and P 3.2 signed the contract on 9 September 2021 and 28 December 2022 respectively. INGO namely Knowledge Management Consultants Ltd (KMC) is working for the resettlement plan implementation for packages P3.1 and P3.2.

Reporting Period and Frequency of Submission

35. In compliance with the requirement of paragraph 91 of item B. Monitoring under section IX. Performance Monitoring, Evaluation, Reporting, and Communication of the Project Administration Manual (PAM) (December 2020) this Social Safeguards Monitoring Report is due Semi-annually.

36. The submission would cover six months period; January to June and July to December of each year, till the project completion report is prepared.

4. Compensation and Rehabilitation

4.1 Framework, Policies, and Acts for Resettlement Plan Implementation


37. Involuntary resettlement has been addressed based on applicable legal and policy frameworks of the Government of Bangladesh that include Acquisition of Immovable Property Ordinance (ARIPO) of 1982 as well as Acquisition and Requisition of Immovable Property Act (ARIPA) of 2017 and ADB’s Safeguard Policy Statement (2009).

38. Resettlement Plans for Sections 1, 2, and 4 have been updated based on the then ARIPO of 1982 as the land acquisition processes for the sections started before ARIPA, 2017 was enacted. The Act, ARIPA 2017, is applicable for updating and implementing Resettlement Plans for Resettlement Plan Sections 3, 5, and 6. Packages P3.1 and P3.2 will also be following ADB SPS and GoB law.

4.2 Process of Resettlement Plan Implementation

39. The Resettlement Plan implementation, starting from Identification of land details and preparing Land Acquisition proposal by DWASA to handing over the site to contractor post completion of settlement of payments to affected persons, follows a systematic and lengthy process, which may be defined in a 6-staged process as presented below:

Figure 4.1: Process of Resettlement Plan Implementation and site handover to Contractor

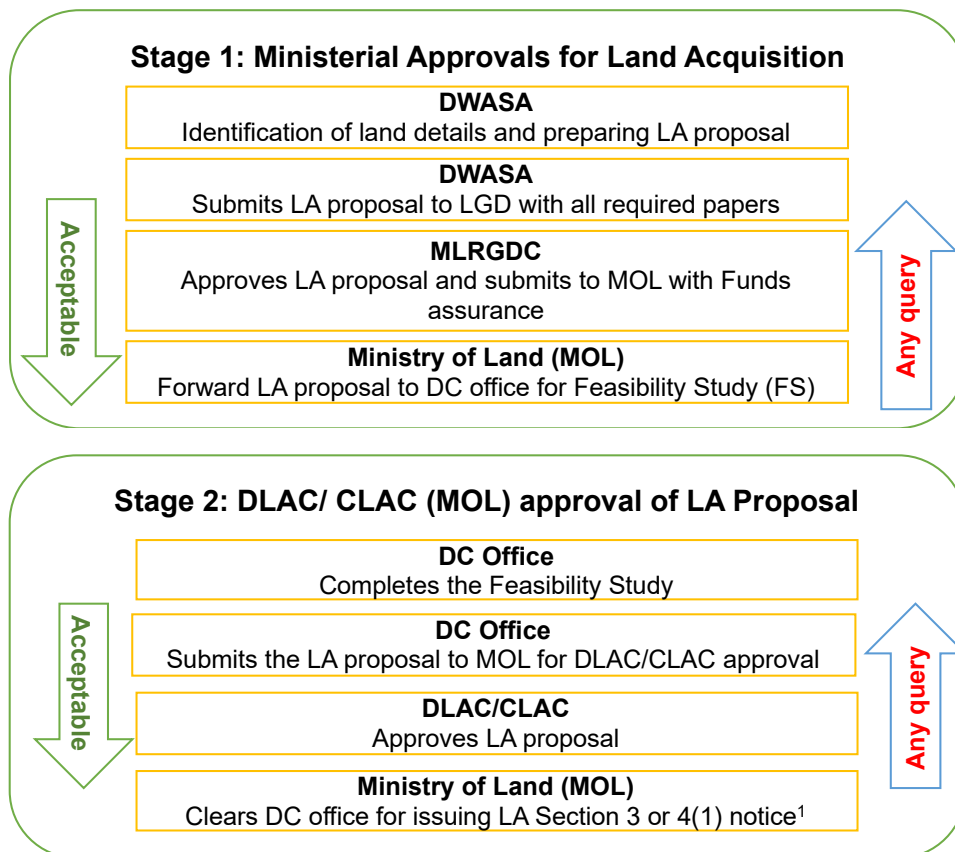

¹ Section 3 in compliance with Acquisition and Requisition of immovable Property Ordinance ARIPO 1982 (applicable to Resettlement Plan for Section 1 and 2) and Section 4(1) in compliance with Acquisition and Requisition of Immovable Property Act (ARIPA), 2017 (applicable to RP Section 3, 5, 6, P3.1 and P3.2). This applies to other Land Acquisition Sections as referred under Stage 3.

Stage 3: Payment of Cash Compensation under Law (CCL)

DC Office (+MOL)

- DC serves notices under Section 3 or 4(1)
 - Joint Verification Survey²
- Final Govt. Approval of LA Cases (if needed)
 - Resolving APs' Objection (Section 5) of any
- Final decision under Section 6 or 7(1) (DC/ DvC/MoL)³
- DC serves Section 6 or 7(1) notices on LA final decision
- DC prepares Award Book and submits Estimate to DWASA
 - DWASA deposits the estimated (CCL) amount to DC
- DC issues Section 7 or 8(3) LA notices to APs (Claim CCL)
 - DC pays CCL to APs under Section 10 or 11
- CCL deemed have been paid (*60 days after Section 10/11 notice*)
 - Resolving APs' Arbitrator under Section 28 or 29 if any

DC Handover Lands to DWASA

²Comprises of Deputy Commissioner's LA offices, PMU, and other relevant government departments and ministries.

³Depends on the size of required lands; Deputy Commissioner's (<50 bighas) or Divisional Commissioner (> 50 bighas).

Stage 4: Payment of Resettlement Benefits (Additional) to APs

INGO

- Collects CCL payment documents from DC Office
- Prepares and distributes AP's Identity Cards
 - Prepares statement of CCL payments
- Prepares Entitlement Cards and Voucher (**After RP is approved**) and submits to PMU

PMU, DWASA

Pays resettlement benefits to APs⁴

⁴Subject to the approval of Resettlement Plan.

Stage 5: RP gets ADB concurrence to start Civil works

PMU, DWASA

Submits updated RP to ADB for 'No Objection' to start work

ADB

Reviews and issues 'No Objection'

Acceptable

Any query

Stage 6: Site Handover to Contractor

PMU handover site to Contractor to start Civil Works

4.3 Progress of Resettlement Plan Implementation

4.3.1 Updating Resettlement Plans

40. ADB approved draft Resettlement Plans for Sections 1, 2, 3, 4, 5 and 6. Resettlement Plan for Section 2 (1st 10 km through 21 priority mouzas and 2nd 4 km through 3 mouzas of raw water pipeline) was updated further with payment status and received ADB concurrence.

41. The section-wise Resettlement Plan implementation status is presented below:

Table 4.1: Section-wise Resettlement Plan Implementation Status

RP Section 1	<i>Water Intake (P1) at Bishnandi, AraihasarUpazila</i>
Status of Draft Resettlement Plan	ADB approved (19 November 2018)
Status of Updated Resettlement Plan	Submitted to ADB ¹ (12 December 2020)
Land handed over by Deputy Commissioner	April 2018
ADB Concurrence to start Civil Works	November 2019
Access to Contractor	100%
Status of Construction	Construction in progress
RP Section 2	<i>Raw Water Pipeline (P1): Water Intake to Baliapara (end of AraihasarUpazila)</i>
Status of Draft Resettlement Plan	ADB approved (4 April 2019)
Status of Updated Resettlement Plan	Received ADB Approval (26 August 2022)
Land handed over by Deputy Commissioner	April 2018
ADB Concurrence to start Civil Works	February 2021 (part, 10 km), February 2022 (part, 4 km)
Access to Contractor	100%
Status of Construction	Construction in progress
RP Section 3	<i>Raw Water Pipeline (P1) and Treated Water Pipeline (P2): Darikandi Chak (start of RupganjUpazila) to Murapara via Gandharbpur WTP</i>
Status of Draft Resettlement Plan	ADB approved (28 November 2019)
Status of Updated Resettlement Plan	DDR for LA Case 5/2018-19 and LA Case 10/2018-19 received ADB approval on 6 September 2022 and .23 January 2023 respectively.
Land handed over by Deputy Commissioner	Deputy Commissioner handed over land.
ADB Concurrence to start Civil Works	Concurrence received for lands under LA Case 5/2018-19 and LA Case 10/2018-19.
Access to Contractor	100%
Status of Construction	Construction is in progress
RP Section 4	<i>Water Treatment Plant (P1) at Gandharbpur</i>
Status of Draft Resettlement Plan	ADB approved (19 November 2018)
Status of Updated Resettlement Plan	Payment has been completed on approved Resettlement Plan
Land handed over by Deputy Commissioner	DWASA's own land
ADB Concurrence to start Civil Works	November 2019
Access to Contractor	100%
Status of Construction	Construction in progress

RP Section 5	<i>Treated Water Pipeline (P2): Rupganj (Shitalkhya West bank) to Balu River (East bank)</i>	
Status of Draft Resettlement Plan	Received approval	¹ This resettlement plan has been revised based on 1.9 km final alignment of DWASA. Remaining 3 km long RAJUK land (Major Road-5ka) is being used by DWASA.
Status of Updated Resettlement Plan	ADB approved ¹ (30 September 2022)	
Land handed over by Deputy Commissioner	Deputy Commissioner handed over land of this section covered by LA case 10/2018-19 (23 August 2022) and LA case 10/2020-21 (2 January 2023).	
ADB Concurrence to start Civil Works	Received ADB concurrence on DDR for LA case 10/2018-19 (23 January 2023) and on DDR regarding RAJUK land under Major Road- 5ka (26 April 2023).	
Access to Contractor	100%	
Status of Construction	Construction is in progress.	
RP Section 6	<i>Treated Water Pipeline (P2): Balu River (West bank) to Pragati Sarani and Madani Avenue junction at Natun Bazar</i>	
Status of Draft Resettlement Plan	RP received approval on 15 November 2021	
Status of Updated Resettlement Plan	Resettlement assistance has been paid to non-title affected persons as per resettlement plan	
Land handed over by Deputy Commissioner	Deputy Commissioner handed over land (01 November 2022)	
ADB Concurrence to start Civil Works	Received concurrence to start the civil works in Madani Avenue (public lands owned by RAJUK) (16 March 2022). PMU will apply for ADB concurrence for starting civil works on 280m private land as payment not completed yet.	
Access to Contractor	Access has been given for 5.5 km public lands owned by RAJUK (84% of the Section) (15 April 2022). Out of 1.0 km. (private lands), 720m has been handed over to the contractor.	
Status of Construction	Construction is in progress	
Package 3.1	<i>Primary distribution pipelines in Dhaka</i>	
Status of Draft Resettlement Plan	Due Diligence Record (DDR) ¹ approved and uploaded on 3 December 2019	¹ No resettlement impact reported.
Status of Updated Resettlement Plan	Will be updated before starting civil works	
Land handed over by Deputy Commissioner	No land acquisition required	
Access to Contractor	Expected in August 2023	
Status of Construction	Contract signed on 9 September 2021	

Package 3.2	Feeder pipelines distribution in Dhaka	
Status of Draft Resettlement Plan	Resettlement Plan approved and uploaded ¹ on 15 May 2020	¹ Out of 28 pipeline routes, 1 route has temporary relocation impact.
Status of Updated Resettlement Plan	Will be updated before starting civil works	
Land handed over by Deputy Commissioner	No land acquisition required	
Access to Contractor	Expected in August 2023	
Status of Construction	Contract Signed on 28 December 2022	


4.3.2 Progress in Lands Acquisition and handing over to Contractor

42. The Deputy Commissioner completed land acquisition process of Package 1 and 2 areas. Compensation payment under P1 and P2 has been completed except for land with legal issues only. CCL and other resettlement assistance payment is ongoing for those affected persons who are yet to prepare required legal land documents to receive CCL. The Deputy Commissioner's office handed over land to DWASA under all Resettlement Plan areas except Resettlement Plan Section 4. Land under Resettlement Plan Section 4 is owned by DWASA. Deputy Commissioner handed over land under LA case 10/2020-21 during this reporting period, on 2 January 2023. Land under this LA Case covers part of Resettlement Plan Section 5. There is no requirement of land acquisition for P3.1 and P3.2 areas as explained earlier.

43. DWASA handed over land to contractor in all Resettlement Plan in all Sections. In Section 1 (Water Intake), Resettlement Plan Section 2 [part of raw water pipeline (14 km)], Resettlement Plan 3 [part of raw water pipeline and part of treated water pipeline), Resettlement Plan Section 4 (WTP), Resettlement Plan Section 5 (treated water pipeline) and in Resettlement Plan Section 6, 6.2km out of 6.5km has been handed over .for civil works.

44. The following **Figure 4.2** shows major stages of land acquisition and percentages of progress under P1 and P2. P3.1 and P3.2 do not require any land acquisition. The graph depicts that;

- The Deputy Commissioner's Office has handed over 100% of required lands of Sections 1, 2, 3, 5 and 6. DWASA owns land of Section 4.
- CCL payment for Section 1 is at 99% completion, for Section 2 is at 94%, for Section 3 is at 85%, for Section 5 is at 87% and for Section 6 is at 82%.
- All affected persons who received CCL also received resettlement assistance as per entitlement matrix.
- Resettlement Plan of all sections under P1 and P2 received ADB approval.
- Resettlement Plan Section 1, Section 2, Section 3, Section 4, Section 5 were cleared by ADB. In Section 6 (RAJUK land), except for 280 m, the rest of the alignment has received ADB concurrence to start of civil works; and
- Sites under Sections 1, 2, 3, 4, 5 and a large part of Section 6 (RAJUK land in Madani Avenue) have been handed over to contractors.

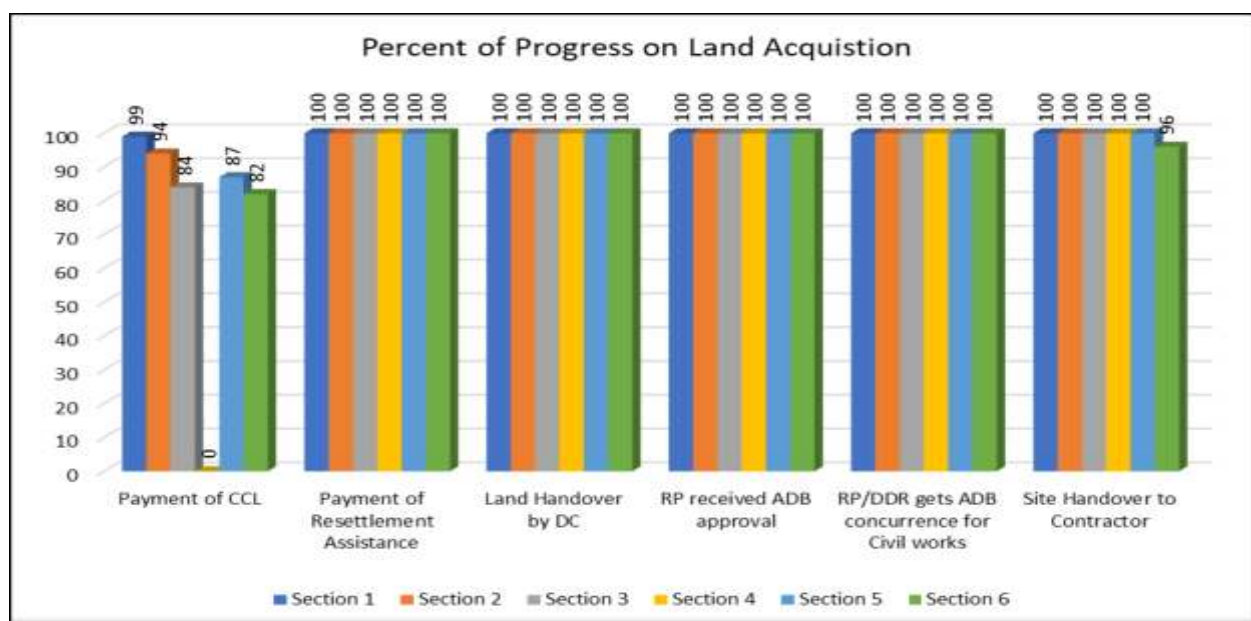Figure 4.2 : Progress on Land Acquisition**Status of Encumbrance-free Land Availability**

45. According to the construction contract conditions, DWASA has to handover the encumbrance-free sites (lands) to contractors. There are 2053 plots in the project alignment in 6 resettlement plan sections. Out of those, compensation for 1630 plots have been fully paid. There are 262 plots with structures. Out of those 260 have been rendered encumbrance-free, after paying full compensation. There are 287 plots with trees, of which 285 have been cleared after paying full compensation.

46. The following table briefly presents the section-wise status of work front availability in Resettlement Plan sections at the end of this reporting period.

Table 4.2: Availability of Work Front

Figures are in numbers of Plots

RP Section	Total Plots	Plots with Structure	Plots with Trees	Plots Fully Paid	Structures Cleared	Trees Cleared	Comments
Section 1	127	None	None	127	n/a	n/a	Construction ongoing
Section 2	899	101	131	700	101	131	Construction ongoing
Section 3	476	103	89	367	103	89	Construction ongoing
Section 4	385	20	29	385	20	29	Construction ongoing
Section 5	100	28	28	41	28	28	Construction ongoing
Section 6	66	10	10	10	8	8	Construction ongoing
Total	2053	262	287	1630	260	285	

Source: DESWSP database

4.3.3 Progress in Payment of CCL and Other Resettlement Assistancess

47. The Deputy Commissioner’s office is paying CCL for Resettlement Plan Section 1, 2, 3, 5 and in Section 6. DWASA is also disbursing resettlement assistance (other benefits/resettlement assistance) efficiently in these sections. Payment has been completed in Resettlement Plan Section 4. In total BDT 4,609,079,821 (USD 42,676,665) has been paid to the total 2733 (2292 titled and 441 non-titled) affected persons. BDT 1,317,259,641 (USD 12,196,849) was paid during this reporting period. List of affected persons who received payment in Section 2, Section 3, Section 5 and Section 6 during this reporting period is attached as **Appendix 11.1, Appendix 11.2, Appendix 11.3 and Appendix 11.4** respectively.

48. Investment allowance has been provided to 114 affected persons in February 2023 who received training in December 2022.

49. The affected persons in Resettlement Plan Sections 2, 3, 5 and 6 who have received compensation for relocating residential structures have built new houses which are better than pre-resettlement ones. This reflects the improvement of housing standards and quality of life of affected persons.

50. The progress so far made in the payment of CCL and other assistances is briefly presented hereunder.

Table 4.3: Progress of CCL payment and other assistances

RP Section 1	<i>Water Intake (P1) at Bishnandi, AraihasarUpozila</i>	
Identified Affected Person	223 + non-titled 9 = 232	<ul style="list-style-type: none"> 9 affected persons claimed ownership over <i>Khas</i> lands and the dispute is not yet settled. 1 affected person remained unpaid due to legal issues. If the above-mentioned 9 affected persons get the ownership, the remaining number would be 1.
Payment of CCL ¹²	222 (99.6%)	
Payment of Top Up ¹³ and other Resettlement Assistance ¹⁴	231 (99.6%)	
CCL remains unpaid	1 (0.4%)	
RP Section 2	<i>Raw Water Pipeline (P1): Water Intake to Baliapara (end of AraihasarUpozila)</i>	
Identified Affected Person	1 547 ¹⁵ + non-titled 73 = 1 620	<ul style="list-style-type: none"> CCL payment remains unpaid for 89 affected persons. PMU has deposited the estimated compensation amount for those affected persons in the Deputy Commissioner's Public Account of Republic and in the dedicated account of DWASA.
Payment of CCL	1 457 (94.2%)	
Payment of Top Up and other Resettlement Assistance	1 530 (94.4%)	
CCL remains unpaid	89 (5.8%)	
RP Section 3	<i>Raw Water Pipeline (P1) and Treated Water Pipeline (P2): DarikandiChak (start of RupganjUpozila) to Murapara via Gandharbpur WTP</i>	
Identified Affected Person	610+63 non-title=673	<ul style="list-style-type: none"> CCL payment remains unpaid for 91 affected persons. PMU has deposited the estimated compensation amount for those affected persons in the Deputy Commissioner's Public Account of Republic and in the dedicated account of DWASA.
Payment of CCL	519 (85.1%)	
Payment of Top-Up and other Resettlement Assistance	582 (86.4%)	
CCL remains unpaid	91 (14.9%)	
RP Section 4	<i>Water Treatment Plant (P1) at Gandharbpur</i>	
Identified Affected Person	260 (Squatters, etc.)	
Payment of CCL	N/A	
Payment of Resettlement Assistance	260 (100%); completed	
Payment for CPR	The graveyard committee paid 100%	

¹²The District Commissioner (DC) pays Cash Compensation under Law (CCL) for land acquired and other affected immovable properties on behalf of the Government of Bangladesh according to Acquisition and Requisition of Immovable Property Ordinance (ARIPO), 1982 for Resettlement Plan Section 1, 2 and 4 and Acquisition and Requisition of Immovable Property Act (ARIPA), 2017 for Resettlement Plan Section 3, 5 and 6.

¹³This is the difference between CCL and current market value (CMV), if any, paid to the Affected Persons in compliance with the ADB Safeguard Policy Statement, 2009, which is determined by the Property Valuation Advisory committee (PVAC) and is paid by DWASA.

¹⁴This is the payable amount to affected persons which is a compliance with ADB's SPS (Safeguard Policy Statement). Titleholders affected persons receive this compensation in addition to applicable Top-up. Non-Titleholders (who are displaced due to the acquisition of the land, e.g., squatters, informal settlers, crops sharers, vulnerable, etc.) receive this compensation for their non-land assets. DWASA pays the amount according to the Resettlement Plan's entitlement matrix.

¹⁵Total number of non-title affected persons is 73. The previous SSMR (July-December 2022) mentioned the number as 70. Though 3 affected persons were paid before that reporting period, but data entries have been done during this reporting period. Numbers of non-titled affected persons have been corrected in this report. Total numbers of non-title affected persons are 79 (tenant 13+wage labour 52+standing crops 10+irrigation pump 4) but total number has been counted as 73 affected persons because out of these 79 affected persons, 6 affected persons have qualified for compensation for two types of losses such as business tenants and wage employees both. One identity card to each of these 6 affected persons has been given though they have qualified for multiple losses. To avoid double counting, the total number has been considered as 73 though they have been paid for both the losses.

RP Section 5	<i>Treated Water Pipeline (P2): Rupgonj (Shitalkhya West bank) to Balu River (East bank)</i>	
Identified Affected Person	54+0 non-title=54	
Payment of CCL	47 (87.0%)	<ul style="list-style-type: none"> • CCL payment remains unpaid for 7 affected persons. PMU has deposited the estimated compensation amount for those affected persons in the Deputy Commissioner's Public Account of Republic and in the dedicated account of DWASA
Payment of Top Up and other Resettlement Assistance	47 (87.0%)	
CCL remains unpaid	7 (13.0%)	
RP Section 6	<i>Treated Water Pipeline (P2): Balu River (West bank) to Pragati Sarani and Madani Avenue junction at Natun Bazar</i>	
Identified Affected Person	65 ¹⁶ +36 non-title=101	<ul style="list-style-type: none"> • CCL payment remains unpaid for 18 affected persons. PMU has deposited the estimated compensation amount for those affected persons in the Deputy Commissioner's Public Account of Republic and in the dedicated account of DWASA.
Payment of CCL	47 (72.3%)	
Payment of Top-Up and other Resettlement Assistance	83 (82.2%)	
CCL remains unpaid	18 (27.7%)	

Payment of Affected Person with legal issues

51. As mentioned above, 199 affected persons have not yet received CCL in Resettlement Plan Sections 1, 2, 3, 5 and 6. DWASA deposited the required claimable amount of compensation to Deputy Commissioner's office for CCL payments and other estimated compensation amount as per ADB SPS in DWASA's escrow/dedicated account. Initially, during the preparation of Due Diligence Report it was 381 affected persons. During the last reporting period it was 289. PMU follows up and monitors with the Deputy Commissioner's office to ensure due payment to the affected persons. As a result, the number of CCL unpaid affected persons has been reduced.

52. Out of 199 CCL unpaid affected persons, 79 have submitted their necessary papers to the Deputy Commissioner's office, 50 has land related ownership conflict and ongoing court case, 25 have mutation problem, 12 are not interested to receive CCL due to small quantity of acquired land. The remaining have various reasons such as vested property, improper land classification, expatriate affected persons etc. INGO sends monthly monitoring report to PMU with the update on the status of CCL payments for those who are yet to receive compensation. Copy of the reports of June 2023 is attached as **Appendix 11.5** for Section 1 and 2, **Appendix 11.6** for part of Section 3 (LA Case 5/2018-19) and **Appendix 11.7** for part of Section 3 and part of Section 5 (LA Case 10/2018-19).

53. It will take time for the affected persons who have not received compensation payment due to their legal and other unavoidable issues to resolve their issues.. Considering project duration, PMU submitted a Due Diligence Report (DDR) to ADB and sought concurrence from ADB to start civil works in the land under part of Resettlement Plan 3 and Resettlement Plan 5 (Land under LA case 10/2018-19 and RAJUK's Major Road-5ka). ADB approved both the DDRs on 23 January 2023 and 26 April 2023.

54. The deposited CCL money will remain intact till the last person receives CCL. On receipt of CCL, affected persons will contact the INGO or DWASA designated persons (in case of absence of NGO) for getting the top-up and other resettlement assistance. This account will remain active and operational with the requisite balance due for the affected persons till the last unpaid affected person is paid, even if project activities are complete.

¹⁶Deputy Commissioner's office distributed LA notice under 8(3) (ka) to 65 affected persons against LA case 14/2020-21.

4.3.4 Progress in Livelihood and Income Restoration Program

55. The Project entitlement matrix allows for livelihood training to the affected persons who are vulnerable and who will lose equal to or more than 50 percent of their land. Since it is resettlement assistance and does not contradict the GoB law, the same has been given to those losing more than 10 percent of their (CCL unpaid affected persons in Resettlement Plan Section 2) agricultural livelihood losses to ensure ADB's SPS compliance.

Table 4.4: Numbers of Affected Persons who are Vulnerable and significantly lost Agriculture-based livelihood according to Resettlement Plan

RP Section	According to Resettlement Plan			Compensation Paid ¹⁷		
	Nos. of Vulnerable Households	Nos. of Significant Loss Households	Total	Nos. of Vulnerable Households	Nos. of Significant Loss Households	Total
Section 1	49	23	72	49	03	52
Section 2	271	121	392	245	157	402
Section 3	74	20	94	36	0	36
Section 4	104	0	104	89	0	89
Section 5	29	12 ¹⁸	40	05	0	05
Section 6	24	91 ¹⁹	103	0	0	0
Total	551	254	805	424	160	584

56. According to all approved Resettlement Plan sections (1-6) 805 affected persons have been identified who are vulnerable and/or those who incur significant loss of agriculture-based livelihood. Out of these 805, 551 are vulnerable and the remaining 254 are in the category of full loss of agriculture-based livelihood.

57. Vulnerable compensation payment has been given in five Resettlement Plan Sections (1, 2, 3, 4 and 5. Up to June 2023, there were 584 affected persons (424 vulnerable and 160 full loss of agriculture-based livelihood) who received payment are eligible for LIRP training. During this reporting period, no vulnerable persons received vulnerability grants.

58. Gender distribution of identified affected persons eligible for training who are vulnerable and or have fully lost their agriculture-based livelihood in Sections 1, 2, 3 and 4 is given below:

Table 4.4.1: Distribution of Eligible (received compensation+ specially advised) Affected Persons who are Vulnerable and incur significant loss of Agriculture-based Livelihood

Section*	Vulnerable AP		APs with Significant loss of agriculture-based livelihood		Total	
	Male	Female	Male	Female	Male	Female
Section 1	30	19	03	-	33	19
Section 2	179	66	90+4 ²⁰	67	269	137

¹⁷ Except below mentioned (footnote 19) 4 affected persons.

¹⁸ 1 affected person is common in vulnerable and significant loss category. So, he is counted as 1 vulnerable person.

¹⁹ 12 affected persons are common in vulnerable and significant loss category. So, they are counted as 12 vulnerable persons.

²⁰ The 4 affected persons received LIRP training and investment grant as per ADB advice because these affected persons were not identified as titleholder by the Deputy Commissioner, but they are reported in the Resettlement

Section*	Vulnerable AP		APs with Significant loss of agriculture-based livelihood		Total	
	Male	Female	Male	Female	Male	Female
Section 3	20	16	-	-	20	16
Section 4	81	08	-	-	81	08
Section 5	05	0			05	0
Sub-total	315	109	93	67	408	180
Total		424		160		588

Skill development training

59. Vulnerable affected persons and those who significantly lost their agriculture-based livelihood, those who received CCL payment and other resettlement assistances and special consideration have been offered skill development training, namely, tailoring, small business, cow and goat rearing, vegetable gardening, fish culture and chicken and duck rearing according to their preferred options through the NGO guided by MDSC.

60. Out of the above mentioned 584 eligible affected persons, up to 30 June 2023, in total 492 (84%) (Section 1= 52, Section-2= 357²¹ and Section 4=83²²) affected persons including 160 affected persons facing full loss of livelihood received training on livelihood and income generation activities based on their preferred livelihood options. Out of the 492 trained APs, 180 were female and the rest 312 were male.

61. Each of the trained affected persons (vulnerable and full loss of agriculture-based livelihood) received Tk. 20,000.00 as investment grants according to the IGA Plan.

62. The following 47 are the affected persons who are yet to receive the trainings section-wise. They will be imparted training by the next reporting period.

- Section 3 – 36 affected persons
- Section 4 – 6 affected persons
- Section 5 – 5 affected persons

Income generation engagement of trained affected persons:

63. Out of 492 trained affected persons from sections 1, 2, and 4, 473 (96%) are engaged in income generation activities to date. Section-wise segregation is as below.

64. In Section 1, 52 (100%) out of trained 52 affected persons (vulnerable-49, full loss of agriculture-based livelihood-3), in Section 2, 340 (95%) out of trained 357²³ affected persons (vulnerable-200 and full loss of agriculture-based livelihood-157) and in Section 4, 81 (98%) out of trained 83 vulnerable affected persons are engaged in income generation activities.

65. The remaining 4% of the total trained affected persons could not engage in income-generating activities due to money spent for other purposes, shortage of time and sickness.

Plan as facing significant loss of their agriculture-based livelihood. So, ADB advised PMU to give this special support to these affected persons so that these affected persons have not fall into poverty trap after handing over the land for civil works.

²¹ In Section 2, in total 406 affected persons who received vulnerable grants and who faced significant loss. Out of these, 38 affected persons are not interested to receive training and 11 affected persons expired.

²² In Section 4, in total 89 affected persons received vulnerable grants. 6 of these affected persons missed the IGA training program for their personal reason. However, these 6 affected persons will be given training with the training batch for Section 3.

²³ Out of 357 affected persons, 114 affected persons received training in December 2022.

In Section-2, 17 affected persons and in Section 4, 2 affected persons have not yet started IGA for the trades for which they received training. In Section 2, out of 17 affected persons, 13 have invested money for other purposes (such as purchased land, leasing in paddy field, started small business, purchased autorickshaw for renting out, built house for renting out, sent son to abroad, etc.) than the trades for which they received training. One (1) spent money for household expenses, 2 have no space for rearing cow, goat or poultry and 1 is busy completing her studies. In Section 2, 1 AP spent all his compensation amount for his medical treatment and another AP is elderly and too sick to start IGA. Post-training follow-up monitoring is ongoing for section 1, 2 and 4. Following is the progress of training and engagement in income generation activities.

Table 4.5: Distribution of Affected Persons who received Training and Engaged in IGA

Training Category	Total Trained			Engaged in Income Generating Activities			Remarks
	Section 1	Section 2	Section 4	Section 1	Section 2	Section 4	
Chicken and Duck Rearing	23	93	13	23 (100%)	90 (97%)	12 (92%)	In Section-2 = 17 APs and Section-4= 2 APs not yet started IGA for the following reasons: In Section 2, out of 17 APs, 13 has invested money for other than the trades for which they received training. One (1) spent money for household purpose, 2 has no space for rearing cow, goat or poultry and 1 is busy to complete her study. In Section 2, 1 AP spent his all money for his treatment and another AP is old aged and sick to start IGA.
Cow and Goat rearing	24	132	44	24 (100%)	120 (91%)	44 (100%)	
Small Business	-	74	14	n/a	74 (100%)	13 (93%)	
Tailoring	3	44	12	3 (100%)	43 (98%)	12 (100%)	
Vegetable Gardening	2	8	-	2 (100%)	8 (100%)	n/a	
Fish Culture	-	6	-	-	5 (83%)	-	
Total	52	357	83	52 (100%)	340 (95%)	81 (98%)	

Status of trained affected persons linked with NGOs/microfinance institutions

66. In Sections 1, 2, and 4, a total of 199 (130 males and 69 females) trained affected persons have been linked with NGOs/micro-credit institutions. The remaining 293 affected persons are not interested in getting linked with NGOs/ microfinance institutions as during discussions they mentioned they did not need additional support from these organizations and also due to religious reasons. Out of those, 37 (71%) from Section 1, 133 (37%) from Section 2, and 29 (35%) from Section 4 have been linked. The below table detailed the status of linking of trained affected persons with NGOs/micro-credit institutions:

Table 4.6: Distribution of Affected Persons who received Training and Linked with NGOs/ microfinance institutions for financial involvement.

Training Category	Total trained			Linked with NGOs/ Micro-credit			Name of NGOs/ micro-credit institutions linked by the APs
	Section 1	Section 2	Section 4	Section 1	Section 2	Section 4	
Chicken and Duck Rearing	23	93	13	16	33	06	Bangladesh Krishi Bank, Grameen Bank, SIDOR NGO, BRAC NGO, Agrani Bank, ASA NGO, Palli Mongal Karmosuchi, Bohumukhi Agrani Bank, Ektee Bari Ektee Khamar, Pubali Bank Ltd, Bohumukhi Somobay samiti SSS NGO, BRAC Bank, Polli Bikash NGO, BURO Bangladesh, CSS, Sajeda Foundation, SAKTI Foundation, DSK, Samajik Seba, Jagoroni Chakro, Uttara Bank, Probashi Kallyan Bank and Jibon Nagar, Sonali Bank, Islami Bank and Al Arafah Islami Bank.
Cow and Goat rearing	24	132	44	17	33	11	
Small Business	-	74	14	n/a	42	06	
Tailoring	3	44	12	02	17	06	
Vegetable Gardening	2	8	-	02	4	n/a	
Fish Culture	-	6		N/A	4	n/a	
Total	52	357	83	37 (71%)	133 (37%)	29 (35%)	

67. Lists of the affected persons linked with NGOs/microfinance institutions since inception in Resettlement Plan Sections 1, 2, and 4 are given in **Appendix 11.8, Appendix 11.9 and Appendix 11.10** respectively.

Status of vulnerable affected persons

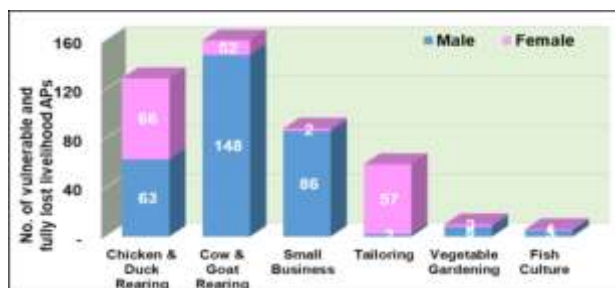
68. As mentioned above, a total of 424 vulnerable affected persons received the vulnerability assistance. The section-wise vulnerable affected person breakdown is as follows:

Table 4.7: Distribution of Vulnerable Affected Persons

Section	Number of Vulnerable Affected Persons		
	Male	Female	Total
Section 1	30	19	49
Section 2	179	66	245
Section 3	20	16	36
Section 4	81	08	89
Section 5	05	0	5
Total	315	109	424

Female participation in livelihood training

69. To date 180 (37%) females of total 492 vulnerable and affected persons facing full loss were trained in Sections 1, 2, and 4. Up to this reporting period, female participation in various categories of livelihood training is presented in the **Figure 4.3**.

Figure 4.3: Female participation in LIRP training

Employment of Skilled, semi-skilled, and unskilled labor by the contractor:

- GWT (Gandharbpur Water Treatment) SNC²⁴ and CAMCE²⁵ (Chi na CAMC Engineering Company Ltd) appointed 1,886 (3%) females out of 54,625 person-days of unskilled/ semi-skilled laborers during this reporting period. Since inception, 8,893 (4%) females out of 218,970 person-days of unskilled/ semi-skilled laborers were appointed against a target of 20%. It is noted that women were engaged in cleaning, housekeeping-related work, and cooking. All female laborers received equal payment with men for an equal value of work.
- During this reporting period, GWT engaged 52,886 person-days of semi-skilled and skilled security guards and other positions staff like Security Supervisor, CCTV Operator, Office Assistant, Office Secretary and Document Controller of which 3,600 (7%) person-days were female. Since its inception 45,635 (18%) person-days of females employed out of 252,061 person-days of semi-skilled/skilled staff employment.

Water and sanitation facilities at P1 and P2 areas:

- **Supply of drinking water:** Safe drinking water is available for all staff and laborers within the project area.
- **Supply of water for sanitation facilities:** Water supply is available in all washrooms including washroom for laborers with all facilities inside the washroom (like toilet tissue, soap, water supply, flashing system, bucket etc).
- **Sanitation facilities:** GWT and CAMCE ensured separate toilet facilities both for male and female including labours in the P1 and P2 areas.
- **Child-care/rest room:** CAMCE established a separate room as a child-care/rest room for female staff of CAMCE at CAMCE office at Purbachal for the DESWS project.

²⁴ It is a contractor's consortium for P1. SNC's full form is not mentioned in the contract.

²⁵ Contractor for P2

5. Public Participation and Consultation

5.1 Public Consultation

70. Under the supervision and guidance of PMU and MDSC, the INGO conducts the following consultation meetings within the resettlement plan areas to make affected persons aware of resettlement aspects:

- Public consultation meetings (as and when required);
- Community meeting with the affected persons (every month); and
- Focus group discussion (FGD) meeting

71. During this reporting period, 102 community meetings were conducted from January to June 2023. No public consultation and FGD were carried out during this reporting period. In community meetings, total participants were 1325 where 518 were male and 807 were female.

72. Issues of discussion were:

- Information dissemination on:
 - a. Land Acquisition (LA) notices
 - b. Papers required for receiving compensation from Deputy Commissioner's office and other resettlement assistance from DWASA
 - c. Compensation entitlements against loss of assets
 - d. Compensation payment issue for those affected persons who are yet to receive CCL.
- Cultivation on acquired land
- Method of payment if there is no NGO
- IGA training, grants and queries regarding training facilities before payment
- Responses to queries on a job opportunity in the project's civil works.
- To make affected persons aware in making land encumbrance free which is already acquired by DWASA.

5.1.1 Public Participation and Information Dissemination on Key Aspects

73. The INGO consulted affected persons and made them aware of different resettlement issues. At the same time, the INGO disseminated various information in response to the affected persons' queries.

74. The INGO on behalf of PMU disseminates information on the following key aspects against issues raised by the affected persons:

- ❖ Required documentation to claim Cash Compensation under Law (CCL)²⁶ from relevant Deputy Commissioners Office. The documents are:
 - Proof of land ownership;
 - Record of updated mutation (transfer or change of title in the records for the concerned property);
 - Up-to-date land tax (revenue) payment receipt;
 - Proof of Nationality (National ID Card)
 - A Bank Account²⁷ with account and bank details.

²⁶The INGO staffs to support and guide affected persons in collecting necessary documentation and to ensure that payments are made fair and transparently.

²⁷ Deputy Commissioner's office made payment only through Account Payee Cheque.

- ❖ Required documentation to claim Top-up Payment and Other Resettlement Assurances from the DWASA (PMU)²⁸. The necessary documents are
 - The Top-up Payment and Other Resettlement Assurances are only claimable by the affected persons who have received CCL;
 - All the above-mentioned documents;
 - Citizenship Certificate from relevant Union Parishad/ Pourashava Chairman;
 - Land share sheet (issued by Deputy Commissioner 's office)
- ❖ Affected Persons' entitlements: According to ARIPA 2017, affected persons are entitled to get a 200% premium on land loss and 100% premium on structures, trees, crops, and fish stock from Deputy Commissioner's office. They are also entitled to receive Top-up Payment [an amount to compensate the loss on land value (by getting government fixed rate from Deputy Commissioner's office) in comparison with the present market value of the land] and other resettlement assistance according to eligibility and entitlement matrix.
- ❖ Determination of present market value of lands: For CCL value Deputy Commissioner's office collects land data from the land office on the preceding deed value of 1 year after the cut-off date. They collect mouza-wise and land category-wise data and calculate an average for fixing land price. CCL value may vary since sometimes deed value seems less than market price. The value of all lands is determined by a market survey. Property Valuation Advisory Committee (PVAC) approves the actual land value. The difference between the payment made Deputy Commissioner's Office (if less than the market price) and the approved market price is paid by DWASA after receiving the CCL, subject to submission of all necessary papers as mentioned above.
- ❖ Compensation for business loss: The affected persons will be fairly compensated according to the market price with a 100% premium from Deputy Commissioner's Office and DWASA will pay compensation for business loss as per the entitlement matrix.
- ❖ Payment for CCL unpaid affected persons with land disputes/court case: The affected persons with unsettled legal issues will be paid as soon as their issues are settled. In the case of Resettlement Plans 1 and 2, to ensure their CCL payments, DWASA has deposited estimated money to Deputy Commissioner's office(s) and Additional Payment and Other Assurances, DWASA deposited the estimated amount to a dedicated account operated by two signatories from DWASA. The accrued interest will be payable to affected persons proportionate to the individual's due amount. The money will be kept in accounts even after completion of the project as long as the payment to affected persons is not completed. The same procedure will be followed for all of the Resettlement Plan areas. If there is no NGO they will get their dues by contacting Dhaka WASA directly. DWASA will have an operational unit in Rugganj and they will be responsible for payment.
- ❖ Livelihood and Income Restoration Program -LIRP (Assistance to vulnerable and who lose whole of their agriculture-based livelihood):
 - Affected Persons who are vulnerable and who lose 10% of their agriculture-based livelihood, will get different trade-based DWASA organized training on the scope of marketing and creating employment opportunities and according to their choice/interest.
 - Affected persons get eligibility subject to receive compensation payment from the project.
 - The Income Generating Activity (IGA) training is provided to them to re-establish or restart the loss of livelihood-based activities for enhancing households' income particularly emphasizing vulnerable women. All of the affected persons is given an investment allowance after receiving training and on the submission of an investment plan.
 - The money which they will receive as compensation and resettlement benefits will have to be used to rebuild the lost structures and restart their livelihood so that they can bring a positive change in their lives or at least at the level of pre-project condition. Affected persons were advised not to use the compensation money/ resettlement benefits in unproductive ways.
 - Training grant recipient affected persons will be monitored and advised regularly by INGO, MDSC, and PMU.
 - The INGO will assist training recipients by involving them with the local level credit institution and NGOs which can provide technical and financial support.

²⁸ Affected persons with the assistance of INGO field staff have to submit all these documentations to INGO Office to prepare the payment vouchers, get approval from PMU and arrange the payments by PMU.

- ❖ Cultivation on acquired land: The affected persons cannot cultivate the acquired land in any way.
- ❖ Job opportunity in project’s civil works: Affected persons want to know if they have any opportunity to work in the project’s civil works. INGO staff informed them the project authority is well concerned about giving the opportunity to be employed in project site based on competence.

75. An item-wise summary of the community meetings is attached as **Appendix 11.11**.

76. Minutes of the Public Consultations were attached with the DDRs submitted to ADB for getting concurrence to start civil works in the area of Resettlement Plan Section 3 and part of Section 5 against LA Case 5/2018-19 and LA Case 10/2018-19.

77. Besides above consultation, PMU distributed awareness campaign notices (copies of notices were appended with the SSMR, July-December 2021) so that the affected persons could be motivated to submit their necessary relevant documents in support of ownership to the land acquisition office for receiving compensation on affected land, structures etc. to Deputy Commissioner’s office. At the same time the affected persons were requested to submit one set of those papers along with a photocopy of compensation received cheque to DORP (INGO) Area office.

5.1.2 Gender mainstreaming


78. As part of gender mainstreaming,

- 43 (72%) DWASA and NGO staff received training on gender mainstreaming;
- 9 including 2 (22%) female representatives of GWT Contractor and Sub-contractors received training on ADB core labor standard and gender mainstreaming;

Female participation in social consultation meetings

79. Since inception, average female participation achieved is 47% against the targeted 40%. Female participation has been increasing day by day and DORP staff suggested keeping up the trend of female participation in the future. Social Development and Gender Specialist of MDSC is regularly following up on this issue and will be guiding DORP to maintain the trend of female participation.


Figure 5.1: Trend of female participation in the social consultation meetings during the immediate last 12 months

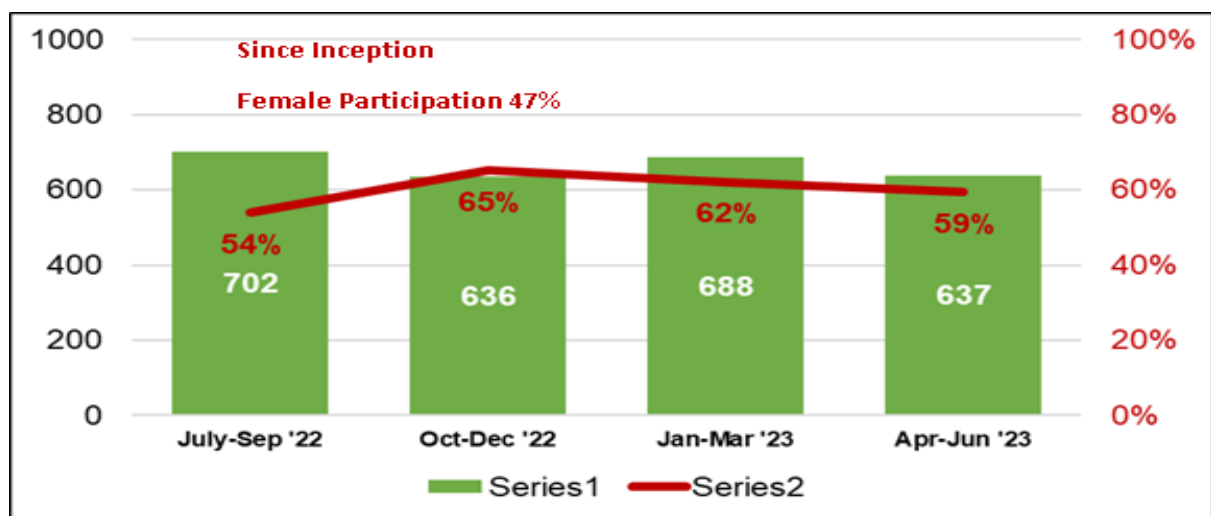

Source: MDSC QPR 2, 2023

The trend of female participation in social consultation meetings during the reporting period of January to June 2023 is presented herein.

Figure 5.2: Trend of female participation in the social consultation meetings during this reporting period

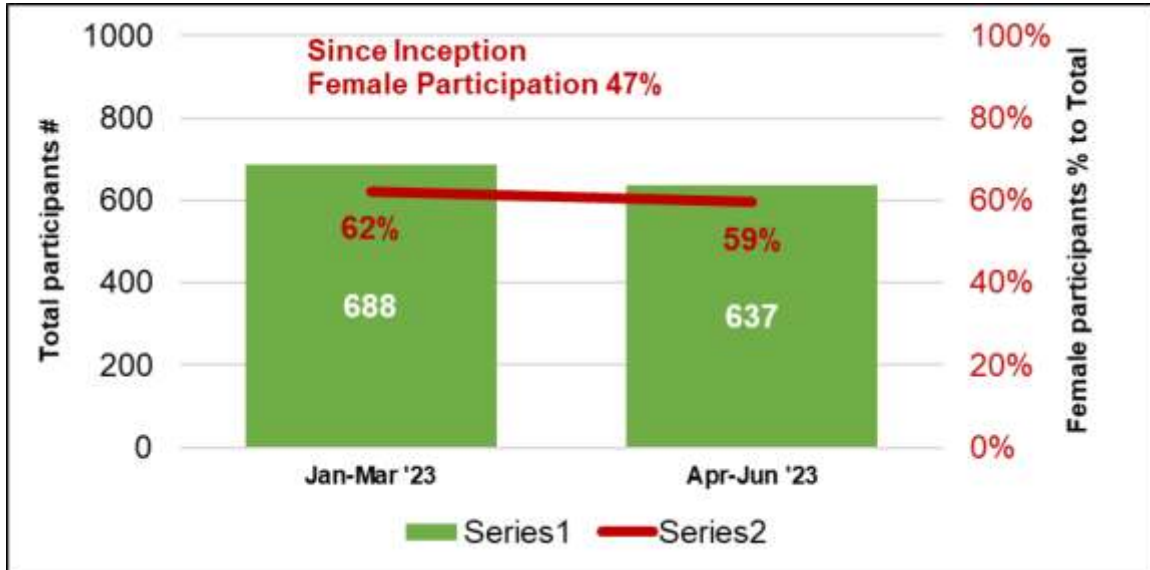

Source: MDSC QPR 2, 2023

5.2 Disclosure of Resettlement Plans


80. In addition to community meetings, all (6) resettlement plans in P1 and P2 have been updated, approved, and disclosed on ADB and DWASA websites. Resettlement plans for Sections 2, 4, 5 and 6 are being translated by MDSC. Translated Resettlement Plan Section has been disclosed in the locality.

81. DDR for P3.1 and Resettlement Plan for P3.2 have been approved and disclosed on ADB and DWASA websites. These will be updated further before the start of civil works.

6. Grievance Redress Mechanism (GRM)

82. The project has established a grievance redress mechanism in compliance with the principle detailed in Appendix 9 in the Project Administration Manual (PAM; December 2020). The GRM is presented below using a Process Flow Chart:

Figure 6.1: Grievance Redress Mechanism Flow Chart

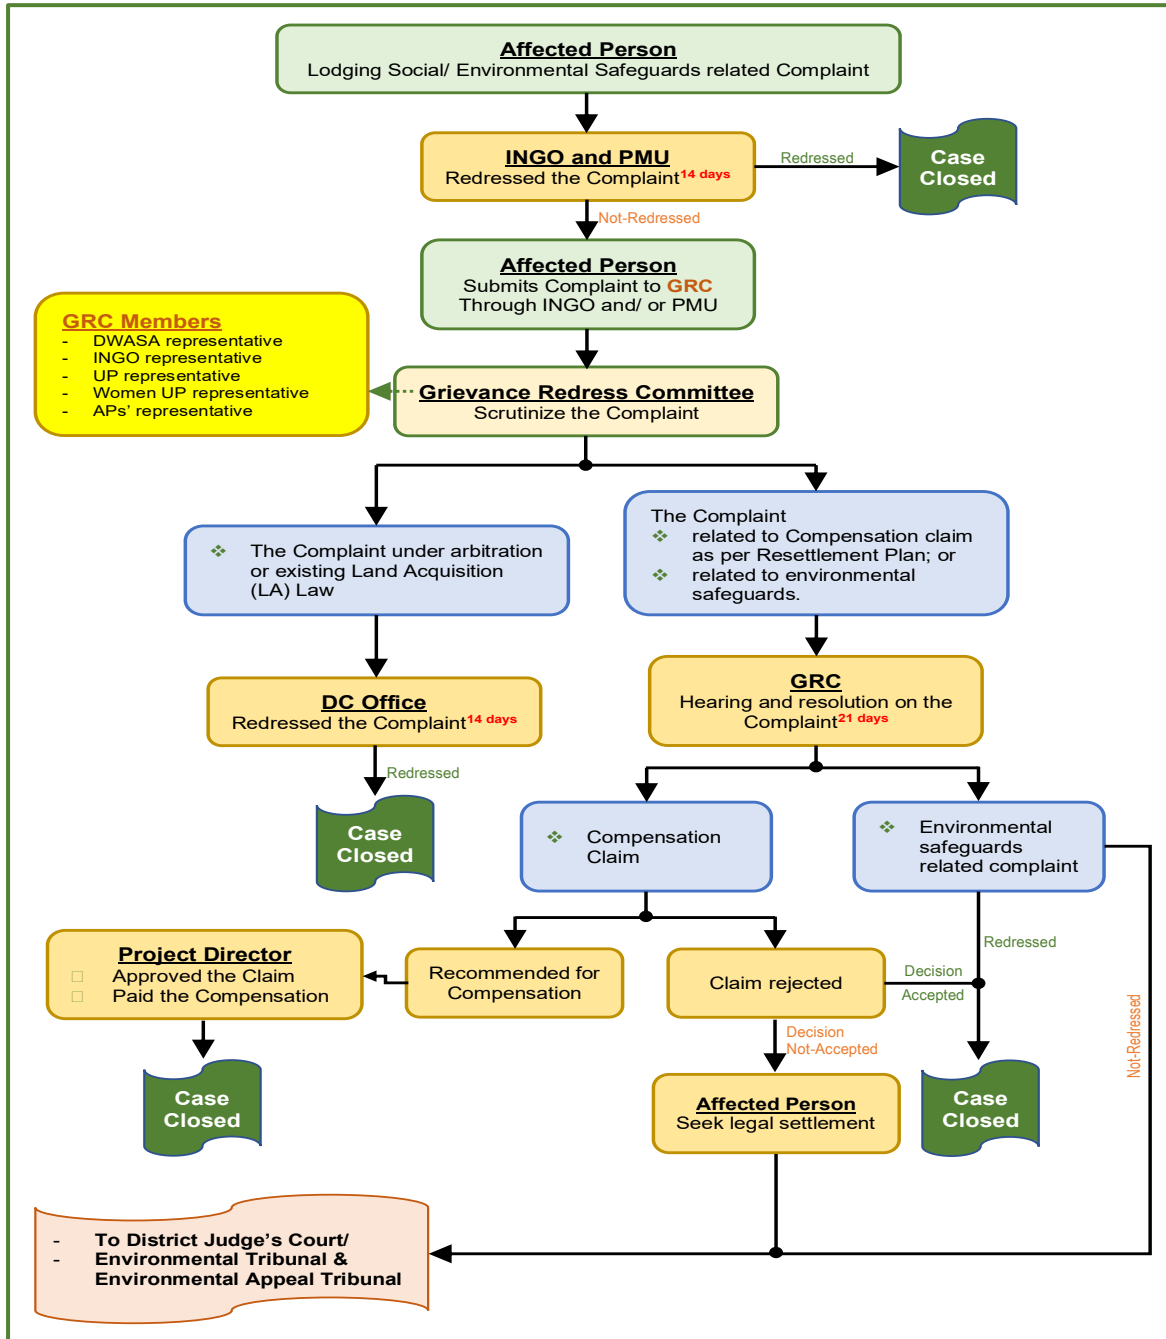

Source: Figure 1, Appendix 9 of PAM (December 2020)

The GRM notwithstanding, an aggrieved person shall have access to the country's legal system at any stage. This can run parallel to accessing the GRM and is not dependent on the negative outcome of the GRM.

83. If the established GRM is not in a position to resolve the issue, the affected person may use the ADB Accountability Mechanism through directly contacting (in writing) the Complaint Receiving Officer (CRO) at ADB headquarters. Before submitting a complaint to the Accountability Mechanism following the ADB process. INGO shall have to assist the grieved AP in this regard.

6.1 Grievance Redress Committees (GRC)

84. GRCs are formed at PMU and community level in each Union/ Pourashava level, wherever resettlement activities kick-started, with representatives from the DWASA, local elected representatives from the Local Government Institutions (LGI), INGO, affected persons' representatives, women affected persons to allow voices of the affected communities to be heard and ensure a participatory decision-making process. The representative of the INGO functions as Member Secretary of any GRC.

85. The Grievance Redress Committees (GRCs) have been established to ensure stakeholders' participation in the implementation process and fair compensation to affected persons and in the resolution of Social and environmental safeguards-related complaints.

86. The Member Secretary of any GRC is regularly available and accessible for affected persons to address concerns and grievances. The female member of GRC and the female affected persons of affected households participate in the grievance redress session(s) when the complainant is a female. The legal advisor and DORP support the GRC regularly and assist the affected persons to formulate their complaints. The grievance cases are recorded with details and results of the cases for review. The affected people are also allowed to go to GRC for any environmental concern as well.


6.2 Scope and Jurisdiction of GRC

87. The GRCs resolve any complaint of safeguard compliance – environment, involuntary resettlement, and indigenous people, design-related issues, compensation, service delivery, or any other issues or concerns related to the project in compliance with the item i. Scope and Jurisdiction of GRC of Appendix 9 (Ref: PAM, December 2020). The process for redressing any complaint follows the GRM as explained earlier.

88. To date, in total 13 GRC meetings have been held including 1 during the reporting period. In these meetings, a total of 133 cases were dealt with. Out of these 133 cases, 63 cases were considered as invalid, 49 cases were advised for payment, and 21 cases forwarded to Deputy Commissioner's office to settle legal issues. Out of 21, 10 cases have been resolved and paid out compensation. The remaining 11 cases have been dismissed by the Deputy Commissioner's office.

89. During this reporting period, 1 GRC meeting was held with affected person from Resettlement Plan Section 3, where 1 affected person was heard. The applicant, Anowar Hossain, claimed that he had land at plot number 2909 in Golakandail Mouza, which was acquired for the project under Dhaka WASA. He had houses, trees, and structures on that land. He cleared the space by removing all the structures. But his father's grave remains on the same land, which was inside the structure. He said he did not receive any compensation for the house or any money for removing the grave. The Convenor of the meeting stated that during the joint verification survey conducted jointly by the office of the Deputy Commissioner and the requiring body Dhaka WASA, the said structure was listed in the Award Book, and after verifying the affected persons' compensation payment file, it was found that that the applicant has received full and fair compensation (CCL and other resettlement assistance) for all assets including structures. The GRC decided that the project might pay the applicant BDT 10000.00 (ten thousand) as the replacement cost for shifting his (the applicant's) father's grave. DWASA paid compensation to the affected person.

90. Overall status regarding nos. of GRC meetings held, decisions were taken and implementation of taken decisions is presented here:

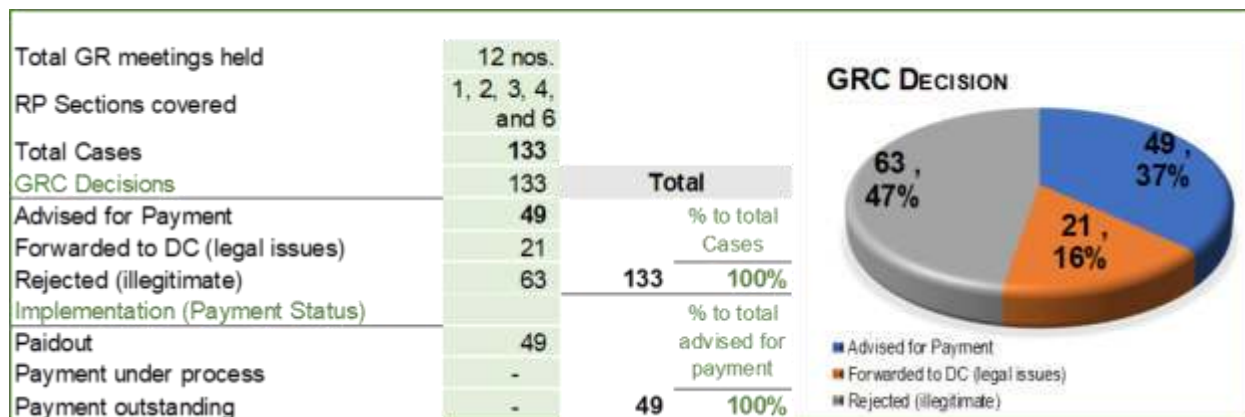

91. Signed copies of Bangla minutes and translated minutes in English of 13th GRC meeting are given as **Appendix 11.12 and Appendix 11.13.**

7. Institutional Arrangement

92. The DESWSP management organizations are as follows:

1. Overall guidance and supervision: Ministry of Local Government, Rural Development and Cooperatives (MLGRDC).
2. Executing Agency: Dhaka Water Supply and Sewerage Authority (DWASA).
3. The Financier: Asian Development Bank and its co-financiers, Agence Française de Développement and European Investment Bank.

93. The roles and responsibilities of each organization are as explained in Table 3: Project Implementation Roles and Responsibility under item A: Project Implementation Organizations: Roles and Responsibilities in section III, Project Management Arrangement if ADB's PAM (December 2020).


7.1 Project Implementation Partners

94. To implement the project successfully a concerted effort among government, funders, and national and international private sector service providers is envisaged. The following services providers are involved.

- (i) Implementing Non-government Organizations (INGOs): to implement Social Safeguard aspects of the project.
- (ii) Management, Design and Supervision Consultant: to assist the Executing Agency in detailed design, procurement, management and supervision of INGO and contractors throughout project implementation.
- (iii) Contractors: in design (design and build contract), construction and operation (operation and maintenance contract) of the project packages.
- (iv) Independent Project Monitoring and Evaluation Agency: To evaluate and monitor the work of NGOs.

95. Working relationships of the project partners and flow of information in respect of Social Safeguards Plans (Resettlement Plans) are shown below.

Figure 7.1: Social Safeguards Plans Implementation partners relationship and information flow

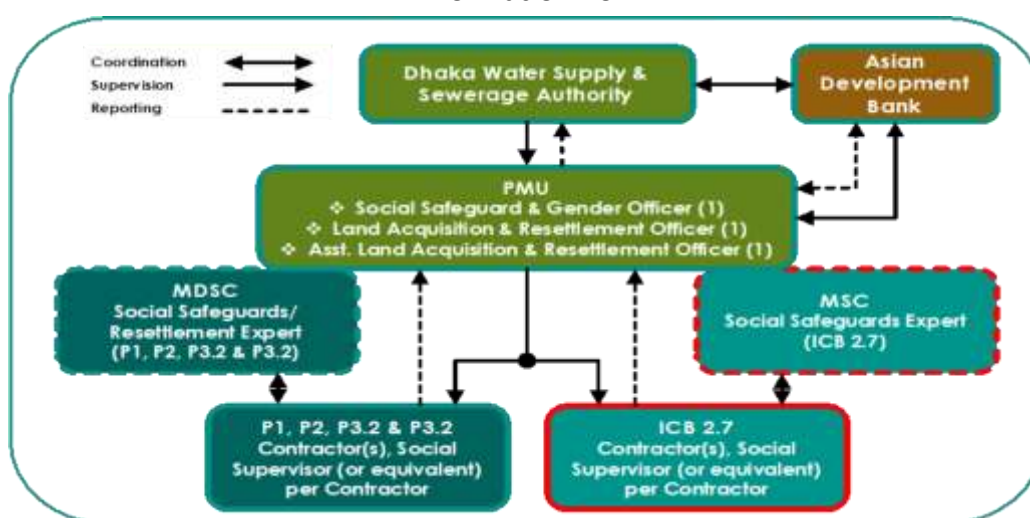

Notes:

MDSC > Management, Design and Supervision Consultant²⁹; MSC > Management and Supervision Consultant

²⁹This report only deals with P1, P2, P3.1 and P3.2.

Source: (Ref: Figure 8 of PAM, December 2020)

96. DWASA established a Project Management Unit (PMU) including a safeguard implementation unit (SIU) staffed with a Safeguard Officer (Social and Gender) and a Safeguard Officer (Environment).

97. A Resettlement Expert and Social Development and Gender Specialist from MDSC assists the SIU. The PMU appointed an NGO, Development Organization for the Rural Poor (DORP), in assisting them in the implementation of Resettlement Plans (RPs)/ Due Diligence Records (DDR) for the Resettlement Plan under packages 1 and 2. The PMU also appointed another NGO, Knowledge Management Consultants (KMC) Ltd. to implement Resettlement Plans (RPs)/ Due Diligence Records (DDR) for P3.1 and P3.2. The MDSC Resettlement Expert and Social Development and Gender Specialist are to oversee the implementation of Resettlement Plans by the INGOs.

98. One Executive Engineer and two Assistant Engineers from PMU are responsible for overseeing and looking after the day-to-day safeguard activities. The Project Director, two Deputy Project Directors, and a Senior Water Supply Engineer are responsible for administering overall safeguards activities. The Senior Water Supply Engineer is yet to be appointed. This position is vacant since 2018.

99. The Management Design and Supervision Consultant (MDSC), led by Mott MacDonald Limited (UK)³⁰, is responsible for monitoring the implementation of the Resettlement Plans/DDRs by INGOs and assist the PMU in preparing the Semiannual Social Safeguard Monitoring Report.

100. With ADB's and government approval, DORP's contract has been extended further on 22 June 2021. DORP and DWASA have signed the contract. This contract will be valid up to March 2023.

101. DORP's Team Leader's position was vacant due to the resignation of Team Leader. At present, DORP's Deputy Team Leader is acting as Team Leader.

102. PMU and MDSC closely coordinate the works of DORP and KMC, the INGOs.

103. The major tasks of DORP are:

- updating resettlement plans;
- conducting public consultations, Focus Group Discussions (FGDs), community meetings, and personal contact with the affected persons and communities for awareness building in affected persons;
- assessing resettlement impacts, collecting the market price of the loss of the properties, activities for making top-up payment and other resettlement assistance;
- skill training for livelihood restoration (LIRP) to the affected persons, livelihood monitoring, etc.
- facilitation and motivation of affected persons for submission of land documents for CCL payment

104. The major tasks of KMC are:

- assist in updating resettlement plans;

³⁰ In association with Fichtner GmbH and Co. KG (GER), Euroconsult Mott MacDonald (Netherlands), Yooshin Engineering Corporation (KOR), BCL Associates Limited (Bangladesh), SARM Associates Limited (Bangladesh) and Associates for Development Services Limited (Bangladesh).

- conducting public consultations, Focus Group Discussions (FGDs), community meetings, and personal contact with the affected persons and communities for awareness building in affected persons;
- assessing resettlement impacts, collecting the market price of the loss of the properties, activities for making top-up payment and other resettlement assistance;

8. Monitoring Results – Findings

105. DWASA is preparing and submitting regularly two separate safeguards monitoring reports, i) on environmental safeguards (Semi-annual Environmental Monitoring Report - SEMR) and ii) on social safeguards (Semi-annual Social Safeguard Monitoring Report - SSMR), in compliance with paragraph 91 of subsection B 'Monitoring', section IX 'Performance, Monitoring, Evaluation, Reporting and Communication' of the ADB's Project Administration Manual (PAM). After securing ADB clearance, both these reports are published in DWASA and ADB websites (www.dwasa.org.bd; and www.adb.org.)

106. The reports follow the requirements of the PAM (ref Appendix 12 for the semi-annual environmental monitoring report, and Appendix 13 for the semi-annual social safeguards monitoring report).

107. Both the safeguard monitoring reports are presented in DESWSP quarterly reports. The following is the 2nd quarter's social safeguards checklist as a ready reference.

Table 8.1: Semi-Annual Social Safeguards Progress Checklist for P1, P2, P3.1, and P3.2

Activity	Package P1	Package P2	Package P3.1	Package P3.2	Remarks (if Answer is 'No')
	Yes/ No	Yes/ No	Yes/ No	Yes/ No	
A. For subproject packages under bidding	@ Construction	@ Construction	@ Awarded	@ Awarded	
1. Resettlement Plans (RP)/Due Diligence Records (DDR)/Indigenous Peoples Plans (IPP) cleared by ADB?					
2. RPs/DDR/PPs included in the bidding documents?					
3. Does the resettlement Plan includes cut-offdate?					
4. Are there changes in the scope of work of the cleared RPs/DDR/PPs?					
5. ID cards prepared for affected persons and distributed?					
6. Are specific actions identified in RP/IPP, if any, that are required of the contractor for impact avoidance or mitigation, incorporated in bid documents?					
7. Does the BOQ line item include any requirements specified in RP/DDR/IPP?					
8. RP/IPP disclosed in form and language understood by stakeholders and affected persons?					
9. Consultations with stakeholders and affected persons/Indigenous People held?					
10. Is the GRM in place and GRC constituted?					
B. For subproject packages with contracts awarded (no works yet)	@ Construction	@ Construction	@ Awarded	@ Awarded	
1. All NOCs/land transfers obtained?			No	No	Under processing
2. Agreement of sale/transfer and third party certificate obtained for negotiated settlement/voluntary donation?			Not applicable	Not applicable	
3. All compensation paid in full?			Not applicable	Not applicable	No resettlement impact identified
4. Detailed measurement survey conducted jointly by contractor, project consultant, and PMU/PIU?			Yes	Not yet	Will conduct soon
5. All community concerns and grievances related to specific sites mitigated through consultations or agreed actions?			Not applicable	Not applicable	Not yet started
6. All common property resources (CPR, including small shrines, trees of worship, etc.) identified and plan for continued access prepared?			Not applicable	Not applicable	Nothing identified
7. Each contractor designated social safeguards and grievance registration officer?			Not yet	Not yet	Will designate during construction
8. For DBO packages, detailed design completed and updated RP/DDR/IPP submitted to ADB?			Not applicable	Not applicable	
9. For DBO packages, serial no. 1-7 accomplished?			Not applicable	Not applicable	
C. For subproject packages with contracts awarded and works on-going	@ Construction	@ Construction	@ Awarded	@ Awarded	
1. Contractors have appointed social safeguards and grievance registration officers per subproject package?	Yes	Yes			

Activity	Package P1	Package P2	Package P3.1	Package P3.2	Remarks (if Answer is 'No')
	Yes/ No	Yes/ No	Yes/ No	Yes/ No	
2. Site-specific signages with a date of start and end of construction and contact number for grievances and safety instructions for the general public posted onsite?	Yes	Yes			Signages put up but contact number not given for P1. Signages put up with contact number for P2.
3. Is the grievance registration register available at each worksite?	Yes	Yes			
4. Site fencing/protection works etc. undertaken before the start of physical construction work?	Yes	Yes			
5. Contractors provided PMU/PIU with a notification/incident report of any grievance or unanticipated impact within 24 hours?	Yes	Yes			
6. Reports of complaints/grievances reported monthly to PMU?	Yes	Yes			
7. Records of information disclosure/consultations submitted by PIUs to PMU monthly?	No	No			There is no PIU in this project.
8. Records of site inspection by PIU and DSC submitted to PMU monthly?	Yes	Yes			
9. Records of site inspection by PMC submitted to PMU monthly?	Yes	Yes			

9. Compliance Status

108. ADB has approved the 15th SSMR on 31 March 2023 and the same has been disclosed on DWASA and ADB websites (www.dwasa.org.bd and www.adb.org).

9.1 Compliance with relevant Loan Covenants

109. The following table presents the status of the covenants related to Social Safeguards of the Loan Agreement:

Table 9.1: Progress in training and income generation engagement

Covenant Description	Progress Status	Compliance Assessment
Involuntary Resettlement		
Schedule 5 Para 4 The Borrower and DWASA shall ensure, that all land and all rights-of-way required for the Project, and all Project facilities are made available to the Works contractor in accordance with the schedule agreed under the related Works contract and all land acquisition and resettlement activities are implemented in compliance with (a) all applicable laws and regulations of the Borrower relating to land acquisition and involuntary resettlement; (b) Involuntary Resettlement Safeguards; and (c) all measures and requirements set forth in the RP, and any corrective or preventative actions set forth in any Safeguards Monitoring Report.	A section-wise approach is adopted for land acquisition and compensation payments, to ensure that all affected persons get payment prior to handing over encumbrance-free land to the contractor. As above As above	Being complied Being complied Being complied
Schedule 5 Para 5 Without limiting the application of the Involuntary Resettlement Safeguards or the RP, the Borrower and DWASA shall ensure that no physical or economic displacement takes place in connection with the Project until: (a) compensation and other entitlements, as relevant, have been provided to affected people in accordance with the RP; and (b) a comprehensive income and livelihood restoration program has been established in accordance with the RP.	Works in progress Done and works in progress	Being Complied Being Complied
Human and Financial Resources to Implement Safeguards Requirements		
Schedule 5 Para 6 The Borrower and DWASA shall make available necessary budgetary and human resources to fully implement the RP.	Amounts required for cash compensation under law (CCL) has been transferred in the concerned Deputy Commissioner's Public Account of Republic. Resources for the top-up payments and other resettlement assistances are available in DWASA's GoB account.	Complied
Safeguards - Related Provisions in Bidding Documents and Works Contracts		
Schedule 5 Para 7		

Covenant Description	Progress Status	Compliance Assessment
<p>The Borrower and DWASA shall ensure that all bidding documents and contracts for Works contain provisions that require contractors to:</p> <p>(a) comply with the measures relevant to the contractor as set forth in the RP (to the extent they concern impacts on affected people during construction), and any corrective or preventative actions set forth in a Safeguards Monitoring Report;</p> <p>(b) make available a budget for all such social measures;</p> <p>(c) provide the Borrower and DWASA with a written notice of any unanticipated resettlement or small ethnic community peoples risks or impacts that arise during construction, implementation or operation of the Project that were not considered in the RP;</p> <p>(d) adequately record the condition of roads, agricultural land and other infrastructure prior to starting to transport materials and construction; and</p> <p>(e) fully reinstate pathways, other local infrastructure, and agricultural land to at least their pre-project condition upon the completion of construction.</p>	<p>Contractor has been made aware that any impact due to construction will suitably be mitigated by the contractor.</p> <p>Available</p> <p>As required. There are no small ethnic community identified.</p> <p>Recorded</p> <p>Works in progress</p>	<p>Complied</p> <p>Complied</p> <p>Complied</p> <p>Complied</p> <p>Being Complied</p>
Safeguards Monitoring and Reporting		
<p>Schedule 5 Para 8 The Borrower shall do the following or cause DWASA to do the following:</p> <p>(a) submit semiannual Safeguards Monitoring Reports to ADB and disclose relevant information from such reports to affected persons promptly upon submission;</p> <p>(b) if any unanticipated social risks and impacts arise during construction, implementation or operation of the Project that were not considered in the RP, promptly inform ADB of the occurrence of such risks or impacts, with detailed description of the event and proposed corrective action plan in accordance with the SPS; and</p> <p>(c) report any actual or potential breach of compliance with the measures and requirements set forth in the RP promptly after becoming aware of the breach.</p>	<p>SSMRs are being submitted and disclosed on PMU and ADB websites</p> <p>No risk identified</p> <p>No breach of compliance identified yet</p>	<p>Being Complied</p> <p>Complied</p> <p>Complied</p>
<p>Schedule 5 Para 9 The Borrower shall ensure that no proceeds of the Loan are used to finance any activity included in the list of prohibited investment activities provided in Appendix 5 of the SPS.</p>	Complied	Complied
Grievance Redress Mechanism		
<p><u>Schedule 5 Paragraph 15</u></p> <p>Within 6 months of effectiveness date, the Borrower shall establish and maintain a grievance redress committee with representation from all stakeholders in the Project facilities for the purpose of addressing any grievances, from affected peoples concerning land acquisition, environment, and any other social issues, in a timely manner.</p>	<p>GRCs are formed at PMU and the community level in each Union/ Pourashava level, wherever resettlement activities kick-started, with representatives from the DWASA, local elected representatives from the Local Government Institutions (LGI), INGO, affected person representatives, women affected persons.</p>	Complied
Social Covenants		

Covenant Description	Progress Status	Compliance Assessment
Labor Standards		
<p>Schedule 5 Para 16</p> <p>The Borrower and DWASA shall ensure that</p> <p>(a) civil works contractors comply with all applicable labor laws and regulations of the Borrower, do not allow employment of child labor for construction and maintenance activities, encourage the employment of the poor, particularly women, and provide appropriate facilities for women and children in construction campsites, disseminate information on sexually transmitted diseases (including HIV/AIDS) and human trafficking to employees and local communities surrounding the project construction sites;</p> <p>(b) people directly affected by the Project are given priority to be employed by the Project;</p> <p>(c) contractors do not differentiate wages between men and women for work of equal value; and</p> <p>(d) specific clauses ensuring these are included in bidding documents.</p>	<p>These conditions are included in the DBO Contract documents, P2, P3.1 and P3.2. DWASA regularly reports compliance with these conditions.</p> <p>Affected persons are being given priority for employment depending on their willingness and skills.</p> <p>This condition is included in the DBO, P2, P3.1 and P3.2 Contract documents. DWASA regularly reports compliance with condition.</p> <p>This loan covenant is included in the DBO, P2, P3.1 and P3.2 Contract documents.</p>	<p>Complied</p> <p>Being Complied</p> <p>Complied</p> <p>Complied</p>
Gender Action Plan		
<p>Schedule 5. Para 17.</p> <p>The Borrower and DWASA shall ensure that the GAP is effectively implemented to achieve its objectives in a timely manner over the entire Project period, and that adequate resources are allocated for this purpose.</p>	<p>GAP monitoring reports are regularly submitted to ADB.</p>	<p>Being Complied</p>

10. Follow up Actions, Recommendations, and Disclosure

110. The section-wise implementation of resettlement plans is going on along with simultaneous updating of the same as explained in earlier sections. However, some outstanding issues need to be resolved in expediting the lands to be ready for the start of civil works in time as soon as the contractor(s) are appointed. Several meetings have been held among PMU, DORP, and MDSC to ensure timely implementation of resettlement plans. The following actions are in place and/ or recommended for actions by the project development partners.

Table10.1: Follow up actions, recommendations, and disclosure

Outstanding Issues	Recommendation/Required Actions
Hand over 280m of land to contractor in Resettlement Plan Section 6 is needed for construction of 1 shaft and part of treated water pipeline.	PMU could not make compensation payment to the affected persons of this 280m of land and the contractor has been appointed long before, in 2021. If land is not handed over for civil works, the contractor will claim huge financial compensation. Considering all, PMU may prepare a Due Diligence Report (DDR) for this portion of land and submit to ADB for giving special concurrence to get rid of huge loss to the nation.
	PMU may prepare DDR and submit to ADB for concurrence.
CCL payment to all affected persons	Affected persons need to be helped by the DORP more proactively in processing legal papers for getting CCL. In addition, with the assistance of respective Union Parishad (UP) representatives, support will be provided to those affected persons who have conflicts to resolve.
	PMU will follow up with Deputy Commissioner's office to facilitate payment. PMU needs to inform Deputy Commissioner's office that regardless of the quantity the amount has to be cleared.
Non-submission of necessary documents to Deputy Commissioner's Office by individual affected persons (other than government land, court case and vested property) in all mouzas of Resettlement Section 2 and 3.	INGO to take proactive measures in convincing the affected persons, who are delaying in the submission of their land papers as the land handover is urgent in this section.
	DORP will follow up helping and motivating the affected persons.
Livelihood Restoration of affected persons	DORP needs to organize skill development training for the affected persons who received vulnerable grants. DORP should monitor the livelihood restoration activities of the affected persons who received training and post-training investment allowance.
	DORP to impart training to the remaining paid vulnerable affected persons. LIRP monitoring reports on Sections 1 and 2 need to be prepared. LIRP post-training monitoring report needs to be finalized.
Finalization of LIRP post-training monitoring report for Section 4	MDSC provided comments on the Section 4 LIRP post-training follow-up monitoring report on 7th June 2020.
	DORP to finalize the report in compliance with MDSC comments.
LIRP post-training monitoring report of section 1	Report preparation is in progress.
	DORP to prepare the draft report and submit it to PMU and MDSC for review.
Performance of DORP	DORP should give training to PMU on operating the web-based database.
	DORP management should visit the field more often to ensure regular monitoring of the field activities related to the implementation of land acquisition and resettlement.
	PMU has assigned Mr. Mustafizur Rahman, Executive Engineer, and Mahrin Binte Islam, Assistant Engineer to supervise DORP activities on behalf of PMU.

Sl No	ID No.	Asset Book No.	EP's Name	Father's/Husband Name	Mother's Name	Muzas	LA Case No.	Plot No.	Land Type	Land Affectee (Decimal)	Additional Grant For Land (AG)	AL	HL	WL	CPS	GT	SC	TP	CGS LI	RS	BS	SS	CPE AM	AEI	BB	LIP	VH	SA	NRC	STG	SRG	CGMU C	SOT	BAR O	UW	Total Amount	Peppole Amount	Signed by AP										
377	12073116499	29/GA	MD MONIR MOLLAH	LATE ANOWAR ULLAH MOLLAH	MST ROWSON ABA	Golkandol	05/2018-2019	2436	Null	0.86000	0	0	0	0	0	0	559	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	50900	50900	স্বাক্ষর										
378	12073116503	29/GA	MD HUMAYUN KABB	LATE ABDUS SOBHAN MOLLAH	MST HALIMA BEGUM	Golkandol	05/2018-2019	2436	Null	0.29000	0	0	0	0	0	0	189	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	18978	17367	স্বাক্ষর									
379	12073116498	29/GA	MD SHAHIN MOLLA	LATE ABDUS SOBHAN MOLLA	MST HALIMA BEGUM	Golkandol	05/2018-2019	2436	Null	0.29000	0	0	0	0	0	0	189	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	18978	17367	স্বাক্ষর									
380	12073116495	29/GA	MD IBRAHIM MOLLA	LATE ABDUS SOBHAN MOLLA	MST HALIMA BEGUM	Golkandol	05/2018-2019	2436	Null	0.29000	0	0	0	0	0	0	189	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	18978	17367	স্বাক্ষর									
381	12093216489	9/DA	MD KAMAL HOSEIN	LATE NOWAR ALI	SAHER BANU	Gandharbar (Section 3)	10/2018-2019	874	Null	0.80000	0	0	0	0	0	0	34110	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	39000	10840	স্বাক্ষর									
		9/DA				Gandharbar (Section 3)	10/2018-2019	874	Doba	0.11130	14110																																					
382	12093216490	9/DA	AYMAN BEGUM	ROBULLAH MIA	SAHERA BEGUM	Gandharbar (Section 3)	10/2018-2019	874	Null	0.40000	0	0	0	0	0	0	7061	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	23592	30913	স্বাক্ষর								
		9/DA				Gandharbar (Section 3)	10/2018-2019	874	Doba	0.05560	7061																																					
383	12093216491	9/DA	ZABINA BEGUM	LATE NOWAR ALI	SAHERA BEGUM	Gandharbar (Section 3)	10/2018-2019	874	Null	0.40000	0	0	0	0	0	0	7061	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	23592	30913	স্বাক্ষর								
		9/DA				Gandharbar (Section 3)	10/2018-2019	874	Doba	0.05560	7061																																					
384	12093216492	9/DA	SORIFA	LATE NOWAR ALI	SAHER BANU	Gandharbar (Section 3)	10/2018-2019	874	Null	0.40000	0	0	0	0	0	0	7061	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	23592	30913	স্বাক্ষর								
		9/DA				Gandharbar (Section 3)	10/2018-2019	874	Doba	0.05560	7061																																					
385	12093216494	9/DA	ROKIANA AKTER	LATE NOWAR ALI	SAHER BANU	Gandharbar (Section 3)	10/2018-2019	874	Null	0.49000	0	0	0	0	0	0	7049	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	23588	30916	স্বাক্ষর								
		9/DA				Gandharbar (Section 3)	10/2018-2019	874	Doba	0.05550	7049																																					
386	12093216493	9/DA	MST AFSANA BEGUM	LATE NOWAR ALI	MST SAHARA BAN	Gandharbar (Section 3)	10/2018-2019	874	Null	0.40000	0	0	0	0	0	0	7049	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	23588	30916	স্বাক্ষর								
		9/DA				Gandharbar (Section 3)	10/2018-2019	874	Doba	0.05550	7049																																					
387	12073216332	91/GHA	SHAFALI BISWAS	NORCHOR BISWAS	MERCDA BISWAS	Golkandol	05/2018-2019	2930	Homesite	6.50000	0	0	0	0	0	0	4500	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	72000	1025000	8745	11860	6000	0	0	0	1108805	1108805	স্বাক্ষর
		58/KA						2930	Structure	0	0.00000																																					
		36/KA						2930	Tree	0	0.00000																																					
388	12093216538	24/KA				Gandharbar (Section 3)	10/2018-2019	931	VH	12.50000	0	0	0	0	0	0	19500	0	2111	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	2762038	2762038	স্বাক্ষর							
		25/DA				Gandharbar (Section 3)	10/2018-2019	932	VH	11.50000	0																																					
		32/DA	MOHRI HOSSEIN	LATE NURU MIA	SORIFA BEGUM	Gandharbar (Section 3)	10/2018-2019	979	VH	7.50000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0							
		32/DA				Gandharbar (Section 3)	10/2018-2019	979	Pond	5.00000	0																																					
		1/CA				Nowagon	10/2018-2019	79	Null	3.25000	0																																					

SI No	ID No.	Award Book No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plet No.	Land Type	Land Affected (Decimals)	Additional Grant for Land (AGL)	AL	HL	WB	CPS	GT	SC	TP	CES LL	BS	BS	SS	CPR MF	AEE	BR	LIP	VH	RA	BRIC	STG	SRG	CGRU C	SGT	BAR O	LUJ	Total Amount	Payable Amount	Remarks						
Col1	Col2	Col3	Col4	Col5	Col6	Col7	Col8	Col9	Col10	Col11	Col12	Col13	Col14	Col15	Col16	Col17	Col18	Col19	Col20	Col21	Col22	Col23	Col24	Col25	Col26	Col27	Col28	Col29	Col30	Col31	Col32	Col33	Col34	Col35	Col36	Col37	Col38							
461	12083116609	14/KHA	MD. DALAL ARAH	MD ABUL HOSEN	MST MOJIBUL BEGUM	Vulta	10/2018-19	906	Nall	0.85000	0	0	0	0	0	0	553	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	55675	55675	50/10/19					
462	12083116608	14/GA 15/KHA 3/KA	MD SALIM	SIDDIQUE RAHMAN	MST DANA KHATUN	Vulta	10/2018-19	906	Nall	0.28900	0	0	0	0	0	0	182	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	203003	203003	Salim					
						Vulta	10/2018-19	864	Doba	0.50000	68937	0	0	0	0	0	182	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	203003	203003	Salim					
463	12083116562	17/LMD 20/LMD	MUR HOSSAIN PRODHAN	ABDUL GOFUR	AMENA KHATUN	Gandharbar (Section 3)	10/2018-19	913	Homestead	0.75000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	129980	129980	20/12/19					
						Gandharbar (Section 3)	10/2018-19	917	Wi	0.34000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	129980	129980	20/12/19					
464	12073116616	12/KHA	MOHAMMED MOAZEM HOSSAN BHUIA	MOHAMMED MUSA MIA SHUBA	BIBI RAHMA BEGUM	Dorikandi	05/2018-19	2026	Nall	3.75000	0	0	0	0	0	0	2438	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	88257	176514	Power AP				
465	12073116617	12/KHA	YESMIN AKTER	MOSTAN CHAR BILLAH	MAHFUJAH BEGUM	Dorikandi	05/2018-19	2026	Nall	3.75000	0	0	0	0	0	0	2438	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	88257	176514	Power AP			
466	12083116614	2/GA	ASHIK HOSSAIN	AKTER HOSSAIN	REHENA AKTER	Gandharbar (Section 3)	10/2018-19	856	Wi	0.25000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	18635	37270	Power AP				
467	12083116615	2/GA	AKSANA YASMIN DAYNA	MD AKTER HOSSAIN PRODHAN	REHENA AKTER	Gandharbar (Section 3)	10/2018-19	856	Wi	0.25000	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	18635	37270	Power AP				
468	12073116605	34/KA 13	MD. ABUL HASHEM OM BEHALF OF HASHEM FOODS LIMITED	MD IBRAHIM MIA	SEMINA KHATUN	Golokandi	05/2018-19	2450	Wi	3.00000	71049	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	238574	238574	Power AP			
						Golokandi	2450	2450	Structure	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	238574	238574	Power AP			
469	12073116314	38/GA	ASRAFUL	ABDUL BAGHD	LOTIFA	Dorikandi	05/2018-19	2243	Nall	6.87500	0	0	0	0	0	0	4469	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	163805	163805	Power AP			
470	12083116541	34/KHA 36/KHA	TARIKUL ISLAM	LATE DENGU MIA	LATE MURJUN HESA	Vulta	10/2018-19	983	Nall	5.50000	0	0	0	0	0	0	7475	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	753255	753255	Power AP			
						Vulta	10/2018-19	985	Nall	6.00000	0	0	0	0	0	0	7475	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	753255	753255	Power AP		
471	12073116183	28/GHA	MD AMIR HOSSAIN	MD TOMIZ UDDM	BANU BIBI	Dorikandi	05/2018-19	2049	Nall	5.33000	0	0	0	0	0	0	3465	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	125443	125443	Power AP			
Total Amount:										38.92500	138986	0	70349	68937	3450	0	21038	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1881917	1881917	

Agricultural Land (AL), Residential Land (RL), Water Bodies (Canals & Non-irrigated) (WB), Current Fish Stock (CFS), Grant for Trees (GT), Shrub/Crop (SC), Tree Plantation (TP), Cash Grant (CG) and non-Cash (NCG), Livestock and Janors of agricultural land (LJ), Residential structure (RS), Business structure (BS), Secondary structure (SS), Physical Cultural Resources (PCR) / Common Property Resources (CPR) Management Fund (CPMF), Affected Employees' Wage Sectors (AWE), Business Rehabilitation (BR), Land/road improvement Program (LIP), Suburban households (SH), Rehabilitation scheme (RS), Relief of Registration Cost (Stamp Duty) (RC), Structure Transfer Grant (STG), Structure Reconstruction Grant (SRG), New Utilities Connection (CGUC), Shading Grant for Tenant (SGT), Rental assistance for both residential and commercial structures of the Rentee-Out (RO) (BAR), Unforeseen Adverse Impact (UAI)

11.5 Appendix: Monitoring Result of CCL unpaid Affected Persons in Section 1 and 2**Section-1****Date: 30-06-2023**

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
01	Anowara	Sombupura	131	4	Yes	Paper Submitted to DC's Office For CCL.	No	Paper Submitted to DC's Office For CCL.

Section-2

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
1.	Mosle Uddin	Choitonkanda	2815	4	Yes	Paper Submitted to DC's Office for CCL.	No	Paper submitted to DC's Office for CCL
2.	Motaleb	Choitonkanda	2815	2	Yes	Do	No	
3.	Shohel	Choitonkanda	2818	2	Yes	Do	No	Shohel is unable to submit all his documents as he is abroad.

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
4.	Md. Helal Uddin	Atabdi	176	4	Yes	Do	No	Paper submitted to DC's Office for CCL.
5.	Suruji Mia	Verarkur	120, 121	4	No	Mutation Problem	No	Due to mutation problem unable to receive CCL payment.
6.	Md. Bakul	Bazinaband	14	4	No	Mutation Problem	No	Due to mutation problem unable to receive CCL payment.
7.	Shahidullah	Hazishahadi	310,312	2	No	Do	No	They have no valid land documents.
8.	Name	Hazishahadi	310,312	4	Yes	Do	No	
9.	Jakir Hossain	Hazishahadi	310,312	4	Yes	Do	No	
10.	Md. Lutfor Rahman Vuiya	Hazishahadi	313	4	Yes	Do	No	Dulal submitted papers to the DC's Office for CCL.
11.	Dulal	Hazishahadi	409, 410	4	Yes	Paper Submitted to DC Office For CCL	No	
12.	Abul Kalam	Hazishahadi	444	4	Yes	Do	No	There is an RS record in favour of one Hindu person. But the land is under government ownership. So, the case is ongoing.
13.	High School- Adv. Rashid	Lengurdi	237	4	Yes	Mutation Problem	No	The mutation will be completed soon.
14.	High School	Lengurdi	330	4	Yes	Do	No	

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
15.	High School- Adv. Rashid	Lengurdi	331	4	Yes	Do	No	
16.	Labu	Lengurdi	350	4	No	Do	No	Raja Mia has expired. Share certificate not done.
17.	Raja Mia	Lengurdi	350	4	Yes	Do	No	
18.	Moulovi Abu Hanifa	Lengurdi	351	4	Yes	Do	No	Paper Submitted to DC office for CCL.
19.	Safaz Uddin	Laxmipur	19	4	Yes	Do	No	Paper Submitted to DC office for CCL (He got IGA training at the advice of ADB)
20.	Abdur Rahim	Kumarbag	12	4	Yes	Mutation Problem	No	He has no proper valid documents for mutation.
21.	Momtaj Uddin	Idbardi	81	4	Yes	Do	No	Submitted Papers to DC's Office For CCL.
22.	Abu Talek	Baliapara	610	4	Yes	Do	No	He has a small quantity of land. DC office is not interested to handle his file. File submitted to dc's office.
23.	Halima Begum	Baliapara	673	4	Yes	Do	No	Submitted Paper to DC's Office For CCL.
24.	Mukti Sikder	Baliapara	105	4	Yes	Do	No	There is a conflict between ownership. This was a Hindu property. The identified affected person Mukti Sikder claimed property ownership. But he has

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
								no land documents in favor of his claim. So, he cannot do mutation from the land office.
25.	Md. Kamal Uddin	Aguandi	150	4	Yes	Do	No	Papers Submitted to DC Office For CCL.
26	Nosu Mia	Idbardi	480	4	Yes	Do	No	Document submitted to DC's office earlier but aa it is a small quantity of land DCc office not interested to handle this file.
27.	Soliman	Idbardi	480	4	Yes	Do	No	
28	Jomiruddin	Idbardi	480	4	Yes	Do	No	
29.	Mohiuddin Bhuiyan	Idbardi	633	4	Yes	Do	No	He was not interested to submit papers for CCL because small amount of land. But NGO motivated him to receive money. Finally, he agreed to submit papers for ccl which is not yet done.
30.	Tara Mia	Kahindi	379, 380	4	No	Court Case Is Ongoing	No	Expired. Part of the land is vested property, so the court case is ongoing. (But NGO has no evidence about vested property.)
31.	Md. Kashem	Kahindi	491	4	No	Submitted Papers to DC's office.	No	There are 6 brothers of which 4 brothers are living abroad. share distribution problems. They are all unable to meet together to
32.	Md. Unush Ali	Kahindi	491	4	No	Do	No	

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
33.	Md. Hanif	Kahindi	491	4	No	Do	No	come to a solution but they have submitted papers to the DC's office for ccl.
34.	Md. Shajahan	Kahindi	491	4	No	Do	No	
35.	Md. Al- Amin	Kahindi	491	4	No	Do	No	
36.	Md. Shohel	Kahindi	491	4	No	Do	No	
37.	Md. Shamsulhaquebhuiyan	Atabdi	45.46	4	No	Do	No	Court Case Pending.
38.	Jahirulhaquebhuiyan	Atabdi	45,46	4	No	Do	No	Court Case Pending.
39.	Md. Shamsulhaquebhuiyan	Atabdi	45.46	4	No	Do	No	Court Case Pending.
40.	Jahirulhaquebhuiyan	Atabdi	45,46	4	No	Do	No	Court Case Pending.
41.	EID Ga- Adv. Omorfaruk	Lengurdi	111	4	No	Do	No	He got ownership from court and submitted papers to the DC's office for CCL.
42.	Sombhu Kanto Das	Aguandi	368	4	No	Do	No	A small amount of land. So, he is not interested to go DC's office.
43.	Abdul Azij	Idbardi	26, 27	4	No	Do	No	Court case almost going to be solved.
44.	Abdul Awaul	Idbardi	26, 28	4	No	Do	No	
45.	Amir Hossain	Idbardi	26, 29	4	No	Do	No	
46.	Rupban	Idbardi	26, 30	4	No	Do	No	
47.	Safia	Idbardi	26, 31	4	No	Do	No	
48.	Rubi	Idbardi	26, 32	4	No	Do	No	

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
49	Saenta	Idbardi	26, 33	4	No	Do	No	
50.	Md. Asadsikder	Baliapara	80	4	No	Do	No	Court Case ongoing
51.	Most.Mazeda Begum	Baliapara	80	4	No	Do	No	
52.	Md. Sagor Hossain Molla	Baliapara	80	4	No	Do	No	
53	Hamidulhaque	Kamaldi	2053	4	No	Submitted papers to the DC's office for CCL.	No	Submitted papers to the DC's office for CCL.
54.	Ala- Uddin(Late)	Kamaldi	2115	4	No	Do	No	Land listed as Khas Khotian which means government owns the land. AP named Ataur Rahman claimed himself owner of this land. But he does not have proper legal document to get the mutation of the land.
55	Ataur Rahman(Din Mohmmed)	Kamaldi	2161	4	No	Do	No	
56.	Abulkalam	Kadirdia	410	4	No	Do	No	RS Record Problem.
57.	Md. Babul Molla	Ranidi	22	4	No	Do	No	The amount of land is small so not Interested in mutation.
58.	Abed Ali	Sreepoti	25	4	No	Do	No	The amount of land is small so not Interested to go the DC

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
								office. After motivation, he agreed to submit papers to the DC office.
59.	Begum Samsunnaharkhond okar	Parashilmandi	314	4	No	Do	No	She has expired. Her heir lives abroad.
60.	Siddikur Rahman	Bazinaband	15	4	No	Do	No	(Expired)His son lives abroad. Mutation Problem.
61.	Tara Mia	Hazishahadi	314	4	No	Do	No	Submitted paper to the land office for mutation but there is a problem of ownership.
62.	Bokul Mia	Hazishahadi	314	4	No	Do	No	Ownership problem so could not do mutation.
63.	Md. Kashem	Hazishahadi	315	4	No	Do	No	Lack of proper documents, cannot do mutation.
64.	Md. Hashem	Hazishahadi	315	4	No	Do	No	Lack of proper documents, cannot do mutation.
65.	Md. Selim	Hazishahadi	315	4	No	Do	No	
66.	Md. Monir	Hazishahadi	316, 445	4	No	Do	No	Due to lack of proper documentation, the mutation is not done. Md. Monir is not the owner Mojibur is the owner.
67.	Lal Mia	Hazishahadi	427	4	No	Do	No	Ownership problem. Small amount, so they are not
68.	Sona Mia	Hazishahadi	427	4	No	Do	No	
69.	Golesha Begum	Hazishahadi	427	4	No	Do	No	

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
								interested in submitting papers for CCL.
70.	Komol Mia	Lengurdi	350	4	No	Do	No	Co-owners live aboard, so he cannot withdraw money from the DC office.
71.	Abu Taleb	Lengurdi	351	4	No	Do	No	Papers were submitted to the DC office. Due to small quantity of land, DC office is delaying.
72.	Most. Hosneara Begum	Lengurdi	416	4	No	Do	No	Mutation is not done.
73.	Abulhasemmolla	Idbardi	747	4	No	Do	No	Mutation problem. He lives in Dhaka.
74.	Md. Al Amin	Baliapara	80	4	No	Do	No	Court Case Ongoing.
75.	Hazera	Baliapara	80	4	No	Do	No	
76.	Yanus Miah	Baliapara	669	4	No	Do	No	Document submitted to DC's office for CCL.
77.	Doly Akhter	Kamaldi	2214	4	No	Vested Property	No	Vested Property.
78.	Asis Kumar Dey	Bijoynagar	2	4	No	Do	No	Vested Property.
79.	Sharafat	Bijoynagar	57	4	No	Do	No	Vested Property.
80.	Firoj Mia	Baliapara	100	4	No	Do	No	Vested Property.
81.	Abdurrouf	Aguandi	232	4	No	Do	No	Due to the small quantity of land and share distribution problems APs are not interested to go to the DC office for CCL payment
82.	Delowar	Aguandi	353	4	No	Do	No	
83.	Md. Ismail	Aguandi	353	4	No	Do	No	
84.	Abdul Wahab	Aguandi	353	4	No	Do	No	

SL. No.	Name of Affected Person	Mouza	Plot No.	Number of Times Contacted within the Reporting Period	Papers Submitted to DC's Office Yes/ No	Status Of the Case for the Reporting Period	Payment Received Yes/No	Current Monitoring Status
85	Joni	Kumarbag	85	4	No	Do	No	
86.	Most. Piara Begum	Kumarbag	85	2	No	Do	No	
87.	Sahina Begum	Kumarbag	85	2	No	Do	No	
88	Md. Romij Uddin	Idbardi	67	4	No	Do	No	Land classification is not proper. So, he is not interested to receive CCL.
89.	Moslem Miah	Idbardi	633	4	No	Do	No	Due to the small quantity of land AP is not interested to go to the DC office for CCL payment
90.	Rahmatullah	Kahindi	506	4	No	Do	No	Due to the small quantity of land AP is not interested to go to the DC office for CCL payment

11.6 Appendix: Monitoring Result of CCL unpaid Affected Persons in part of Section 3 (LA Case 5/2018-19)

Sl No.	Name of Affected Persons	Plot No.	Total Land (Decimal)	Total Land Owned by Affected Persons (In Decimal)	Affected Land (In Percent)	Loss Significant or Insignificant (Significant >10% , Insignificant <10%)	In Case of Significant Loss, AP's Source of Income	Information on Economic Losses	Information on Physical Displacement, If Any	CCL to be Paid by Deputy Commissioner (Due) (Bdt)	Additional Payment Top Up to be Paid by DWASA (Bdt)	Other Resettlement Benefits to be Paid by DWASA (Bdt)	Vulnerable	Plan of Action	Time-Bound	Responsible Person/ Department/ Organization	Reason of Non-Payment
1	Md. Abul Kalam Ga2	1	30	2.25	7.5	Insignificant		Business loss	There Will Be No Physical Displacement	509,287.50	131,962.50	64,125.00		Court Will Determine Ownership.	This is A Legal Process. Timeline Not Certain.	NGO and PMU	Ownership Problem, Objection DC Office
2	Mana Ranjan Biswash	2	70	4	7.5714	Insignificant		Do	There Will Be No Physical Displacement	905,400.00	234,600.00	192,500.00	Bgl, Family Member= 3	Do	He Will Get CCL Soon	NGO and PMU	Ownership Problem, Objection DC Office
3	Chitta Ranjan Biswash	2	200	4	8.13	Insignificant		Do	Yes	905,400.00	234,600.00	114,000.00		Do	Do	NGO and PMU	Ownership Problem, Objection DC Office
		1		2.25		Insignificant		Do	Yes	509,287.50	131,962.50	64,125.00		Do	Do	NGO and PMU	Ownership Problem, Objection DC Office
4	Md. Rashed Mia	1	30	2.25	7.5	Insignificant		Do	There Will Be No Physical Displacement	339,525.00	54,225.00	39,375.00		Do	Do	NGO and PMU	Ownership Problem, Objection DC Office
5	Md. Rony Hossain	1	2.25	2.25	100	Significant	Agriculture	Full Loss Of Agriculture Based Livelihoods	There Will Be No Physical Displacement	339,525.00	54,225.00			Do	Do	NGO and PMU	Ownership Problem, Objection DC Office
6	Abdul Malek	2156		2	9.29	Insignificant		Do	There Will Be No Physical Displacement	457,704.00		45,770.40		Court Will Determine Ownership.		NGO and PMU	Ownership Problem, Objection DC Office
7	Khurshed Alam	2034	800	17.25	7.44	Insignificant		Do	There Will Be No Physical Displacement	3,947,697.00	-	394,769.70		DDRP and PMU will Pursue and Assist AP in Arranging Papers	He Will Get Soon.	NGO and PMU	Waiting for Hearing By DC, Submitted Documents for CCL
		2045		11.5		Insignificant		Do	There Will Be No Physical Displacement	2,631,798.00	-	263,179.80		Do	He Will Get Soon.	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL
8	Md. Habibur Rahman	2010		1	0.8	Insignificant		Do	There Will Be No Physical Displacement	228,852.00	-	22,885.20		Do	He Will Get Soon.	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL
9	Golam Maola Bhuyan	2014		1	7.5	Insignificant		Do	There Will Be No Physical Displacement	343,278.00	-	34,327.80		Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents for CCL
10	Abdur Rashid	2025	250	17	8.8	Insignificant		Do	There Will Be No Physical Displacement	3,890,484.00	-	448,048.40	Elderly Headed Household Family Member= 2	Do	This is Legal Procees	NGO and PMU	Ownership Problem, Objection DC Office
11	Hari Chandra Shil	2054	60	5	8.3333	Insignificant		Do	There Will Be No Physical Displacement	1,144,260.00		114,426.00		Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL
12	Md. Aminul Islam	2806	50	1	2	Insignificant		Do	There Will Be No Physical Displacement	1,547,538.00	-	154,753.80		Court will Decide Ownership	Court Will Determine Ownership Time is Not Certain	NGO and PMU	Ownership Problem, Objection DC Office
13	Joyal Gong	2901		0.5	6.67	Insignificant		Do	There Will Be No Physical Displacement	292,729.50	-	29,272.95		DDRP and PMU will Pursue and Assist AP in Arranging	He Will Get Soon.	NGO and PMU	There is No Proper Document. He Lives in Dhaka.

14	Tio Nando-Monkara	2388		-0.75	6.20	Insignificant	Do	There Will Be No Physical Displacement	439,094.25	-	43,909.43	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
		2451		4.25		Insignificant	Do	There Will Be No Physical Displacement	2,488,200.75	-	248,820.08	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
15	Mr. Sharouf Rahman	2817	80	1.5	3	Insignificant	Do	There Will Be No Physical Displacement	878,188.00	-	87,818.80	Court Will Determine Ownership	Do	NGO and PMU	Ownership Problem, Objection DC Office	
16	Mr. Bilal Hossain	2817	20	1.5	7.0	Insignificant	Do	There Will Be No Physical Displacement	2,321,307.00	-	232,130.70	Court Will Determine Ownership	Court Will Determine Ownership	NGO and PMU	Ownership Problem, Objection DC Office	
17	Salam Miah	2064	120	9	7.0	Insignificant	Do	There Will Be No Physical Displacement	5,269,131.00	-	526,913.10	Do	Do	NGO and PMU	Ownership Problem, Objection DC Office	
18	Hazi Al Mamun	2064	150	9	6	Insignificant	Do	There Will Be No Physical Displacement	5,269,131.00	-	526,913.10	Do	Do	NGO and PMU	Ownership Problem, Objection DC Office	
19	Rafiq Mubir	2932	80	1	1.1111	Insignificant	Do	There Will Be No Physical Displacement	585,545.00	-	58,545.50	DCRP and PMU will Pursue and Assist AP in Arranging Papers	He Will Get CCL Soon	NGO and PMU	Mutation Problem, Misc. Case Ongoing	
20	Mr. Rafiquddin Miah	2932	155	1	1.98	Insignificant	Do	There Will Be No Physical Displacement	1,547,738.00	-	154,753.80	Do	He Will Get CCL Soon	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
		2933		1		Insignificant	Do	There Will Be No Physical Displacement	1,547,738.00	-	154,753.80	Court will Determine Ownership	Legal Process, Timeline is Not Certain	NGO and PMU	Ownership Problem, Objection DC Office	
21	Joyrat	2901	80	0.5	2	Insignificant	Do	There Will Be No Physical Displacement	292,729.50	-	29,272.95	DCRP and PMU will Pursue and Assist AP in Arranging Papers	He will Get CCL Soon	NGO and PMU	There is No Proper Document, He Lives in Dhaka	
		2902		0.5		Insignificant	Do	There Will Be No Physical Displacement	292,729.50	-	29,272.95	DCRP and PMU will Pursue and Assist AP in Arranging Papers	Do	NGO and PMU	There is No Proper Document, He Lives in Dhaka	
22	Mr. Hany	2064	120	10.25	8.5417	Insignificant	Do	There Will Be No Physical Displacement	6,000,964.75	-	600,096.48	Court will Determine Ownership	This is Legal Process	NGO and PMU	Ownership Problem, Objection DC Office	
23	Nando = Islam Group	2432		9.8	7.3	Insignificant	Do	There Will Be No Physical Displacement	5,561,860.50	-	556,186.05	DCRP and PMU will Pursue and Assist AP in Arranging Papers	He will Get CCL Soon	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
		2431		20		Insignificant	Do	There Will Be No Physical Displacement	14,036,473.00	-	1,403,647.50	Court Will Determine Ownership	This is a legal issue	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
24	Islam Group = Ferdousy Begum	2434	25000	12	0.00	Insignificant	Do	Yes	7,025,508.00	-	702,550.80	DCRP and PMU will Pursue and Assist AP in Arranging Papers	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
		2451		3		Insignificant	Do	There Will Be No Physical Displacement	1,796,377.00	-	179,637.70	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
25	Hazi Islam Uddin	2433	600	5.5	7.71	Insignificant	Do	There Will Be No Physical Displacement	8,511,459.00	-	851,145.90	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
		2434		13		Insignificant	Do	There Will Be No Physical Displacement	7,610,967.00	-	761,096.70	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
		2435		13		Insignificant	Do	There Will Be No Physical Displacement	7,610,967.00	-	761,096.70	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
26	Biyas Osman	2432		0.5		Insignificant	Do	There Will Be No Physical Displacement	5,561,860.50	-	556,186.05	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL	
		2010		2		Insignificant	Do	There Will Be No Physical Displacement	457,704.00	-	45,770.40	Do	Do	NGO and PMU	Waiting For Hearing By DC, Submitted Documents For CCL	
27	Mr. Kasol Neher Begum	2037	200	11.0	0.75	Insignificant	Do	There Will Be No Physical Displacement	2,631,708.00	-	261,170.80	Female Headed Family Member -4	Do	Do	NGO and PMU	Waiting for Hearing By DC, Submitted Documents For CCL

11.7 Appendix: Monitoring Result of CCL unpaid Affected Persons in part of Section 3 and part of Section5 (LA Case 10/2018-19)

Sl.No	Reference No	Name	Misc Name	Plot No.	Total Land (Decimal)	Total Land Owned by Affected Persons (In Decimal)	Affected Land (In Percent)	In Case of Significant Loss, AP's Source of Income	Information on Economic Losses	Information on Physical Displacement, if Any	CCL to be Paid by Deputy Commissioner (Dot) (Bdt)	Additional Payment/Top Up to be Paid By DWA SA (Bdt)	Other Resettlement Benefits to be Paid By DWA SA (Bdt)	Vulnerable	Plan of Action	Time-Bound	Responsible Person/ Department/ Organization	Reason of Non-Payment	
1	41.12.302044	Sultanuddin	Gandharapur	872	150	0.50000	0.67		Partial loss	There Will Be No Physical Displacement	621168	0	62117		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
2	41.12.301603	MD. JASHUDDIN SHUPAN	Gandharapur	872	130	0.50000	1.67		Partial loss	There Will Be No Physical Displacement	1555159	0	155516		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
			Nirwagan	300															1.17000
3	41.12.301658	Md. Javed Ali Pradhan	Gandharapur	900	155	11.00000	8.55		Partial loss	There Will Be No Physical Displacement	10039000	0	1003900		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
			Gandharapur	916															0.25000
4	41.12.301686	Moin Hossain	Gandharapur	926	540	5.50000	9.40		Partial loss	There Will Be No Physical Displacement	4904217	0	490422		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
			Nirwagan	80															36.00000
			Nirwagan	84															7.00000
			Nirwagan	88															19.25000
5	41.12.331589	ABUSOQUIR RAHMAN BHUNAN	Ramgaj	557	60	2.00000	3.33		Partial loss	There Will Be No Physical Displacement	948840	0	94885		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
6	41.12.331595	MD. MENBUL HOSSAIN	Ramgaj	557	60	1.00000	5.00		Partial loss	There Will Be No Physical Displacement	1423269	0	142327		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
7	41.12.331586	MST. SURYA BEGUM	Ramgaj	557	60	2.00000	3.33		Partial loss	There Will Be No Physical Displacement	948840	0	94885		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
8	41.12.331587	RIHANOR ISLAM TURAG	Ramgaj	557	60	3.00000	5.00		Partial loss	There Will Be No Physical Displacement	1423269	0	142327		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
9	41.12.331588	MD. ALI MOOR ISLAM BHUNAN	Ramgaj	557	60	2.00000	3.33		Partial loss	There Will Be No Physical Displacement	948840	0	94885		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
10	41.12.331595	AMFahaduddin	Ramgaj	558	60	3.00000	3.33		Partial loss	There Will Be No Physical Displacement	948840	0	94885		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
11	41.12.311579	Aysha Akter	Ramgaj	573	60	0.35000	0.58		Partial loss	There Will Be No Physical Displacement	160048	0	16005		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
12	41.12.311580	Saman Bhuiyan	Ramgaj	573	60	0.35000	0.58		Partial loss	There Will Be No Physical Displacement	160048	0	16005		DORP and PMU will pursue and assist AP in arranging papers	He will get soon	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	

13	411231598	MD. JAKIR HOSSAIN SARKER	Kornogup	573	60	0.40000	0.67		Partial loss	There Will Be No Physical Displacement	189769	0	18977		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
14	411231584	Md.Zobayer Alam Bhuiyan	Kornogup	573	40	0.35000	0.88		Partial loss	There Will Be No Physical Displacement	166048	0	16605		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
15	4212311581	Afsana Akter Runa	Kornogup	573	40	0.35000	0.88		Partial loss	There Will Be No Physical Displacement	166048	0	16605		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
16	4112311583	Sultan Ahmed Bhuiyan	Kornogup	573	40	0.35000	0.88		Partial loss	There Will Be No Physical Displacement	166048	0	16605		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
17	4112311582	Sakil Bhuiyan	Kornogup	573	50	0.35000	0.70		Partial loss	There Will Be No Physical Displacement	166048	0	16605		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
18	4112331597	MD. SALIM BHUYAN	Kornogup	594	100	8.25000	8.25		Partial loss	There Will Be No Physical Displacement	3913990	0	391399		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
19	4112351620	Jitu Mia	Nowagaon	73	90	1.75000	1.94		Partial loss	There Will Be No Physical Displacement	818165	0	81817		Abroad		NGO and PMU	Live in abroad.
20	4112351619	Sahab Uddin	Nowagaon	73	40	1.75000	4.38		Partial loss	There Will Be No Physical Displacement	818165	0	81817		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
21	4212351601	NAZMA BEGUM	Nowagaon	100	86	6.75000	7.85		Partial loss	There Will Be No Physical Displacement	6366398	0	715140	FHH, Family Member = 3	DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
22	4112351603	SOHEL BHUYAN	Nowagaon	100	19	1.17000	6.16		Partial loss	There Will Be No Physical Displacement	547002	0	54700		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
23	4112351604	OASIM BHUYAN	Nowagaon	100	67	1.16000	1.73		Partial loss	There Will Be No Physical Displacement	542327	0	54233		DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
24	4112352007	Abdul Kader	Nowagaon	100	97	0.75000	0.77		Partial loss	There Will Be No Physical Displacement	350642	0	133064	8pl, Family Member = 4	DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
25	4112351624	Md.Anowar Hossain	Nowagaon	103	60	1.80000	3.00		Partial loss	There Will Be No Physical Displacement	841541	0	84154		Court will Decide	This is a legal proces	NGO and PMU	Court case ongoing.
26	4112351614	Md.Sharif Mia	Nowagaon	146		2.50000			Partial loss	There Will Be No Physical Displacement	5266134	0	526613		Court will Decide	Do	NGO and PMU	Court case ongoing.
			Nowagaon	103	180	1.30000	3.99	There Will Be No Physical Displacement		Court will Decide					Do	NGO and PMU	Court case ongoing.	
			Nowagaon	144		3.39000		There Will Be No Physical Displacement		Court will Decide					Do	NGO and PMU	Court case ongoing.	
27	4212351618	Fatema	Nowagaon	103	60	1.50000	2.50		Partial loss	There Will Be No Physical Displacement	701285	0	70128		Court will Decide	Do	NGO and PMU	Court case ongoing.
28	4112351606	MOHAMMAD SIRAZUL ISLAM	Nowagaon	103	60	1.00000	1.67		Partial loss	There Will Be No Physical Displacement	467523	0	46752		Court will Decide	Do	NGO and PMU	Court case ongoing.

29	4112351615	Md.Rufik Mia	Nowagaon	103	180	1.30000	3.99	Partial loss	There Will Be No Physical Displacement	5266134	0	526613	Court will Decide	Do	NGO and PMU	Court case ongoing.	
			Nowagaon	144		3.39000			There Will Be No Physical Displacement				Court will Decide	Do	NGO and PMU	Court case ongoing.	
			Nowagaon	146		2.50000			There Will Be No Physical Displacement				Court will Decide	Do	NGO and PMU	Court case ongoing.	
30	4112302028	Abdul Mojid	Nowagaon	103	60	1.30000	2.17	Partial loss	There Will Be No Physical Displacement	607780	0	60778	Court will Decide	Do	NGO and PMU	Court case ongoing.	
31	4112351637	Md.Tara Mia	Nowagaon	103	180	1.30000	3.99	Partial loss	There Will Be No Physical Displacement	5266134	0	566113	Bpl, Family Member = 1	Court will Decide	Do	NGO and PMU	Court case ongoing.
			Nowagaon	144		3.39000			There Will Be No Physical Displacement					Court will Decide	Do	NGO and PMU	Court case ongoing.
			Nowagaon	146		2.50000			There Will Be No Physical Displacement					Court will Decide	Do	NGO and PMU	Court case ongoing.
32	4112351613	Mohammad Sabuj Mia	Nowagaon	144	220	2.00000	5.23	Partial loss	There Will Be No Physical Displacement	10128921	0	1012892	Court will Decide	Do	NGO and PMU	Court case ongoing.	
			Nowagaon	145		9.50000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
33	4112351625	Mohammad Farid Mia	Nowagaon	146	120	2.50000	5.33	Partial loss	There Will Be No Physical Displacement	5139371	0	513937	Court will Decide	This is a legal proces	NGO and PMU	Court case ongoing.	
			Nowagaon	144		3.90000			There Will Be No Physical Displacement				Court will Decide	Do	NGO and PMU	Court case ongoing.	
34	4212351610	Nasima Begum	Nowagaon	144	120	3.51000	5.01	Partial loss	There Will Be No Physical Displacement	4479334	0	565433	FHH, Family Member = 5	Court will Decide	Do	NGO and PMU	Court case ongoing.
			Nowagaon	146		2.50000			There Will Be No Physical Displacement					Court will Decide	Do	NGO and PMU	Court case ongoing.
35	4212351612	Rahima	Nowagaon	144	120	3.03000	4.61	Partial loss	There Will Be No Physical Displacement	4318813	0	431881	Court will Decide	Do	NGO and PMU	Court case ongoing.	
			Nowagaon	146		2.50000			There Will Be No Physical Displacement				Court will Decide	Do	NGO and PMU	Court case ongoing.	
36	4112352009	Md.Rasel Hossain	Nowagaon	144	60	1.25000	2.08	Partial loss	There Will Be No Physical Displacement	584404	0	58440	Court will Decide	Do	NGO and PMU	Court case ongoing.	
37	4212351616	Mst.Hena Begum	Nowagaon	144	100	1.00000	4.00	Partial loss	There Will Be No Physical Displacement	3297033	0	427703	Bpl, Family Member = 4	Court will Decide	Do	NGO and PMU	Court case ongoing.
			Nowagaon	146		3.00000			There Will Be No Physical Displacement					Court will Decide	Do	NGO and PMU	Court case ongoing.
38	4212351626	Hasina Begum	Nowagaon	144	80	1.00000	1.25	Partial loss	There Will Be No Physical Displacement	467523	0	164252	Bpl, Family Member = 5	Court will Decide	Do	NGO and PMU	Court case ongoing.
39	4123352003	Munsi Sabiruzzaman	Nowagaon	144	70	2.39000	3.41	Partial loss	There Will Be No Physical Displacement	1396723	0	139672	Court will Decide	Do	NGO and PMU	Court case ongoing.	
40	4112351608	Aynal Hoque	Nowagaon	146	60	2.50000	4.17	Partial loss	There Will Be No Physical Displacement	1461008	0	146101	Court will Decide	Do	NGO and PMU	Court case ongoing.	
41	4112352078	Baytul Noor Jame. Mosjid	Nowagaon	238	40	3.16000	7.90	Partial loss	There Will Be No Physical Displacement	2980417	0	298042	DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	

42	4112311569	Kazi Muktesur Rahaman	Vulta	791	55	1.00000	5.45	Partial loss	There Will Be No Physical Displacement	1945512	0	194551	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	867		2.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
43	4112311571	Kazi Ferdous	Vulta	871	160	2.00000	3.59	Partial loss	There Will Be No Physical Displacement	372898	0	372890	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	791		1.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	867		2.75000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
44	4112311568	Kazi Abul Kashem	Vulta	791	360	0.75000	2.22	Partial loss	There Will Be No Physical Displacement	8393292	0	839329	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	792		0.50000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	867		3.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	870		0.25000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	872		0.50000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
45	4112311570	Kazi Mizanur Rahman	Vulta	791	180	1.00000	3.33	Partial loss	There Will Be No Physical Displacement	5493654	0	549365	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	867		2.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	871		3.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
46	4212311677	Moslama begum	Vulta	1281		8.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1282		15.75000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
47	4112311697	Md.Sirajul Islam	Vulta	865	220	4.00000	5.91	Partial loss	There Will Be No Physical Displacement	13485660	2700000	1618566	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	866		9.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
48	4112392057	MD. AKTER HOSSAIN	Gandharbpur	871	60	5.00000	8.33	Partial loss	There Will Be No Physical Displacement	2484675	0	346468	Bpl, Family Member = 4	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
49	4112311576	Abid Mustafizur Rahman	Vulta	872	170	1.00000	9.41	Partial loss	There Will Be No Physical Displacement	12645828	2100000	1474583	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	873		7.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	898		2.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
50	4112311698	Mostafizur Rahman Bhuiyan	Vulta	872	80	0.50000	0.63	Partial loss	There Will Be No Physical Displacement	324252	0	32425		Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.

51	4112311699	Md.Humayon Kabir	Vulta	1055	831	10.00000	7.16	Partial loss	There Will Be No Physical Displacement	56821134	14400000	7122113	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1060		5.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1280		16.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1283		0.50000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1286		6.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1281		8.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1282		14.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
52	4112311574	Md. Anwar Hossain	Vulta	1055	1540	10.00000	6.62	Partial loss	There Will Be No Physical Displacement	99260258	27300000	12656026	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1056		10.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1057		15.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1059		39.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1280		17.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1283		0.50000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1284		2.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1286		6.75000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
53	4112311578	Hazi Akkas Ali Mullah	Vulta	1343	120	2.50000	5.42	Partial loss	There Will Be No Physical Displacement	6352116	0	635212	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Vulta	1344		4.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
54	4112311562	Hazi Islam Uddin	Tetlabo	41	220	0.50000	9.32	Partial loss	There Will Be No Physical Displacement	9689571	4660429	1435000	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Tetlabo	42		20.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
55	4112311563	Eliyas Dewan	Tetlabo	42	260	22.00000	8.46	Partial loss	There Will Be No Physical Displacement	10398564	5001436	1540000	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Shibgonj	8		11.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
56	4112391712	Murapara Pallot High School	Shibgonj	11	880	14.00000	9.43	Partial loss	There Will Be No Physical Displacement	70281246	4418754	7470000	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
			Shibgonj	13		58.00000			There Will Be No Physical Displacement				DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.
57	4112392059	MD.SHAH ALAM	Shibgonj	11	60	5.00000	8.33	Partial loss	4233810	266190	450000	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
58	4112431836	ABDUL KAMAL AZAD	Horina graam	615	40	2.50000	6.25	Partial loss	636503	0	63650	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
59	4112432097	ABDUS SAMAD	Horina graam	734	97	7.00000	7.22	Partial loss	1782207	0	178221	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	

60	4112441828	JALSHIRI ABASON	Horina graam	618	10725	3.00000	0.90	Partial loss	24568997	0	2456900	There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				642		0.75000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				564		11.50000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				565		10.00000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				616		15.00000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				617		4.25000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				619		10.50000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				620		12.50000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				621		4.00000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
61	4112432089	MD AKTER HOSSAIN BHUIYAN	Horina graam	625	80	2.00000	9.38	Partial loss	3494250	7755750	1125000	There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				646		10.50000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				647		9.25000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	He will Submit papers soon	NGO and PMU	Will submit land documents to DC's office soon.	
				648		3.00000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	He will Submit papers soon	NGO and PMU	Will submit land documents to DC's office soon.	
				680		1.00000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	He will Submit papers soon	NGO and PMU	Will submit land documents to DC's office soon.	
				682		3.00000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
				707		5.00000						There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	He will Submit papers soon	NGO and PMU	Will submit land documents to DC's office soon.	
62	4112431832	MD.SIRAIUL HOQUE	Horina graam	734	80	7.50000	9.38	Partial loss	3494250	7755750	1125000	There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	He will get soon.	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
63	4112431831	MOSARAF HOSEN	Horina graam	734	218	15.50000	7.11	Partial loss	7221450	16028550	2325000	There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
64	4212431833	NASIMA	Horina graam	682	60	2.75000	4.58	Partial loss	1281225	2843775	530000	There Will Be No Physical Displacement	DORP and PMU will pursue and assist AP in arranging papers	Do	NGO and PMU	Submitted land documents to DC's office. Waiting for hearing for CCL payment.	
Total						686.16000			480227389	87474884	57534727						

11.8 Appendix: Microfinance Access by Trained Affected Persons in Section 1

Monitoring Month: June 2023,

Name of Upazila: Araidhazar,

Name of District: Narayanganj,

Date: 30/06/2023

SI No.	AP ID No.	Name of the trained Person	Name of Father/Husband	Name of Mouza	Name of Trade	Involved with IGA	Name of NGO/financial institutions	Cell Number
1.	11011110342	Jahanara	Late Nuruzzaman	Sumbupura Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	01833404646
2.	11011110548	Hossain Ali	Late Akkal Ali	Sumbupura Mouza	Cow and Goat Rearing	Yes	SIDOR NGO	01869434557
3.	11011210347	Minara	Late Taijul Islam	Tatea Mouza	Cow and Goat Rearing	Yes	BRAC NGO	01883364216
4.	11011110256	Al Amin	Late Abdul Munaf	Sumbupura Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	01720309661
5.	11011210004	Sorif	Late Rabiul	Sumbupura Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	01949866627
6.	11011110003	Rup Miah	Late Chan Mia	Sumbupura Mouza	Cow and Goat Rearing	Yes	Agrani Bank	01927383428
7.	11011110094	Md. Khaliur	Late HaziNeowaz Ali	Sumbupura Mouza	Cow and Goat Rearing	Yes	SIDOR NGO	01827795267
8.	11011110016	Shohel Miah	Late. Abdul Berek	Sumbupura Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	01726107209
9.	11011112798	Mojibor Rahman	Mongol Miah	Sumbupura Mouza	Cow and Goat Rearing	Yes	ASA NGO	01717920834
10.	11011110091	Jobed Ali	Late Korom Ali	Sumbupura Mouza	Cow and Goat Rearing	Yes	Grameen Bank	01754592743
11.	11011110001	Abdul Aziz	Late Abdul ohab	Sumbupura Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	-
12.	11011110002	Ayesa	Late Abu hanif	Sumbupura Mouza	Cow and Goat Rearing	Yes	SSS NGO	-
13.	11011110103	MdMostafa	Neyas Ali Hazi	Sumbupura Mouza	Cow and Goat Rearing	Yes	ASA NGO	-
14.	11011110008	Sub Mia	Late Mojajffor Ali	Sumbupura Mouza	Cow and Goat Rearing	Yes	Sokti Foundation	-

15.	11011110232	MdharunurRoshed	Late Lal Mia Beparey	Sumbupura Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	-
16.	11011210261	AyesaKhatun	Amir ali	Sumbupura Mouza	Cow and Goat Rearing	Yes	ASA NGO	-
17.	11011110520	Sahidullah	Late.Afil Uddin	Sumbupura Mouza	Chicken and Duck Rearing	Yes	Grameen Bank	01736936794
18.	11011210534	Lakiba	Safikul Islam	Sumbupura Mouza	Chicken and Duck Rearing	Yes	BRAC NGO	01831125520
19.	11011212721	SamsuzzamanLimom	Md. Ismail Mia	Sumbupura Mouza	Chicken and Duck Rearing	Yes	Bangladesh Krishi Bank	01776271440
20.	11011210557	Fatema	Late Sirajul Islam	Sumbupura Mouza	Chicken and Duck Rearing	Yes	Palli Mongal Karmosuchi	01790453308
21.	11011210100	SufiyaKhatun	Late Joj Mia	Sumbupura Mouza	Chicken and Duck Rearing	Yes	Palli Mongal Karmosuchi	01749396835
22.	11011110241	Hosna	Late Kawsar	Sumbupura Mouza	Chicken and Duck Rearing	Yes	ASA NGO	01754451793
23.	11011110239	Roshan Ali	Late.Abdul Rahim	Sumbupura Mouza	Chicken and Duck Rearing	Yes	ASA NGO	017261746283
24.	11011212814	Jahanara Begum	Jamal Uddin	Sumbupura Mouza	Chicken and Duck Rearing	Yes	BRAC NGO	01764350258
25.	1101112747	Kamal Hossen	Mohiuddin	Sumbupura Mouza	Chicken and Duck Rearing	Yes	Bangladesh Krishi Bank	01817014445
26.	11011110099	Rohima Begum	Dulal Hossain	Sumbupura Mouza	Chicken and Duck Rearing	Yes	Grameen Bank	-
27.	11011210093	SamaAkter	Nurul Amin	Sumbupura Mouza	Chicken and Duck Rearing	Yes	SIDOR NGO	-
28.	11011112747	Md. Kamal Hossain	Mohi Uddin	Sumbupura Mouza	Chicken and Duck Rearing	Yes	ASA NGO	01817014446
29.	11011112788	SHOQR MOHAMMAD	Late mortobali	Sumbupura Mouza	Chicken and Duck Rearing	Yes	SIDOR NGO	01728160865
30.	11011210302	MONORA	Sadar Ali	Sumbupura Mouza	Chicken and Duck Rearing	Yes	ASA NGO	01776674381

31.	11011110105	Md Jomir Ali	Late Mekarrom Ali	Sumbupura Mouza	Chicken and Duck Rearing	Yes	ASA NGO	
32.	11011213882	Rahima Begum	Hafijuddin	Sumbupura Mouza	Tailoring	Yes	ASA NGO	01744681787
33.	11011213880	Halima	Iman Ali	Sumbupura Mouza	Tailoring	Yes	Grameen Bank	01770512377
34.	11011113980	Osor Uddin	Late Meher Ali	Sumbupura Mouza	Vegetable Gardening	Yes	Palli Mongal Karmosuchi	-
35.	11011113878	Md Jabed Ali	Late Sona Mia	Sumbupura Mouza	Vegetable Gardening	Yes	Palli Mongal Karmosuchi	-
36.	11011110234	Shon Miah	Late Abdul Aziz	Sumbupura Mouza	Cow and Goat Rearing	Yes	BRAC NGO	-
37.	11011110235	Alamgir Hossain	Late Rafiqul Islam	Sumbupura Mouza	Chick and Duck Rearing	Yes	BRAC Bank	-

11.9 Appendix: Microfinance Access by Trained Affected Persons in Section 2

Monitoring Month June-2023		Name of Upazila: Arai hazar			Name of District: Narayanganj		Date: 30-06-2023	
SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
1	11052210206	Masuda Begum	Nurul Haque	Kamaldi Mouza	Cow and Goat Rearing	Yes	Grameen Bank	1796277834
2	11052213027	Saleha Akter	MdAlauddin	Ranidi Mouza	Cow and Goat Rearing	Yes	BRAC NGO	1902218906
3	11032213218	Fajila	Late Taizuddin	Aguandi Mouza	Cow and Goat Rearing	Yes	Grameen Bank	1779185115
4	11062113679	Dolal Bhuiyan	Late Abdul Ali Bhuiyan	Ibardi Mouza	Cow and Goat Rearing	Yes	BRAC NGO	1812181546
5	11062213811	Monuara Begum	Ayet Ali	Baliapara Mouza	Cow and Goat Rearing	Yes	BRAC NGO	1717838224
6	11032110051	Alomgir Hossain	Abdul Batan	Aguandi Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	1793320529
7	11042213216	Mst Salma	Late Abdul Motaleb	Atadi Mouza	Cow and Goat Rearing	Yes	Palli Mongal Karmosuchi	1845251037
8	11042113137	Bilkis	Jalal	Kardirdia Mouza	Cow and Goat Rearing	Yes	Grameen Bank	1991049392
9	11062110288	Shahjahan Mia	Late Tufani Miah	Baliapar Mouza	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank	1922961602
10	11052110157	Md Babul Miah	Md. RobiulMolla	Atabdi Mouza	Cow and Goat Rearing	Yes	BRAC NGO	1959612627
11	11032110044	Md. Babul Hosun	Late Hazrat Ali	Aguandi Mouza	Cow and Goat Rearing	Yes	ASA NGO	1779629055
12	11032210201	Peyara	Helal Uddin	Halima	Cow and Goat Rearing	Yes	BRAC NGO	1868293441
13	11032111718	Hossain Ali	Late Abdul Aziz	Aguandi	Cow and Goat Rearing	Yes	BRAC NGO	1861998451
14	11052113254	Md Abed Ali	Late AbdurRahamn	Sripoti	Cow and Goat Rearing	Yes	ASA NGO	1736684537

SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
15	11052110154	Md Sohidlla Molla	Late OliullahMolla	Atabdi	Cow and Goat Rearing	Yes	ASA NGO	1822551840
16	11052113075	Md Abdul Baten Molla	Late AzzillaMomlla	Atabdi	Cow and Goat Rearing	Yes	Grameen Bank	1933488642
17	11052113078	Md Mamun	MdNurul Islam	Auguandi Mouza	Cow and Goat Rearing	Yes	ASA NGO	
18	11062113041	Arifur Rahaman	SahajaddinBhuyan	Lenguardi	Cow and Goat Rearing	Yes	Palli Mongal Karmosuchi	
19	11032110058	Md Sojol Mia	Abdul Matin	Laxmipura	Cow and Goat Rearing	Yes	ASA NGO	
20	11032110053	Najarul	Late Aual	Auguandi	Cow and Goat Rearing	Yes	BRAC NGO	
21	11062113759	Firoz Miah	Abdul Kader Prodam	Eibaridi	Cow and Goat Rearing	Yes	Probashi Kollan Bank	
22	11032213249	Fatema	F.Momen	Auguandi Mouza	Tailoring	Yes	Bangladesh Krishi Bank	1989472779
23	11052213241	Joni Akter	H.MdNaym	Tilchandi Mouza	Tailoring	Yes	Grameen Bank	1986794758
24	11052213793	Shirin Shila	H. SalimBhuiyan	Hazishadi Mouza	Tailoring	Yes	ASA NGO	1846790314
25	11062110422	Tanvir	Md Abdul Baten Miah	Idbardi Mouza	Tailoring	Yes	Ektee Bari Ektee Khamar	1766302227
26	11062210430	Sahera	Moba rak Hossain	Idbardi Mouza	Tailoring	Yes	Bangladesh Krishi Bank	1648187942
27	11062110428	Jorina Akter	H. MdEbrahimBhuyain	Idbardi Mouza	Tailoring	Yes	Bangladesh Krishi Bank	1965473381
28	11062113805	Parul Akter	H. Nobi Hossain	Idbardi Mouza	Tailoring	Yes	SIDOR NGO	1940627441
29	11052113219	Israt Jahan	H. Alamin	RanidiMouza	Tailoring	Yes	Palli Mongal Karmosuchi	1929572494
30	11032110055	Sufia Begum	Abdul Aual	AuguandiMouza	Tailoring	Yes	Bangladesh Krishi Bank	1872116871
31	11042213528	Khaleda Akter	H. FazlulHaque	Atadi Mouza	Tailoring	Yes	Grameen Bank	

SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
32	11032213249	Fatema	F. Momen	Aguandhi	Tailoring	Yes	Grameen Bank	1989472779
33	11062113276	Sharmin akter	Kazi Md. Billal	Baliapara	Tailoring	Yes	ASA NGO	
34	11052112889	Amjad Hosan	MdSerajul Islam	Ranidi Mouza	Small Business	Yes	Grameen Bank	1710666871
35	11052113197	Md Montaz Uddin Mollah	Late Jahor Ali Molla	Ranidi Mouza	Small Business	Yes	BRAC NGO	1711220287
36	11062113791	Md Ruhul Amin Molla	Kopil Uddin Molla	Idbardi Mouza	Small Business	Yes	Grameen Bank	1856876374
37	11062110442	Md Jaynal	Abu Siddik	Idbardi Mouza	Small Business	Yes	BRAC NGO	1724793954
38	11062110392	Akter Hosan	Late Nurul Islam	Idbardi Mouza	Small Business	Yes	Bangladesh Krishi Bank	1726197675
39	11062113782	Abdus Salam	MdSerajul Islam	Mouza	Small Business	Yes	ASA NGO	1993519185
40	11062113630	Md Shahabuddin Molla	Late HasibMolla	Idbardi Mouza	Small Business	Yes	Grameen Bank	1929155972
41	11062110514	Ali Ahmmad	Yousof Ali	Idbardi Mouza	Small Business	Yes	BRAC NGO	1948767443
42	11061110107	Md Joynal Abedin	MdTyob Ulla Miah	Idbardi Mouza	Small Business	Yes	Palli Mongal Karmosuchi	1918417018
43	11062113792	Md Tota	Late Aziz Rahaman	Eidbardi	Small Business	Yes	ASA NGO	1956772290
44	11062113677	Md Kobir Sarkar	Easin	Eidbardi	Small Business	Yes	Bangladesh Krishi Bank	1799090666
45	11062110427	Waliulla	Miraj Uddin	Eidbardi	Small Business	Yes	SIDOR NGO	1928363083
46	11062113848	Salem Mia	Late Abdul MalekMia	Eidbardi	Small Business	Yes	Palli Mongal Karmosuchi	1724793953
47	11062112819	Asrafal	Md Osman Molla	Baliapara	Small Business	Yes	Bangladesh Krishi Bank	1720906138
48	11062110280	Joj Mia	Late Tajjuddin	Baliapara	Small Business	Yes	BRAC NGO	1720906138
49	11062113821	Delower	MdShahajoddin	Baliapara	Small Business	Yes	ASA NGO	
50	11062112953	Faruk Hossan	Sona Mia	Baliapara	Small Business	Yes	BURI Bangladesh	
51	11062113775	Shalom	Samsu Mia	Baliapara	Small Business	Yes	GRAMEEN Bank	

SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
52	11062110481	Jobayer Hasan	Ashad Miah	Eidbardi	Small Business	Yes	Bangladesh Krishi Bank	
53	11062110436	Shibli	MdNurul Islam	Eidbardi	Small Business	Yes	ASA NGO	
54	11062110381	Nasim	Md Halim Sarker	Eidbardi	Small Business	Yes	BRAC NGO	
55	11062113710	Babul Miah	Late Alauddin	Eidobardi	Small Business	Yes	Polli Bikas NGO	
56	11062113142	Md Sofiqul Islam	Late Haji SerajolHaque	Kumarabag	Small Business	Yes	Sokti Foundation	
57	11042113451	Md Kamal	Aktaruzzaman	Aguandi	Small Business	Yes	BRAC NGO	
58	11032110200	Arju Miya	Late Sona Mia	Aguandi	Small Business	Yes	GRAMEEN Bank	
59	11012112942	Abdul Ali	Hazrat Ali	Choitankanda	Small Business	Yes	ASA NGO	
60	11052113002	Md Sopan	MdHelal Uddin	Atabdi	Small Business	Yes	ASA NGO	
61	11062112767	Khokon Buya	Chan Mia	Eidbardi	Small Business	Yes	Sokti Foundation	
62	11062113823	Jalil	Late Abu Taleb Ali	Baliapara	Small Business	Yes	ASA NGO	
63	11062110293	Noor Mohammad Mia	Late Ashraf Ali Mia	Baliapara	Small Business	Yes	BRAC NGO	
64	11062113700	Md Shahin Mia	LatyeNayeb Ali	Baliapara	Small Business	Yes	Sokti Foundation	
65	11062113595	Tota Miah	Late Razzak	Eidbardi	Small Business	Yes	Palli Mongal Karmosuchi	
66	11042113646	Md Abdul Karim	Chomir Uddin	Atadi	Small Business	Yes	ASA NGO	
67	11042110079	Khokan Chabdra Mitra	Late GojendroMohon	Bijoy Nagar	Small Business	Yes	BRAC NGO	
68	11052114056	Tara Mia	Late Abdul Aziz	Hazishadi	Small Business	Yes	Grameen Bank	
69	11062211562	Jobeda Begum	Late Abdul Mojid	Baliapara Mouza	Chicken and Duck Rearing	Yes	GRAMEEN Bank	1406297443
70	11052112884	Rajib	Konak Dar	Ranidi Mouza	Chicken and Duck Rearing	Yes	Grameen Bank	1911704449
71	11052110216	Sakib	Babul Mollah	Kamaldi Mouza	Chicken and Duck Rearing	Yes	Pubali Bank Ltd	1746107663

SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
72	11042213621	Majeda Begum	Late Munsur Ali	Atadi Mouza	Chicken and Duck Rearing	Yes	Palli Mongal Karmosuchi	1744290701
73	11052113345	Omar Faruk	MdEbrahim Mia	Hazishadi Mouza	Chicken and Duck Rearing	Yes	BRAC NGO	1726712713
74	11062110286	Md Arman Bhuyan	Late Abdul High	Baliapara Mouza	Chicken and Duck Rearing	Yes	Bohumukhi Somobay Somiti	1720827185
75	11062110513	Shoel Molla	MdMejba Uddin Molla	Baliapara Mouza	Chicken and Duck Rearing	Yes	Bohumukhi Somobay Somiti	1977265374
76	11062112954	Mintu Mia	Shafiqul Islam	Idbardi Mouza	Chicken and Duck Rearing	Yes	Grameen Bank	1989273283
77	11062110435	Azzijul Hakim	Ali Ahamed	Eidbardi	Chicken and Duck Rearing	Yes	SIDOR NGO	1766242970
78	11032110049	Monir Hossan	Late Hazrat Ali	Auguandi	Chicken and Duck Rearing	Yes	Grameen Bank	1779629056
79	11042113751	Faruk	Late Hasem	Atadi	Chicken and Duck Rearing	Yes	ASA NGO	1729747584
80	11062110515	Kamal Hossain	Late Alauddin	Eidbardi	Chicken and Duck Rearing	Yes	BRAC NGO	1631813887
81	11032113580	Abdul Ohab	Late Madhbor Ali	Auguandi	Chicken and Duck Rearing	Yes	Grameen Bank	1811156938
82	11062213906	Shain Mia	Late AbdurRasidBuyan	Eidbardi	Chicken and Duck Rearing	Yes	BRAC Bank	1716402833
83	11042113785	Khadiza	MdNurul Islam	Atadi	Chicken and Duck Rearing	Yes	Grameen Bank	1846239440
84	11032110251	Rehana	MdRofikBuyan	Auguandi	Chicken and Duck Rearing	Yes	Grameen Bank	1786491776
85	11042212976	Mst. Asaifa Begum	Late Mulsem Uddin	BAZINABOND	Chicken and Duck Rearing	Yes	Grameen Bank	
86	11022213196	Rowshanara Begum	Late. Abdur Rahman	Laxmipur	Chicken and Duck Rearing	Yes	SIDOR NGO	

SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
87	11062213724	Parvin Begum	Hasibur	Kumarabag	Chicken and Duck Rearing	Yes	BRAC Bank	
88	11042213675	Akhlima Begum	Late Abdul Haque	Atadi	Chicken and Duck Rearing	Yes	Palli Mongal Karmosuchi	
89	11062210118	Mina Haque	Safor Ali	Eidobardi	Chicken and Duck Rearing	Yes	Grameen Bank	
90	11062210384	Giasmin	Kobir Hossain	Eidobardi	Chicken and Duck Rearing	Yes	CSS NGO	
91	11062110434	Parvin	PEAR ALI	Eidobardi	Chicken and Duck Rearing	Yes	Grameen Bank	
92	11052213073	Md Mostafa Molla	Late SofiullahMollah	Atabdi	Chicken and Duck Rearing	Yes	Sokti Foundation	
93	11062113150	HARUN AR RASID	Late Saheb Ali	Langurdi	Chicken and Duck Rearing	Yes	Palli Mongal Karmosuchi	
94	11042113570	Md Nobil Hossan	Late. Mohammad	Kamaldi	Chicken and Duck Rearing	Yes	ASA NGO	
95	11052110207	Md Al Amin	Abdul Baten	Kamaldi	Chicken and Duck Rearing	Yes	Grameen Bank	
96	11012212847	Foyjullah Begum	Romij Uddin	Choitankanda	Chicken and Duck Rearing	Yes	SIDOR NGO	
97	11042210549	Morium Begum	Abdur Rahman	Atadi	Chicken and Duck Rearing	Yes	Palli Mongal Karmosuchi	
98	11052110164	Md Sanaula Molla	Late SafiullahMollah	Atabdi	Fish Culture	Yes	Palli Mongal Karmosuchi	
99	11062110429	Nadim Buyan	MdNazrul Islam	Eidbardi	Fish Culture	Yes	ASA NGO	
100	11052110215	Md Sirajul Islam	Late Hasen Ali	Kamaldi	Fish Culture	Yes	Grameen Bank	
101	11052112880	Taslina	RustumBuya	Auguandi	Vegetable Gardening	Yes	Grameen Bank	
102	11052112981	Sofikul Islam	MdNurulHaque	RANIDI	Vegetable Gardening	Yes	ASA NGO	

SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
103	11062110504	Hajerea Begum	Ianus Mia	Baliapara	Vegetable Gardening	Yes	Palli Mongal Karmosuchi	
104	11012113499	Din Islam	Babul Mia	Choitankanda	Vegetable Gardening	Yes	Grameen Bank	
105	11062113799	Minara	Jasirul	Eidbardi	Tailoring	Yes	Samajik Seba (NGO)	
106	11062113850	Mojammal	Zahirul	Eidbardi	Cow and Goat Rearing	Yes	ASA NGO	
107	11062110510	Kalem	Late. Muba rak	Baliapara	Cow and Goat Rearing	Yes	Samajik Seba (NGO)	
108	11062110369	Babu	Difty	Baliapara	Cow and Goat Rearing	Yes	Jagorne Chokro(NGO)	
109	11052113303	Soman	Late Ohi Uddin	Kahindi	Cow and Goat Rearing	Yes	Krishi Bank	
110	11052113391	A K M Berek Ahmmed	Late Abdul Hakim Buyan	Bererkor	Small Business	Yes	BRAC (NGO)	
111	11062110403	Nur Mohammad	Solaiman	Eidbardi	Small Business	Yes	Krishi Bank	
112	11062110433	Mridul	Monir	Eidbardi	Small Business	Yes	Uttara Bank	
113	11062110502	Anwar Hossain	Late Sokkur Ali	Atabdi	Small Business	Yes	Social Islami Bank	
114	11052110160	Shilpi	Md. Nanno Miah	Ranidi	Tailoring	Yes	BRAC (NGO)	
115	11062110406	Jakiya Begum	H. Amir Hossain	Eidbardi	Tailoring	Yes	Buro (NGO)	
116	11062210109	Nurul Islam	Late Abdul Malek	Baliapara	Cow and Goat Rearing	Yes	Crishi Bank	
117	11062113676	Azharul Islam	Md. Yeasin Mullah	Eidbardi	Cow and Goat Rearing	Yes	Crishi Bank	
118	11062110281	Nargis Begum	Md. Halim	Baliapara	Fish Culture	Yes	Grameen Bank	
119	11062210296	Nazma	H. Anwar Hossain	Baliapara	Cow and Goat Rearing	Yes	Sajeda Foundation	

SI - No	AP ID No.	Name of the trained person	Name of Father/Husband	Name of Mouza	Name of Trade on which Received Training	Involved IGA	Name of NGO/Financial Institutions	Number
120	11062110501	Mokbul Hossain	Late Sokkor Ali Munsu	Baliapara	Cow and Goat Rearing	Yes	Sajeda Foundation	
121	11062113809	Shahidullah	Md. Afjal Bhuiyan	Komarbag	Cow and Goat Rearing	Yes	BRAC (NGO)	
122	11062113356	Md. Milon mia	Md. Abdul Khaleq	Eidbardi	Cow and Goat Rearing	Yes	BRAC (NGO)	
123	11052113115	Afaj Uddin	Asmot ali	Kahindi	Cow and Goat Rearing	Yes	SSS (NGO)	
124	11052110161	Sultana	Md. Latif	Ranidi	Cow and Goat Rearing	Yes	BRAC (NGO)	
125	11042113138	Sadiqur Rahman	Abdul Malek	Atadi	Cow and Goat Rearing	Yes	ASA (NGO)	
126	11052213433	Sheuli	F. Abdul Motin bhuiya	Ranidi	Small Business	Yes	Grameen Bank	
127	11052110165	Anamul	Chanmia	Ranidi	Small Business	Yes	BRAC (NGO)	
128	11021113029	Abdul Malek	Abed Ali	Laxipur	Small Business	Yes	Krisi Bank	
129	11052110143	Md. Rahim Uddin	Mohij Uddin	Atabdi	Chicken and Duck Rearing	Yes	Al Arafa Islami Bank	
130	11042213628	Aysa Begum	H. Monir Hossen	Atadi	Chicken and Duck Rearing	Yes	ASA (NGO)	
131	11032213228	Momutaz	Abdur Rahman	Agundi	Chicken and Duck Rearing	Yes	ASA (NGO)	
132	11052110333	Liza Sultana	Nurul Islam	Ranidi	Tailoring	Yes	SSS (NGO)	
133	11052213210	Mst. Shahanaz Akter	Sajahan mia	Ranidi	Tailoring	Yes	BRAC (NGO)	

11.10 Appendix: Microfinance Access by Trained Affected Persons in Section 4

Monitoring Month: June 2023

Name of Upazila: Rupganj

District: Narayanganj

Reporting Date: 30-06-2023

Sl. No.	AP's ID No.	AP's Name	Name of Father/Husband	Name of Mouza	Name of Trade	Involved in IGA	Name of NGO/financial institutions
1	12094145005	Md. Aynal Haque	Late Hazi Shahabuddin	Char Gandharbpur	Small Business	Yes	Bangladesh Krishi Bank
2	12094145085	Ashma	Late Odud Miah	Char Gandharbpur	Small Business	No	Grameen Bank
3	12094145070	Solim	F.Shajahan Fakir	Char Gandharbpur	Small Business	Yes	AsA (NGO)
4	12094145006	Jhuma	Alauddin	Char Gandharbpur	Tailoring	Yes	ASA (NGO)
5	12094145150	Roksana	F. Magibur Rahman	Char Gandharbpur	Tailoring	Yes	Grameen Bank
6	12094145066	Md. Rabbi Prodhan	Md. Mofijul Prodhan	Char Gandharbpur	Chicken and Duck Rearing	Yes	Bangladesh Krishi Bank
7	12094145030	Mst. Lutfor Nahar	H. Jahidul Islam	Char Gandharbpur	Chicken and Duck Rearing	Yes	DSK (NGO)
8	12094140538	Selina Begum	Habibullah Prodhan	Char Gandharbpur	Chicken and Duck Rearing	Yes	Grameen Bank
9	12094145205	Abdul Kadir Bhuiya	Abdul Bhuiyan	Char Gandharbpur	Chicken and Duck Rearing	Yes	Sajeda Foundation
10	12094140523	Mizanur Rahman	Abdul Halim	Char Gandharbpur	Cow and Goat Rearing	Yes	ASA (NGO)
11	12094145120	Md. Arab Ali	Shahabuddin	Char Gandharbpur	Cow and Goat Rearing	Yes	ASA (NGO)
12	12094145051	Solaiman	Md. Wali ullah	Char Gandharbpur	Cow and Goat Rearing	Yes	Bangladesh Krishi Bank
13	12094145210	Kabir Hossain	Was Uddin	Char Gandharbpur	Cow and Goat Rearing	Yes	SIDOR (NGO)
14	12094145156	Md. Shohidullah	samsuuddin	Char Gandharbpur	Cow and Goat Rearing	Yes	Sajeda Foundation
15	12094145159	Abdul Halim	Late Abyedullah	Char Gandharbpur	Cow and Goat Rearing	Yes	Jibon nagor
16	12094145187	Johir uddin	Billal prodan	Char Gandharbpur	Cow and Goat Rearing	Yes	Jibon nagor

Sl. No.	AP's ID No.	AP's Name	Name of Father/Husband	Name of Mouza	Name of Trade	Involved in IGA	Name of NGO/financial institutions
17	12094145153	Siraj miah	Somser Ali	Char Gandharbpur	Cow and Goat Rearing	Yes	ASA (NGO)
18	12094145123	Alamgir	Joynal abedin	Char Gandharbpur	Cow and Goat Rearing	Yes	Samajik Seba (NGO)
19	12094145146	Shohidullah	Late shabuddin	Char- Gandharbpur	Cow and Goat rearing	Yes	Samajik Seba (NGO)
20	12094145164	Shahadat	Shomser ali	Char- Gandharbpur	Small Business	Yes	Jibon nagor
21	12094245012	kod banu	Shohidullah	Char- Gandharbpur	Small Business	Yes	AsA (NGO)
22	12094245116	Rani	Mojibur Rahman	Char- Gandharbpur	Tailoring	Yes	Grameen Bank
23	12094145121	Shirajul Islam	Abdul salam	Char- Gandharbpur	Chicken and Duck rearing	Yes	AsA (NGO)
24	12094145023	Mizanur Rahman	Munna prodhan	Char- Gandharbpur	Chicken and Duck rearing	Yes	AsA (NGO)
25	12094145151	Amjad hossain	Gohon ali	Char- Gandharbpur	Cow and Goat rearing	Yes	AsA (NGO)
26	12094145025	Lipe	Bazlur Rahman	Char- Gandharbpur	Tailoring	Yes	AsA (NGO)
27	12094145057	Homayan prodhan	Late Chan mia	Char- Gandharbpur	Small Business	Yes	Sajeda Foundation
28	12094145079	Tanzina	Shafiullah	Char- Gandharbpur	Tailoring	Yes	AsA (NGO)
29	12094145006	Mafiya	H. Solaiman Hossen	Char- Gandharbpur	Tailoring	Yes	Islami Bank

11.11 Appendix: Summary of Community Meetings held during January to June 2023

Acronyms:

ADB: Asian Development Bank

AP: Affected Person

CCL: Cash Compensation under Law

DESWSP: Dhaka Environmentally Sustainable Water Supply Project

DORP: Development Organisation of the Rural Poor

ID: Identity

DC: Deputy Commissioner

NGO: Non- Government Organization

NID: National Identity

INGO: Implementing Non-Government Organization

RP: Resettlement Plan

SPS: Safeguard Policy Statement

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Semi-annual summary of the community meetings discussion Conducted by DORP Period: January to June 2023		
Key Issues of Discussion	Participants Responses	Project Response
	<p>From January to June 2023 a total number of 102 community meetings with a total of 1325 participants (M-518, F-807) were held in the project site of Araihasar, Rupganj and Dhaka area. The above 102 meetings were held in all the 6 sections during this reporting period. The section-wise distribution of meetings and meeting participants is given below: -</p> <p>a. In section-1 total 12 meetings were held with a total of 157 participants (Male-67, Female-90);</p> <p>b. In section-2 total 21 meetings were held with a total of 275 participants (Male-101, Female-174);</p> <p>c. In section-3 total 24 meetings were held with a total of 311 participants (Male-109, Female-202);</p> <p>d. In section-4 total 12 meetings were held with a total of 155 participants (Male-58, Female-97);</p> <p>e. In section-5 total 16 meeting held with a total of 208 participants (Male-78, Female-130);</p> <p>f. In section-6 total 17 meeting was held with a total of 219 participants (Male-105, Female-114).</p> <p>The following questions/queries were raised by the participants in the meetings: -</p>	<p>In reply to the query made by the meeting participants, the following responses were made from the project: -</p>
1.Regarding wrong name inclusion in the final notice for CCL receipt.	1.One affected person informed that Deputy Commissioner's office issued final notice for receiving CCL against her land but not after her name, to another person's name who is not the actual owner of the land. She wanted to know what she should	1.The project advised her to submit all legal documents regarding land ownership to the Land Acquisition Section of the Deputy Commissioner's office. The Land Acquisition Section would verify the documents and issue correct notice.

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Semi-annual summary of the community meetings discussion Conducted by DORP Period: January to June 2023		
Key Issues of Discussion	Participants Responses	Project Response
	do then.	
<p>2. Papers required in receiving compensation from the Deputy Commissioner's office and additional payment/resettlement benefits from DWASA.</p>	<p>2. The meeting participants wanted to know how they will receive their compensation money from the Deputy Commissioner's office and additional payment/other resettlement benefits from DWASA. They also wanted to know the kind of papers they will need to submit to the Deputy Commissioner's office for compensation and papers to be submitted to INGO DORP for receiving additional payment/other resettlement benefits.</p> <p>The participants wanted to know what benefits they will get if they buy land elsewhere after getting LA notice under section 8(3)(ka).</p>	<p>2. The participants were informed in the meeting that the kind of papers they needed for receiving compensation from Deputy Commissioner's office is, Ownership document of the land, updated mutation, land tax receipt, national ID card, bank account number, etc. DORP will try its utmost so that payments are made fair and transparent. The INGO personnel assured the participants that they will guide them in collecting papers accordingly.</p> <p>In response to the query about papers to be collected for receiving additional payment and other resettlement benefits, the meeting participants were informed that they will receive additional payment according to the current market value and according to the project entitlement matrix. INGO DORP will assist/guide them in preparing/collecting necessary papers to be submitted to DWASA for receiving additional payment and other resettlement benefits. In this regard, they need to open an individual bank account. In response to the participant's question, they were informed that those who have already been received CCL from the Deputy Commissioner's office, all those papers along with the affected person's ID card, Photocopy of NID/SMART card, citizenship certificate from Union Parishad Chairman, or Pouroshava Chairman, account number, share sheet, etc. death certificate in case of death, the stamp of Rs. 300, etc. will be required. These required papers need to be submitted to DORP local office for payment of additional/resettlement benefits.</p> <p>After receiving the Section 7 notice, if affected persons purchase land elsewhere, they will get the money for the stamp cost of registering the land after CCL payment.</p>

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Semi-annual summary of the community meetings discussion Conducted by DORP Period: January to June 2023		
Key Issues of Discussion	Participants Responses	Project Response
3. The affected persons want to know about the reason of taking so much time by Deputy Commissioner's office in processing papers for distributing CCL now-a-days.	3. The affected persons wanted to know why it takes so much paperwork for CCL payment now-a-days, and they want a list of kinds of papers needed in getting CCL.	3. On behalf of the project, DORP stated that the Land Acquisition Officer (LAO) checks all the papers for CCL and if all papers are okay, he pays CCL as soon as possible. He asks for all papers together so that affected persons do not need to go to the Deputy Commissioner's office frequently. Sometimes Deputy Commissioner's office are short staffed. PMU is committed to taking care of the issue. PMU has held several meetings with the Deputy Commissioner's office on this issue so that Deputy Commissioner's office takes less time in paying CCL. DORP provided a list of required papers for getting CCL to the affected persons.
4. Regarding Cultivation on acquired land.	4. Affected persons wanted to know why Dhaka WASA has not started work on some cropland which has been acquired by them. Affected persons wanted to know if they can cultivate those lands.	4. According to the project, it has been informed that the acquired land cannot be cultivated in any way. The contractor will start work at any time.
5. Discussion on CCL unpaid affected persons' payment.	5. Affected persons who are yet to receive CCL want to know how to get money if it takes a long time to resolve their land	5. The project informed them that the CCL money is deposited in the Deputy Commissioner's Public Account of Republic as per estimated CCL amount of their land. The money that they will receive from Dhaka WASA in the future is also deposited in a separate dedicated account. Payment of their compensation is ensured.
6. Discussion on how affected persons will receive money if there is no NGO.	6. Affected persons wanted to know how to get money by submitting documents since it takes time to resolve their land issues. They wanted to know how they can get money if there is no NGO. Who will collect their documents and submit them to Dhaka WASA?	6. According to the project, if there is no NGO, they will get their dues by contacting Dhaka WASA directly. A unit will be opened in Dhaka WASA at Rupganj Water Treatment Plant site. Affected persons may submit their documents to that management unit.
7. Discussion about not getting land compensation yet	7. Affected persons want to know why they are not getting CCL from the Deputy Commissioner's office after submitting the necessary paper to the Deputy Commissioner's office.	7. On behalf of the project, it is said that INGO will help before submitting the document to the Deputy Commissioner's office such as whether all the documents are in order, what type of documents are required, etc. However, Deputy Commissioner's office follows its own

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Semi-annual summary of the community meetings discussion Conducted by DORP Period: January to June 2023		
Key Issues of Discussion	Participants Responses	Project Response
		course in paying CCL. Despite, PMU and Project Director are trying their best on behalf of the project so that the Deputy Commissioner's office pays this payment immediately. In addition, affected persons can contact the land office to get the CCL soon. If affected persons need any cooperation from the land office or anywhere else, then the project side/ DORP will extend their all cooperation.
8. Court Case related problem discussed	8. Affected persons wanted to know what to do to get money if there is a case for land or infrastructure	8. In reply, on behalf of the project, INGO informed everyone that if there is a court case on the acquired land, it has to be settled. Affected persons will not receive any money until a settlement has been reached between the two parties. Rightful owners will receive compensation if the case has been settled.
9. The market value of the land in Section-5 is and Section 6 discussed.	9. Affected persons stated the price of land that the Deputy Commissioner's office will pay is much less. It is not possible to buy land elsewhere with this money. So how do they buy alternate land?	9. In reply, on behalf of the project – it is informed that all affected persons will get three times more than their mouza rate. In most cases, Deputy Commissioner's rate is low because of the low cost of registration while buying or selling land. If the Deputy Commissioner's rate is less than market price, then DWASA will pay top up. So, the affected persons will be able to buy new land.
❖ 10. Discussion on training and borrowing.	10. Participants wanted to know if the project can provide a loan for the business after the training. If they take a loan from somewhere else, they have to pay a lot of interest.	10. Participants were informed that those who were affected by the project were compensated. Those who are very poor are given grants from this project, training is provided, and training allowance of tk. 20,000 is given at the end of the training. With this money, the person can start a business. Even then, if the business needs more money, all the lenders will be contacted. So that they can take loans. There is no opportunity to give a loan under this project.
11. Whether training is available before payment is received. ❖	11. Affected person wanted to know if LIRP training is available before receiving compensation because he could not receive CCL due to court case ongoing over land.	11. Affected person was informed that training offer is not available before CCL is received because he will not be able to prove his land ownership over land until he received CCL from Deputy Commissioner. If he received CCL, he can receive training if he qualifies the training criteria that fixed by the project's entitlement matrix.
12. Investment of	12. In the meeting proper	12. In this regard the participants were

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Semi-annual summary of the community meetings discussion Conducted by DORP Period: January to June 2023		
Key Issues of Discussion	Participants Responses	Project Response
compensation, additional and other resettlement benefits in income-generating activities.	utilization of the compensation money and other benefits provided by the project were discussed. The affected persons were informed that the compensation from the DC office and additional/resettlement benefits from DWASA is to support the affected person to invest the money in income-generating activities so that they can improve their economic status better compared to their present status. The participants showed their positivity to use the money in productive sectors. They committed to using their compensation money and resettlement benefits to re-start or re-establish their livelihoods activities at the previous level or better off compared to their previous life. The meeting participants requested DORP to guide them regarding spending the compensation money and other resettlement benefits properly.	informed that the money which they have received and are yet to be received as compensation and resettlement benefits will have to be used to re-establish and restart their livelihood so that they can bring a positive change in their lives or at least at the level of pre-project status. Affected persons were advised by the project personnel that due to the intervention of the project they have lost land, residential and business structures, crops, trees, and employment. So, these amounts of money are to be used in purchasing land, constructing structures, re-start businesses, and re-establishes livelihoods. They should not be using the compensation money/ resettlement benefits in unproductive ways,
13. Discuss on WTP Job opportunities for affected persons.	13. Some affected persons are looking at job opportunities in the WTP.	13. It was mentioned that many persons have lost their livelihood due to the project, because of which the project has provided additional skill training on specific works. the affected persons can make a living by investing the money that has been given to them. Moreover, the project also has the option about getting employment opportunities in project construction work based on competence.
14. Investment of compensation, additional and other resettlement benefits in income-generating activities.	14. In the meeting, using compensation money and other benefits by the project affected persons, were discussed. They have been informed that the compensation from the Deputy Commissioner's office and additional/resettlement benefits from DWASA made intending to invest the money in income-generating activities so that they can improve their economic status better compared to their present status. The participants showed	14. In this regard the participants were informed that the money which they have received and are yet to be received as compensation and resettlement benefits will have to be used to re-establish and restart their livelihood so that they can bring a positive change in their lives or at least at the level of pre-project status. Affected persons were advised by the project personnel that due to the intervention of the project they have lost land, residential and business structures, crops, trees, and employment. So, these amounts of money are to be used in

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Semi-annual summary of the community meetings discussion Conducted by DORP Period: January to June 2023		
Key Issues of Discussion	Participants Responses	Project Response
	<p>their positivity to use the money in productive sectors. They committed to using their compensation money and resettlement benefits to re-start or re-establish their livelihoods activities at the previous level or better off compared to their previous life. The meeting participants requested DORP to guide them regarding spending the compensation money and other resettlement benefits properly.</p>	<p>purchasing land, constructing structures, re-start businesses, and re-establishes livelihoods. They should not be using the compensation money/ resettlement benefits in unproductive ways.</p>
<p>15. Providing support to the ongoing/ensuing project construction work by the affected persons.</p>	<p>15. In the meeting, participants were requested to cooperate with the contractors during project construction work, especially by making free of the project acquired land by removing the structures, trees, etc. irrespective of those who have received resettlement benefits and those who did not receive yet due to problems with papers, ownership, shareholders, land record/mutation and court cases.</p> <p>The participants raised questions that they have been not yet compensated for their lost properties, whether they will receive their payment faster.</p>	<p>15. Regarding assisting in the smooth project implementation both groups those who have received payment and those who did not receive payment yet were informed to support the project construction works. Both the groups have been notified several times and requested verbally to let the land make free by removing the structures for the smooth construction work as their land has already been acquired by the government for pipeline installation purposes. For those who did not receive payment yet, payment was delayed mostly due to legal problems and lack of mutation according to RS record, etc. So, as long as their problems will remain unsettled the compensation money will be kept safe in Deputy Commissioner's Public Account of Republic and in a separate account (Dedicated) opened for them and as soon as their problems will be solved, they can receive their payments. The participants agreed to cooperate with the contractors during project construction work, by making the project acquired land free of encumbrances.</p>
<p>16. Take away or remove the structures from the project-acquired land.</p>	<p>16. Based on discussions, the participants who have been paid fully and did not remove the structures were asked to remove the structures. On this ground, non-paid participants raised questions that whether they will be</p>	<p>16. In the meeting the participants were informed that those who have already fully paid have been notified several times (verbally and written) but did not remove structures yet and those who did not receive compensation yet from the Deputy Commissioner's office and resettlement</p>

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Semi-annual summary of the community meetings discussion Conducted by DORP Period: January to June 2023		
Key Issues of Discussion	Participants Responses	Project Response
	<p>paid their compensation before shifting their structures. Unless they fully paid up, they will not shift their structures and will not make the project area free for project construction work. The participants mentioned that the project must pay all their compensation and benefits due to them and give them sufficient notice to allow them a reasonable time for shifting etc.</p>	<p>benefits from DWASA due to legal issues and mutation problems their amount will be safely deposited to the Deputy Commissioner's office and DWASA as well in an account (Dedicated) opened separately for them. Being assured from the project side they agreed to shift their structures and to make the project area free for project construction work.</p>
<p>17. Whether there are facilities for women separately from the project</p>	<p>17. Affected persons wanted to know whether the project has any facilities for affected women.</p>	<p>17. It was informed that project has special emphasis on women in development. Female headed households receive vulnerable grant and skill development training and investment allowance in addition to CCL, top-up and other resettlement assistance. Moreover, female affected persons are given priorities in case of employment in project work opportunities.</p>

11.12 Appendix: Minutes of 13th GRC Meeting in Bangla (Signed)

ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই (DESW) প্রজেক্ট
ঢাকা পানি সরবরাহ ও পয়ঃনিষ্কাশন কর্তৃপক্ষ
গণপ্রজাতন্ত্রী বাংলাদেশ সরকারের স্থানীয় সরকার পল্লী উন্নয়ন ও সমবায় মন্ত্রণালয়ের অধীনে
স্মারক নং : ৪৬.০০.০০০০.০৮৫.০৬২.২০১৭-৮৩১ তাং-২৭/১১/২০১৭ এর মাধ্যমে গঠিত কমিটি
ক্ষোভ নিরসন সভার কার্যবিবরণী (সেকশন-৩)।

স্মারক নং- ৪৬.১১৩.৬১৮.০০.০০.G243/(V-1)/DESWSP/ 6704

তারিখ: ০৯/০২/২৬

তারিখ : ১৭-০১-২০২৩ খ্রিঃ
সময় : সকাল ১০:০০ ঘটিকা।

সংস্থানঃ ডব্লু এরিয়া অফিস (রূপগঞ্জ), ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।

আলোচ্য বিষয় :

ক) আবেদনকারী জনাব আনোয়ার হোসেন এর অবকাঠামো এবং অবকাঠামোর ভেতরে স্থাপিত তার বাবার কবর স্থানান্তর বাবদ ক্ষতিপূরণ প্রদান করার বিষয়ে আলোচনা এবং সিদ্ধান্ত গ্রহণ।

সভায় উপস্থিত কমিটির সদস্য ও অন্যান্যদের নাম ও পদবী :

১. জনাব গাজী হাবিবুল হায়দার, নির্বাহী প্রকৌশলী ও উপ-প্রকল্প পরিচালক, আহ্বায়ক জিআরসি, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
২. জেসমিন সাহানা, টিম লিডার (ভারপ্রাপ্ত), ডব্লু, ডিইএসডব্লিউএস প্রকল্প।
৩. ড. রাফেজা আক্তার, মনোনীত প্রতিনিধি, এমডিএসসি, রিসেটেলমেন্ট এন্ড পার্ট (ন্যাশনাল) ও সদস্য জিআরসি।
৪. জনাব তোফাজ্জল হোসেন, সেইফপার্ট অফিসার (সোসাল এ্যান্ড জেডার), ডিইএসডব্লিউএস প্রকল্প ও সদস্য জিআরসি, ঢাকা ওয়াসা।
৫. জনাব এম.ডি সাইয়িদুর রহমান, এরিয়া ম্যানেজার, ও সদস্য সচিব, জিআরসি, ডব্লু, ডিইএসডব্লিউএস প্রকল্প।
৬. জনাব লুতফর রহমান, সার্ভেয়ার, ডব্লু, ডিইএসডব্লিউএস প্রকল্প।
৭. জনাব আনোয়ার হোসেন (আবেদনকারী), গোলাকান্দাইল, রূপগঞ্জ, নারায়নগঞ্জ।

সভার সূচনা বক্তব্য :

জনাব গাজী হাবিবুল হায়দার, উপ-প্রকল্প পরিচালক ও সভার আহ্বায়ক উপস্থিত সকলকে শুভেচ্ছা জানিয়ে সভার কার্যক্রম শুরু করেন। তিনি সকলকে নিজ নিজ পরিচয় দেওয়ার জন্য অনুরোধ করেন। উপস্থিত সকলে নিজ নিজ পরিচয় প্রদান করেন।

পরিচয় পূর্ব শেষে উপ-প্রকল্প পরিচালক বলেন, আপনারা অবগত আছেন যে, ঢাকা ওয়াসা তথা বাংলাদেশ সরকার, Dhaka Environmentally Sustainable Water Supply Project (DESWSP) নামে একটি মেগা প্রকল্প বাস্তবায়ন করছে। এমতাবস্থায় আরপি সেকশন-৪ চরগঙ্গাবন্দ পুর মৌজার ওয়াটার ট্রিটমেন্ট প্লান্টের কাজ চলমান রয়েছে এবং আরপি সেকশন-৩ এলাকায় দড়িকান্দি মৌজা হতে গঙ্গাবন্দ পর্যন্ত পাইপ লাইন স্থাপন কাজ ইতোমধ্যে শুরু হয়েছে। গোলাকান্দাইল মৌজায় ২৯০৯ দাগে একটি স্থাপনার ভেতরে আবেদনকারী জনাব আনোয়ার হোসেন এর বাবার কবর রয়েছে, তার আবেদনের প্রেক্ষিতে উক্ত কবর স্থানান্তর এর খরচের জন্য এবং যে স্থাপনার ভেতরে কবরটি বিদ্যমান সেই স্থাপনার ক্ষতিপূরণের আবেদন করেছেন। তার আবেদনের প্রেক্ষিতে স্থানীয় অনুষ্ঠিত হবে এবং সিদ্ধান্ত গ্রহণ করা হবে।

ড. রাফেজা আক্তার, মনোনীত প্রতিনিধি, এমডিএসসি, রিসেটেলমেন্ট এন্ড পার্ট (ন্যাশনাল) ও সদস্য জিআরসি আবেদনকারীকে তার অভিযোগের বিষয় বর্ণনা করতে অনুরোধ করেন।

জনাব আনোয়ার হোসেন বলেন, গোলাকান্দাইল মৌজায় ২৯০৯ দাগে তার জমি ঢাকা ওয়াসার প্রকল্প কাজে অধিগ্রহণ করা হয়েছে।

কিন্তু একই জমিতে একটি ঘরের মধ্যে তার বাবার কবর ছিল। তিনি উক্ত ঘরের ক্ষতিপূরণের টাকা পান নাই এবং কবর সরানো বাবদ কোনো টাকা পান নাই।

সভার আহ্বায়ক বলেন, জেলা প্রশাসকের কার্যালয় এবং প্রত্যাশি সংস্থা ঢাকা ওয়াসার সমন্বয়ে গঠিত যৌথ তদন্তের সময়ে আবেদনকৃত স্থাপনা এওয়ার্ডভুক্ত হয়েছিল, এবং ঢাকা ওয়াসা কর্তৃক প্রদানকৃত পুনর্বাসন সুবিধার নথি যাচাই বাছাই করে দেখা যায় তিনি সকল স্থাপনার নায্য ক্ষতিপূরণ এবং পুনর্বাসন সুবিধার টাকা পেয়েছেন। কিন্তু আবেদনকারী তার বাবার কবর স্থানান্তর বাবদ কোন আর্থিক ক্ষতিপূরণ প্রাপ্ত হন নাই। এমতাবস্থায় সভায় উপস্থিত সকলের মতামতের ভিত্তিতে এবং পূর্বে আলোচ্য প্রকল্পের আওতায় একই রকম কবর স্থানান্তরের জন্য প্রদানকৃত নথি যাচাইয়ের ভিত্তিতে আবেদনকারীর বাবার কবর স্থানান্তর করার জন্য প্রকল্পের পক্ষ থেকে ১০০০০.০০/- (দশ হাজার) টাকা প্রদান করা যেতে পারে।


ক্ষেত্র নিরসন সভার সিদ্ধান্ত :


ক্রমিক সং	অভিযোগকারীর নাম ও ঠিকানা	অভিযোগের বিষয়	আলোচনা ও পর্যালোচনা	সিদ্ধান্ত
১	আনোয়ার হোসেন, মৌজাঃ গোলাকান্দাইল, উপজেলাঃ রূপগঞ্জ, জেলাঃ নারায়ণগঞ্জ। দাগ নং- ২৯০৯	অবকাঠামোর ক্ষতিপূরণ এবং কবর স্থানান্তর বাবদ খরচ এর টাকা দেওয়া হয় নাই।	জমি, অবকাঠামো, গাছ-পালা এবং ফসলের টাকা জেলা প্রশাসকের জুমি অধিগ্রহণ শাখা থেকে প্রদান করা হয়, ক্ষতিগ্রস্ত ব্যক্তি আনোয়ার হোসেন জেলা প্রশাসকের কার্যালয় হতে তার সকল অবকাঠামোর টাকা পেয়েছেন। জেলা প্রশাসকের কার্যালয় থেকে কবর স্থানান্তর বাবদ কোনো টাকা প্রদান করা হয় নাই।	আবেদনকারীর আবেদনের প্রেক্ষিতে তার ফাইল যাচাই বাছাই করে তার বাবার কবর স্থানান্তর করার জন্য ১০০০০.০০/- (দশ হাজার) টাকা প্রদান করা হবে মর্মে সিদ্ধান্ত গৃহীত হয়।

উক্ত সভায় আর কোন আলোচনা না থাকায়, সভার আহ্বায়ক সবাইকে ধন্যবাদ জ্ঞাপন করে জিআরসি সভার সমাপ্তি ঘোষণা করেন।



২৬/০৬/২৩


ম.তি সাইয়্যিদুর রহমান
এরিয়া ম্যানেজার
ডব্লু. ডিইএসডব্লিউএস প্রকল্প
এবং সদস্য সচিব জিআরসি।


গাজী হাবিবুল হারুন
উপ-প্রকল্প পরিচালক,
ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা
এবং আহ্বায়ক জিআরসি।


১০.৬.২০২৩

তোফাজ্জল হোসেন
সেইফগার্ড অফিসার (সোসাল এ্যান্ড
জেতার), ডিইএসডব্লিউএস প্রকল্প
ঢাকা ওয়াসা ও সদস্য জিআরসি।






মোঃ আজিজুল হক
তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক
ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।



ড. রাফেজা আক্তার
রিসেটেলমেন্ট এন্ড পার্ট (ম্যাপনাল)
এমডিএসসি, ডিইএসডব্লিউএস প্রকল্প
এবং সদস্য জিআরসি।

Development Organisation of the Rural Poor-DORP
Dhaka Environmentally Sustainable Water Supply Project-DESWSP
 Rupganj, Narayanganj
Meeting Attendance Sheet

Subject: Grievance Redress Committee Meeting on Section- 03
 Venue: DORP Area Office, Rupganj, Narayanganj.
 Time & Date: 17th January 2023 at 10:00 AM

Sl No.	Name	Organization & Designation	Email/Mobile No.	Signature
01	Enzi Habibul Hydar	Dhaka WASA DD-2, DESWSP	gatihydar@yahoo.com 01673355012	
02	Dr. Rafesa Akter	MDSC, MM NRE	rafesnakter@yahoo.com	Rafesa
03	Jesmin Shalwan	TL-DESWSP- DORP	Jshalwan883@gmail.com	Jesmin
04	Tofazzal Hossen	Safeguard officer DESWSP, DWASA	tofaanpsust@gmail.com	Tofazzal 17.01.2023
05	Md. Saidur Rahman	Area Manager DORP	01611397674	 17/01/23
06	Lutter Rahman	Surveyor	01711-281236	 17.01.2023
07	Muhtor Hossain	AP, Galakendail		

11.13 Appendix: Minutes of 13th GRC Meeting in English

Dhaka Environmentally Sustainable Water Supply Project (DESWSP)

Dhaka Water Supply and Sewerage Authority

The Committee is constituted Under the Ministry of Local Government rural Development and Cooperatives (MLGRDC) of Bangladesh Government

Memo No. 46.000000085.006.0622.017831 Date: 11.11.2015

GRC Meeting Proceedings (Section-3)

Date: 17 January 2023

Time: 10.00 AM

Meeting Venue: DORP Area Office, Rupganj, Narayanganj.

Agenda

1. Discussion and decision regarding payment of compensation for relocation of petitioner Mr. Anwar Hossain's infrastructure and his father's grave placed inside the infrastructure.

Name and designation of the committee members and other meeting attendees:

1. Md. Gazi Habibul Hyder, Executive Engineer, Deputy Project Director-2, DESWSP, DWASA and Convener of GRC Meeting;
2. Dr. Rafeza Akter, National Resettlement Expert, MDSC and Member of the Committee;
3. Md. Tofazzal Hosen, Safeguard Officer (Social and Gender), DESWSP, DWASA;
4. Jesmmin Shahana, Team Leader (acting), DORP, DESWSP
5. Md. Saidur Rahman, Area Manager, DORP and Member Secretary of GRC;
6. Lutfar Rahman, Surveyor, DORP, DESWSP;
7. Anowar Hossain, applicant as an affected person, Golakandail, Rupganj, Narayanganj.

Introductory speech:

Md. Gazi Habibul Hyder, Executive Engineer, Deputy Project Director-2, DESWSP, DWASA and Convener of GRC Meeting; presided over the meeting. In the beginning of the meeting, he expressed his greetings to all of the meeting participants and requested the meeting participants to introduce themselves. All of the meeting participants introduced each other.

The meeting Convener told the participants that they may have been aware about the project. The Government of Bangladesh and Dhaka WASA is implementing a mega project named Dhaka Environmentally Sustainable Water Supply Project (DESWSP). In this situation, the work of water treatment plant in Chargandharbpur Mauza under Resettlement Pan Section-4 is going on. And construction of pipeline from Darikandi Mauza to Gandharbpur in Resettlement Pan Section-3 area is in progress. The grave of the applicant Mr. Anwar Hossain's father is located inside a structure at 2909 Dag in Golakandail Mauza, pursuant to his application, he sought compensation for the cost of shifting the said grave, and applied for compensation to the structure in which the grave is located. Based on his application, a hearing was held and a decision was taken.

Dr. Rafeza Akter, nominated representative, MDSC, Resettlement Expert (National) and Member of GRC requested the petitioner to state the subject matter of his complaint.

Mr. Anowar Hossain said, his land at plot number 2909 in Golakandail Mouza has been acquired for the project under Dhaka WASA. He had houses, trees and structures on that land. He has cleared the space by removing all the structures. But his father's grave is in

structure on the same land. He said he has not received any compensation for the house, and he has not received any money for removing the grave. The Convenor of the meeting stated that during the joint verification survey conducted jointly by the office of the Deputy Commissioner and the requiring body Dhaka WASA, the said structure was listed in the Award Book, and after verifying the affected persons' coGRMmpensation payment file, it is found that that the applicant has received full and fair compensation (CCL and other resettlement assistance) for all assets including structures. The project may pay the applicant BDT10000.00 (ten thousand) for shifting his (the applicant) father's grave.

Decisions of the Grievance Redress Committee:

Sl. No.	Name and address of Complainant	Subject matter of complaint	Discussions and review	Decision
1	Name: Md. Anowar Hossain Mouza: Golakandail, Upazila: Rupganj, District: Narayanganj. Plot no. 2909	The applicant claimed that compensation for structures and expense for shifting of grave had not been paid.	Compensation for land, structures, trees and crops are provided by the Land Acquisition Section of the District Commissioner's office, the applicant affected person Anowar Hossain received his full compensation (CCL and other resettlement assistance) for all of his lost assets including structures from the Deputy Commissioner's office and from the Dhaka WASA. The District Commissioner's office did not pay for shifting the grave.	Based on the applicant's application, after verifying his (the applicant) compensation payment file, it was decided to pay BDT 10000.00 (ten thousand taka) for shifting his father's grave.

As there was no further discussion in the said meeting, the convener thanked everyone and declared the GRC meeting closed.

Md. Saidur Rahman
Area Manager (Acting)
DORP, DESWS Project and
Member Secretary, GRC

Tofazzal Hosen
Safeguard Officer (Social and
Gender), DESWS Project and
Member, GRC

Dr. Rafeza Akter
Resettlement Expert (National)
MDSC, DESWS Project and
Member of GRC

Gazi Habibul Hyder
Executive Engineer,
DESWS Project, Dhaka WASA
and Convener of the GRC
