People's Republic of Bangladesh

Ministry of Local Government Rural Development & Cooperatives

Dhaka Water Supply and Sewerage Authority

9th-floor DWASA Bhaban, 98 Kazi Nazrul Islam Avenue, Kawran Bazar, Dhaka 1215

Dhaka Environmentally Sustainable Water Supply Project (DESWSP)

ADB Loan No. 3051-BAN (SF)

SEMI–ANNUAL SOCIAL SAFEGUARDMONITORING REPORT

(COVERS PACKAGES P1, P2, P3.1 & P3.2)

JULY–DECEMBER 2021

February 2022

Funded by:

INTERNAL. This information is accessible to ADB Management and staff. It m ropriate permission.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Executive Summary

This is the 13th Semi-annual Social Safeguard Monitoring Report (SSMR) prepared for project implementation under Dhaka Environmentally Sustainable Water Supply Project (DESWSP) of the Dhaka Water Supply and Sewerage Authority (DWASA) for submission to the Asian Development Bank (ADB).

The project is funded by Asian Development Bank (ADB), Agence Francaise de Development (AFD), and European Investment Bank (EIB). The total project cost is 1104 million USD of which ADB contributes 390m, AFD 204.90 million, EIB 136million, and Bangladesh government 374 million. The cost of resettlement (social safeguard) has been borne by the government.

The DESWSP has a target impact (Goal) of "Improved access to and quality of sustainable water supply services in Dhaka (City)". The project aims to achieve an outcome of "More reliable and improved security of water supply and sanitation in Dhaka" and to achieve the target 'impact' through these defined outputs:

- **Output 1: New surface water supply system developed** comprises of 1,050 MLD river intake, 500 MLD water treatment works (phase 1), 22 km raw water pipeline, 14 km treated water transmission, 24 km primary distribution pipelines, and 44 km feeder pipelines (Figure2.1). [*Completion target: December 2024*]
- **Output 2: Distribution network strengthened** comprises rehabilitating 376 km of distribution networks and 32,000 household and community connections, and legalization of 37,000 household and community connections at MODS Zone 6 (Figure2.2). [*Completed)*
- **Output 3: Project management and administration adequately supported.** [*Completion target: December 2024*]
- **Output 4: Empowerment of women and vulnerable groups supported**(new scope) along with the construction of at least 1,000 community toilets and bathing chambers with separate units for males/females in low-income communities in Dhaka city.[1] [Completion target: *December 2023*]

Package 3.2and Output 4 have been added as a new scope under the additional financing that got effective on03 January 2022.

Output 1 is divided into four contract packages, such as P1 (water intake, raw water pipelines, and water treatment plant), P2 (treated water transmission pipelines), P3.1 (primary distribution pipelines), and P3.2 (feeder pipelines)

The report is prepared on Output 1 by Mott MacDonald, the Consultant of the project, to assist the DWASA Project Management Unit (PMU) in updating ADB and development partners on the implementation of the Social Safeguard Plans (Resettlement Plans) of the project.

The DESWSP's output 1 is delivered through several contract packages by several consultants, contractors, and NGOs under DWASA's project management unit (PMU). Mott MacDonald is responsible for the four main construction contracts through their management, design, and supervision consultancy (MDSC) contract. Under MDSC, Mott MacDonald is acting as the Employer's designer for Packages 2 and P3.1 and P3.2 and as the supervision consultant for Packages 1, 2,P3.1, and P3.2. Contractors have been appointed for P1, P2, and P3.1. The award of contract for P3.2 is under evaluation. P1 is a Design, Build & Operate (DBO) contract.

The bulk water supply system runs 36 km from the Meghna River to Dhaka, passing through Araihazar and RupganjUpazila and Madani Avenue after crossing Sitalakshya and Balu rivers. This project will use 310.71acres of land of which Dhaka WASA owns 81.53 acres (in Gandharbpur). Public land is another 46.03acres. The rest of the land (183.15acres) is privately

[1]For output 4, it will be supported by an ADF grant to strengthen access of women and vulnerable groups in underserved low-income communities (slums) of Dhaka to basic infrastructure and social services and to promote their legal empowerment.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

owned. The project will impact private and government land of different organizations including structures, assets, crops, fish, trees, etc.

The DESWSP falls under Category 'A'according to ADB classification based on involuntary resettlement impacts of projects. It falls under Indigenous Peoples' Category 'C' according to ADB Indigenous People's Categorization of projects. No indigenous people's householdshave been found during the surveys.

Issues of involuntary resettlement are being implemented following two national (GoB) Legislations such as Acquisition and Requisition of immovable Property Ordinance (ARIPO) 1982 – for land acquisition initiated before the 2017 Act came into force, and Acquisition and Requisition of Immovable Property Act (ARIPA), 2017, for subsequent land acquisition. In addition, ADB Safeguard Policy Statement (SPS), 2009 is being followed. Land under resettlement plans 1 and 2 is being acquired following ARIPO, 1982. After repealing ARIPO, 1982, land under resettlement plans 3, 5, and 6 is being acquired following newly enacted ARIPA, 2017. A Resettlement Framework (RF) was developed for DESWSP in 2013 to guide the Executing Agency (EA) in making and updating resettlement plans and implementation.

DWASA is the executing agency. PMU has a Safeguard Implementation Unit (SIU) for monitoring safeguard activities implementation. An independent External Monitoring Agency (EMA) has been engaged as a third-party monitor for Resettlement Plan (RP) implementation. To carry out the resettlement activities, PMU contracted DORP, a local NGO in February 2015.

For the convenient implementation of the Resettlement Plans, P1 and P2 areas were divided into 6 separate Resettlement Plan Sections (1-6). Five resettlement plans for Sections 1, 2, 3, 4 and 6 in P1 and P2 received approval and disclosed on ADB and DWASA websites. Resettlement plan for Section 2 and 5 is being updated. Due Diligence Record (DDR) P3.1 and Resettlement Plan for P3.2 received approval which isdisclosed on ADB and DWASA websites. The resettlement plan for Section 5 will be revised because DWASA needs to useRAJUK[2]'sland within a part of the alignment. This will be submitted by February2022. The resettlement plan for Section 6 has received ADB approvalon 15 November 2021.

Land acquisition is in progress infive sections; 1, 2, 3, 5, and 6. Land in Resettlement Plan 4 is owned by DWASA. In Section 1, 99.6% of the affected persons have been fully paid (CCL and other resettlement assistance). About 90.0% of CCL payment has been completed in Section 2. Payments for the remaining affected persons are still pending due to legal issues. The CCL unpaid affected persons will receive CCL as soon as they submit required land documents to Deputy Commissioner's office. DWASA has deposited the estimated CCL amount to Deputy Commissioner's bank account for the affected persons who are yet to receive CCL. All affected persons who received CCL also received full resettlement assistance which they are entitled to from DWASA. Affected persons who are yet to receive CCL will also receive other applicable resettlement assistance according to the entitlement matrix. PMU has deposited the full estimated amount of BDT 15362393.00 for payment of resettlement assistance in a dedicated account. The required amount for paying resettlement assistance will be kept intact until the last affected person has been paid. CCL payment is on-going in Resettlement Plan section 3 under LA case 5/2018-19. Under this LA case compensation notices have been distributed to 234 affected persons. Out of those 234, About 23% received compensation including resettlement assistance. Another 9% affected persons submitted papers to Deputy Commissioner's office for getting CCL. Out of the remaining 68% affected persons some are processing papers to submit to Deputy Commissioner's office, some have court cases related to land ownership, some have conflict with co-sharers, etc.DORP is motivating affected persons by personal contacts, community meetings, announcements, leaflet distribution, etc. to resolve their problems and receive compensation. Resettlement Plan Section 3 has another LA case 10/2018-19 (it covers a small part of a mouza of Resettlement Plan 5 also). Under this LA case notices under section 7(1) have been distributed to 504 affected persons.

Upon ADB's concurrence, DWASA has handed over land [1st 10 km of raw water pipeline (RWP)] to the DBO contractor on 4 February 2021. The Contractor has started civil works in Section 2.

[2]Rajdhani UnnayanKartripakkha, or RAJUK – the Capital Development Authority of the Government of Bangladesh. It is a Bangladeshi public agency responsible for coordinating urbandevelopment in Dhaka, Bangladesh

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Resettlement plan is being updated for the rest of the 4 km. Contractor will start work in the rest of the 4 kms based on ADB's concurrence on the resettlement plan.They will start work on the rest of the RWP by February2022, subject to ADB approval.

Compensation payment has not started in resettlement plan Section5 and 6. There is a LA case 10/2020-21 in resettlement plan Section5under which 138 LA notices under section 7(1) has been distributed. Resettlement Plan 6 has a LA case 14/2020-2021. In this section 48 LA noticeshave been distributedto the affected persons under section 7(1)

In this reporting period, DORP arranged livelihood and income restoration training programs for 99 affected persons; 1affected person of Section 1 on cow and goat rearing and 98 of Section 2 on cow and goat rearing,chicken and duck rearing, small business, fish culture and tailoring. About 97% of total training recipients are engaged in income-generating activities.

In addition to regular personal contact, in this reporting period, DORP has conducted 92 community meetings. No public consultation wasconducted due to COVID-19. The total number of participants was 923 (359male and 564 female). Key discussion points were: papers required in receiving compensation from Deputy Commissioner's office and additional payment/other resettlement benefits from DWASA,Affected Persons' entitlementspayment for loss of business, trees, etc., determination of the present market value of lands, payment for affected persons with land disputes, livelihood training, unpaid CCL issues, Job opportunities in project's civil works, seeking support from the affected persons in ongoing/ensuing project construction works,and COVID-19 awareness campaign, etc.

Two (2) Grievance Redress Committee (GRC) meetings have been held during this reporting periodfor Resettlement Plan Section 4. In these 2 meetings 2 cases from 2 affected persons have been heard regarding loss of fisheries The 2 affected personshave been advised by GRC for payment.Out of them 1 received payment and another one is under process.

Major tasks that need to be accomplished over the next SSMR period:

- Approval and disclosure of resettlement plans for 5;
- Handing over the rest of the RWP to the contractor, subject to approval by ADB, by February 2022;
- Following up with Deputy Commissioner's office in serving Land Acquisition notices under Section 8(3)(ka) in Resettlement Plan part of 3, 5 and 6;
- Collecting estimate of payable compensation from the Deputy Commissioner's office so that payment could be completed by June 2022;
- Following up with Deputy Commissioner's office to facilitate payment in all the Sections, except Section 4;
- Collecting compensation payment data from Deputy Commissioner's office to update the web-based database;
- Handing over the land of BWDB land to the contractor by March 2022;
- Appointing a Land and Resettlement Officer has been advised to support affected persons and SIU, PMU to facilitate resolution of the legal problems and CCL receipt.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

ABBREVIATIONS

ADB	Asian Development Bank
AFD	Agence Française de Dévelopment
BDT	Bangladeshi Taka
CCGP	Cabinet Committee for Government Purchase
CLAC	Central Land Acquisition Committee
COVID-19	Coronavirus disease of 2019
DBO	Design-Build-Operate or Design-Build-Operation
DLAC	District Land Acquisition Committee
DORP	Development Organization for the Rural Poor
DDR	Due Diligence Record
DESWSP	Dhaka Environmentally Sustainable Water Supply Project
DWASA	Dhaka Water Supply and Sewerage Authority
EIA	Environmental Impact Assessment
EIB	European Investment Bank
FGD	Focus Group Discussion
GRC	Grievance Redresses Committee
GRM	Grievance Redresses Mechanism
JVC	Joint Verification Committee
JVS	Joint Verification Survey
MLGRDC	Ministry of Local Government Rural Development Cooperatives
MDSC	Management, Design and Supervision Consultant
MLD	Millions of Litres Per Day
MML	Mott MacDonald Limited
MODS	Maintenance, Operations and Distribution Services
MoU	Memorandum of Understanding
MSC	Management and Supervision Consultant
PMC	Project Management Consultant
PPMS	Project Performance Management System
PMU	Project Management Unit
PVAC	Property Valuation Advisory Committee
RAC	Resettlement Advisory Committee
RWP	Raw Water Pipeline
SIU	Safeguard Implementation Unit
SPS	Safeguard Policy Statement
ToR	Terms of Reference
WIA	Water Intake Area
WTP	Water Treatment Plant

Contents

EXECUTIVE SUMMARY 3

ABBREVIATIONS 6

CONTENTS 6

1 PREAMBLE 9

2 BACKGROUND OF THE REPORT AND PROJECT DESCRIPTION 11

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

2.1 Background (/context) of the Report 11
2.2 DESWSP Components 12
2.3 Project Description 13
2.3.1 Output 1: New surface water supply system developed 13
2.3.2 Project Cost 14
2.3.3 Project Completion Targets 15
2.3.4 Output 1 Implementation Progresses 15
2.4 Social Safeguards Categorization of the Project 15
2.4.2 Indigenous People's Categorization 16

3 SCOPE OF THE SOCIAL SAFEGUARDS IMPACTS BY THE PROJECT 17

Source: Prepared by PMU 18
3.1 Summary of Identified Impacts and Mitigation 19
3.1.1 Resettlement Plan Update and Public Consultation 22
3.2 Reporting Period and Frequency of Submission 22

4 COMPENSATION AND REHABILITATION 23

4.1 Framework, Policies, and Acts for Resettlement Plan Implementation 23
4.2 Process of Resettlement Plan Implementation 23
4.3 Progress of Resettlement Plan Implementation 25
4.3.1 Updating Resettlement Plans 25
4.3.2 Progress in Lands Acquisition and handing over to Contractor 27
4.3.3 Progress in Payment of CCL and Other Benefits 29
4.3.4 Progress in Livelihood and Income Restoration Program 31

5 PUBLIC PARTICIPATION AND CONSULTATION 36

5.1 Public Consultation 36
5.1.1 Public Participation and Information Dissemination on Key Aspects 36
5.1.2 Gender segregation 38
5.2 Disclosure of Resettlement Plans 39

6 GRIEVANCE REDRESS MECHANISM (GRM) 40

6.1 Grievance Redress Committees (GRC) 41
6.2 Scope and Jurisdiction of GRC 41

7 INSTITUTIONAL ARRANGEMENT 43

7.1 Project Implementation Partners 43

8 MONITORING RESULTS – FINDINGS 45

9 COMPLIANCE STATUS 49

9.1 Compliance to relevant Loan Covenant 49

10 FOLLOW UP ACTIONS, RECOMMENDATIONS, AND DISCLOSURE 52

11 APPENDIX 54

11.1 Minutes PVAC meeting_Section-3 (LA case-5)_Bangla 54
11.2 Minutes PVAC meeting_Section-3 (LA case-5)_English 60

ORGANIZED BY WATER SUPPLY AND SEWERAGE AUTHORITY DHAKA UNDER THE MINISTRY OF LOCAL GOVERNMENT RURAL DEVELOPMENT AND COOPERATIVES (MLGRDC) 60

11.3 List of affected persons in Section 2_paid in reporting period 65
11.4 List of affected persons in Section 3_paid in reporting period 67
11.5 Photos of Comparative Structures 77
11.6 Monitoring Report on CCL Unpaid Affected Persons 80
11.7 Cow & goat rearing in Section 1 92
11.8 Cow & Goat_3rd Batch 93
11.9 Cow & Goat_4th Batch 95

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.10 Small business training (2nd Batch) 97
11.11 Small Business (3rd Batch)....99
11.12 Chicken & Duck Rearing (3rd Batch)....102
11.13 Fish Culture....104
11.14 Tailoring....105
11.15 Pictures on Community Meeting, LIRP & IGA....107
11.16 Microfinance involvement in Section-1....112
11.17 Microfinance involvement in Setion-2....117
11.18 Microfinance involvement in Section-4....129
11.19 Request Letter for COVID Vaccine on Site_Bangla....132
11.20 Request Letter for COVID Vaccine on Site_Engalish....133
11.21 Summary of Community Meetings (July to December 2021)....134
11.22 Awareness Campaign Notice to APs regarding CCL and Resettlement Assistance_Bangla....136
11.23 Awareness Campaign Notice to APs regarding CCL and Resettlement Assistance _English.....137
11.24 8th GRC Meeting Minutes_14-10-2021_Bangla....146
11.25 9th GRC meeting minute_23.12.2021_Bangla....150
11.26 8th GRC Meeting Minutes_14-10-2021_English....153
11.27 9th GRC Meeting Minutes_23.12.2021_English....156
11.28 Summary of GRC meetings in English....158

Tables

Table 2.1: Funding of project....14
Table 2.2: Project completion target dates....15
Table 3.1: Land Acquisition and Resettlement Impacts....19
Table 3.2: Length of Pipelines in each Section of Resettlement Plan and DDR....21
Table 4.1: Availability of Work Front....29
Table 4.2: Distribution of Eligible Affected Persons who are Vulnerable and who lose Full Agriculture-based Livelihood....32
Table 4.3: Distribution of Affected Persons by Type of Training Received....32
Table 4.4: Distribution of Affected Persons who received Training and Engaged in IGA....33
Table 4.5: Distribution of Affected Persons who received Training and Linked with NGOs/ microfinance institutions....34
Table 4.6: Distribution of Vulnerable Affected Persons....34
Table 8.1: Semi-Annual Social Safeguards Progress Checklist for P1, P2, P3.1, and P3.2....47
Table 9.1: Progress in training and income generation engagement....49
Table 10.1: Follow up actions, recommendations, and disclosure....52

Figures

Figure 2.1: Source- Surface water treatment and transmission....12
Figure 2.2: Services – distribution network strengthened....12
Figure 2.3: 3D view of Meghna river Intake....13
Figure 2.4: 3D view of Water Treatment plant....13
Figure 2.5: 3D view of a River Crossing....14
Figure 2.6: 3D view of a large diameter Pipeline....14
Figure 3.1: Location Map of Pipeline Route for Packages 1, 2, 3.1, and 3.2....18
Figure 4.1: Process of Resettlement Plan Implementation and site handover to Contractor....23
Figure 4.2: Progress on Land Acquisition....28
Figure 4.3: Female participation in LIRP training....35
Figure 5.1: Trend of female participation in the social consultation meetings....38
Figure 6.1: Grievance Redress Mechanism Flow Chart....40
Figure 7.1: Social Safeguards Plans Implementation partners relationship and flow of information....43

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

1 Preamble

The Asian Development Bank approved a loan amounting to $250 million equivalent from its Special Funds resources for Dhaka Environmentally Sustainable Water Supply Project on 22 October 2013. Subsequently, Loan Agreements between the Government of Bangladesh and each of Asian Development Bank, AgenceFrançaise de Développement, and European Investment Bankwere signed on 24 April 2014, 29 January 2015, and 30 June 2014, respectively.

Dhaka Water Supply and Sewerage Authority, on behalf of the Government of Bangladesh, is the executing Authority of the project.

DWASA presentsthis13thSemi-annual Social Safeguards Monitoring Report (Semi-annual SSMR) in compliance with the requirement of paragraph 91 of item B. Monitoring under Section IX. Performance Monitoring, Evaluation, Reporting, and Communication of the Project Administration Manual (PAM) (December 2020).

The contents of this report, as outlined in Appendix 13 of the PAM, are

- Executive Summary
- Background of the Report and Project Description
- Scope of Impacts
- Compensation and Rehabilitation
- Public participation and consultation
- Grievance Redress Mechanism (GRM)
- Institutional Arrangement
- Monitoring Results – Findings
- Compliance Status

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

2 Background of the Report and Project Description

2.1 Background (/context) of the Report

According to the Resettlement Framework (ref Appendix C - copy of Appendix 13 of the PAM), the Project Director has to submit to ADB, a semi-annual report on the status of implementation of safeguard plans and progress made towards the desired outcomes of the project in compliance with the ADB Safeguard Policy Statement (2009).

PMU has prepared this report as a deliverable to ADB. MDSC assistedPMUin compliance with the Clause no. 18 (iii) of the Terms of Reference for the Management, Design and Supervision Consultant (MDSC) - Mott MacDonald to assist the Project Director in reporting to ADB on the status of implementation of 'Social Safeguard Plans', which are termed as 'Resettlement Plans' for the DESWSP.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

2.2 DESWSP Components

The DESWSP comprises,

i. (Source/Intake) development, water treatment, and distributionpipelines, comprising: 1,000 MLD river intake, 500 MLD treatment works (phase -1),22 km raw water and14 km treated water transmission pipelines, 24 km primary distribution pipelines,and 42 km of feeder pipelines to northern Dhaka;
ii. (Services) distribution network strengthened, comprising: rehabilitating 376 km of distribution networks and 32,000 household and community connections, and legalization of 37,000 households and community connections at MODS Zone – 6;
iii. Construction of at least 1,000 community toilets and bathing chambers with separate units for males/females in low-income communities in Dhaka city (added in 2020).

Figure2.1:Source- Surface water treatment and transmission

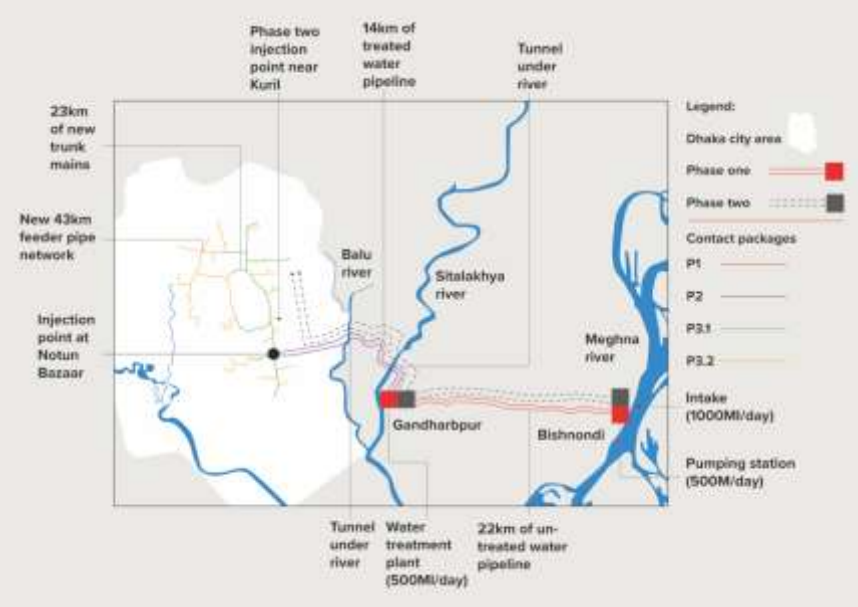

Figure2.2:Services – distribution network strengthened

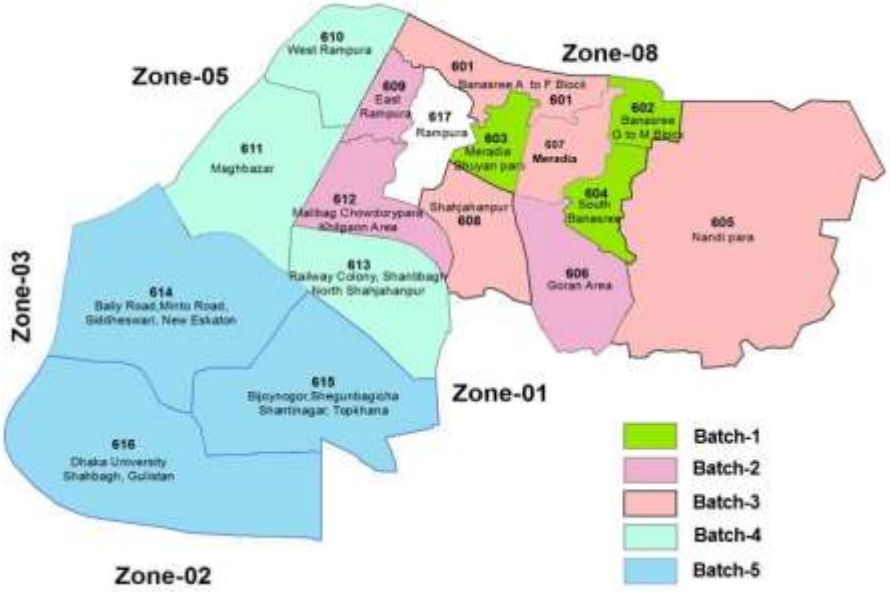

This report covers implementation progresses of the 'Social Safeguard Plans; for Output 1: New surface water supply system developed (ref: **Figure 2.1**) out of 4 defined outputs (detailed below) of the DESWSP.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

2.3 Project Description

The Dhaka Environmentally Sustainable Water Supply Project (DESWSP) has a target impact (Goal) of "Improved access to and quality of sustainable water supply services in Dhaka (City)".

The Project's Design Monitoring Framework defined an outcome of "More reliable and improved security of water supply and sanitation in Dhaka" resulting fromthe project achieving the targeted 'impact'. The DMF defined the following additional outputs toachieve the 'outcome':

- **Output 1: New surface water supply system developed (Figure2.1)**;
- Output 2: Distribution network strengthened (**Figure2.2**);
- Output 3: Project management and administration adequately supported; and
- Output 4: Empowerment of women and vulnerable groups supported.

Output 4 was added with the proposal for additional funding in 2020.Implementation of Outcome 4 will commence upon loan effectivity.

2.3.1 Output 1: New surface water supply system developed

The Social Safeguards Plans, this report covers, for the components (indicators) of the 'new surface water supply system developed' are described hereunder.

Package 1: River intake, raw water pipeline, and Gandharbpur treatment plant

- 1000 MLD river intake in the Meghna river at Bishnandi, AraihazarUpazila, with a 500MLD raw water pumping station, stand-by power supply station, workshops, offices, and accommodation for DWASA staff.

Figure2.3: 3D view of Meghna river Intake

Figure2.4: 3D view of Water Treatment plant

- 22km raw water transmission pipeline (twin 1600 mm pipes sized for 500MLD) through rural areas with an access road beside from the river intake to the water treatment plant (**Figure2.1**). and
- 500 MLD surface water treatment plant (WTP) at Gandharbpur, Rupgonj Upazila, with storage reservoir, treated water pumping station, standby power supply, workshop, chemical storage, offices, and accommodation for DWASA staff (**Figure2.1**:**Source- Surface water** treatment and transmission**)**.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Figure2.5: 3D view of a River Crossing

Package 2: Treated water transmission pipeline to Dhaka

Construction activities of P2 will take 36 months. The construction will include:

- 14 km treated water transmission pipeline (twin 1600mm pipes) from Gandharbpur WTP to Dhaka (Vatara junction on Madani Avenue, at Natun Bazar near the American Embassy), where it connects to the P3.1 pipeline (**Figure2.1**).
- Two under-river tunnels for the pipeline: one at Murapara - Isakhali under the Sitalakhya river, and one at Beraid under the Balu river (**Figure2.1**:Source- Surface water treatment and transmission)

Figure2.6: 3D view of a large diameter Pipeline

Package 3.1: Primary distribution pipelines in Dhaka

Construction activities of P3.1 will take36 months. Theconstruction will include:

24 km of large diameter pipes of 0.8m to 1.6m diameter, all under major Dhaka highways to transfer the potable water to the P3.2 feeder pipelines (**Figure2.1**).

Package 3.2: Feeder pipelines distribution in Dhaka

Construction activities of P3.2 will take 30 months. The construction will include:

42 km of feeder pipes from 350 to 800mm diameter, all under Dhaka roads, to deliver water to the District Metering Areas (DMAs) that feed individual water supply zones of Dhaka City (**Figure2.1**).

2.3.2 Project Cost

The overall cost including additional funding of the DESWSP stated in the 1st December 2020 Aide Memoire is US$ 1 104.9 million as summarized inTable2.1: Funding of project.Additional funding is still being finalized between GoB and Financiers.

Table2.1: Funding of project

Source of Funding	Original	Additional	Total
ADB	250.00	140.00	390.00
Regular loan (OCR)	*-*	*85.00*	*85.00*
Concessional Loan (OCR)	*250.00*	*50.00*	*300.00*
Special Funds Resources (AFD)	*-*	*5.00*	*5.00*
AFD	64.00	140.90	204.90
EIB	136.00	-	136.00
Government	224.90	149.10	374.00
Total	**674.90**	**430.00**	**1 104.90**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

2.3.3 Project Completion Targets

The revised project completion target, as agreed during November 2020 ADB Mission, is December 2024. The target dates toachieve the project outcome and outputs are given below.

Table2.2: Project completion target dates

Outcome:	More reliable and improved security of water supply and sanitation in Dhaka		December 2025
	Output 1:	**New surface water supply system developed**	**December 2024**
	Output 2:	Distribution network strengthened	Completed
	Output 3:	Project management and administration adequately supported	December 2024
	Output 4:	Empowerment of women and vulnerable groups supported	December 2023

2.3.4 Output 1 Implementation Progresses

At the end of the reporting period, the engineering works progress of various components of the Output 1: New surface water supply system developed are as below:

Package 1: River intake, raw water pipeline, and Gandharbpur treatment plant

Construction Component	Progress	Time elapsed	Comments
Construction (Overall)	**46.8%**	**53.5%**	**6.7% delay**
Intake (River)	50.0%	59.0%	9% delay
Water Treatment Plant	57.5%	58.6%	Catching up on the delay
Raw Water Pipeline	10.1%	28.8%	Site inundated by flood

***Source**: MDSC QPR Q4 2021*

Package 2: Treated water transmission pipeline to Dhaka

Project Stage	Signing of Contract	**Commencement**	15 September 2021
Progress	Contract Signed on 6 May 2021		

***Source**: MDSC QPR Q4 2021*

Package 3.1: Primary distribution pipelines in Dhaka

Project Stage	Signing of Contract	**Commencement**	March 2022 (scheduled)
Progress	Contract Signed on9 September 2021		

***Source**: MDSC QPR Q4 2021*

Package 3.2: Feeder pipelines distribution in Dhaka

Project Stage	Procurement	**Bid Evaluation**	March2022(Expected)
Progress	Technical Bid Evaluation Report approved on 30 November 2021.	**ADB Approval to Bid Evaluation Report**	Financial Bid under Evaluation. (Expected by March 2022)

***Source**: MDSC QPR Q4 2021*

2.4 Social Safeguards Categorization of the Project

2.3.1 Involuntary Resettlement Categorization

Considering the extent of the significance of involuntary resettlement impacts, ADB has classified projects into four categories; A, B, C, and FI. The DESWSP falls under Category A as there would be 200 or more persons physically displaced from home and/or lose 10% or more of their productive and/or income-generating assets.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

2.4.2 Indigenous People's Categorization

The DESWSP falls under Indigenous People's Category C as there noIndigenous People's household has been found during the socioeconomic household surveys.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

3 Scope of the Social Safeguards Impacts by the Project

A single Resettlement Plan for the project was prepared in 2013 covering the then identified three packages P1: River intake, raw water pipeline, and Gandharbpur treatment plant, P2: Treated water transmission pipeline to Dhaka,and P3: Distribution Reinforcement Pipeline. At a later stage, during detailed designing, package P3 was divided into two, namely, P3.1: Primary distribution pipelines in Dhaka and P3.2: Feeder pipelines distribution in Dhaka.

The Resettlement Plan identified that the project has major impacts on both private and public lands, and other assets such as structures, livelihoods, crops, and trees.

A single Resettlement Plan for the DESWSP,covering areas required for Output 1 (P1, P2, P3) and ICB 2.7 under Output 2, was prepared in 2013, which identified major impacts on lands, the scope of land acquisition, and other resettlement impacts based on the design of the project. The areas of P1 and P2were subsequently divided into 6 sections to facilitate the Resettlement Plan implementation. The packages P1 and P2 require a total of 310.71acres of land where a total of 183.15acres privately owned lands and 46.03acres of public-owned except water treatment plant. DWASA owns the required land (81.53 acres) for the water treatment plant.

P3.1 and P3.2 run through the developed lands (roads) of Dhaka North and South City Corporations. No land acquisition is required for these packages rather necessary permission to work through the alignment would be sorted from the City Corporations.

Due Diligence Report (DDR) for P3.1 has been approved and disclosed by ADB in February 2020. PMU with the assistance of MDSC prepared Resettlement Plan for P3.2 as temporary impacts(temporary income losses to shopowners/vendors and employees) were found due to laying of the feeder pipelines for an estimated period of 14 daysin one of the pipe routes. ADB has provided no objection on 15 May 2020. This RP has been updated during loan processing for additional financing.

According to the design for the implementation of P1 and P2, water intake sits on only private lands that needed land acquisition; the Water treatment plant is situated on DWASA's own lands (81.50 acres). A few encroacherswere identified on this land. All the encroachershave been compensated. DWASA has handed over 4.67 acres of land to Bangladesh Water Development Board (BWDB) that fall within the corridor of pipelines, which needs to be taken back following government procedures.The remaining required public lands require the acquisition and/or securing permissions from various government and semi-government/autonomous organizations.

Later, for easy management and implementation of Resettlement Plans, the whole area, required by the packages P1 and P2,is divided into 6 sections as detailed below:

- RP Section 1: Water Intake Area
- RP Section 2: Intake to Baliapara (Raw water pipeline)
- RP Section 3: Darikandi Chak to Murapara via Gandharbpur WTP (Part of Raw water pipeline+part of treated water pipeline)
- RP Section 4: Water Treatment Plant (WTP) at Gandharbpur
- RP Section 5: Rupganj (Shitalkhya West bank) to Balu River (East bank) (Treated water pipeline) and
- RP Section 6: West Bank of Balu River to Vatara along Madani Avenue up to Baridhara[3].

The spread of each Resettlement Plan section is shown in below **Figure 3.1**.

[3]Resettlement Plan mentioned at Vatara but later, during detailed designing, the location has been identified as Balu River (West bank) to the junction of Pragati Sarani and Madani Avenue at Natun Bazar.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Figure3.1:Location Map of Pipeline Route for Packages 1, 2, 3.1, and 3.2

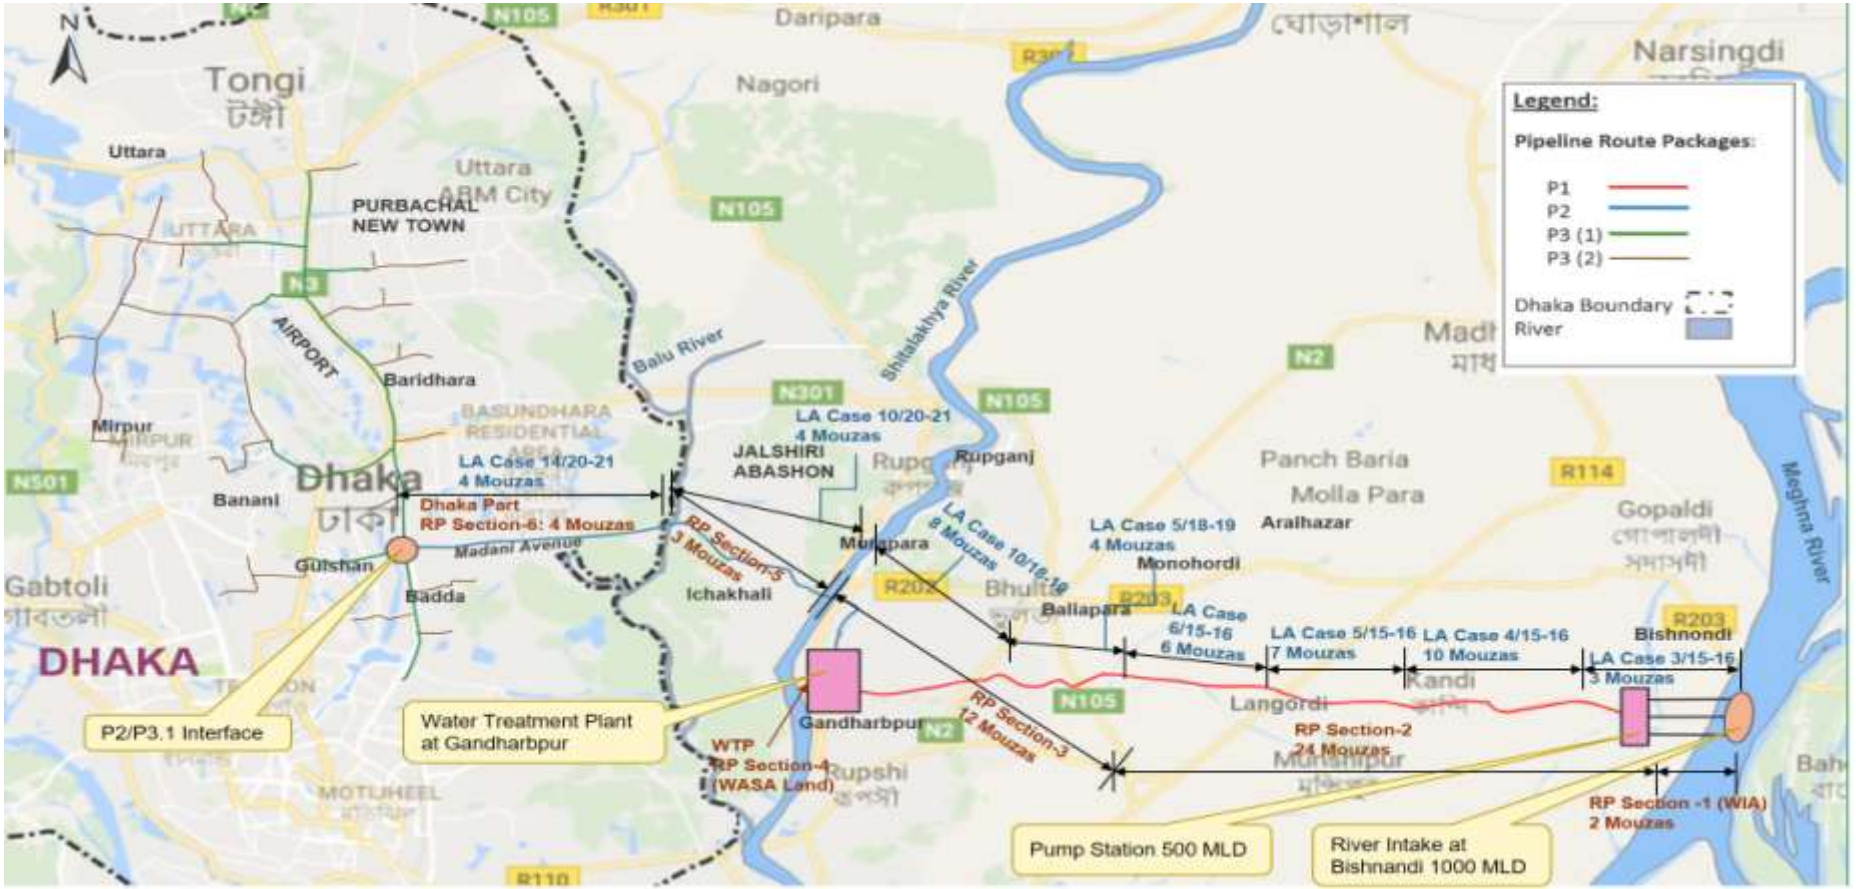

Source: Prepared by PMU

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

3.1 Summary of identified Impacts and mitigation

The below table presentsa summary of the land requirements with areas and types of impacts identified so farwithin the areas of packages P1 and P2.

Table3.1: Land Acquisition and Resettlement Impacts

RP Section Nos.	Locations	Land Requirement for Acquisition(in acre)			Structure and other impacts	Comments / Status
		Total	Public	Private		
1 (P1)	Water Intake Area (WIA)	21.37	7.15	14.22	Agriculture and fish livelihood	232[4] affected persons have been identified by the Deputy Commissioner's office and by the executing agency (DWASA) including non-titleholders. These numbers may vary after the completion of payment (CCL and other resettlement assistances). Compensation.23 households significantly lose their agriculture-based livelihood. Compensation was paid to 231 affected persons. The remaining 1 person submitted papers to Deputy Commissioner's office for getting CCL.
2 (P1)	Intake to Balia Para	109.32	4.59	104.73	Agriculture, livelihood, and structure	1656[5] affected persons have been identified by the Deputy Commissioner's office and by the executing agency (DWASA)includingtenants and wage labors. These numbers may vary after the completion of all payments (CCL and other resettlement assistances). Therewere 290 structures also affected.All of the structures have been paid and relocated now. 47 households significantly lose their agriculture based livelihood.In total 1510 affected persons received CCL and other resettlement assistance. The remaining are 158[6] affected persons who have legal issues.
3 (P1+P2)	DarikandiChak (start of Rupganj) to Murapara via Gandharbpur WTP	62.74	25.04	37.70	Agriculture, structure and livelihood	Approximately 738[7] affected persons have been estimated by the Deputy Commissioner's office after the Joint verification survey. These numbers may vary after the completion of all payments (CCL and other resettlement assistances). In addition, 53 non-titleholders affected persons have been identified

[4]In total 231 (222 titled+9 non-titled) affected persons.
[5] In total 1656 (1590 titled+66others (13 tenants+53 wage labor) affected persons of which 1510 receivedpayment.
[6]There were 166 CCL unpaid affected persons were reported. Out of them 1 affected person won the courtcase and received CCL and 7 affected persons lost the case. Three (3) newly identified affected persons also received CCL.
[7]There are two LA cases in section 3 such as LA case 5/2018-19 and LA case 10/2018-19.LA notice under 8(3)(ka) distributed to 234 affected persons against LA case 5/2018-19 and LA notice under 7(1) distributed 504 affected persons against LA case 10/2018-19. CCL paymenthas been started forLA case 5/2018-19 but yet to start forLA case 10/2018-19.PMU awaits for estimate for CCL payment for LA case 10/2018-19.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

RP Section Nos.	Locations	Land Requirement for Acquisition(in acre)			Structure and other impacts	Comments / Status
		Total	Public	Private		
						who will be compensated. There are 141 primary structures and 266 secondary structures will also be affected. 20 households significantly lose their agriculture based livelihood.
4 (P1)	Water Treatment Plant (WTP)	81.53	DWASA land	No private land	Structure, agriculture, and livelihood	This land is DWASA's own land. 258 affected persons have been identified as non-titleholders.It also impacted 60 structures (51 primary and 9 secondary). 257 affected persons and all structures have been paid and relocated.Four (4) affected persons have been identified by GRC. One (1) affected person has been requested to submit proper documents for getting compensation.
5 (P2)	Rupganj (West bank of Sitalakhya river) to Balu river (East bank)	21.52	0.45	21.07	Structure, pond, agriculture, and livelihood	138 affected persons have received Land Acquisition notice under section 7(1)[8]. These numbers may vary after the completion of all payments (CCL and other resettlement assistances.In addition, according to Resettlement Plan 197 primary and 170 secondary structures will be affected. No households face significant loss of their agriculture base livelihood.It may vary because resettlement plan is being revised based onactual 1.9 km area only.
6 (P2)	Balu river to the junction of Pragati Sharani and Madani Avenue at Natun Bazar	14.23	8.79 [6.5 km(RAJUK road)=7.88 acres + 0.92acres (Public lands)]	5.43	Agriculture, Structures, and livelihood	Land Acquisition notice under section 7 (1)[9] has been distributed to 48affected persons by Deputy Commissioner's office. These numbers may vary after the completion of all payments (CCL and other resettlement assistances). It also impacts 33 non-titleholder affected persons(28 business person and 5 wage laborers). There are 6 primary structures identified.91 households are facing significant loss of their agriculture base livelihood. Out of 6.5 km long pipelines, about 5.5km RAJUK[10]roads will be used for the installation of pipes.
P3.1	Primary Distribution Pipelines	0	0	0	No resettlement impact found	24 km pipelines. Due Diligence Report (DDR) has been approved and

[8]This LA notice has been distributed under LA case 10/202-21.
[9]This LA notice has been distributed under LA case 14/202-21.
[10]Rajdhani UnnayanKartripakkha, or RAJUK – the Capital Development Authority of the Government of Bangladesh. It is a Bangladeshi public agency responsible for coordinating urbandevelopment in Dhaka, Bangladesh.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

RP Section Nos.	Locations	Land Requirement for Acquisition(in acre)			Structure and other impacts	Comments / Status
		Total	Public	Private		
						disclosed. The pipeline will be laid along roads/land which belong to different organizations such as Dhaka North City Corporation (DNCC), Roads & Highways Department (RHD), Dhaka Cantonment Board (DCB) and Bangladesh Railways (BR). No objection certificates (NOC) will be obtained for use of the land before project implementation.
P3.2	Feeder Pipelines				Temporary impact on livelihood and temporary structures.	42 km pipelines. There are 28 pipeline routes covering 42 km. Involuntary resettlement impacts has been identified in one pipeline route, named Matikata Bazar (other pipeline routes do not have any impact). In this route, there are 95 temporary shop owners/vendors and 113 employees who will be affected due to the laying of the feeder pipelines for an estimated period of 7 days. The entire civil works under this component for the feeder pipeline network are proposed on the land owned by different government organizations, Dhaka North City Corporation (DNCC), Roads and Highway Department (RHD), Dhaka Cantonment Board (DCB), and Bangladesh Railways (BR), etc. No objection certificates (NOC) will be obtained for use of the land before project implementation.
Total land		**310.71**	**127.56**	**183.15**		

Source: PMU provided plot schedule as of June 2020. No change occurred during this reporting period.

The section-wise length of the pipelines is given below:

Table3.2: Length of Pipelines in each Section of Resettlement Plan and DDR

Name of Section	Type of Pipeline	Length
Section 2	Raw Water Pipeline	14.25 km
Section 3	Raw Water Pipeline +Treated Water Pipeline	7.75 km + 2 km
Section 5	Treated Water Pipeline	5 km.
Section 6	Treated Water Pipeline	7 km.
P3.1	Primary Distribution Pipelines	24 km.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Name of Section	Type of Pipeline	Length
P3.2	Feeder Pipelines	42 km.
Total		**102 km.**

3.1.1 Resettlement Plan Update and Public Consultation

The INGO, DORP under the guidance of MDSC is assisting DWASA in updating the Resettlement Plans and implementation of the resettlement activities for the Resettlement Plan Sections 1 to 6 covering Packages P1 and P2. DORP has updated six (6) draft resettlement plans (1-6).Out of these, Resettlement Plan for Section 2 (non-priority mouzas) and Section 5 are due for approval. Resettlement Plan for Section 6 received approval during this reporting period on 15 November 2021. Updated Resettlement Plan Section 5 had been submitted to ADB on 25 November 2021. But it needs further update as per ADB advice. The Resettlement Plan will be prepared only for the actual pipe alignment proposed under DESWSP.

Resettlement Plan Section 2 for non-priority mouzas has been submitted to ADB on 1 December 2021 and comments have beenreceived.

Regular consultations with the affected persons and other stakeholders are being conducted by DORP to ensure that affected persons are fully aware of the project interventions and about their entitlements in case of involuntary land acquisition and resettlement assistances for affected persons (titled and non-titled holders).

PMU with the assistance of MDSC has prepared DDR for P3.1 which is approved by ADB and uploaded on ADB and DWASA website. Resettlement Plan has been prepared for P3.2 which received no objection from ADB, which has also been disclosed on ADB and DWASA website. This will be updated beforethe start of civil works.The contract for P3.1 has been signed on 9 September 2021. INGO namely Knowledge Management Consultants Ltd (KMC)has been appointedfor resettlement plan implementation for packages P3.1 and P3.2. KMC signed contract with DWASA on 20 December 2021.

3.2 Reporting Period and Frequency of Submission

In compliance with the requirement of paragraph 91 of item B. Monitoring under section IX. Performance Monitoring, Evaluation, Reporting, and Communication of the Project AdministrationManual (PAM) (December 2020) this Social Safeguards Monitoring Report is due Semi-annually.

The submission would cover six months of every January to June and July to December of each year till the completion of the project.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

4 Compensation and Rehabilitation

4.1 Framework, Policies, and Acts for Resettlement Plan Implementation

Involuntary resettlement follows DESWSP Resettlement Framework of 2013, ADB Safeguard Policy Statement (SPS) of 2009, and national legislations of GoB that include Acquisition of Immovable Property Ordinance (ARIPO) of 1982 as well as Acquisition and Requisition of Immovable Property Act (ARIPA) of 2017.

Resettlement Plans for Sections 1, 2, and 4 have been updated based on the then ARIPO of 1982 asthe land acquisition processes for the sections started beforeARIPA 2017 was enacted. The Acts, ARIPA 2017, is applicable for updating and implementing Resettlement Plans for Resettlement PlanSections 3, 5, and 6. Packages P3.1 and P3.2 will also be following ARIPA 2017.

4.2 Process of Resettlement Plan Implementation

The Resettlement Plan implementation, starting from Identification of land details and preparing Land Acquisition proposalby DWASA to handing over the site to contractor post completion of settlement of payments to affected persons, follows a systematic and lengthy process, which may be defined in a 6-staged process as presented below:

Figure4.1:Process of Resettlement Plan Implementation and site handover to Contractor

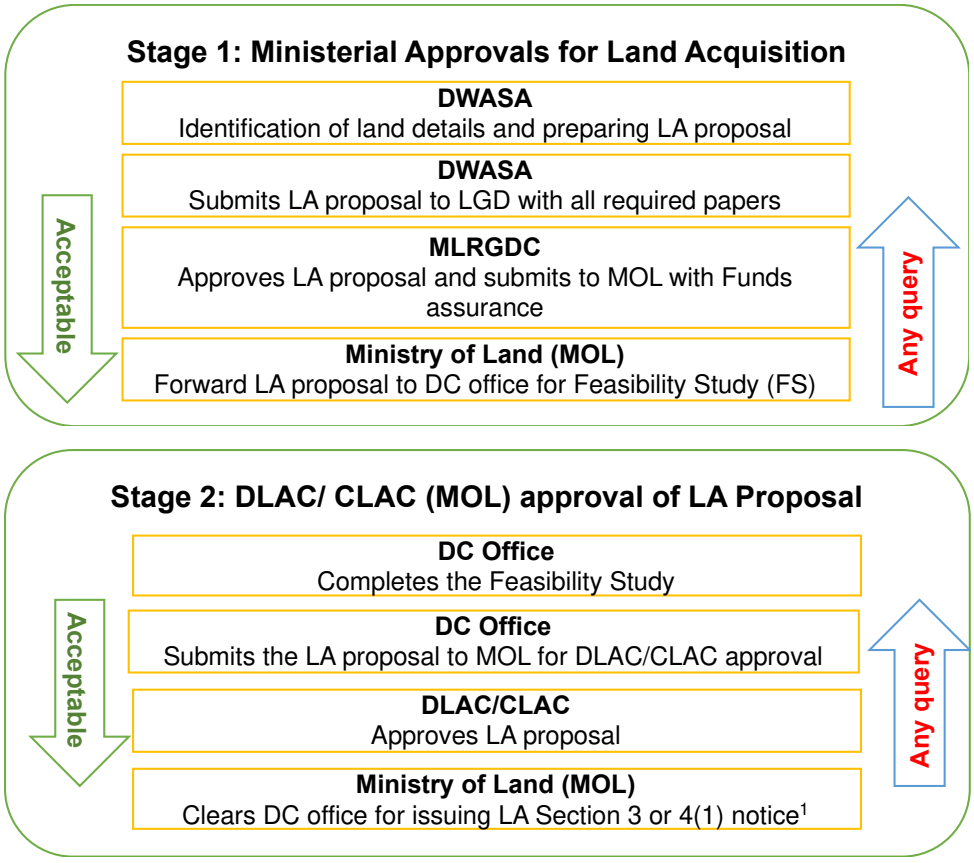

[1] Section 3 in compliance with Acquisition and Requisition of immovable Property Ordinance ARIPO 1982 (applicable to RP for Section 1 and 2) and Section 4(1) in compliance with Acquisition and Requisition of Immovable Property Act (ARIPA), 2017 (applicable to RP Section 3 to 6 and p3.1 and P3.2). This applies to other Land Acquisition Sections as referred to next.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

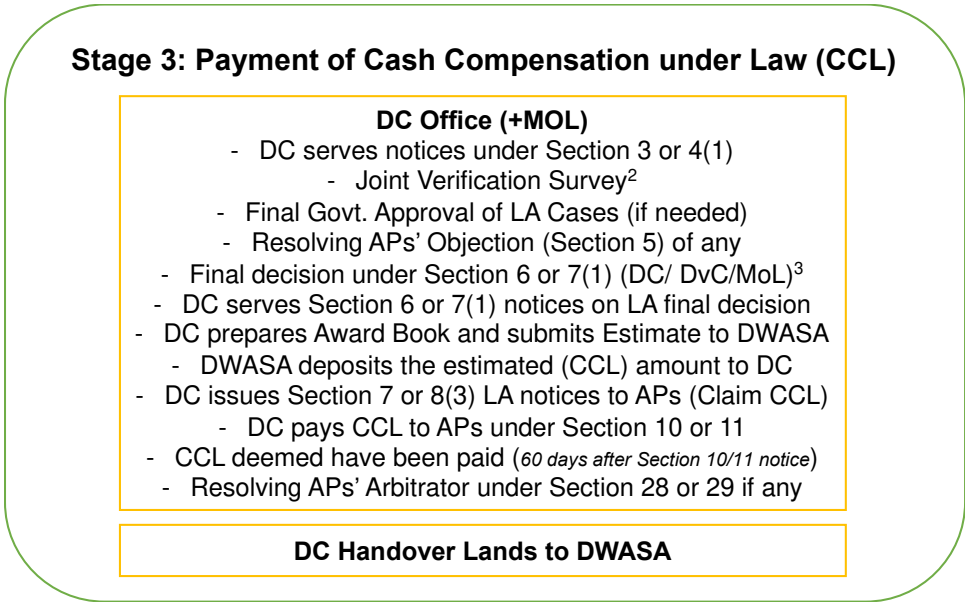

[2] Comprises of Deputy Commissioner's LA offices, PMU, and other relevant government departments and ministries.

[3]Depends on the size of required lands; Deputy Commissioner's (<50 bighas) or Divisional Commissioner (> 50 bighas).

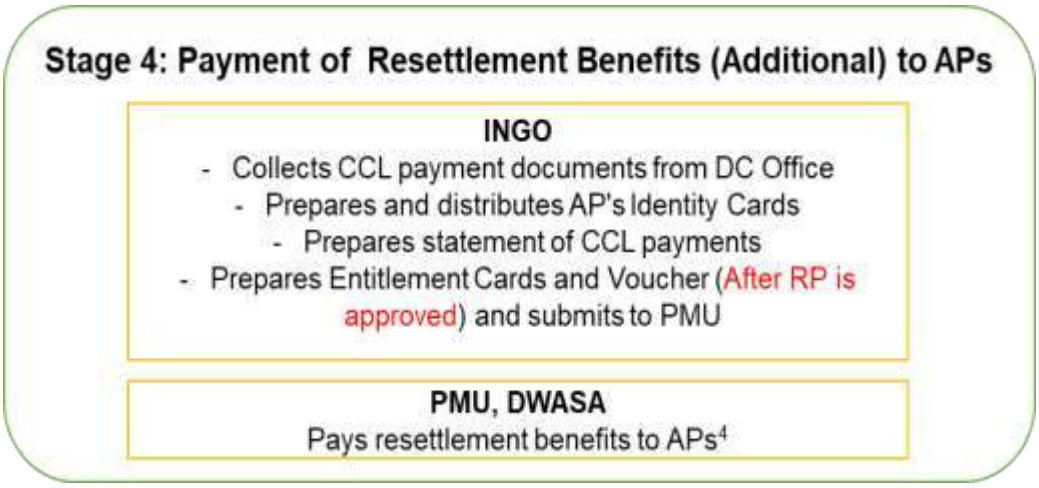

[4]Subject to the approval of Resettlement Plan.

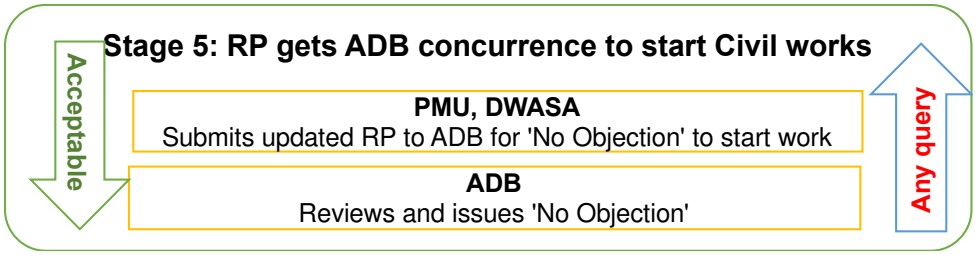

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

4.3 Progress of Resettlement Plan Implementation

4.3.1 Updating Resettlement Plans

ADB approved draft Resettlement Plans for Sections 1, 2, 3,4, and 6. Resettlement Plan for Section 2 (10 km of raw water pipeline through 21 priority mouzas) updated further with payment status and received ADB concurrence on 3 February 2021.

Draft Resettlement Plan forSection 5 was submitted to ADB on 25 November 2021. However, this Resettlement Planneeds to befurther updatedas mentioned in the previous section. This resettlement plan will be updated based on the final alignment.

The third revision of the Resettlement Plan for Section2 (non-priority mouzas)has been submitted to ADB on 01 December 2021 and awaiting for clearance by ADB.

The section-wise Resettlement Plan status is presented below:

RP Section 1	*Water Intake (P1) at Bishnandi, Araihazar Upazila*	
Status of Draft Resettlement Plan	ADB approved (19 November 2018)	[1] updated further with payment data and dedicated account details.
Status of Updated Resettlement Plan	Submitted to ADB[1] (12 December 2020)	
Land handed over by Deputy Commissioner	April 2018	
ADB Concurrence to start Civil Works	November 2019	
Access to Contractor	100%	
Status of Construction	Construction in progress (at 50.0%)	

RP Section 2	*Raw Water Pipeline (P1): Water Intake to Baliapara (end of Araihazar Upazila)*	
Status of Draft Resettlement Plan	ADB approved (4 April 2019)	[1] updated further with payment data and DDR for the 4 km second priority mouzas.
Status of Updated Resettlement Plan	Submitted to ADB[1] (December 2021)	
Land handed over by Deputy Commissioner	April 2018	
ADB Concurrence to start Civil Works	February 2021 (part, 10 km)	
Access to Contractor	First 10 km of RWP. The remaining 4 km will be given in February 2022 subject to ADB 's concurrence on the resettlement plan for this remaining 4 km.	
Status of Construction	Construction in progress (at 10.10%)	

RP Section 3	*Raw Water Pipeline (P1) & Treated Water Pipeline (P2): Darikandi Chak(start of Rupganj Upazila) to Murapara via Gandharbpur WTP*
Status of Draft Resettlement Plan	ADB approved (28 November 2019)
Status of Updated Resettlement Plan	Will be updated with DDR
Land handed over by Deputy Commissioner	CCL payment started, 7% completed. Land yet to handover
ADB Concurrence to start Civil Works	Subject to payment
Access to Contractor	Yet to handover
Status of Construction	Yet to start

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

RP Section 4	*Water Treatment Plant (P1) at Gandharbpur*
Status of Draft Resettlement Plan	ADB approved (19 November 2018)
Status of Updated Resettlement Plan	No need of further updateas payment is completed
Land handed over by Deputy Commissioner	DWASA's own land
ADB Concurrence to start Civil Works	November 2019
Access to Contractor	100%
Status of Construction	Construction in progress (at 57.50%)

RP Section 5	*Treated Water Pipeline (P2): Rupganj (Shitalkhya West bank) to Balu River (East bank)*	
Status of Draft Resettlement Plan	Draft submitted on 25 November 2021	[1]This resettlement plan will be revised. Revision will be based on 1.9 kmfinal alignment of DWASA. A due diligence report (DDR) will be prepared for 3 km long RAJUK land upon acquisition by RAJUK which will be used by DWASA for pipeline installation.
Status of Updated Resettlement Plan	Comments received from ADB[1]	
Land handed over by Deputy Commissioner	LA case (10/2020-21) issued LA notice under section 7(1), CCL payment not started	
ADB Concurrence to start Civil Works	Not yet received as Resettlement Plan is being revised	
Access to Contractor	Access to be delayed; expected in June 2022	
Status of Construction	Contractor appointed on 6 May 2021	

RP Section 6	*Treated Water Pipeline (P2): Balu River (West bank) to Pragati Sarani and Madani Avenue junction at Natun Bazar*
Status of Draft Resettlement Plan	RP received approval on 15 November 2021
Status of Updated Resettlement Plan	Yet to due
Land handed over by Deputy Commissioner	LA case (14/2020-21) issued LA notice under section 7(1), CCL payment not started
ADB Concurrence to start Civil Works	Subject to payment
Access to Contractor	Access to be delayed Expected access to be given for 6 km (public lands) by March 2022 and 1.0 km. (private lands) by June 2022
Status of Construction	Contractor appointed on 6 May 2021

Package 3.1	*Primary distribution pipelines in Dhaka*	
Status of Draft Resettlement Plan	Due Diligence Record (DDR)[1] approved and uploaded	[1] No resettlement impact reported. [2]Implementing NGO (INGO) appointment on 20 December 2021.
Status of Updated Resettlement Plan	Will be updated before starting civil works	
Land handed over by Deputy Commissioner	No land acquisition required[3]	
ADB Concurrence to start Civil Works	Yet to receive	
Access to Contractor	March 2022	
Status of Construction	Contract signed on 9 September 2021	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Package 3.2	*Feeder pipelines distribution in Dhaka*	
Status of Draft Resettlement Plan	Resettlement Plan approved and uploaded[1]	[1] Out of 28 pipeline routes, 1 has a temporary relocation impact. INGO appointed for P3.1 will be working hereto.
Status of Updated Resettlement Plan	Will be updated before starting civil works	
Land handed over by Deputy Commissioner	No land acquisition required[1]	
ADB Concurrence to start Civil Works	Yet to receive	
Access to Contractor	Yet to be given	
Status of Construction	Bids under evaluation	

4.3.2 Progress in Lands Acquisition and handing over to Contractor

The land acquisition process of Package 1 & 2 areas is progressing.Compensation payment under P1 (except part of Resettlement Plan Section 3) has been completed except for land with legal cases only. Payment has started in part of Resettlement Plan Section 3. Compensation payment of Package 2 areas (Resettlement Plan Section 3 (part), 5, and 6) has not started yet. There is no requirement of land acquisition for P3.1 and P3.2 areas as explained earlier.

Civil works are being carried out in Resettlement Plan Section 1 (Water Intake), part of raw water pipeline (1st 10 km), and Resettlement Plan Section 4 (WTP).

The progress made at the end of this reporting period in land Acquisition in P1, P2, P3.1, and P3.2 is briefly detailed hereunder.

As mentioned above, there are two LA cases in Resettlement Plan Section 3; LA case 5/2018-19 and LA case 10/2018-19with a small part of a mouza of Resettlement Plan 5 also. Payment has started for LA case 5/2018-19. Overall,7% (23% out of 234 affected persons who received LA notice under section 8(3)(ka) only) CCL have been disbursed. Affected persons who received CCLhaveall received top up and resettlement assistances. In Resettlement Plan Section 3, LA notice under section 7(1) has been distributedto the affected persons against LA case 10/2018-19 during last SSMR period in April 2021. Resettlement Plan Section 5 has another LA case (LA Case 10/2020-21). LA notice under section 7(1) has been distributed to the affected persons during this reporting period in November 2021. Resettlement Plan Section 6 has one LA case (LA Case 14/2020-21). LA notice under section 7(1) has been distributed to the affected persons during this reporting period in October 2021.PMU is awaiting to receive CCL estimate from the Deputy Commissioner's office for LA Case 10/2018-19, LA Case 10/2020-21 and LA Case 14/2020-21 in Resettlement Plan Section 3 (part), 5 and 6.

As mentioned earlier CCL payment has started in the part of Resettlement Plan Section 3 under LA case 5/2018-19. In order to determine market price of land, structures and trees a Property Valuation Advisory Committee (PVAC) meeting was held for this LA case area on 15.09.2021 where rates were fixed by mutual consensus. Minutes of the PVAC meeting in Bangla and English are attached herewith as **Appendix 11.1 and Appendix 11.2.**

Bangladesh Water Development Board (BWDB) has 24.875 acres of land in Section 3 to be handed over to DWASA in 10 mouzas namely Vulta, Karnagop, Narsingol, Deboi, Noagaon, Gandharbpur, Brahmongaon, Shibganj, Goalkandail and Tetlabo.Length of this area is 5 km, of which 3 km is in P1 area and another 2 km is in P2 area. A Memorandum of Understanding (MoU) has been signed between DWASA and BWDB on 21 December 2021. There are 53 squatters in this BWDB land. The project is going to carry out a joint verification survey in January 2022 to assess their losses and to pay compensation. Thereafter the project will be able to hand over this land to the P1 and P2 contractor with the concurrence of ADB.

There are about 6 km RAJUK road in the Resettlement Plan section 6. In this RAJUK road there are 28 squatters and 5 wage laborers. The project is going to conduct joint verification survey to assess losses of those squatters and to pay them. The project will pay them compensation by February 2022.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

It has been mentioned in the last SSMR that DESWSP has deposited required fees for road cutting permission. RAJUK also agreed that road cutting permission will be issued gradually and segment wise on demand of DWASA project. Therefore, the construction of treated water pipe line (package-2) road cutting permission will be issued as accordingly. In order to get road cutting permission RAJUK requested to DWASA to submit a schedule of program prior to start the said Treated Water Pipeline Construction in Madani avenue of RAJUK. With the permission from RAJUK and the concurrence of ADB the project can handover this land to the P2 contractor.

The following **Figure 4.2** shows major stages of land acquisition and percentages of progress under P1 and P2. P3.1 and P3.2 do not require any land acquisition.The graph depicts that

- Land acquisition proposals for all the 6 sections got the ministerial approvals;
- District Land Acquisition Committee (DLAC)/ Central Land Acquisition Committee (CLAC) approved the land acquisition proposal for all the 6 sections;
- CCL payment for Sections 1 is at 99% completion, for Section 2 is at 91% and for part of Section 3 is at 7%.CCL payment for part of Sections 3, 5, and 6 is yet to start;
- Out of eligible affected persons, payment of resettlement assistance for Sections 1, 2, and 4 is completed, and that for other sections is yet to start;
- Deputy Commissioner's Office has handed over 100% of required lands of Sections 1, 2.DWASA owns land of Section 4. That for the other 3 sections is yet to complete the CCL payments before initiating the land hand over;
- ADB has approved Resettlement Plans for Sections 1, 2, 3, 4, and 6. The Resettlement Plans for Sections 5;needs revision based on ADB comments.
- Resettlement Section 1, part of Section 2, and Section 4 have got ADB concurrence for the start of civil works; and
- Sites under Sections 1, 2 (part), and 4 have been handed over to contractors.

Figure4.2:Progress on Land Acquisition

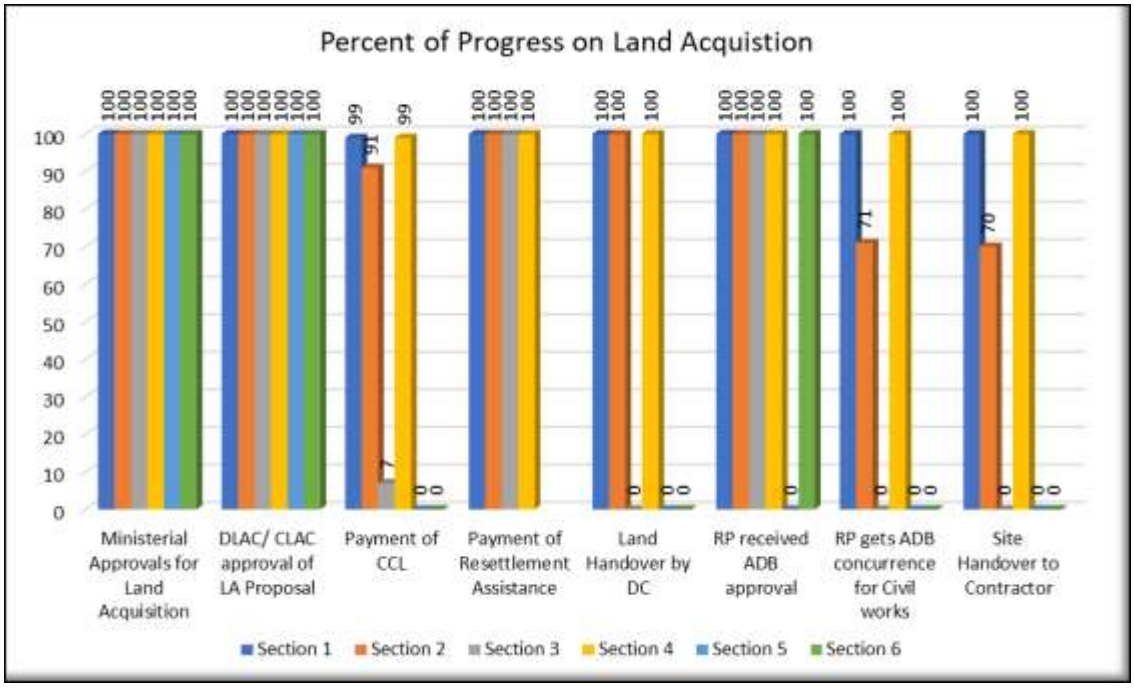

Status of Land Clearance

According to the construction contract conditions, DWASA has to handover contractors the encumbrance-free sites (lands). There are no structures in the Resettlement Plan Sections which have handed over to the contractors. There were 5 structuresin Resettlement Plan Section 2 (4

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

residential and 1 commercial) owned by the 4 affected persons who are still to receive CCLpayment. Out of them commercial owners affected person received CCL payment in this reporting period. Others 3 affected persons received compensation for their structures from GWT based on social recognition. All of them have relocated their structures of their own. They have rebuilt their structures before relocation. At present no structures remain in the raw water pipeline in RP Section 2.

The following table briefly presents the lands clearing status of Resettlement Plan sections at the end of this reporting period.

Table4.1: Availability of Work Front

Figures are in numbers of Plots

RP Section	Total Plots	Plots with Structure	Plots with Trees	Plots Fully Paid	Structures Cleared	Trees Cleared	Comments
Section 1	127	None	None	127	n/a	n/a	Construction ongoing
Section 2	899	101	131	698	101	131	Construction ongoing
Section 3	280	103	89	8	5	5	
Section 4	385	20	29	385	20	29	Construction ongoing
Section 5	236	28	28	None	None	None	
Section 6	66	10	10	None	None	None	
Total	**1 993**	**262**	**287**	**1202**	**126**	**165**	

–100% cleared (ready to handover to Contractor)

Source: DESWSP database

4.3.3 Progress in Payment of CCL and Other Benefits

Deputy Commissioner's office is paying CCL for Resettlement Plan Section 1, 2 and part of 3. DWASA is also disbursing resettlement assistance (other benefits) efficiently in these three sections. Payment has been completed in Resettlement Plan Section 4 except 1 affected person who was identified in December 2021 by the GRC. In total BDT 1,493,290,898(17,363,848 USD) has been paid to the total 1510 affected persons of which BDT 284,758,237 (3,311,142 USD) during this reporting period. Lists of affected persons who received payment in Section 2 and 3 during this reporting period is attached as **Appendix 11.3** and **Appendix 11.4.**

This amount does notinclude the investment allowance under LIRP. Out of these 1,510 affected persons, 378 received LIRP support i.e., training and one-time investment allowance atBDT 20,000 in Section 1 and 2. Total amount is BDT 7,560,000 (87,907 USD)

The affected persons in Resettlement Plan 2 who have received compensation for relocating residential structures have built new houses which is better than pre-resettlement ones. Pictures of some houses newly built by affected persons are presented in **Appendix 11.5** that shows the improvement of living standards of affected persons. The affected persons in Resettlement Plan 3 who have received compensation for relocating residential structuresare currently constructing their new house before dismantling the affected structures.

The progress so far made in the payment of CCL and other assistances is briefly presented hereunder.

Table 4.1.1: Progress of CCL payment and other assistances

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

RP Section 1	*Water Intake (P1) at Bishnandi, Araihazar Upozila*	
Identified Affected Person	223 + non-titled 9 = 232	• 9 affected persons claimed ownership over Khas lands and the dispute is not yet settled. • 1 affected person remained unpaid due to legal issues. If the above-mentioned 9 affected persons get the ownership, the remaining number would be 10.
Payment of CCL[11]	222 (99.6%)	
Payment of Top Up[12]**& other Resettlement Assistance**[13]	231 (99.6%)	
CCL remains unpaid	1 (0,004%) Legal issues	

RP Section 2	*Raw Water Pipeline (P1): Water Intake to Baliapara (end of AraihazarUpozila)*	
Identified Affected Person	1 590 + non-titled 66 = 1 656	• CCL payment remains unpaid for 158[14] affected persons. PMU has deposited the estimated compensation amount in a dedicated account for those affected persons.
Payment of CCL	1 432 (90.0%)	
Payment of Top Up & other Resettlement Assistance	1 510 (91.0%)	
CCL remains unpaid	158 (10.0%)	

RP Section 3	*Raw Water Pipeline (P1) & Treated Water Pipeline (P2): DarikandiChak (start of RupganjUpozila) to Murapara via Gandharbpur WTP*	
Identified Affected Person	738[15];	• CCL payment started for LA case 5/2018-19. • LA notice under Section 7(1) served on 13 April 2021 for LA case 10/2018-19. • Estimate yet to be prepared by Deputy Commissioner's Office for LA case 10/2018-19.
Payment of CCL	54 (7%)	
Payment of Top-Up & other ResettlementAssistance	31 (4%)	
CCL remains unpaid	683 (93%)	

RP Section 4	*Water Treatment Plant (P1) at Gandharbpur*	
Identified Affected Person	258 (Squatters, etc.)	• 2 newly identified affected persons through GRC
Payment of CCL	N/A	
Payment of Resettlement Assistance	258 (100%); completed	
Payment for CPR	The graveyard committee paid 100%	

[11] The District Commissioner (DC) pays Cash Compensation under Law (CCL) for acquisitioned and affected other immovable properties on behalf of the Government of Bangladesh according to Acquisition and Requisition of Immovable Property Ordinance (ARIPO), 1982 for Resettlement Plan Section 1, 2 & 4 and Acquisition and Requisition of Immovable Property Act (ARIPA), 2017 forResettlement PlanSection 3, 5 & 6.

[12] This is the difference between CCL and current market value (CMV), if any, paid to the Affected Persons in compliance with the ADB Safeguard Policy Statement, 2009, which is determined by the Property Valuation Advisory committee (PVAC) and is paid by DWASA.

[13] This is the amount payable to Affected Persons, Titleholders a compensation other than Top Up and Not-Titleholders (displaced due to the acquisition of the land, e.g., squatters, informal settlers, crops sharers, vulnerable, etc.) for their non-land assets in compliance with ADB's SPS policy. DWASA pays the amount according to the Resettlement Plan matrix.

[14] Up to last reporting period it was 166 but in the meantime 1 affected person received payment and 7 has lost the case.

[15] Deputy Commissioner's office distributed LA notice under 8(3)(ka) to 234 affected persons and distributed LA notice under 7(1) to 504 affected persons.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

RP Section 5	*Treated Water Pipeline (P2): Rupgonj (Shitalkhya West bank) to Balu River (East bank)*	
Identified Affected Person	138[17]	• DORP is updating revised Resettlement Plan based on 1.9 km actual alignment by DWASA. • Expected submission of RP re-scheduled to February 2022. • Deputy Commissioner's office is preparing the Award Book.
Payment of CCL	Yet to start	
Payment of Top Up & other Resettlement Assistance	-	
CCL remains unpaid	-	

RP Section 6	*Treated Water Pipeline (P2): Balu River (West bank) to Pragati Sarani and Madani Avenue junction at Natun Bazar*	
Identified Affected Person	48[18]	• Deputy Commissioner's office is preparing the Award Book.
Payment of CCL	Yet to start	
Payment of Top-Up & other Resettlement Assistance	-	
CCL remains unpaid	-	

Payment of Affected Person with legal issues

As mentioned earlier DWASA deposited the required claimable amount of compensation to Deputy Commissioner's office for CCL payments for 166affected persons (according to field data) with unsettled legal issues with their claims of Sections 1 and 2.This number has reducedto 158 cases at present. Out of 158 CCL unpaid affected persons, 45 have submitted their necessary papers to Deputy Commissioner's office. T PMU sends a monthly monitoring report to ADB with the update on the status of CCL payments for those who are yet to receive compensation. Copy of the report of December 2021 is attached as **Appendix 11.6.**

To ensure payment of top-up and other benefits to qualified affected persons on settlement of legal issues and getting CCL payments, DWASA has deposited the full estimated amount of BDT 12848331.00 in a dedicated account in the corporate branch of Janata Bank Ltd., Karwan Bazar in August 2020. This is done according to the ADB agreed Resettlement Framework.

The dedicated account's customer ID is 0100210340372. This account is being operated by joint signaturesfromthe Project Director and the Senior Finance and Accounts Officer of the project. On receipt of CCL, affected persons will contact the INGO for getting the top-up and other resettlement assistance. This account will remain active and operational with the requisite balance due for the affected persons till the last unpaid affected persons even if project activities are complete. It was agreed with ADB that the accrued interest will also be distributed proportionately to the affected persons. Interest on the CCL amount will also be paid, to meet ADB SPS requirement of replacement cost. It has been found that this existing account is not interest bearing. The PMU will open an interest accruing dedicated accountin which previous dedicated account's money will be re-deposited.

4.3.4 Progress in Livelihood and Income Restoration Program

The Project entitlement matrix allows for livelihood training to the affected persons who are vulnerable and who will lose equal to or more than 50 percent of their land. Since it is resettlement assistance and does not contradict the GoB law, the same has been given to those losing more than 10 percent of their (CCL unpaid affected persons in Resettlement Plan Section 2) productive losses to ensure ADB's SPS compliance.

Affected Persons who are Vulnerable and fully lost Agriculture-based livelihood

[17]Deputy Commissioner's office distributed LA notice under 7(1) to 138 affected persons against newly issued LA case 10/2020-21
[18]Deputy Commissioner's office distributed LA notice under 7(1) to 48 affected persons against LA case 14/2020-21

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

In all Resettlement Plan sections (1-6) five hundred and fifty-five (555)affected persons have been identified who are vulnerable and whowill lose their full agriculture-based livelihood. Out of these 485 are vulnerable and the remaining 70 are in full loss category.

Compensation payment has been given in the 4 Resettlement Plan Sections 1, 2, 3 and 4.Up to December 2021 there were438 affected persons (388 vulnerable and 50 full loss of agriculture-based livelihood) who received payment are eligible for LIRP training. During this reporting period 6 vulnerable persons received vulnerable grant in Resettlement Plan Section 3.

Gender distribution of identified training eligible affected persons who are vulnerable and have fully lost their agriculture-based livelihood in Sections 1, 2,3 and 4 is given below:

Table4.2: Distribution of Eligible Affected Persons who are Vulnerable and who lose Full Agriculture-based Livelihood

Section*	Vulnerable AP		Fully lost livelihood AP		Total	
	Male	Female	Male	Female	Male	Female
Section 1	30	19	03	-	33	19
Section 2	179	65	37	10	216	75
Section 3	04	02			04	02
Section 4	81	08	-		81	08
Sub-total	**294**	**94**	**40**	**10**	**334**	**104**
Total		**388**		**50**		**438**

** Sections listed only where compensation payment is in progress*

Skill development training

Vulnerable affected Persons at those who fully lost their agriculture-based livelihood, those who received CCL payment and other benefits have been offered skill development training, namely, Tailoring, Small Business, Cow andGoat Rearing, and Chicken & Duck Rearing according to their choice through the NGO guided by MDSC.

Out of the abovementioned 438 eligible affected persons, 378 (86%) received LIRP training. In this reporting period,99affected persons received skill development training on their preferred income-generating activities. Each of the trained vulnerable affected persons received Tk. 20,000.00 as investment grants according to the IGA Plan. The status of section-wise training is given below:

Section-1: In this reporting period, 1male affected personhas received LIRP training on cow and goat rearing with a combined batch of section-2. Up toDecember 2021, a total of 52 affected persons (31 males and 21 females) including 3 affected persons with full loss of agriculture-based livelihood have received LIRP training and investment grant. Training is completed in this section. A detail of the affected person who received training during this period is attached as **Appendix 11.7**.

Section-2: In this reporting period, 98affected persons (M-80, F-18) have received LIRP training in5 training batches on 5 trades such as cow and goat rearing, small business,chicken & duck rearing, fish culture and tailoring. Trade wise disaggregation of total and male-female participants are given below:

Table4.3: Distribution of Affected Persons by Type of Training Received

Category of training	Total participants				
	Female			Male	Total
	Female headed HHs	Male headed HHs	Total		
Cow andgoat	3	2	5	29	34

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

rearing					
Chicken andduck rearing	2	1	3	13	16
Small business	-	-	-	33	33
Fish culture	-	1	1	5	6
Tailoring	5	4	9	-	9
Total	**10**	**8**	**18**	**80**	**98**

Lists of the affected persons of Section 2 who received training during this reporting period on cow and goat rearing (3rd batch), cow and goat rearing (4th batch), small business (2nd batch), small business (3rd batch),chicken & duck rearing, fish culture and tailoring are given in **Appendix 11.8, 11.9, 11.10, 11.11, 11.12, 11.13 and 11.14**respectively**.** Some pictures on livelihood training and IGAs are attached as **Appendix 11.15.**

Six affected persons in Resettlement Plan 3 are yet to receive training. They will be imparted training by next reporting period.

Income generation engagement of Trained Affected Persons:

Out of 378trained affected personsfrom sections 1, 2, and 4,365 (97%) areengaged in income generation activities todate. Section-wise segregation is as below.

In Section 1, 52 (100%) out of trained 52 affected persons (vulnerable-49, full loss of agriculture-based livelihood-3), in Section 2, 235 (97%) out of trained 243 affected persons (vulnerable-200 and full loss of agriculture-based livelihood-43) and in Section 4, 78 (94%) out of trained 83 vulnerable affected persons are engaged in income generation activities. The remaining 3% of trained affected persons could not engage in income-generating activities due to shortage of funds, sickness, and COVID-19 outbreak. Post-training follow-up monitoring is ongoing for section-1, 2 & 4. Following are the progress of training and engagement in income generation activities.

Table4.4: Distribution of Affected Persons who received Training and Engaged in IGA

Training Category	Total trained			Engaged in IGA			Remarks
	Section 1	Section 2	Section 4	Section 1	Section 2	Section 4	
Tailoring	3	31	12	3 (100%)	31 (100%)	12 (100%)	In section-4, 5 APs not yet started IGA for following reasons: • Shortage of fund because money has spent for family expenditure • Sickness • COVID-19 outbreak
Small Business	-	57	14	n/a	57 (100%)	12 (86%)	
Cow and Goat rearing	24	84	44	24 (100%)	77 (92%)	44 (100%)	
Chicken and Duck Rearing	23	57	13	23 (100%)	57 (100%)	10 (77%)	
Vegetable Gardening	2	8	-	2 (100%)	8 (100%)	n/a	
Fish Culture	-	6	-		5(83%)	-	
Total	**52**	**243**	**83**	**52 (100%)**	**235 (97%)**	**78 (94%)**	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Status of trained affected persons linked with NGOs/microfinance institutions

In Sections 1, 2, and 4, a total of 133 (87 males, 46 females) trained affected persons have been linked with NGOs/micro-credit institutions. Out of those,33 (63%) from Section1, 89 (37%) from Section2, and 11 (13%) from Section 4 have been linked. The below table detailed the status of linking of trained affected persons with NGOs/micro-credit institutions:

Table4.5: Distribution of Affected Persons who received Training and Linked with NGOs/ microfinance institutions

Training Category	Total trained			Linked with NGOs/ microfinance institutions			Name of NGOs/ microfinance institutionsinstitutions linked by the APs
	Section 1	Section 2	Section 4	Section 1	Section 2	Section 4	
Tailoring	3	31	12	02	10	02	Bangladesh Krishi Bank, SIDOR NGO, BRAC NGO, Agrani Bank, ASA NGO, Grameen Bank, Palli Mongal Karmosuchi,BohumukhiSomobaysomiti, Ektee Bari Ektee Khamar, Pubali Bank Ltd., SSS, Sokti Foundation , BRAC Bank, Polli Bikash NGO, BURI Bangladesh, CSS, Sajeda Foundation & TMSS
Small Business	-	57	14	n/a	25	02	
Cow and Goat rearing	24	84	44	16	20	04	
Chicken and Duck Rearing	23	57	13	15	27	03	
Vegetable Gardening	2	8	-	0	4	n/a	
Fish Culture	-	6		-	3		
Total	**52**	**243**	**83**	**33 (63%)**	**89 (37%)**	**11 (13%)**	

Lists of the affected persons linked with NGOs/microfinance institutions since inception in Resettlement Plan Sections 1, 2, and 4 are given in **Appendix 11.16, Appendix 11.17and Appendix 11.18respectively.**

Status of vulnerable affectedpersons

As mentioned above total 388 vulnerable affected persons including 6affected persons during this reporting period have received the vulnerable assistance among which 94affected persons are female and are heads of their households. Section-wise vulnerable affected person breakdown is as follows:

Table4.6: Distribution of Vulnerable Affected Persons

Section	Number of Vulnerable Affected Persons		
	Male	Female	Total
Section 1	30	19	49
Section 2	179	65	244
	04	02	6
Section 4	81	08	89
Total	**294**	**94**	**388**

Female participation in livelihood training

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Todate 121 (32%) female of total 378 vulnerable and fully lost livelihood affected persons trained in Sections 1, 2, 3& 4. Female participation in various categories of livelihood training is presented at the right.

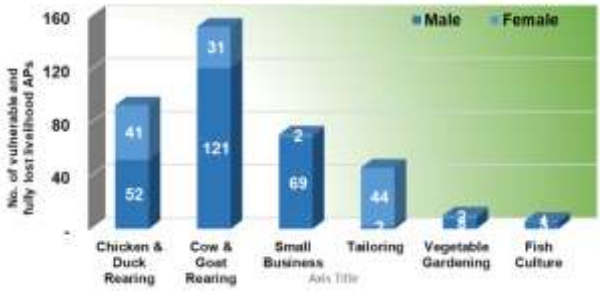

Figure4.3: Female participation in LIRP training

Employment of Skilled, semi-skilled, and unskilled labor by the contractor:

- GWT appointed 834 (7%) females out of 12324 person-days of unskilled/ semi-skilled labours during this reporting period. Since inception, 4056 (6%) females out of 70955 person-days of unskilled/ semi-skilled labours appointed against a targeted of 20%. It is noted that women engaged in cleaning, housekeeping and cooking related work.. All female laborers received equal payment with men for equal value of work.
- GWT engaged 3600 (12%) person days of female security guard out of 30480 person-days of semi-skilled/skilled security guard during this reporting period. Since inception 34835 (28%) females out of 122957 person-days of semi-skilled/skilled security guards in the project area under different positions such as security guard, Security Supervisor, CCTV Operator, Office Assistant, Office Secretary and Document Controller etc

Water and sanitation facilities at intake and WTP area:

- **Supply of drinking water**: Safe drinking water is available for all staffs and labours within the project area.

  Supply of water for sanitation facilities: Proper water supply is available in all wash rooms including wash room for labour's with all facilities inside the wash room (like: toilet tissue, soap, water supply, flushing system, bucket etc).

- **Sanitation facilities:** GWT has ensured separate toilet facilities for male and female including labour's in the intake & WTP area.

Covid-19vaccination

In this reporting period PMU took initiative of an 'on Site Covid-19 Vaccination' to the manpower (national and international) who are engaged in construction work of water treatment plan at Gandharbpur under DWASA. A request letter to the Secretary, Ministry of Local Government **Rural Development and Cooperatives as attached in Bangla and English as Appendix 11.19** and **Appendix11.20.**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

5 Public Participation and Consultation

5.1 Public Consultation

Under the supervision and guidance of PMU and MDSC, the INGO conducts the following consultation meetings within the resettlement plan areas to make affected persons aware of resettlement aspects:

- Public consultation meetings (as and when required);
- Community meeting with the affected persons (every month); and
- Focus group discussion (FGD) meeting

During this reporting period, community meetings were conducted due to the COVID-19 outbreak and subsequent lockdown. In total 92 community meetings were conducted from July to December 2021. In addition, 5 FGDs had been carried out for External Monitoring Agency. Total participants were 923 where 359were male and 564 were female.

Issues of discussion were:

- Information dissemination on:
    a. Land Acquisition (LA) notices
    b. Papers required for receiving compensation from Deputy Commissioner's office and other resettlement assistance from DWASA
    c. Compensation entitlements against loss of assets
    d. Compensation payment issue for those affected persons who are yet to receive CCL.

- Guidance in using compensation money in productive ways and continuing IGA activities during COVID-19.
- Responses to queries on a job opportunity in the project's civil works.
- To make affected persons aware in making land encumbrance free which isalready acquired by DWASA.

5.1.1 Public Participation and Information Dissemination on Key Aspects

The INGO consulted affected persons in making them aware of different resettlement issues. At the same time disseminate various information in response to the affected persons' queries.

The INGO on behalf of PMU disseminates information on the following key aspects against issues raised by the affected persons:

- Required documentationto claim Cash Compensation under Law (CCL)[19] from relevant Deputy Commissioners Office. The documents are:
    - Proof of land ownership;
    - Record of updated mutation (transfer or change of title in the records for the concerned property);
    - Up-to-date land tax (revenue) payment receipt;
    - Proof of Nationality (National ID Card)
    - A Bank Account[20] with account and bank details.
- Required documentation to claim Additional Payment and Other Resettlement Assistances from the DWASA (PMU)[21]. The necessary documents are
    - The Additional Payment and Other Resettlement Assistances are only claimable by the affected persons who have received CCL;

[19]The INGO staffs to support and guide affected persons in collecting necessary documentation and to ensure that payments are made fair and transparently.
[20] Deputy Commissioner's office made payment only through Account Payee Cheque.
[21] Affected persons with the assistance of INGO field staff have to submit all these documentations to INGO Office to prepare the payment vouchers, get approval from PMU and arrange the payments by PMU.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

- All the above-mentioned documents;
- Citizenship Certificate from relevant Union Parishad/ Pourashava Chairman;
- Land share sheet (issued by Deputy Commissioner 's office)

- Affected Persons' entitlements:According to ARIPA 2017, affected persons are entitled to get a 200% premium on land loss and 100% premium on structures, trees, crops, and fish stock from Deputy Commissioner's office. They are also entitled to receive Additional Payment [an amount to compensate the loss on land value (by getting government fixed rate from Deputy Commissioner'soffice) in comparison with the present market value of the land] and Other Resettlement Assistance according to eligibility and entitlement matrix of resettlement framework.
- Determination of present market value of lands:For CCL value Deputy Commissioner's office collects land data from the land office on the preceding deed value of 1 year after the cut-offdate. They collect mouza-wise and land category-wise data and calculate an average for fixing land price. CCL value may variate since sometimes deed value seems less than market price. The value of all lands will be determined by a market survey. Property Valuation Advisory Committee (PVAC) will approve the actual land value. The difference between the payment made Deputy Commissioner's Office (if less than the market price) and the approved market price will be paid by DWASA after receiving the CCL, subject to submission of all necessary papers as mentioned above.
- Compensation for business loss: The affected persons will be fairly compensated according to the market price with a 100% premium from Deputy Commissioner's Office and DWASA will pay compensation for business loss as per the entitlement matrix.
- Payment for affected persons with land disputes/court case: The affected persons with unsettled legal issues will be paid as soon as their issues are settled.In the case of Resettlement Plans 1 and 2, to ensure their CCL payments, DWASA has deposited estimated money to Deputy Commissioner's office(s) and Additional Payment and Other Assistances, DWASA deposited the estimated amount to a dedicated account operated by two signatories from DWASA. The accrued interest will be payable to affected persons proportionate to the individual's due amount. The money will be kept in accounts even after completion of the project as long as the payment to affected personsis not completed. The same procedure will be followed for the rest of the Resettlement Plan areas. If there is no *NGO* they will get their dues by contacting Dhaka WASA directly. DWASA will have an operational unit in Rupganj and they will be responsible for payment.
- Livelihood and Income Restoration Program -LIRP (Assistance to vulnerable and who lose whole of their agriculture-based livelihood):
  - Affected Persons who are vulnerable and who lose full of their agriculture-based livelihood, will get different trade-based DWASA organized training on the scope of marketing and creating employment opportunities and according to their choice/interest.
  - The Income Generating Activity (IGA) training will be provided to them to re-establish or restart the loss of livelihood-based activities for enhancing households' income particularly emphasizing vulnerable women. All of the affected personswill be given an investment allowance after receiving training and on the submission of an investment plan.
  - The money which they will receive as compensation and resettlement benefits will have to be used to rebuild the lost structures and restart their livelihood so that they can bring a positive change in their lives or at least at the level of pre-project condition. Affected persons were advised not to use the compensation money/ resettlement benefits in unproductive ways.
  - Training grant recipient affected persons will be monitored and advised regularly by INGO, MDSC, and PMU.
  - The INGO will assist training recipients by involving them with the local level credit institution and NGOs which can provide technical and financial support.
- Job opportunity in project's civil works: Affected person who are jobless due to the COVID-19 pandemic. Affected persons want to know if they have any opportunity to work in the project's civil works. INGO staff informed them there is a restriction from the contractor to appoint local workers at present because of pandemic precautions.
- Employees of Rupganj Dockyard who will lose their job were informed that all of their entitled compensation will be given from the project.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

- COVID-19 preparedness: Safety precautions on COVID-19 in preventing the illness. The affected persons weregiven suggestions with an emphasis on a. wearing a mask in case going out; b. washing hands frequently at least for 20 seconds; c. using elbow and tissue during sneezing/ coughing; d. keeping surroundings neat and clean; e. taking care of other ill persons, f. not to panic but consulting physicians in case of illness and e.g. get acquainted with the government notification time-to-time on COVID-19 updates and obey the instructions.

Item-wise summary of the community meetings is attached as **Appendix 11.21.**

Besides above consultation, PMU distributed awareness campaign notices so that the affected persons could be motivated to submit their necessary relevant documents in support of ownership to the land acquisition office for receiving compensation on affected land, structures etc. to Deputy Commissioner's office. At the same time the affected persons were requested to submit one set of those papers along with a photocopy (both side) of compensation received cheque to DORP (INGO) Area office. Copies of the awareness campaign notice is attached as **Appendix 11.22** as Bangla and **Appendix 11.23** in English.

5.1.2 Gender mainstreaming

As part of gender mainstreaming,

- 43 (72%) DWASA andNGO staff received training on gender mainstreaming;
- 9 including 2 (22%) female representatives of GWT Contractor and Sub-contractors received training on ADB core labor standard and gender mainstreaming;

Female participation in social consultation meetings

Since inception, 43%[22] (5586) female of a total of 13,021affected persons participated in social consultation meetings. Reported female participation during immediate last 12 months is54%.The below figure presents the trend of female participation during the preceding twelve months.

Figure5.1:Trend of female participation in the social consultation meetings

[22]There is an ADB requirement of ensuring at least 40% of female participation in these meetings.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

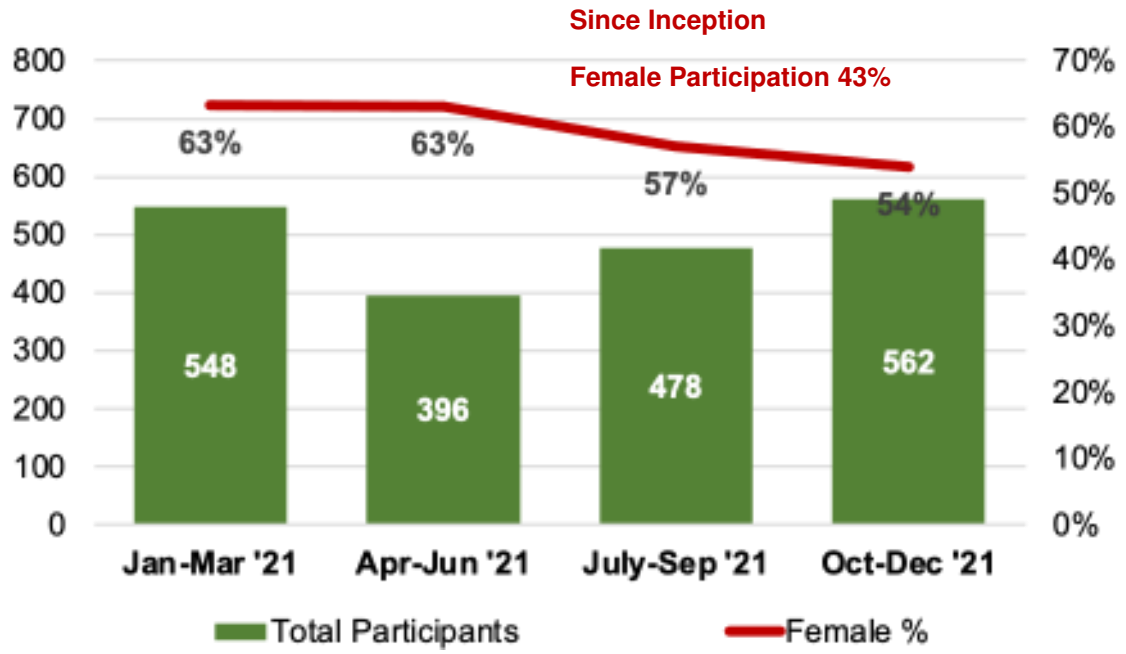

Source: MDSC QPR 4, 2021

5.2 Disclosure of Resettlement Plans

In addition to community meetings, out of six resettlement plans in P1 and P2, 5 resettlement plans for Sections 1, 2, 3,4 and 6 have been updated, approved, and disclosed on ADB and DWASA websites. Resettlement plans for Sections 1, 2, 3, and 4 are being translated by DORP and Safeguard Officer (Social and Gender), PMU. Translation of Resettlement Plan Section 3 has been completed, will be disclosed in the locality by January 2022.

The resettlement plan 6 received ADB approval in this reporting period, on 15 November 2021.

The resettlement plan Sections 5 is being updated as stated in earlier section. Updating of this resettlementplan is delayed due to design change of alignment.

Submitted DDR for P3.1 and Resettlement Plan for P3.2 were approved and disclosed on ADB and DWASA websites. These will be updated further beforethe start of civil works.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

6 Grievance Redress Mechanism (GRM)

The project has established a grievance redress mechanism in compliance with the principle detailed in Appendix 9 in the Project Administration Manual (PAM; December 2020). The GRM is presented below using a Process Flow Chart:

Figure6.1:Grievance Redress Mechanism Flow Chart

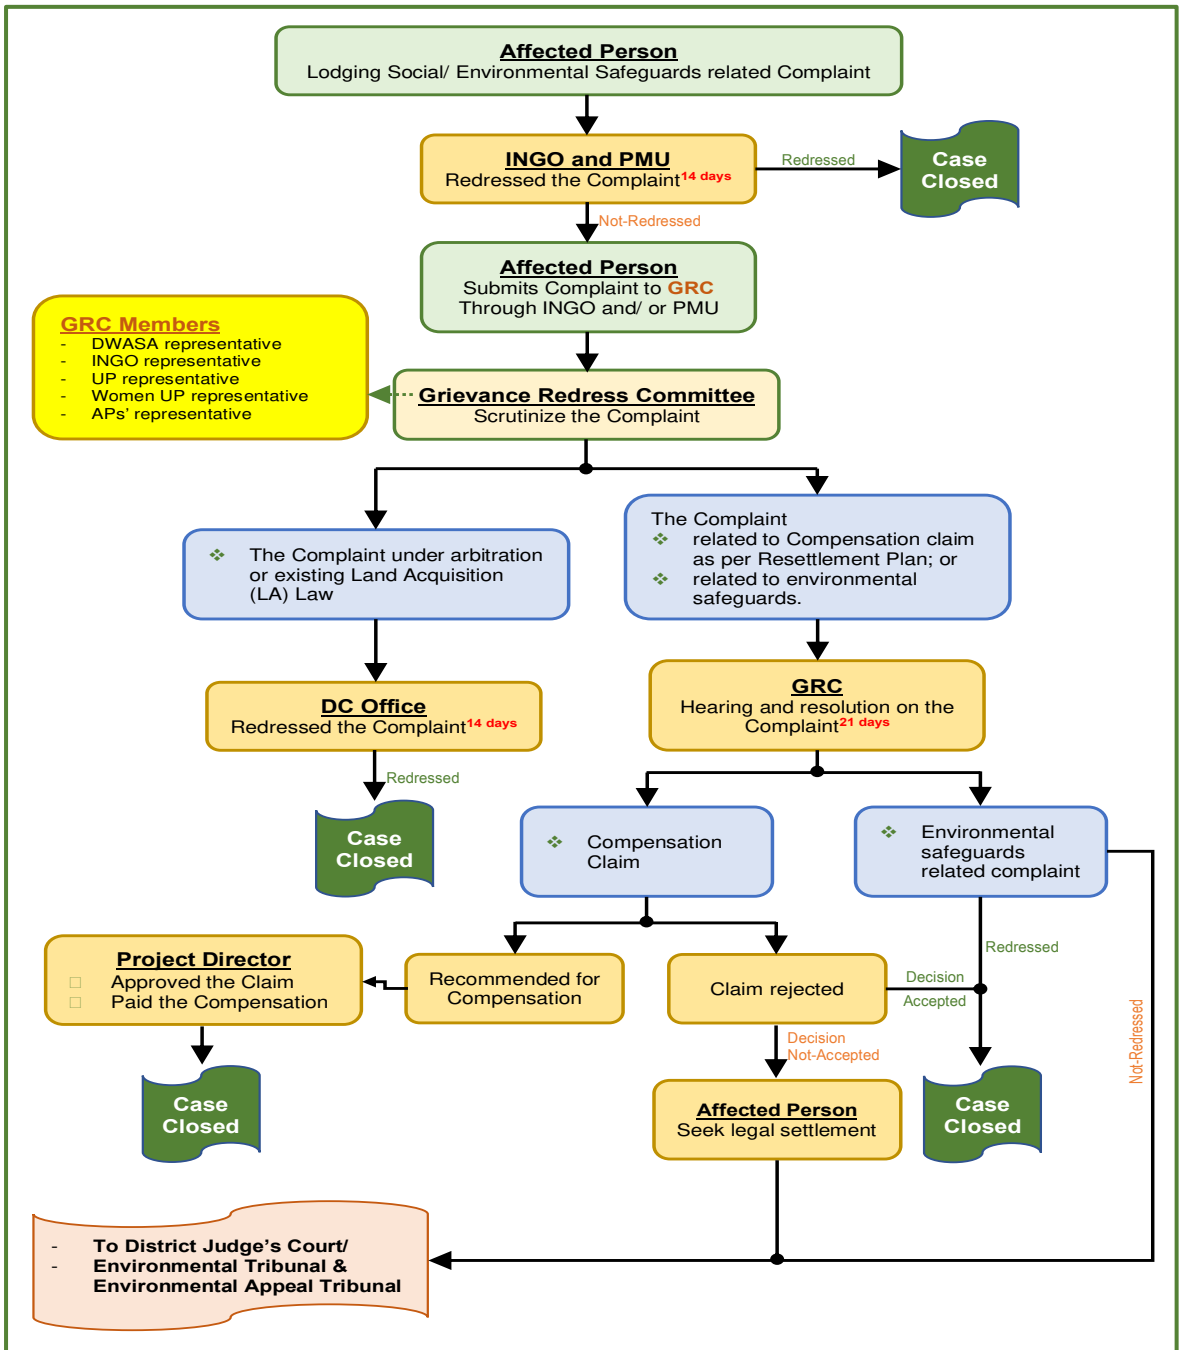

Source: Figure 1, Appendix 9 of PAM (December 2020

The GRM notwithstanding, an aggrieved person shall have access to the country's legal system at any stage. This can run parallel to accessing the GRM and is not dependent on the negative outcome of the GRM.

If the established GRM is not in a position to resolve the issue, the affected person may use the ADB Accountability Mechanismthrough directly contacting (in writing) the Complaint Receiving

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Officer (CRO) at ADB headquarters. Before submitting a complaint to the Accountability Mechanism following the ADB process. INGO shall have to assist the grieved AP in this regard.

6.1 Grievance Redress Committees (GRC)

GRCs are formed at PMU and community level in each Union/ Pourashava level, wherever resettlement activities kick-started, with representatives from the DWASA, local elected representatives from the Local Government Institutions (LGI), INGO,affected persons' representatives, women affected persons to allow voices of the affected communities to be heard and ensure a participatory decision-making process. The representative of the INGO functions as Member Secretary of any GRC.

The Grievance Redress Committees (GRCs) have been established to ensure stakeholders' participation in the implementation process and fair compensation to affected persons and in the resolution of Social and environmental safeguards-related complaints.

The Member Secretary of any GRC is regularly available and accessible for affectedpersons to address concerns and grievances. The female member of GRC and the female affectedpersons of affected households participate in the grievance redress session(s) when the complainant is a female. The legal advisor and DORP support the GRC regularly and assist the affectedpersons to formulate their complaints. The grievance cases are recorded with details and results of the cases for review. The affected people are also allowed to go to GRC for any environmental concern as well.

6.2 Scope and Jurisdiction of GRC

The GRCs resolve any complaint of safeguard compliance - environment, involuntary resettlement, and indigenous people, design-related issues, compensation, service delivery, or any other issues or concerns related to the project in compliance with the item i. Scope and Jurisdiction of GRC of Appendix 9 (Ref: PAM, December 2020). The process for redressing any complaint follows the GRM as explained earlier.

There were 9 GRC meetings todate including 2 during the reporting period. Todate total of 117 cases were dealt with, 63 cases were considered as invalid, 33 cases were advised for payment, and 21 cases forwarded to Deputy Commissioner's office to settle legal issues.

During this reporting period, 2 GRC meetings were held with affected persons from resettlement planSections4 where2 affected persons (who were absent in the meeting before) have been heard. In total 2 affected persons have been heard and both the persons were advised for payment.

Overall status regarding nos. of GRC meetings held, decisions were taken and implementation of taken decisions is presented hereunder:

Total GR meetings held	9 nos.		
RP Sections covered	1, 2 & 4		
Total Cases	**119**		
GRC Decisions	119	**Total**	
Advised for Payment	**33**		
Forwarded to DC (legal issues)	21		
Rejected (illegitimate)	65	**119**	100%
Implementation (Payment Status)			
Paidout	32		
Payment under process	1		
Payment outstanding	-	**33**	100%

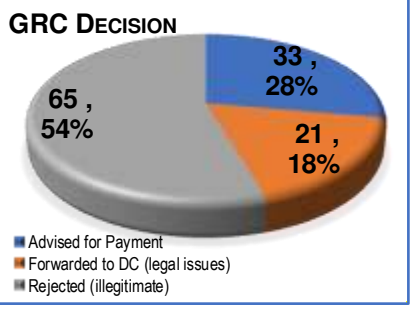

Signed copies of Bangla minutes of 8th and 9th GRC are given as **Appendix 11.24and Appendix 11.25** English translated minutes of 8th and 9thmeetings are appended **Appendix 11.26 and Appendix 11.27.**summary of 8th and 9th GRC meetings is attached as **Appendix11.28.**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

During last reporting period GRC had suggested to the contractor (GWT) to pay compensation to 16 affected persons who losttheir crops due to sand dispersal due to the construction.GWT has paid the compensation to these 16 affected persons during this reporting period. One affected person declined to receive compensation because he was not willing to sign on the stamp paper.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

7 Institutional Arrangement

The DESWSP management organizations are

1. Overall guidance and supervision: Ministry of Local Government, Rural Development and Cooperatives (MLGRDC).
2. Executing Agency: Dhaka Water Supply and Sewerage Authority (DWASA).
3. The Financier: Asian Development Bank and its co-financiers, Agence Française de Dévelopement and European Investment Bank.

The roles and responsibilities of each organization are as explained in Table 3: Project Implementation Roles and Responsibility under item A: Project Implementation Organizations: Roles and Responsibilitiesin section III, Project Management Arrangement if ADB's PAM (December 2020).

7.1 Project Implementation Partners

To implement the project successfully a concerted effort among government, funders, and national and international private sector service providers is envisaged. The following services providers are involved.

i. Implementing Non-government Organizations (INGOs): to implement Social Safeguard aspects of the project.
ii. Management, Design andSupervision Consultant: to assist the Executing Agency in detailed design, procurement, management & supervision of INGO and contractors throughout project implementation.
iii. Contractors: in design (design and build contract), construction andoperation (operation & maintenance contract) of the project packages.
iv. Independent Project Monitoring and Evaluation Agency: To evaluate and monitor the work of NGOs.

Working relationships of the project partners and flow of information in respect of Social Safeguards Plans (Resettlement Plans)areshown below.

Figure7.1:Social Safeguards Plans Implementation partners relationship and flow of information

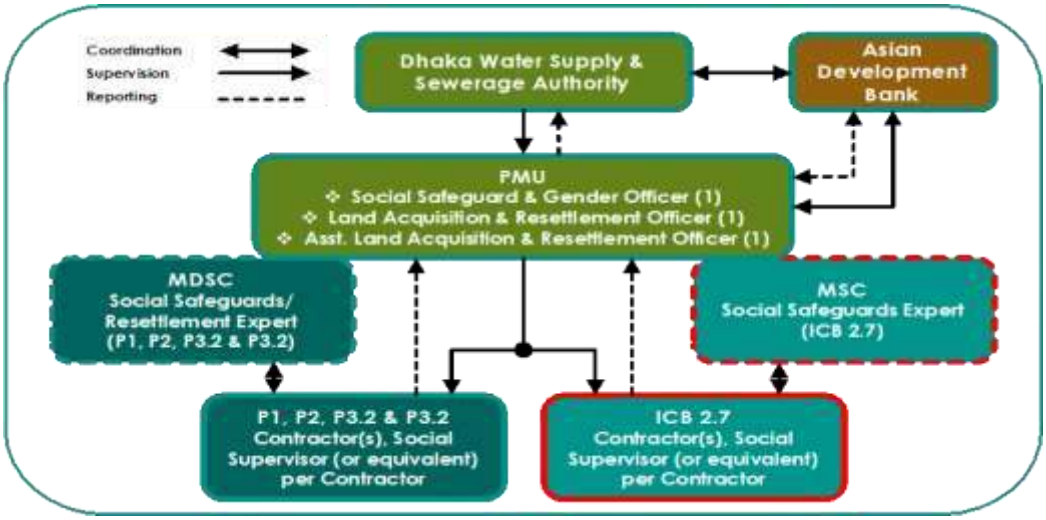

Notes: *MDSC > Management, Design and Supervision Consultant[23]; MSC> Management and Supervision Consultant*
Source: *(Ref: Figure 8 of PAM, December 2020)*

[23]This report only deals with P1, P2, P3.1 and P3.2.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

DWASA establisheda Project Management Unit (PMU) including a safeguard implementation unit (SIU) staffedwith a Safeguard Officer (Social and Gender) and a Safeguard Officer (Environment).

A Resettlement Expert and Social Development and Gender Specialist from MDSC assist the SIU. The PMU appointed an NGO, Development Organization for the Rural Poor (DORP), in assisting them in the implementation of Resettlement Plans (RPs)/ Due Diligence Records (DDRs)for the Resettlement Planunder packages 1 and 2. The MDSC Resettlement Expert and Social Development &Gender Specialist are to oversee the implementation of Resettlement Plans by the INGO.

The PMU has yet to appointan ADB-suggestedLand Acquisition and Resettlement Officer (LARO) and two additional staff, another LARO, an Assistant to the LAROs to assist PMU in the huge task of land acquisition activities and also to assist affected persons in processing their claims. DWASA agreed to hire one Surveyor cum Resettlement Coordinator in addition to these which is also yet to be appointed.

One Executive Engineer and two Assistant Engineers from PMU are responsible for overseeing and looking after the day-to-day safeguard activities. The Project Director, two Deputy Project Directors, and a Senior Water Supply Engineer are responsible for administering overall safeguards activities. The Senior Water Supply Engineer is yet to be appointed This position is vacant since 2018.

The Management Design and Supervision Consultant (MDSC), led by the Mott MacDonald Limited (UK)[24], is responsible for monitoring the implementation of the Resettlement Plans by INGO and assist the PMU in preparing the Semiannual Social Safeguard Monitoring Report.

With ADB's and government approval, DORP's contract has been extended further on 22 June 2021. DORP and DWASA have signed the contract. This contract will be valid up to June 2023.

DORP's Team Leader's position is vacant due to the resignation ofthe present Team Leader. DORP has to propose a replacement.

PMU and MDSC closely coordinate the works of DORP, the INGO. The major tasks of DORP are

- updating resettlement plans;
- conducting public consultations,Focus Group Discussions (FGDs), community meetings, and personal contact with the affected persons and communities for awareness building in affected persons;
- assessing resettlement impacts, collecting the market price of the loss of the properties, activities for making top-up payment and other resettlement assistance;
- skill training for livelihood restoration (LIRP) to the affected persons, livelihood monitoring, etc.

[24] In association with Fichtner GmbH & Co. KG (GER), Euroconsult Mott MacDonald (Netherland), Yooshin Engineering Corporation (KOR), BCL Associates Limited (Bangladesh), SARM Associates Limited (Bangladesh) and Associates for Development Services Limited (Bangladesh).

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

8 Monitoring Results – Findings

DWASA is preparing and submitting regularly two separate safeguards monitoring reports, i) on environmental safeguards (Semi-annual Environmental Monitoring Report - SEMR) and ii) on social safeguards (Semi-annual Social Safeguard Monitoring Report - SSMR), in compliance with paragraph 91 of subsection B 'Monitoring', section IX 'Performance, Monitoring, Evaluation, Reporting and Communication' of the ADB's Project AdministrationManual (PAM). After securing ADB clearance, both these reports are published in DWASA and ADB websites (www.dwasa.org.bd; and www.adb.org.)

The reports follow the requirements of the PAM (ref Appendix 12 for the semi-annual environmental monitoring report, and Appendix 13 for the semi-annual social safeguards monitoring report).

Both the safeguard monitoring reports are presented in DESWSP quarterly reports. The following is the 4th quarter's social safeguards monitoring report as a ready reference.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Table8.1: Semi-Annual Social Safeguards Progress Checklist forP1, P2, P3.1, and P3.2

Activity	Package P1	Package P2	Package P3.1	Package P3.2	Remarks (if Answer is 'No')
	Yes/ No	Yes/ No	Yes/ No	Yes/ No	
A. For subproject packages under bidding	@ Construction	Awarded	Awarded	@ Procurement	
1. Resettlement Plans (RP)/Due Diligence Records (DDR)/Indigenous Peoples Plans (IPP) cleared by ADB?				Yes	
2. RPs/DDRs/IPPs included in the bidding documents?				Yes	
3. Does the resettlement Plan includea cut-offdate?				No	P3.1 and P3.2 have not yet started
4. Are there changes in the scope of work of the cleared RPs/DDRs/IPPs?				No	No changes
5. ID cards prepared for affected persons and distributed?				No	None of the project started
6. Are specific actions identified in RP/IPP, if any, that are required of the contractor for impact avoidance or mitigation, incorporated in bid documents?				No	See note 1 below this table.
7. Does the BOQ line item include any requirements specified in RP/DDR/IPP?				Yes	
8. RP/IPP disclosed in form and language understood by stakeholders and affected persons?				Yes and No	Disclosed, but not in local language.
9. Consultations with stakeholders and affected persons/Indigenous People held?				Yes	
10. Is the GRM in place and GRC constituted?				No	See note 2 below this table.
B. For subproject packages with contracts awarded (no works yet)	@ Construction	Awarded	Awarded	@ Procurement	
1. All NOCs/land transfers obtained?		No	No		
2. Agreement of sale/transfer and third party certificate obtained for negotiated settlement/voluntary donation?		Not applicable	Not applicable		
3. All compensation paid in full?		No	Not applicable		
4. Detailed measurement survey conducted jointly by contractor, project consultant, and PMU/PIU?		No	Yes		
5. All community concerns and grievances related to specific sites mitigated through consultations or agreed actions?		No	Not applicable		No grievance reported
6. All common property resources (CPR, including small shrines, trees of		Yes	Not		

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Activity	Package P1	Package P2	Package P3.1	Package P3.2	Remarks (if Answer is 'No')
	Yes/ No	Yes/ No	Yes/ No	Yes/ No	
worship, etc.) identified and plan for continued access prepared?			applicable		
7. Each contractor designated social safeguards and grievance registration officer?		Not yet	Not yet		
8. For DBO packages, detailed design completed and updated RP/DDR/IPP submitted to ADB?		Not applicable	Not applicable		
9. For DBO packages, serial no. 1-7 accomplished?		Not applicable	Not applicable		
C. For subproject packages with contracts awarded and works on-going	@ Construction	Awarded	Awarded	@ Procurement	
1. Contractors have appointed social safeguards and grievance registration officers per subproject package?	Yes				
2. Site-specific signages with a date of start and end of construction and contact number for grievances and safety instructions for the general public posted onsite?	Yes				Signages put on but contact number not given.
3. Is the grievance registration register available at each worksite?	Yes				
4. Site fencing/protection works etc. undertaken before the start of physical construction work?	Yes				
5. Contractors provided PMU/PIU with a notification/incident report of any grievance or unanticipated impact within 24 hours?	Yes				
6. Reports of complaints/grievances reported monthly to PMU?	Yes				
7. Records of information disclosure/consultations submitted by PIUs to PMU monthly?	No				Yet to start
8. Records of site inspection by PIU and DSC submitted to PMU monthly?	Yes				
9. Records of site inspection by PMC submitted to PMU monthly?	Yes				

Notes:

1. Packages 3.1 and 3.2 do not have any special requirements.
2. 1 Resettlement Plan out of 3 has been approved and disclosed for P2. Resettlement activities for P2and P3.2 are yet to start. P3.1 does not require any resettlement activities. GRCs will be formed in due course for all required packages.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

9 Compliance Status

ADB has approved the 12th SSMR on 8 December 2021 and the same has been disclosed on DWASA and ADB websites (www.dwasa.org.bd and www.adb.org) on 15 December 2021.

9.1 Compliance to relevant Loan Covenant

The following table presents the status of the covenants related to Social Safeguards of the Loan Agreement:

Table9.1: Progress in training and income generation engagement

Covenant Description	Progress Status	Compliance Assessment
Involuntary Resettlement		
Schedule 5 Para 4 The Borrower and DWASA shall ensure, that all land and all rights-of-way required for the Project, and all Project facilities are made available to the Works contractor in accordance with the schedule agreed under the related Works contract and all land acquisition and resettlement activities are implemented in compliance with		
(a) all applicable laws and regulations of the Borrower relating to land acquisition and involuntary resettlement;	A section-wise approach is adopted for land acquisition and compensation payments, to ensure that all affected persons get payment prior to handing over encumbrance-free land to the contractor.	Complied
(b) Involuntary Resettlement Safeguards; and	As above	Complied
(c) all measures and requirements set forth in the RP, and any corrective or preventative actions set forth in any Safeguards Monitoring Report.	As above	Complied
Schedule 5 Para 5 Without limiting the application of the Involuntary Resettlement Safeguards or the RP, the Borrower and DWASA shall ensure that no physical or economic displacement takes place in connection with the Project until:		
(a) compensation and other entitlements, as relevant, have been provided to affected people in accordance with the RP; and	Works in progress	Complied
(b) a comprehensive income and livelihood restoration program has been established in accordance with the RP.	Works in progress	Complied
Human and Financial Resources to Implement Safeguards Requirements		
Schedule 5 Para 6 The Borrower and DWASA shall make available necessary budgetary and human resources to fully implement the RP.	Amounts required for cash compensation under law are being transferred to the concerned DC's office. Resources for the top-up payments and other resettlement benefits are available in DWASA's GoB account.	Complied
Safeguards - Related Provisions in Bidding Documents and Works Contracts		
Schedule 5 Para 7 The Borrower and DWASA shall ensure that all bidding documents and contracts for Works contain provisions		

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

that require contractors to: (a) comply with the measures relevant to the contractor as set forth in the RP (to the extent they concern impacts on affected people during construction), and any corrective or preventative actions set forth in a Safeguards Monitoring Report; (b) make available a budget for all such social measures; (c) provide the Borrower and DWASA with a written notice of any unanticipated resettlement or small ethnic community peoples risks or impacts that arise during construction, implementation or operation of the Project that were not considered in theRP; (d) adequately record the condition of roads, agricultural land and other infrastructure prior to starting to transport materials and construction; and (e) fully reinstate pathways, other local infrastructure, and agricultural land to at least their pre-project condition upon the completion of construction.	Contractor has been made aware that any impact due to construction will suitably mitigated by the contractor. Available As required. There are no small ethnic community identified. Recorded Works in progress	Complied Complied Complied Complied Complied
Safeguards Monitoring and Reporting		
Schedule 5 Para 8 The Borrower shall do the following or cause DWASA to do the following: (a) submit semiannual Safeguards Monitoring Reports to ADB and disclose relevant information from such reports to affected persons promptly upon submission; (b) if any unanticipated social risks and impacts arise during construction, implementation or operation of the Project that were not considered in the RP, promptly inform ADB of the occurrence of such risks or impacts, with detailed description of the event and proposed corrective action plan in accordance with the SPS; and (c) report any actual or potential breach of compliance with the measures and requirements set forth in the RP promptly after becoming aware of the breach.	SSMRs are being submitted and disclosed on PMU and ADB websites Norisk identified No breach of compliance identified yet	Complied Complied Complied
Schedule 5 Para 9 The Borrower shall ensure that no proceeds of the Loan are used to finance any activity included in the list of prohibited investment activities provided in Appendix 5 of the SPS.	Complied	Complied
Grievance Redress Mechanism		
Schedule 5 Paragraph 15 Within 6 months of effectiveness date, the Borrower shall establish and maintain a grievance redress committee with representation from all stakeholders in the Project facilities for the purpose of addressing any grievances, from affected peoples concerning land acquisition, environment, and any other social issues, in a timely manner.	GRCs are formed at PMU and the community level in each Union/ Pourashava level, wherever resettlement activities kick-started, with representatives from the DWASA, local elected representatives from the Local Government Institutions (LGI), INGO, affected person representatives, women affected persons.	Complied
Social Covenants		
Labor Standards		
Schedule 5 Para 16 The Borrower and DWASA shall ensure that (a) civil works contractors comply with all applicable labor laws and regulations of the Borrower, do not allow employment of child labor for construction and maintenance activities, encourage the employment of the poor, particularly women,	These conditions are included in the DBO Contract documents, P2, P3.1 and P3.2. DWASA regularly reports compliance with these conditions.	Complied

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

and provide appropriate facilities for women and children in construction campsites, disseminate information on sexually transmitted diseases (including HIV/AIDS) and human trafficking to employees and local communities surrounding the project construction sites;		
(b) people directly affected by the Project are given priority to be employed by the Project;	Affected persons are being given priority for employment depending on their willingness and skills.	Complied
(c) contractors do not differentiate wages between men and women for work of equal value; and	This condition is included in the DBO,P2, P3.1 and P3.2 Contract documents. DWASA regularly reports compliance with condition.	Complied
(d) specific clauses ensuring these are included in bidding documents.	This loan covenant is included in the DBO, P2, P3.1 and P3.2 Contract documents.	Complied
Gender Action Plan		
Schedule 5. Para 17. The Borrower and DWASA shall ensure that the GAP is effectively implemented to achieve its objectives in a timely manner over the entire Project period, and that adequate resources are allocated for this purpose.	GAP monitoring reports areregularly submitted to ADB.	Complied

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

10 Follow up Actions, Recommendations, and Disclosure

The section-wise implementation of resettlement plans is going on along withsimultaneous updating of the same as explained in earlier sections. However, some outstanding issues need to be resolved in expediting the lands to be ready for the start of civil works in time as soon as the contractor(s) are appointed. Several meetings have had held among PMU, DORP, and MDSC to ensure timely implementation of resettlement plans. The following actions are in place and/ or recommended for actions by the project development partners.

Table10.1: Follow up actions, recommendations, and disclosure

Outstanding Issues	Recommendation/Required Actions
Approval ofupdated Resettlement Plan for Section 2	Resettlement Plan has been submitted with Due Diligence Record (DDR) to ADB
	Follow up needed for approval.
Submission of Resettlement Plan for Section 5.	Revised resettlement plan for Section 5 will be submitted based on actual alignment which will be used by DWASA other than the area which is being used by RAJUK now.Resettlement Plan submission delays due to this alignment change.
	PMU needs tohelp DORP in determining actual alignment and follow up strongly in the completion of the resettlement plan preparation.
CCL payment to all affected persons	Affected persons need to be helped by the DORP more proactively in processing legal papers for getting CCL. In addition, with the assistance of respective Union Parishad (UP) representatives, support will be provided to those affected persons who have conflicts to resolve.
	Deputy Commissioner's office needs to be followed up in considering affected persons' problems and to facilitate payment.
Non-submission of necessary documents to Deputy Commissioner's Office by 113 individual affected persons (other than government land) in all mouzas of Resettlement Section 2.	INGO to take proactive measures in convincing the affected persons, who are delaying in the submission of their land papers asthe land handover is urgent in this section.
	DORP will follow up helping and motivatingthe affected persons.
Collection of CCL data and the correct number of affected persons from Deputy Commissioner's Office, which are affecting real-time updating of Web-based database and authenticate reporting.	DORP's staff are facing difficulties in getting compensation payment data from the Deputy Commissioner's office.
	PMU needs to have further discussion with Deputy Commissioner's Office.
Open an interest accruing dedicated account by January 2022	An interest-bearing dedicated account needs to be opened.
	The PMU will open the above mentioned account.
Land Acquisition in Section 3, 5 and 6	Land handover from government and private sources are essential now for part of section 3 (Raw water pipeline towards WTP) because DBO contractor needs encumbrance-free land as a part of their contract with DWASA.
	Deputy Commissioner's office will be contacted for completion of the award book for Section 3, issuenew Land Acquisition cases for Section 5 and Section 6.
	Deputy Commissioner's office will be contacted to expedite land acquisition (both public and private land). Multiple meetings will be arranged with the Ministry of Land and Deputy Commissioner to expedite land acquisition and handing over land in all sections of resettlement plans.
	Land Acquisition and Resettlement Officer will be appointed to support affected persons and Safeguard Implementation Unit to facilitate resolution of the legal problems and CCL receipt.
	To be deployed by PMU soon.
Completion of Award books and estimate by Deputy Commissioner(part of section 3, 5 & 6)	Completion of Award Books and estimate required for compensation payment in Sections 3 (part), 5 and 6.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Outstanding Issues	Recommendation/Required Actions
	PMU to check with Deputy Commissioner's office for completion of award books and estimate.
Livelihood Restoration of affected persons	DORP needs to monitor the livelihood restoration activities of the affected persons who received training and post-training investment allowance. LIRP monitoring reports on Sections 1 and 2 need to be prepared. LIRP post-training monitoring report needs to be finalized.
Finalization of LIRP post-training monitoring report for Section 4	MDSC commented on the Section 4 LIRP post-training follow-up monitoring report on 7th June 2020.
	DORP to finalize the report in compliance with MDSC comments.
LIRP post-training monitoring report of section 1	Report preparation is in progress.
	DORP to prepare the draft report and submit it to PMU and MDSC for review.
Grievance Redress	One decision taken by the GRC for Section 4 are needed to be implemented soon. Some affected persons were forwarded to Deputy Commissioner's office.
	Taken decisions to be facilitated as per Resettlement Plans. Deputy Commissioner's office to be followed up for checking and making payments to those affected persons who have been referred by the GRC as eligible.
	DORP has been advised to put up GRC members' lists with their names and contacts in their offices and other important public places in the area.
	GRC should be declared in the Resettlement Plan Section 6.
Performance of DORP	DORP should give training to PMU on operating the web based database.
	Regular follow-up with DORP should be carried out regarding completion of database and providing training.
	DORP management should visit the field more often to ensure regular monitoring of the field activities related to the implementation of land acquisition and resettlement.
	PMU has assigned Mr. Mustafizur Rahman, Executive Engineer, and Mahrin Binte Islam, Assistant Engineer to supervise DORP activities on behalf of PMU.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11 Appendix

11.1 Minutes PVAC meeting_Section-3 (LA case-5)_Bangla

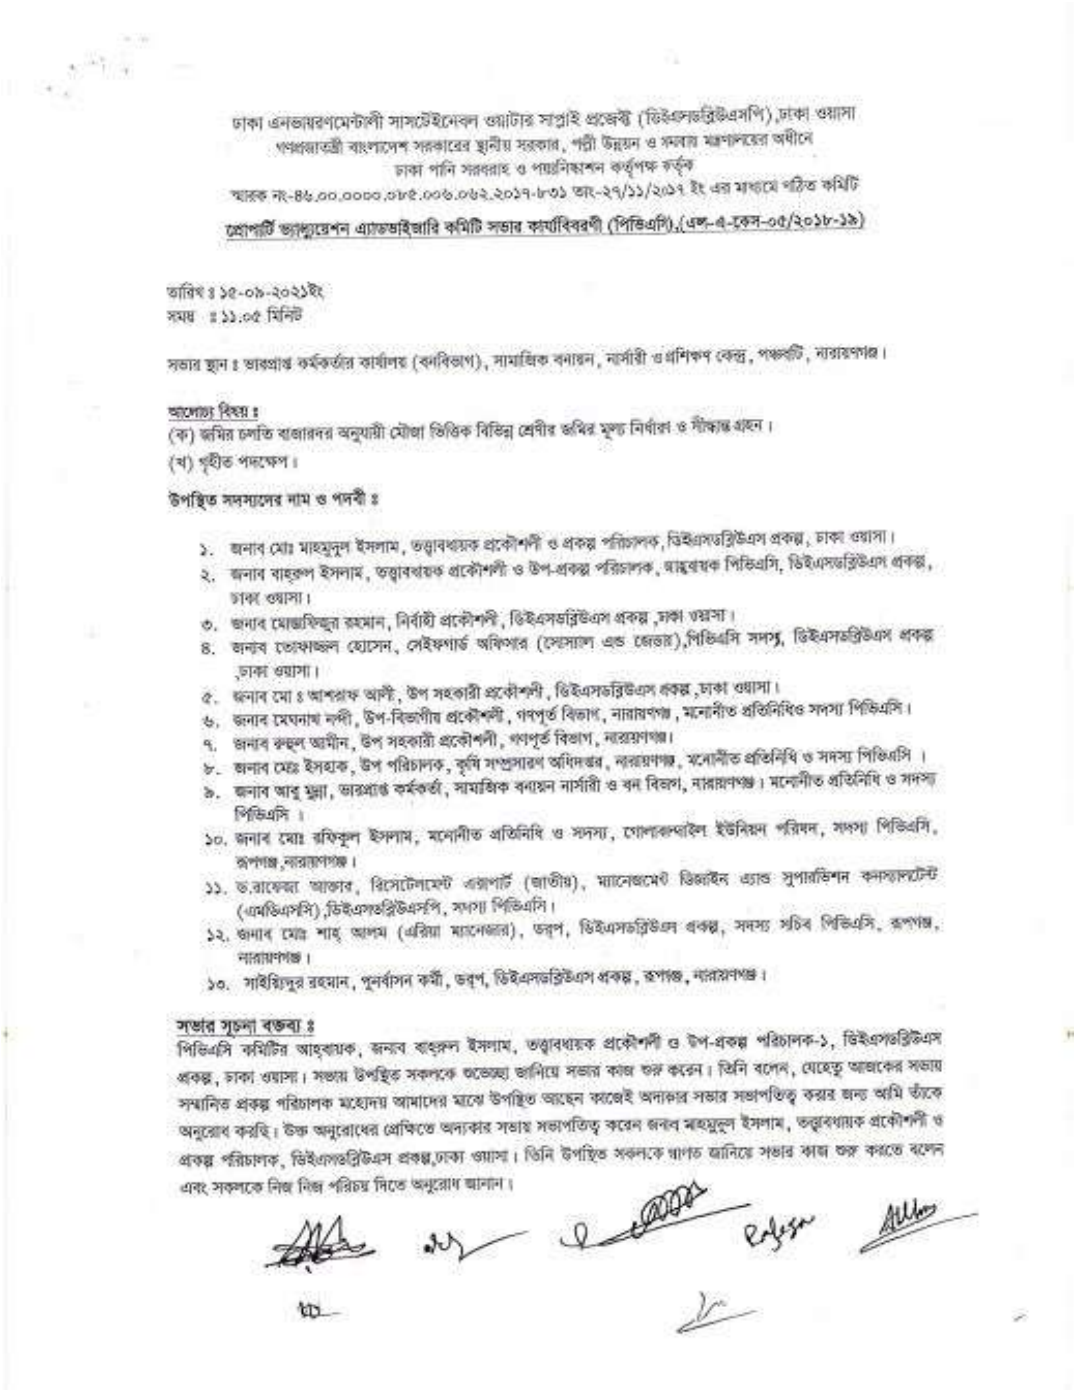

ঢাকা এনভায়রণমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্ট (ডিইএসডব্লিউএসপি),ঢাকা ওয়াসা
গণপ্রজাতন্ত্রী বাংলাদেশ সরকারের স্থানীয় সরকার, পল্লী উন্নয়ন ও সমবায় মন্ত্রণালয়ের অধীনে
ঢাকা পানি সরবরাহ ও পয়ঃনিষ্কাশন কর্তৃপক্ষ কর্তৃক
স্মারক নং-৪৬.০০.০০০০.০৮৫.০০৬.০৬২.২০১৭-৮৩১ তাং-২৭/১১/২০১৭ ইং এর মাধ্যমে গঠিত কমিটি

প্রোপার্টি ভ্যালুয়েশন এ্যাডভাইজারি কমিটি সভার কার্যবিবরণী (পিভিএসি),(এল-এ-কেস-০৫/২০১৮-১৯)

তারিখ ঃ ১৫-০৯-২০২১ইং
সময় ঃ ১১.০৫ মিনিট

সভার স্থান ঃ ভারপ্রাপ্ত কর্মকর্তার কার্যালয় (বনবিভাগ), সামাজিক বনায়ন, নার্সারী ও প্রশিক্ষণ কেন্দ্র, পঞ্চবটি, নারায়ণগঞ্জ।

আলোচ্য বিষয় ঃ
(ক) জমির চলতি বাজারদর অনুযায়ী মৌজা ভিত্তিক বিভিন্ন শ্রেণীর জমির মূল্য নির্ধারণ ও সীমান্ত গ্রহন।
(খ) গৃহীত পদক্ষেপ।

উপস্থিত সদস্যদের নাম ও পদবী ঃ

১. জনাব মোঃ মাহমুদুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক,ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
২. জনাব বাহরুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক, আনুষঙ্গিক পিভিএসি, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
৩. জনাব মোজাফিজুর রহমান, নির্বাহী প্রকৌশলী, ডিইএসডব্লিউএস প্রকল্প ,ঢাকা ওয়াসা।
৪. জনাব তোফাজ্জল হোসেন, সেইফগার্ড অফিসার (সোসাল এন্ড জেন্ডার),পিভিএসি সদস্য, ডিইএসডব্লিউএস প্রকল্প ,ঢাকা ওয়াসা।
৫. জনাব মো ঃ আশরাফ আলী, উপ সহকারী প্রকৌশলী, ডিইএসডব্লিউএস প্রকল্প ,ঢাকা ওয়াসা।
৬. জনাব মেঘনাথ নন্দী, উপ-বিভাগীয় প্রকৌশলী, গণপূর্ত বিভাগ, নারায়ণগঞ্জ, মনোনীত প্রতিনিধিও সদস্য পিভিএসি।
৭. জনাব রুহুল আমীন, উপ সহকারী প্রকৌশলী, গণপূর্ত বিভাগ, নারায়ণগঞ্জ।
৮. জনাব মেঃ ইসহাক, উপ পরিচালক, কৃষি সম্প্রসারণ অধিদপ্তর, নারায়ণগঞ্জ, মনোনীত প্রতিনিধি ও সদস্য পিভিএসি ।
৯. জনাব আবু মুন্না, ভারপ্রাপ্ত কর্মকর্তা, সামাজিক বনায়ন নার্সারী ও বন বিভাগ, নারায়ণগঞ্জ। মনোনীত প্রতিনিধি ও সদস্য পিভিএসি ।
১০. জনাব মোঃ রফিকুল ইসলাম, মনোনীত প্রতিনিধি ও সদস্য, গোলকান্দাইল ইউনিয়ন পরিষদ, সদস্য পিভিএসি, রূপগঞ্জ,নারায়ণগঞ্জ।
১১. ড.রাফেয়া আক্তার, রিসেটেলমেন্ট এক্সপার্ট (জাতীয়), ম্যানেজমেন্ট ডিজাইন এ্যান্ড সুপারভিশন কনসালটেন্ট (এমডিএসসি),ডিইএসডব্লিউএসপি, সদস্য পিভিএসি।
১২. জনাব মোঃ শাহ্ আলম (এরিয়া ম্যানেজার), ভত্রপ, ডিইএসডব্লিউএস প্রকল্প, সদস্য সচিব পিভিএসি, রূপগঞ্জ, নারায়ণগঞ্জ।
১৩. সাইয়িদুর রহমান, পুনর্বাসন কর্মী, ভত্রপ, ডিইএসডব্লিউএস প্রকল্প, রূপগঞ্জ, নারায়ণগঞ্জ।

সভার সূচনা বক্তব্য ঃ
পিভিএসি কমিটির আহ্বায়ক, জনাব বাহরুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক-১, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা। সভায় উপস্থিত সকলকে শুভেচ্ছা জানিয়ে সভার কাজ শুরু করেন। তিনি বলেন, যেহেতু আজকের সভায় সম্মানিত প্রকল্প পরিচালক মহোদয় আমাদের মাঝে উপস্থিত আছেন কাজেই অদ্যকার সভার সভাপতিত্ব করার জন্য আমি তাঁকে অনুরোধ করছি। উক্ত অনুরোধের প্রেক্ষিতে অদ্যকার সভায় সভাপতিত্ব করেন জনাব মাহমুদুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক, ডিইএসডব্লিউএস প্রকল্প,ঢাকা ওয়াসা। তিনি উপস্থিত সকলকে স্বাগত জানিয়ে সভার কাজ শুরু করতে বলেন এবং সকলকে নিজ নিজ পরিচয় দিতে অনুরোধ জানান।

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

পরিচয় পর্ব ঃ
সভাপতির আহবানে সভায় অংশগ্রহণকারীগণ নিজ নিজ পরিচয় তুলে ধরেন।

বক্তব্যঃ- পরিচয় পর্ব শেষ হলে সভাপতি মহোদয় বলেন আপনারা অবগত আছেন যে, গণপ্রজাতন্ত্রী বাংলাদেশ সরকার ঢাকা ওয়াসা'র মাধ্যমে ঢাকা এনভায়রনমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্ট (ডিইএসডব্লিউএস) নামে একটি মেগা প্রকল্প বাস্তবায়ন করছে। প্রকল্পটি নারায়ণগঞ্জ জেলার আড়াইহাজার উপজেলার বিশনন্দী পয়েন্ট-এ মেঘনা নদী থেকে অপরিশোধিত পানি উত্তোলন করে পাইপ লাইনের মাধ্যমে রূপগঞ্জ উপজেলার গন্ধর্বপুরে ঢাকা ওয়াসা নিজস্ব ভূমিতে প্রস্তাবিত পানি শোধনাগার প্ল্যান্টে নিয়ে তা পরিশোধন করে পরিশোধিত নিরাপদ পানি ঢাকা শহরের বিভিন্ন এলাকায় (গুলশান, বনানী, বাড্ডা, মহাখালী, মিরপুর, উত্তরা ইত্যাদি) বসবাসকারীদের মধ্যে সরবরাহ করবে। তিনি আরও বলেন, প্রকল্পটি বাস্তবায়নের জন্য রূপগঞ্জ উপজেলাধীন সেকশন ৩ এর জন্য ৩৭.৭০ একর জমি অধিগ্রহণ করা হচ্ছে।

যেহেতু প্রকল্পটি Asian development Bank (ADB) এর আর্থিক সহায়তায় বাস্তবায়িত হচ্ছে, তাই প্রকল্পটিতে পুনর্বাসন পরিকল্পনা (রিসেটেলমেন্ট প্লান) বাস্তবায়নের শর্ত রয়েছে। পুনর্বাসন পরিকল্পনা বাস্তবায়নে প্রকল্পে ক্ষতিগ্রস্ত ব্যক্তিদের অধিগৃহীত সম্পদের যথাযথ মূল্য নির্ধারণ ও তা প্রদানের কথা বলা হয়েছে।

কমিটির আহ্বায়ক জনাব বাহারুল ইসলাম, (তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক, ডিইএসডব্লিউএস প্রকল্প) বলেন, জনসাধারণ জমি ক্রয়-বিক্রয় করার সময় কম মূল্যে জমির দলিল করে থাকে,পরবর্তীতে তাদের জমি জনস্বার্থে অধিগ্রহণ করা হলে জেলা প্রশাসকের কার্যালয় হতে সরকার নির্ধারিত মূল্য পরিশোধ করা হয়। সেখানে দেখা যায় জনসাধারণ বর্তমান বাজারমূল্য থেকে কম টাকা পেয়ে থাকে, তাই অধিগৃহীত সম্পদের মালিকগন যেন ক্ষতিগ্রস্ত না হয় সেই লক্ষ্যে বিভিন্ন তথ্য ও বাজার দর জরীপের ভিত্তিতে অধিগৃহীত সম্পদের যথাযথ মূল্য নির্ধারণ-ই (পিভিএসি) কমিটির কাজ। আজকের সভায় মূলত প্রকল্পের রূপগঞ্জ উপজেলার ০৪ টি মৌজার অধিগৃহীত ভূমির মূল্য নির্ধারণ বিষয়ে আলোচনা ও সিদ্ধান্ত গ্রহণ করা হবে।

ড.রাফেজা আক্তার, (রিসেটেলমেন্ট এক্সপার্ট (জাতীয়), ম্যানেজমেন্ট ডিজাইন এ্যান্ড সুপারভিশন কনস্যালটেন্ট (এমডিএসসি), সদস্য পিভিএসি) বলেন, অধিগৃহীত সম্পদের মালিকগন যেন কোন অবস্থায় বর্তমান বাজার মূল্যের কম টাকা না পায় সেই জন্যে সহযোগী বাস্তবায়নকারী বেসরকারী সংস্থা ভরুপ জমির বর্তমান বাজারমূল্য জরীপ পরিচালনা করেছে। জরীপ টিম এলাকার বিভিন্ন শেণীর মানুষের কাছ থেকে বর্তমানে জমি ক্রয়-বিক্রয়ের মূল্য সংগ্রহ করেছে। জরীপকৃত এবং জেলা প্রশাসক নির্ধারিত জমির মূল্য বিবেচনায় পিভিএসি জমির বাজার মূল্য নির্ধারন করবে।

প্রকল্প পরিচালক মহোদয় মৌজা ভিত্তিক শ্রেণী অনুযায়ী জমির বর্তমান বাজার মূল্যের তথ্য উপস্থাপনের জন্য পিভিএসি কমিটির সদস্য সচিব, মোঃ শাহ্ আলম, (এরিয়া ম্যানেজার, ভরুপ,ডিইএসডব্লিউএসপি এবং সদস্য সচিব পিভিএসি) কে অনুরোধ করেন।

বিষয় ভিত্তিক আলোচনাঃ
প্রকল্প পরিচালক মহোদয়ের অনুরোধে মোঃ শাহ্ আলম বলেন, রূপগঞ্জ উপজেলায় ০৩টি এল-এর অধীনে ৫ ১১টিমৌজায় ৩৭.৭০ একর জমি অধিগ্রহণ করা হচ্ছে। এ জন্য নিয়মানযায়ী যাবতীয় কার্যক্রম চালিয়ে যাওয়া হচ্ছে এবং রিসেটেলমেন্ট প্লান বাস্তবায়ন একটি গুরুত্বপূর্ণ কাজ। প্রকল্পের পুনর্বাসন পরিকল্পনা প্রণয়ন ও বাস্তবায়নের সুবিধার্থে রূপগঞ্জ উপজেলার কাজকে ৩টি সেকশনে (সেকশন ৩, ৫ রূপগঞ্জ উপজেলাধীন এবং সেকশন ৬ ঢাকা জেলাধীন) ভাগ করা হয়েছে। এলএ কেস ০৫/২০১৮-২০১৯ দড়িকান্দি চক, ভাতেরকান্দি, দড়িকান্দি, গোলাকান্দাইল মৌজা সমূহের জেলা প্রশাসক প্রদত্ত মূল্য তালিকা এবং সংগৃহীত বাজার মূল্য তালিকা উপস্থাপন করা হল ঃ

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

ক্রমিক নং	মৌজার নাম	জমির শ্রেণী	জমির পরিমাণ (শতাংশে)	নির্ধারিত বাজারমূল্য (মূল্য বিধি অনুযায়ী)	জেলা প্রশাসক কর্তৃক নির্ধারিত	জেলা প্রশাসক কর্তৃক নির্ধারিত ১৫% বেশি	সর্বোচ্চ মূল্য প্রদান করা হবে
১	দড়িকান্দি	ভিটি	১৬.৬৬০০	২৯০,০০০.০০	১১৪৪২৯.০০	৩৪৩২৮৮.০০	৫৩,২৭৮.০০
		নাল	৬৭৪.৮৪০০	২২০,০০০.০০	৭৬২৮৪.০০	২২৮৪৫২.০০	১৮,৮৫২.০০
		চালু	৭.৫০০০	২৬৬,০০০.০০	৯৫৩১৫.০০	২৮৬০৬৫.০০	২০,০৬৫.০০
২	দড়িকান্দি চক	বাড়ি	৩৭.৭৫০০	২৭৪,০০০.০০	৭৩৪৫০.০০	২২৬৩৫০.০০	৪৭,৬৫০.০০
		ভিটি	৩.০০০০	২৬৮,০০০.০০	৭৫৪০০.০০	২২৬৩৫০.০০	৪১,৬৫০.০০
		নাল	২০.০০০০	১৮২,০০০.০০	৫০৩০০.০০	১৫০৯০০.০০	৩১,১০০.০০
৩	দত্তেরকান্দি	নাল	১০৫.০০০০	১৮১,২৫০.০০	৫০৩০০.০০	১৫০৯০০.০০	৩০,৩৫০.০০
৪	গোলাকান্দাইল	বাড়ি	২৪৮.৩০০০	৭৫২,৮৫৭.১৪	৫১৫৮৪৬.০০	১৫৪৭৫৩৮.০০	-৭৯৪,৬৮০.৮৬
		ভিটি	৭.০০০০	৫৬৭,১৪২.৮৬	১৭৫৪৫৯.০০	৫২৬৩১৭.০০	৪০,৮২৫.৮৬
		নাল	১০৬৮.২০০০	৪৮৪,৫৭১.৪৩	১৯৫১৫৩.০০	৫৮৫৪৫৯.০০	-৯৬,৮৮৭.৫৭
		চালু	১১.০০০০	৫২৫,৭১৪.২৯	২৪৩৯৪১.২৫	৭৩১৮২৩.৭৫	-২০৬,১০৯.৪৬
		ডোবা	৭.৫০০০	১৭৫০০০.০০	৪৮৭৮৮.২৫	১৪৬৩৬৪.৭৫	২৮,৬৩৫.২৫

কমিটির মতামত ও সুপারিশের আলোকে গৃহীত সিদ্ধান্ত সমূহ ঃ

১. জনাব মোঃ রফিকুল ইসলাম, মনোনীত প্রতিনিধি ও সদস্য, গোলাকান্দাইল ইউনিয়ন পরিষদ, সদস্য পিডিএসি, বলেন জেলা প্রশাসক দড়িকান্দি চক মৌজায় প্রতি শতাংশ বাড়ি জমির মূল্য ২,২৬,৩৫০ টাকা প্রদান করছেন, যাহা বর্তমান বাজার মূল্য থেকে কম। এই মৌজায় বাড়ি জমির মূল্য বৃদ্ধি না করলে আমার এলাকার মানুষ ক্ষতিগ্রস্ত হবে। তার কথার ভিত্তিতে কমিটির অন্যান্য সদস্যগণ আলোচনা করে একমত পোষন করলে উক্ত মৌজায় বাড়ি জমির মূল্য প্রতি শতাংশ বৃদ্ধি করে ২,৮৫,০০০ টাকা নির্ধারনের সিদ্ধান্ত গৃহীত হয়।

২. জনাব মো ঃ আশরাফ আলী, উপ সহকারী প্রকৌশলী, ডিইএসডব্লিএস প্রকল্প ,নকা ওয়াসা, বলেন জেলা প্রশাসক দড়িকান্দি চক মৌজায় প্রতি শতাংশ ভিটি জমির মূল্য ২,২৬,৩৫০ টাকা প্রদান করছেন, যাহা বর্তমান বাজার মূল্য থেকে কম। এই মৌজায় ভিটি জমির মূল্য বৃদ্ধি করা প্রয়োজন। তার কথার ভিত্তিতে কমিটির অন্যান্য সদস্যগণ আলোচনা করেন এবং উপস্থিত মোঃ রফিকুল ইসলাম কে জিজ্ঞাসা করেন। উত্তরে মোঃ রফিকুল ইসলাম এই মৌজায় ভিটি জমির বাজার দর বাড়িয়ে ২,৬০,০০০ টাকা দেওয়ার প্রস্তাব করেন। কমিটির সকলে উক্ত মৌজায় ভিটি জমির মূল্য প্রতি শতাংশে ২,৬০,০০০ টাকা নির্ধারনের সিদ্ধান্ত গ্রহনের জন্য মতামত দেন।

৩. জনাব মোঃ রফিকুল ইসলাম, মনোনীত প্রতিনিধি ও সদস্য, গোলাকান্দাইল ইউনিয়ন পরিষদ, সদস্য পিডিএসি, বলেন জেলা প্রশাসক দড়িকান্দি চক ও দত্তেরকান্দি মৌজায় প্রতি শতাংশে নাল জমির মূল্য ১,৫০,৯০০ টাকা প্রদান করছেন, যাহা বর্তমান বাজার মূল্য থেকে কম। এই দুইটি মৌজায় নাল জমির মূল্য বৃদ্ধি না করলে আমার এলাকার মানুষ ক্ষতিগ্রস্ত হবে এবং তারা এই দামে অন্যত্র জমি ক্রয় করতে পারবে না। তার কথার ভিত্তিতে কমিটির অন্যান্য সদস্যগণ আলোচনা করে সকলের সম্মতিতে উক্ত দুইটি মৌজায় নাল জমির মূল্য প্রতি শতাংশে বৃদ্ধি করে ১,৭৫,০০০ টাকা নির্ধারনের সিদ্ধান্ত গৃহীত হয়।

৪. জনাব মোঃ রফিকুল ইসলাম, মনোনীত প্রতিনিধি ও সদস্য, গোলাকান্দাইল ইউনিয়ন পরিষদ, সদস্য পিডিএসি, বলেন জেলা প্রশাসক গোলাকান্দাইল মৌজায় প্রতি শতাংশে ভিটি জমির মূল্য ৫,২৬,৩১৭ টাকা প্রদান করছেন, যাহা বর্তমান বাজার মূল্য থেকে অনেক কম। এই মৌজায় ভিটি জমির মূল্য বৃদ্ধি করা প্রয়োজন। তার কথার ভিত্তিতে প্রকল্প পরিচালক মহোদয় অন্যান্য সদস্যদের সাথে আলোচনা করেন। কমিটির সদস্য জনাব মেখনাথ নন্দী, উক্ত জমির মূল্য ৫,৫০,০০০ করার প্রস্তাব করলে, উপস্থিত সদস্যগণ তাঁর প্রস্তাবে সম্মতি জ্ঞাপন করেন এবং সভায় সিদ্ধান্ত গৃহীত হয়।

৫. প্রকল্প পরিচালক মহোদয় বলেন গোলাকান্দাইল মৌজায় ডোবা জমির মূল্য জেলা প্রশাসক প্রতি শতাংশে ১,৪৬,৩৬৩.৭৫ টাকা প্রদান করছেন, যাহা বর্তমান বাজার মূল্য থেকে কম। জনাব মোঃ রফিকুল ইসলাম বলেন, এখানে ডোবা জমির মূল্য বৃদ্ধি করা প্রয়োজন। প্রকল্প পরিচালক মহোদয় ১,৭৫,০০০ টাকা প্রস্তাব করলে উপস্থিত সকলে সম্মত হন এবং সর্বসম্মতিক্রমে সভায় সিদ্ধান্ত গৃহীত হয়।

INTERNAL. This ate permission.

উক্ত সভায় বৃদ্ধিকৃত জমির মূল্য তালিকা নিম্নে প্রদান করা হলঃ

ক্রমিক নং	মৌজার নাম	ভূমির শ্রেণী	ভূমির পরিমাণ (শতাংশ)	প্রতি শতাংশের মূল্য (টাকা)	মোট মূল্য (টাকা)	ক্ষতি গ্রস্থের ১৫% অতিরিক্ত (টাকা)	মূল্য ও ক্ষতিপূরণ (টাকা)	মন্তব্য
১	সড়িকান্দি	ভিটি	১৬.৬৬০০	২৯০,০০০.০০	১১৪৪২৬.০০	৩৪৩২৭৮.০০	-৫৩,২৭৮.০০	-
		নাল	৬৭৪.৮৪০০	২২০,০০০.০০	৭৬২৮৪.০০	২২৮৫২.০০	-৮,৮২২.০০	-
		চালা	৭.৫০০০	২৬৬,০০০.০০	২৫৩৫৫.০০	২৮৬৬৫.০০	-২০,০৬৫.০০	-
২	সড়িকান্দি চক	বাড়ি	৩৭.৭৫০০	২৭৪,০০০.০০	৭৫৪৫০.০০	২২৬৩৫০.০০	৪৭,৬৫০.০০	২,৮৫,০০০.০০
		ভিটি	৩.০০০০	২৬৮,০০০.০০	৭৫৪৫০.০০	২২৬৩৫০.০০	৪১,৬৫০.০০	২,৬০,০০০.০০
		নাল	২০.০০০০	১৮২,০০০.০০	৫০৩০০.০০	১৫০৯০০.০০	৩১,১০০.০০	১,৭৫,০০০.০০
৩	দক্ষেরকান্দি	নাল	১০৫.০০০০	১৮১,২৫০.০০	৫০৩০০.০০	১৫০৯০০.০০	৩০,৩৫০.০০	১,৭৫,০০০.০০
৪	গোলাকান্দাইল	বাড়ি	২৪৮.৩০০০	৭৫২,৮৫৭.১৪	৫১৫৮৪৬.০০	১৫৪৬৫৩৮.০০	-৭৯৪,৬৮০.৮৬	-
		ভিটি	৭.০০০০	৫৬৭,১৪২.৮৬	১৭৫৪৩৯.০০	৫২৬০১৭.০০	৪০,৮২৫.৮৬	৫,৫০,০০০.০০
		নাল	১০৭৮.২০০০	৪৮৮,৫৭১.৪৩	১৯৫১৫৩.০০	৫৮৫৫৫৯.০০	-২৬,৮৮৭.৫৭	-
		চালা	১১.০০০০	৫২৫,৭১৪.২৬	২৪৩৯৪১.২৫	৭৩১৮২৩.৭৫	-২০৬,১০৯.৪৯	-
		ডোবা	৭.৫০০০	১৭৫০০০.০০	৪৮৭৮.২৫	১৪৬৩৬৪.৭৫	২৮,৬৩৫.২৫	১,৭৫,০০০.০০

সভায় আর কোন আলোচনার বিষয় না থাকায় সভাপতি মহোদয় সকলকে ধন্যবাদ জানিয়ে সভার সমাপ্তি ঘোষণা করেন।

মোঃ শাহ্ আলম
এরিয়া ম্যানেজার ও সদস্য সচিব পিডিএসি, ডিইএসডব্লিউএসপি, ডব্লপ, রূপগঞ্জ, নারায়ণগঞ্জ।

তোফাজ্জল হোসেন
সেইফগার্ড অফিসার (সোসাল এন্ড জেন্ডার) ডিইএসডব্লিউএস প্রকল্প, সদস্য পিডিএসি,ঢাকা ওয়াসা।

মোঃ আবু মুছা
ভারপ্রাপ্ত কর্মকর্তা (বন বিভাগ), ও সদস্য পিডিএসি,নারায়ণগঞ্জ।

মোঃ ইসহাক
উপ পরিচালক, কৃষি সম্প্রসারণ অধিদপ্তর, ও সদস্য পিডিএসি, নারায়ণগঞ্জ।

মোঃ রফিকুল ইসলাম
স্থানীয় জন প্রতিনিধি, সদস্য পিডিএসি, গোলাকান্দাইল, রূপগঞ্জ, নারায়ণগঞ্জ।

ড. রাফেজা আক্তার
পুনর্বাসন বিশেষজ্ঞ (জাতীয়), এনডিএসসি, ডিইএসডব্লিউএসপি ও সদস্য পিডিএসি।

মেঘনাথ লস্কর
উপ-বিভাগীয় প্রকৌশলী পলাশুর বিভাগ, সদস্য পিডিএসি, নারায়ণগঞ্জ।

(বাহারুল ইসলাম)
তত্ত্বাবধায়ক প্রকৌশলী, উপ-প্রকল্প পরিচালক ও আহ্বায়ক পিডিএসি, ডিইএসডব্লিউএস প্রকল্প,অব্লোক পিডিএসি, ঢাকা ওয়াসা।

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Office of the Project Director
Dhaka Environmentally Sustainable Water Supply Project (DESWSP)
Dhaka Water Supply and Sewerage Authority (WASA)
WASA Bhaban, 98, Kazi Nazrul Islam Avenue (9th Floor)
Kawran Bazar, Dhaka-1215
Email: pddeswspgwdp@gamil.com

Attendance Sheet

Subject: Property Valuation Advisory Committee (PVAC) meeting

Date of Meeting: 15.09.2021

Venue : Forest office, Narayanganj.

SL No.	Name	ORG & Designation	E-mail/Mobile No.	Signature
1.	MD NAH NUDUL ISLAM	PD / DESWSP project DWASA	pddeswspgwdp@gmail.com	
2.	BAHRUL ISLAM	SE/DPD DESWSP DWASA	dpddeswsp@gmail.com	
3.	Dr. Rafeza Akter	NRE. MOSC MM DESWSP, DWASA	rafeza.akter@yahoo.com	Rafeza
4.	Md. Shafique	DD, DAE	ddaenarayanganj@yahoo.com 01912-219064	
5.	Meghnad Nandi	SDE, PWD, Narayanganj	01711180354	15/9/2021
6.	Abu Munna	O.C Social forest narayanganj	01717122868	15.09.21
7.	MD. Rabiqul Islam	Bolakandal UP 3-No. Wordad	01738-910188	15.09.21
8.	Md. Rukel Amen	S.A.E. - PWD. Narayanganj	01720002123	
9.	Md. Ashraf Ali	SAE. DWASA	01921-725453	
10.	Tofazzel Hossen	SGO(SRG) DESWSP, DWASA	01745421948	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Office of the Project Director
Dhaka Environmentally Sustainable Water Supply Project (DESWSP)
Dhaka Water Supply and Sewerage Authority (WASA)
WASA Bhaban, 98, Kazi Nazrul Islam Avenue (9th Floor)
Kawran Bazar, Dhaka-1215
Email: pddeswspgwtp@gamil.com

Attendance Sheet

Subject: Property Valuation Advisory Committee (PVAC) meeting

Date of Meeting: 15 September, 201

Venue : Forest office, Narayanganj.

Sl. No.	Name	ORG & Designation	E-mail/Mobile No.	Signature
11.	Md. Saidur Rahman	R.O. DoRP	01611997674	
12.	Md. Shah Alam	Am. DORP	01552436508	
13				
14				
15				
16				
17				
18				
19				
20				

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.2 Minutes PVAC meeting_Section-3 (LA case-5)_English

Minutes of Meeting of Property Valuation Advisory Committee (PVAC)
Dhaka Environmentally Sustainable Water Supply Project (DESWSP),
Dhaka WASA
Organized by Water Supply and Sewerage Authority Dhaka under the Ministry of Local Government Rural Development and Cooperatives (MLGRDC)

Committee formed under the Memo No. 46.00.0000.085.006.062.2017-831 date: 27-11-2017

Meeting Proceedings of Property Valuation Advisory Committee (PVAC), LA case-05/2018-19

Date: 15.09.2021
Time: 11.05 am

Meeting Venue: Training Center of Social Forestry and Nursery (under the office of the acting Forest Officer), Forest Department, Panchobati, Narayanganj.

Agenda:

(a) Assessment and determination of the current market price of different types of land and approval of the rate;
(b) Steps taken.

Name and Designation of the attendees:

1. Md. Mahmudul Islam, Superintending Engineer, and Project Director of DESWSP;
2. Mr. Bahrul Islam, Superintending Engineer, and Deputy-project Director-1, DESWSP, Dhaka WASA and Convener of the PVAC Committee;
3. Mr. Mostafizur Rahman, Executive Engineer, DESWSP, Dhaka WASA. Nominated Representative and Member of the PVAC Committee;
4. Mr. Tofazzal Hossain, Safeguard Officer (Social/Gender), DESWSP, Dhaka WASA;
5. Mr. Ashraf Ali, Sub Assistant Engineer, DESWSP, Dhaka WASA;
6. Mr. Meghnath Nandi, Sub Divisional Engineer, Public Works Department, Narayangonj. Nominated Representative and Member of the Committee;
7. Mr. Ruhul Amin, Sub Assistant Engineer, Public Works Department, Narayangonj;
8. Mr. Ishaque, Deputy Director, Agriculture Extension Department, Narayanganj, Nominated Representative and Member of the Committee;
9. Mr. Abu Munna, Officer In-charge, Social Forestry, Nursery, Forest Department, Narayanganj, Nominated Representative and Member of the Committee;
10. Md. Rafiqul Islam, Golakandail Union Parishad, Nominated Representative and Member of the PVAC Committee,
11. Dr. RafezaAkter, National Resettlement Expert, MDSC, DESWSP, Member of the PVAC Committee;
12. Md. Shah Alam, Area Manager, DORP, DESWSP, Rupganj, Narayanganj. Member Secretary of PVAC;
13. Md. Saidur Rahman, Resettlement Organizer, DORP, DESWSP, Rupganj.

Meeting Opening Speech:

The convener of the meeting Mr. Bahrul Islam, Superintending Engineer, and Deputy-project Director-1, DESWSP, Dhaka WASA presided over the meeting. He expressed thanks to all participants. As the

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

honorable Project Director, DESWSP was present in the meeting, so, he requested him to preside over the meeting. So, the meeting was chaired by the Project Director Md. Mahmudul Islam, Superintending Engineer and Project Director of DESWSP, Dhaka WASA. The chair of the meeting welcomed the participants and started the meeting proceedings. At the beginning he requested the participants to introduce themselves.

Introducing Session:

In response to the request of the chair of the meeting the participants introduced themselves .

After the introduction the Chairperson said that Government of Bangladesh and Dhaka WASA was going to implement a mega project named Dhaka Environmentally Sustainable Water Supply Project (DESWSP). He said that through the project raw water will be pumped from the river Meghna at Bishnandi point of AraihajarUpazila and will be delivered to the proposed Water Treatment Plant of Dhaka WASA's own land at Gandharbpur in RupganjUpazila of Narayangonj district. The treated water then will be supplied to the different places of Dhaka city (Gulshan, Banani, Badda, Mirpur and Uttara etc.) through the distribution pipelines. He further added that for implementing this project 37.70 acres of land is to be acquired for section-3 under RupganjUpazila.

The Chair of the meeting said that as the project is being implementing with the financial support of Asian Development Bank (ADB) , hence the project has obligation to implement the project according to the Resettlement Plan (RP). In implementing the Resettlement Plan the affected persons by the project intervention are supposed to be compensated at the current market value of the affected assets which are to be determined and provided to the affected persons as per their entitlements.

The Convener of the meeting Mr. Bahrul Islam pointed out that during selling and purchasing of land the land deed registration ishows less value of land compared to the actual market price. But later, when government acquires land for any public interest the Deputy Commissioner pays the affected persons as per government rate, which is generally less. To ensure that the project affected persons are not deprived in any way, the project is collecting different information and verifying the market price through c surveys. To determine the actual price of the assets is the main task of the Property Valuation Advisory Committee. In today's meeting the current land value of 4 mouzas of Rupganjupazila will be discuused and decision will be taken.

Dr. RafezaAkter (National Resettlement Expert), MDSC, told that INGO DORP conducted a survey on current market price of sale and purchase value of land so that the project affected land owners are by no means paid less value for the affected land than the actual current market value. For this purpose the INGO DORP survey team collected information on current market value of land sale and purchase from different sections of people. The PVAC will fix the actual current market value of land by considering and comparing the land value collected by INGO through survey and land value determined by Deputy Commissioner's office.

The Project Director instructed Md. Shah Alam, Area Manager, DORP, Rupganj, and member Secretary of the Property Valuation Advisory Committee (PVAC), DESWSP to present the current market value of the land as per classification and mouza wise.

Agenda Wise Discussions and Decisions:

In response to the request of chair of the meeting and Project Director Md. Shah Alam told the participants that for the implementation of the project 37.70 acres of land is being acquiring from 11 Mouzas of RupganjUpazila under 3 LA cases. With regard to this purpose necessary activities are ongoing. In this regard implementation of Resettlement Plan (RP) is mandatory. For smooth and easy

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

implementation of resettlement plan the activities under RupganjUpazilais divided into 2 sections (section-3 and section-5) and activities under Dhaka District through Section-6. However in today's meeting a comparative scenario of land market price assessed by Deputy Commissions on different types of land in different Mouzas and INGO collected current market rate of land for 4 Mouzas (Darikandirchak, Datterkandi, Darikandi and Golakandail) under LA case 5/2018-2019 for Resettlement Plan Section 3 are presented (below list):

Per decimal land price list of current market value and Deputy Commissioner's office

Sl. No.	Name of Mouza	Classification of land	Land in Decimal	Current market value of land (in decimal)	Deputy Commissioner's rate of land (in decimal)	Rate by including 200% premium (per decimal)	Difference value (per decimal)
1.	Darikandi	*Vita* (Homestead)	16.66	2,90,000	1,14,426	3,43,278	- 53,278
		Nall (Low)	674.84	2,20,000	76,284	2,28,852	-8852
		Chala(Plain)	7.50	2,66,000	95,355	2,88,065	-20,065
2.	Darikandi Chack	*Vita bari* (Homestead)	37.75	2,74.000	75,450	2,26,350	47,650
		Vita (Homestead)	3.00	2,68,000	75,450	2,26,350	41,650
		Nall (Low)	20.00	1,82,000	50,300	1,50,900	31,100
3.	Datterkandi	*Nall* (Low)	105.00	1,81,250	50,300	1,50,900	30,350
4.	Golakandail	*Vita bari* (Homestead)	248.30	7,52,857	5,15,846	15,47538	-7,94,681
		Vita (Homestead)	7.00	5.67,143	1,75,439	5,26,317	40826
		Nall (Low)	1068.20	4,88,572	1,95,153	5,85,459	-96,888
		Chala (Plain)	11.00	5,25,714	2,43,941	7,31,824	-2,06,109
		Dob(*Ditch)*	7.50	1,75,000	48788	1,46,365	28,635

The following decisions have been taken, based on the suggestions and opinion of the Committee:

1. Mr. Rafiqul Islam, Nominated representative and member of the PVAC of Golakandail Union Parishad told that per decimal homestead (*bari/*home) land value of Darikandi Chack mouza has been calculated as BDT 2,26,350 by Deputy Commissioner's office which is less than the current market value of the land. He added that unless the homestead land value of this mouza are not increased the affected persons of this mouza will be disadvantaged. Based on his opinion the committee members of the PVAC discussed the matter in the meeting agreed upon to increase the per decimal proposed homestead land value from BDT 2,26,350 to BDT 2,85,000.
2. Mr. Ashraf Ali, Sub Assistant Engineer, DESWSP, Dhaka WASA told that the per decimal homestead (*vita*) land value of Darikandi-Chack mouza has been determined by Deputy Commissioner's office as BDT 2,26,350 which is less than the current market value of the land. So, the land value needs to be increased. Based on his statement, the committee members discussed among themselves and asked Mr. Rafiqul Islam about the per decimal (*vita* type) land value. Mr. Rafiqul Islam proposed to increase the per decimal land value from BDT 2, 26350 to 2, 60,000. All the committee members opined to increase the per decimal vita land BDT 2, 60,000.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

3. Mr. Rafiqul Islam, Nominated representative and member of the PVAC of Golakandail Union Parishad told that per decimal low (*nall*) land value of Darikandi Chak and Datterkandi mouzas has been calculated as BDT 1,50,900 by Deputy Commissioner's office which is less than the current market value of the land. He told that if the value of this two mouzas are not increased the project affected persons of this two mouzas will be loserdisadvantaged. Based on his proposal the committee members of the PVAC discussed the matter in the meeting and agreed upon to increase the per decimal proposed low (*nall*) land value from BDT 1,50,900 to BDT 1,75,000.
4. Mr. Rafiqul Islam, Nominated representative and member of the PVAC of Golakandail Union Parishad told that per decimal homestead (*vita*) land value of Golakandail mouza has been calculated as BDT 5,26,317 by Deputy Commissioner's office which is less than the current market value of the land. Mr. Meghnath Nandi, the PVAC committee member proposed to increase the per decimal land value at BDT 5, 50,000. Based on his proposal the Project Director discussed the matter with other members of the PVAC. All the committee members gave their consent to increase the per decimal land (*viti*) value, which was approved by the committee in the meeting.
5. The Project Director and chair of the meeting told that the per decimal ditch (*doba*) land value of Golakandail mouza has been calculated as BDT 1,46,365 by the Deputy Commissioner's office which is less than the current market value. Mr. Rafiqul Islam told that that per decimal land (*doba*) value needs to be increased. The Project Director proposed to increase the per decimal (*doba*) land value at the rate of BDT 1, 75,000. All the committee members attended in the meeting consented on his proposal and approved the increased rate (per decimal at BDT1, 75,000) in the meeting.

The list of increased price list by the PVAC

Sl. No.	Name of mouza	Classification of land	Land area in decimal	Current market value per decimal	DC's rate of land (in decimal)	Rate by including 200% premium (per decimal)	Difference value (per decimal)	Rate determined by PVAC
1.	Darikandi	*Vita* (Homestead)	16.66	2,90,000	1,14,426	3,43,278	- 53,278	-
		Nall (Low)	674.84	2,20,000	76,284	2,28,852	-8852	-
		Chala(Plain)	7.50	2,66,000	95,355	2,88,065	-20,065	-
2.	Darikandi-Chack	*Vita bari* (Homestead)	37.75	2,74.000	75,450	2,26,350	47,650	2,85,000
		Vita (Homestead)	3.00	2,68,000	75,450	2,26,350	41,650	2,60,000
		Nall (Low)	20.00	1,82,000	50,300	1,50,900	31,100	1,75,000
3.	Datter Kandi	*Nall* (Low)	105.00	1,81,250	50,300	1,50,900	30,350	1,75,000
4.	Golakandail	*Vita bari* (Homestead)	248.30	7,52,857	5,15,846	15,47538	-7,94,681	-
		Vita (Homestead)	7.00	5.67,143	1,75,439	5,26,317	40826	5,50,000
		Nall (Low)	1068.20	4,88,572	1,95,153	5,85,459	-96,888	-
		Chala (Plain)	11.00	5,25,714	2,43,941	7,31,824	-2,06,109	-
		Dob(*Ditch)*	7.50	1,75,000	48788	1,46,365	28,635	1,75,000

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Having no any other agenda for discussion the chair concluded the meeting with thanks to the Participants.

Md. Shah Alam
Area Manager
Araihazar, Narayangonj
Member Secretary PVAC

Md. Tofazzal Hossain
Safe Guard Officer
(Social/Gender)
Member PVAC, Dhaka WASA

Md. Abu Munna
Officer In-Charge
Forest Department,
Member PVAC,
Narayangonj

Md. Isahaque
Deputy Director,
Member PVAC,
Department of Agriculture
Extension, Narayangonj
Member PVAC

Md Rafiqul Islam,
Local Representative,
Member PVAC,
Golakandail, Rupganj,
Narayanganj

Dr. RafezaAkter
National Resettlement Expert
MDSC, DESWSP, DWASA
Member PVAC Dhaka WASA

Meghnath Nandi
Subdivisional Engineer,
Public works Department
Member PVAC, Narayanganj

Bahrul Islam
Superintending Engineer,
Deputy Project Director and
Convener of the PVAC
committee, DWASA

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.3 List of affected persons in Section 2_paid in reporting period

List of affected persons who have been paid during this reporting period July- December 2021 in RP Section 2

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
1	11052214106	MAZEDA BEGUM	MD JAMAL UDDIN	MST. RUKIA	Kahindi	403	Nall	0.62000	19144
					Kahindi	404	Nall	0.80000	
2	11052114114	ABU SIDDIK	LATE BOSOR UDDIN	RUKIA	Kahindi	403	Nall	1.24000	38287
					Kahindi	404	Nall	1.60000	
3	11052114111	MD ALI HOSSAIN	MD BOSIR UDDIN	MST. ROKEYA BEGUM	Kahindi	403	Nall	1.24000	38287
					Kahindi	404	Nall	1.60000	
4	11052114112	RAFIKUL ISLAM	LATE BOSOR UDDIN	RUKIA BEGUM	Kahindi	403	Nall	1.24000	38287
					Kahindi	404	Nall	1.60000	
5	11052214107	MST ZAYEDA BEGUM	MD. HUMAUN KABIR	RUKIA BEGUM	Kahindi	403	Nall	0.62000	19144
					Kahindi	404	Nall	0.80000	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

6	11052214105	BILKIS BEGUM	ROYEL	RUKIA BEGUM	Kahindi	403	Nall	0.62000	19278
					Kahindi	404	Nall	0.81000	
7	11062114121	KOHINOOR	MONSUR UDDIN	KORIMUN	Baliapara	1471	Nall	0.62500	104739
8	11062164120	MD IMRAN HOSSAIN	ABDUL HAQUE	AMINA BEGUM	Baliapara	100	Wage Labor	0.00000	60000
9	11062114119	BADSHA MIAH	LATE KALAI MIAH	ANWARA BEGUM	Langurdi	404	Nall	4.50000	67540

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.4 List of affected persons in Section 3_paid in reporting period

List of paid affected persons who have been paid during this reporting period July- December 2021 in RP Section 3

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
1	12073116007	RUBEL SHIKDAR	HAZRAT ALI	TAJIMUN BEGUM	Golakandail	05/2018-19	2908	Homestead	1.75000	480279
					Golakandail	05/2018-19	2908	Structure	0.00000	
					Golakandail	05/2018-19	2908	Tree	0.00000	
2	12073116010	SOHEL MIA	HAZRAT ALI	TAJIMUN BEGUM	Golakandail	05/2018-19	2908	Homestead	1.75000	270819
3	12073216011	TAJIMUN BEGUM	SAMED SHIKDAR	ARFOT NESA	Golakandail	05/2018-19	2908	Homestead	0.63000	97495
4	12073216012	JHUMA AKTER	HAZRAT ALI	TAJIMUN BEGUM	Golakandail	05/2018-19	2908	Homestead	0.87000	134636
5	12073116005	MD. TALEB HOSSAIN BHUYAN	LATE UKIL UDDIN BHUYAN	LATE SAMIRA KHATUN	Dorikandi	05/2018-19	2238	Nall	31.00000	847267
					Dorikandi	05/2018-19	2041	Nall	5.00000	
6	12073116006	ABDUL LATIF BHUIYAN	MD HABIBUR RAHMAN BHUIYAN	ANWARA BEGUM	Dorikandi	05/2018-19	2006	Nall	18.00000	507634
					Dorikandi	05/2018-19	2006	Structure	0.00000	
7	12073116014	MD. MAZIBUR	MD NURUL ISLAM	RABEYA BEGUM	Golakandail	05/2018-19	2061	Homestead	7.33000	1480023

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
		RAHMAN			Golakandail	05/2018-19	2061	Nall	1.66000	
					Golakandail	05/2018-19	2061	Structure	0.00000	
8	12073116013	EBRAHIM KHALIL	MD. NURUL ISLAM	RABEYA BEGUM	Golakandail	05/2018-19	2061	Homestead	7.33000	1233203
					Golakandail	05/2018-19	2061	Nall	1.67000	
9	12073116015	ABUL KASEM	MD. NURUL ISLAM	RABEYA KHATUN	Golakandail	05/2018-19	2061	Homestead	7.34000	1234750
					Golakandail	05/2018-19	2061	Nall	1.67000	
10	12073116003	MD. BAZLUL BASAD MIA	MD. ISOB ALI MIAH	AYSHA KHATUN	Golakandail	05/2018-19	2900	Nall	6.25000	369974
11	12073116002	ALI ASROUF	ABUL KASHEM	JORUFA KHATUN	Golakandail	05/2018-19	2812	Homestead	7.50000	1280474
					Golakandail	05/2018-19	2812	Structure	0.00000	
					Golakandail	05/2018-19	2812	Tree	0.00000	
12	12073116004	MD. FARUQUE	SYED JOMADAR	SHENERA BEGUM	Golakandail	05/2018-19	2810	Homestead	6.00000	1030148

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
		HOSSAIN			Golakandail	05/2018-19	2810	Structure	0.00000	
13	12073116009	MD. ABDUL KADER	MD. BOSIR ULLAH TALUKDAR	JOYTUNNESA	Golakandail	05/2018-19	2826	Nall	1.00000	390047
					Golakandail	05/2018-19	2826	Homestead	1.50000	
					Golakandail	05/2018-19	2826	Structure	0.00000	
14	12073116008	MD. SHAHJAHAN KHAN	MD. AJOM KHAN	REJIA BEGUM	Golakandail	05/2018-19	2880	Nall	4.75000	281181
15	12073116001	RASHIDUL KABIR	OYAS UDDIN SARKER	LOJJATUN NESA	Golakandail	05/2018-19	2921	Nall	3.25000	231387
					Golakandail	05/2018-19	2921	Structure	0.00000	
16	12073116020	BACCU MIAH	LATE JALIL MUNSHI	ANWARA BEGUM	Golakandail	05/2018-19	2909	Homestead	1.42000	219750
17	12073116022	AFSARUZZAMAN	LATE ABDUL JALIL	ANWARA BEGUM	Golakandail	05/2018-19	2909	Homestead	1.42000	219750
18	12073216024	FATEMA BEGUM	ABDUL JALIL	ANWARA BEGUM	Golakandail	05/2018-19	2909	Homestead	0.71000	109875
19	12073216025	AYESHA AKTER	ABDUL JALIL	ANWARA BEGM	Golakandail	05/2018-19	2909	Homestead	0.71000	109875
20	12073216026	ANWARA BEGUM	BISAI FOKIR	ASIRUN BEGUM	Golakandail	05/2018-19	2909	Homestead	1.12000	173324

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
21	12073116021	ANSAR HOSSAIN	ABDUL JALIL	ANWARA BEGUM	Golakandail	05/2018-19	2909	Homestead	1.42000	219750
22	12073116028	ANOWAR HOSSAIN	LATE ABDUL JALIL	ANWARA BEGUM	Golakandail	05/2018-19	2909	Homestead	1.43000	642094
					Golakandail	05/2018-19	2908	Nall	5.25000	
					Golakandail	05/2018-19	2909	Structure	0.00000	
					Golakandail	05/2018-19	2909	Tree	0.00000	
23	12073216029	JANNATUL FERDOUS	LATE ABDUL JALIL MUNSHI	ANWARA BEGUM	Golakandail	05/2018-19	2909	Homestead	0.71000	109875
24	12073216023	RAHIMA BEGUM	LATE ABDUL JALIL	ANWARA BEGUM	Golakandail	05/2018-19	2909	Homestead	0.56000	86662
25	12073216030	MOLINA BEGUM	LATE MOJIBUR RAHMAN	LATE HAMIDA KHATUN	Golakandail	05/2018-19	2724	Nall	4.25000	310083
26	12073116003	MD. BAZLUL BASAD MIA	MD. ISOB ALI MIAH	AYSHA KHATUN	Golakandail	05/2018-19	2896	Nall	7.50000	443969
27	12073116016	S.M SHAHADAT	SONA MIAH SHIKDAR	RABEYA BEGUM	Golakandail	05/2018-19	2723	Homestead	3.75000	691027
					Golakandail	05/2018-19	2723	Structure	0.00000	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
					Golakandail	05/2018-19	2723	Tree	0.00000	
28	12073116019	MD. MONIR HOSSAIN	LATE ABDUL MOTIN	LATE TASLIMA BEGUM	Golakandail	05/2018-19	2881	Homestead	2.00000	415008
					Golakandail	05/2018-19	2881	Structure	0.00000	
					Golakandail	05/2018-19	2881	Tree	0.00000	
29	12073216017	MST SHEADIA	MD. ABBAS ALI	AJIMUN	Golakandail	05/2018-19	2881	Homestead	7.50000	1238654
30	12073116018	AMAN PRODHAN	LATE CHAN MIAH	KAMRUNNAHAR	Golakandail	05-2018-19	2881	Homestead	7.50000	1238654
31	12073216027	MST. RAZIA KHATUN	SUMON MOLLA	MST. HENA BEGUM	Golakandail	05/2018-19	2809	Homestead	0.25000	139088
					Golakandail	05/2018-19	2809	Structure	0.00000	
32	12073116053	GHAZI ASHIM IMAM BEHALF OF ULTINGONJ KATH BABOSAHI SAMITI	GAZI ALI IMAM	GAZI FATEMA IMAM	Golakandail	05/2018-19	2823	Homestead	9.20000	1834748.8
					Golakandail	05/2018-19	2823	Nall	3.95000	
					Golakandail	05/2018-19	2823	Structure	0.00000	
					Golakandail	05/2018-19	2823	Structure	0.00000	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
33	12073116055	MD. MANIK	ABU BOKOR SIDDIK	HASINA BEGUM	Golakandail	05/2018-19	2823	Homestead	0.40000	139901.52
34	12073116052	MD HASAN SARDAR	ABU BOKOR SARDER	HASINA BEGUM	Golakandail	05/2018-19	2823	Homestead	0.40000	183451.52
					Golakandail	05/2018-19	2823	Structure	0.00000	
35	12073116050	RAJA MIA SARDER	ABU BOKOR SARDER	HASI BEGUM	Golakandail	05/2018-19	2823	Homestead	0.40000	61901.52
36	12073116035	MD. MOSTFA BHUYEN	MD. SALAM BHUIYAN	MST. FATEMA BEGUM	Golakandail	05/2018-19	2882	Homestead	5.00000	1243346.5
					Golakandail	05/2018-19	2882	Nall	5.50000	
					Golakandail	05/2018-19	2882	Structure	0.00000	
					Golakandail	05/2018-19	2882	Tree	0.00000	
37	12073116039	MD. BABUL MIA	LATE ABU SAID GAZI	JOLEKHA BEGUM	Golakandail	05/2018-19	2909	Homestead	2.75000	527677.95
					Golakandail	05/2018-19	2909	Structure	0.00000	
					Golakandail	05/2018-19	2909	Tree	0.00000	
38	12073116032	MD. HASSAN	LATE KALU BHUIYAN	LATE AMINA BEGUM	Golakandail	05/2018-19	2353	Homestead	1.00000	798525.06

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
		BHUYAN			Golakandail	05/2018-19	2353	Nall	9.00000	
					Golakandail	05/2018-19	2357	Nall	0.45000	
					Golakandail	05/2018-19	2353	Structure	0.00000	
39	12073116038	LITON DEOWAN	LATE ALI HOSSAIN DEWAN	LATE FATEMA BEGUM	Golakandail	05/2018-19	2909	Homestead	3.00000	653081.4
					Golakandail	05/2018-19	2909	Structure	0.00000	
					Golakandail	05/2018-19	2909	Tree	0.00000	
40	12073116033	MD. RAMJAN BHUIYAN	LATE KALU BHUIYAN	LATE AMINA BEGUM	Golakandail	05/2018-19	2793	Homestead	23.50000	3760952.5
					Golakandail	05/2018-19	2357	Nall	0.45000	
					Golakandail	05/2018-19	2793	Structure	0.00000	
41	12073116040	MD. ABU TAHER CHUWDHURY	MD SAYED ALI	HAZERA BEGUM	Golakandail	05/2018-19	2909	Homestead	3.00000	561941.4
					Golakandail	05/2018-19	2909	Structure	0.00000	
					Golakandail	05/2018-19	2909	Tree	0.00000	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
42	12073116031	MOHAMMAD ABU HANIF BHUIYAN	LATE KALU BHUIYAN	LATE AMINA BEGUM	Golakandail	05/2018-19	2792	Nall	6.00000	1678720.8
					Golakandail	05/2018-19	2792	Homestead	8.00000	
					Golakandail	05/2018-19	2792	Structure	0.00000	
					Golakandail	05/2018-19	2792	Tree	0.00000	
43	12073116046	ABUL HOSSEN	ABDUL MANNAN MIAH	KORIMUNNESA	Golakandail	05/2018-19	2889	Nall	9.07000	536906.81
44	12073116045	MONIR HOSSEN	MANNAN MIAH	KORIMONNESA	Golakandail	05/2018-19	2889	Nall	9.06000	536314.85
45	12073116044	MOHAMMAD IQBAL HOSSAIN	HAZI ABDUL MANNAN MIAH	KORIMUNNESA	Golakandail	05/2018-19	2889	Nall	9.06000	536314.85
46	12073116043	MD. HAROUNOR ROSHID	HAZI ABDUL MANNAN	KORIMUNNESA	Golakandail	05/2018-19	2889	Nall	9.06000	614314.85
47	12073116048	MOHAMMAD BANDE ALI	LATE HAJI JINNOT ALI	FATEMA BEGUM	Golakandail	05/2018-19	2810	Nall	1.50000	1626495.5
					Golakandail	05/2018-19	2811	Nall	24.00000	
48	12073116034	DR. GOLAM	ABDUL OHAB	MOMENA BEGUM	Golakandail	05/2018-19	2434	Nall	12.00000	710350.8

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
		MOSTAFA								
49	12073116049	MD RATAN SARDAR	ABU BOKOR SARDAR	HASINA BEGUM	Golakandail	05/2018-19	2823	Homestead	1.40000	307695.32
					Golakandail	05/2018-19	2823	Structure	0.00000	
					Golakandail	05/2018-19	2823	Tree	0.00000	
50	12073116047	ANWAR HOSSAIN	ISLAM BARI	SAJIDON BEGUM	Golakandail	05/2018-19	2823	Homestead	1.50000	589937.05
					Golakandail	05/2018-19	2823	Nall	4.55000	
					Golakandail	05/2018-19	2823	Structure	0.00000	
51	12073116036	SHAMSUL HAQUE	LATE AHMED ALI	SHAMSUNNESA	Golakandail	05/2018-19	2909	Homestead	3.75000	791386.75
					Golakandail	05/2018-19	2909	Structure	0.00000	
					Golakandail	05/2018-19	2909	Tree	0.00000	
52	12073216042	ALEA BEGUM	MD ISLAM	SAJEDA BEGUM	Golakandail	05/2018-19	2823	Homestead	1.85000	386734.53
					Golakandail	05/2018-19	2823	Structure	0.00000	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl No	ID No.	EP's Name	Father's/Husband Name	Mother's Name	Mouza	LA Case No.	Plot No.	Land Type	Land Affected (Decimal)	Total Amount
					Golakandail	05/2018-19	2823	Tree	0.00000	
53	12073116041	SHEK BOJLU RAHMAN	LATE SAHEB ALI	MALI BEGUM	Golakandail	05/2018-19	2823	Homestead	1.85000	286294.53
54	12073116037	MILON DEOWAN	ALI HOSSAIN DEWAN	FATEMA BEGUM	Golakandail	05/2018-19	2909	Homestead	3.00000	653366.4
					Golakandail	05/2018-19	2909	Structure	0.00000	
					Golakandail	05/2018-19	2909	Tree	0.00000	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.5 Photos of Comparative Structures

Previous	Present
AP Name: MahafujurRahaman AP ID: 11052113744 Mouza: Kamaldi Sction-2	AP Name: MahafujurRahaman AP ID: 11052113744 Mouza: Kamaldi Sction-2
AP Name: Mamun Mia AP ID: 11052113746 Mouza: Kamaldi Sction-2	AP Name: Mamun Mia AP ID: 11052113746 Mouza: Kamaldi Sction-2

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Previous	Present
AP Name: Momtaj Uddin AP ID: 11062110421 Mouza: Eidbardi Sction-2	AP Name: Momtaj Uddin AP ID: 11062110421 Mouza: Eidbardi Sction-2
 AP Name: Abul Kasem Mia AP ID: 11062113909 Mouza: Baliapara Sction-2	 AP Name: Abul Kasem Mia AP ID: 11062113909 Mouza: Baliapara Sction-2
 AP Name: Dulalmia AP ID :11062113907 Mouza:Baliapara Section -2	 AP Name: Dulalmia AP ID :11062113907 Mouza:Baliapara Section -2

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Previous	Present
AP Name: MD IBRAHIMAP **ID : 11062112133** **Mouza: Section -2**	**AP Name: MD IBRAHIMAP** **ID : 11062112133** **Mouza: Section -2**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.6 Monitoring Report on CCL Unpaid Affected Persons

Development Organisation of the Rural Poor-DORP

Dhaka Environmentally Sustainable Water Supply Project-DESWSP

Araihazar Area Office, Narayanganj

Reporting Period: December-2021

List of names of non-paid CCL Affected Persons

Section-1

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
01.	Anowara	Sombupura	131	1	Yes	**Paper Submitted to DC office for CCL.**	No	

Section-2

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
1.	Mosle Uddin	Choitonkanda	2815	2	Yes	**Paper Submitted to DC office for CCL.**	No	
2.	Motaleb	Choitonkanda	2815	1	Yes	**Do**	No	
3.	Shohel	Choitonkanda	2818	2	Yes	**Do**	No	
4.	Hazrat Ali	Atabdi	162	1	Yes	**Do**	No	
5.	Md. Helal Uddin	Atabdi	176	2	Yes	**Do**	No	
6.	Tomiz Uddin	Ranidi	593	3	Yes	**Do**	No	
7.	Tota Mia	Ranidi	593	2	Yes	**Do**	No	
8.	Samoddi	Ranidi	593	1		**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
9.	Jahatun	Ranidi	593	2	Yes	**Do**	No	
10.	Laily	Ranidi	593	1	Yes	**Do**	No	
11.	Suruj Mia	Verarkur	120, 121	2	Yes	**Do**	No	
12.	Md. Mostafijur Rahman	Verarkur	166, 168	1	Yes	**Do**	No	
13.	Farzana Boby	Verarkur	166	1	Yes	**Do**	No	
14.	Md. Bakul	Bazinaband	14	3	Yes	**Do**	No	
15.	Shahid Ullah	Hazishahadi	310,312	2	Yes	**Do**	No	
16.	Nazmul	Hazishahadi	310,312	2	Yes	**Do**	No	
17.	Jakir Hossain	Hazishahadi	310,312	3	Yes	**Do**	No	
18.	Md. Lutfor Rahman Vuia	Hazishahadi	313	1	Yes	**Do**	No	
19.	Dulal	Hazishahadi	409, 410	2	Yes	**Do**	No	
20.	Abul Kalam	Hazishahadi	444	2	Yes	**Do**	No	
21.	Abul Basar Mia	Hazishahadi	444, 445	2	Yes	**Do**	No	
22.	Abdul Wahid	Hazishahadi	445	2	Yes	**Do**	No	
23.	High School- Adv. Rashid	Lengurdi	237	2	Yes	**Do**	No	
24.	High School	Lengurdi	330	2	Yes	**Do**	No	
25.	High School- Adv. Rashid	Lengurdi	331	2	Yes	**Do**	No	
26.	Faruk	Lengurdi	350	2	Yes	**Do**	No	
27.	Labu	Lengurdi	350	1	Yes	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
28.	Raja Mia	Lengurdi	350	2	Yes	**Do**	No	
29.	Moulovi Abu Hanifa	Lengurdi	351	1	Yes	Do	No	
30.	Safaz Uddin	Laxmipur	19	2	Yes	**Do**	No	
31.	Abul Bashar	Laxmipur	19	1	Yes	**Do**	No	
32.	Md. Hossain	Laxmipur	19	1	Yes	**Do**	No	
33.	Mizan	Laxmipur	24	2	Yes	**Do**	No	
34.	Md. Asadullah	Laxmipur	24	1	Yes	**Do**	No	
35.	Razu	Laxmipur	24	1	Yes	**Do**	No	
36.	Rasel	Laxmipur	24	1	Yes	**Do**	No	
37.	Poly	Laxmipur	24	1	Yes	**Do**	No	
38.	Fahima	Laxmipur	24	1	Yes	**Do**	No	
39.	Abdur Rahim	Kumarbag	12	2	Yes	**Do**	No	
40.	Momtaj Uddin	Idbardi	81	2	Yes	**Do**	No	
41.	Johirul	Idbardi	621, 866	2	Yes	**Do**	No	
42.	Md. Soriful Islam	Baliapara	80	2	Yes	**Do**	No	
43.	Soron Bhuiyan	Baliapara	80	2	Yes	**Do**	No	
44.	Abu Talek	Baliapara	610	1	Yes	Do	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
45.	Halima Begum	Baliapara	673	1	Yes	Do	No	
46.	Tara Mia	Kahindi	379, 380	2	No	**The case is ongoing Hearing, Due to pending case in the court**	No	
47.	Md. Kashem	Kahindi	491	2	No	**Do**	No	
48.	Md. Unush Ali	Kahindi	491	2	No	**Do**	No	
49.	Md. Hanif	Kahindi	491	2	No	**Do**	No	
50.	Md. Shajahan	Kahindi	491	2	No	**Do**	No	
51.	Md. Al- Amin	Kahindi	491	2	No	**Do**	No	
52.	Md. Shohel	Kahindi	491	2	No	**Do**	No	
53.	Rahmatullah	Kahindi	506	1	No	**Do**	No	
54.	Md. Shamsul Haque Bhuiyan	Atabdi	45.46	1	No	**Do**	No	
55.	Jahirul Haque Bhuiyan	Atabdi	45,46	2	No	**Do**	No	
56.	Jaidul Haque Bhuiyan	Atabdi	45,46	2	No	**Do**	No	
57.	Fazlul Haque Bhuiyan	Atabdi	45,46	2	No	**Do**	No	
58.	Mohsin	Lengurdi	104	3	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
59.	EID Ga- Adv. OmorFaruk	Lengurdi	111	1	No	**Do**	No	
60.	Sombhu Kanto Das	Aguandi	368	1	No	**Do**	No	
61.	Abdul Azij	Idbardi	26, 27	2	No	**Do**	No	
62.	Abdul Awaul	Idbardi	26, 28	2	No	**Do**	No	
63.	Amir Hossain	Idbardi	26, 29	1	No	**Do**	No	
64.	Rupban	Idbardi	26, 30	1	No	**Do**	No	
65.	Safia	Idbardi	26, 31	1	No	**Do**	No	
66.	Rubi	Idbardi	26, 32	1	No	**Do**	No	
67.	Saenta	Idbardi	26, 33	1	No	**Do**	No	
68.	Abdul Motin	Idbardi	36,	1	No	**Do**	No	
69.	Rofiqul	Idbardi	36,	1	No	**Do**	No	
70.	Samsul Haque	Idbardi	36, 39	1	No	**Do**	No	
71.	Abdul Mannan	Idbardi	36, 40	1	No	**Do**	No	
72.	Md. Nasir	Idbardi	36, 41	1	No	**Do**	No	
73.	Md. Based Ali	Idbardi	37	1	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
74.	Md. Tota Mia	Idbardi	40	1	No	**Do**	No	
75.	Bul Mia	Idbardi	40	2	No	**Do**	No	
76.	Abdul Azij	Idbardi	521	2	No	**Do**	No	
77.	Wohab	Idbardi	521	2	No	**Do**	No	
78.	Wahid	Idbardi	521	1	No	**Do**	No	
79.	Saylim	Idbardi	521	2	No	**Do**	No	
80.	Md. AsadSikder	Baliapara	80	1	No	**Do**	No	
81.	Most.Mazeda Begum	Baliapara	80	2	No	**Do**	No	
82.	Md. Sagor Hossain Molla	Baliapara	80	2	No	**Do**	No	
83.	Mukti Sikder	Baliapara	105	2	No	**Do**	No	
84.	Hamidul Haque	Kamaldi	2053	2	No	**Mutation Problem**	No	
85.	Ala- Uddin	Kamaldi	2115	2	No	**Do**	No	
86.	Ataur Rahman	Kamaldi	2161	1	No	**Do**	No	
87.	Abul Kalam	Kadirdia	410	2	No	**Do**	No	
88.	Md. Dillur Rahman	Ranidi	20, 22	2	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
89.	Md. Babul Molla	Ranidi	22	1	No	**Do**	No	
90.	Abed Ali	Sreepoti	25	2	No	**Do**	No	
91.	Begum SamsunnaharKhondokar	Parashilmandi	314	2	No	**Do**	No	
92.	Siddikur Rahman	Bazinaband	15	2	No	**Do**	No	
93.	Tara Mia	Hazishahadi	314	2	No	**Do**	No	
94.	Bokul Mia	Hazishahadi	314	2	No	**Do**	No	
95.	Md. Kashem	Hazishahadi	315	2	No	**Do**	No	
96.	Md. Hashem	Hazishahadi	315	2	No	**Do**	No	
97.	Md. Selim	Hazishahadi	315	2	No	**Do**	No	
98.	Md. Monir	Hazishahadi	316, 445	2	No	**Do**	No	
99.	Abdur Rahman	Hazishahadi	350	1	No	**Do**	No	
100.	Md. Akbor Ali	Hazishahadi	350	1	No	**Do**	No	
101.	Abdul Kadir	Hazishahadi	357, 367, 369,	1	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
			371					
102.	Abdur Rahim	Hazishahadi	367, 369, 371	2	No	**Do**	No	
103.	Abdus Samad	Hazishahadi	367, 369, 371	2	No	**Do**	No	
104.	Lal Mia	Hazishahadi	427	2	No	**Do**	No	
105.	Sona Mia	Hazishahadi	427	1	No	**Do**	No	
106.	Golesha Begum	Hazishahadi	427	2	No	**Do**	No	
107.	Komol Mia	Lengurdi	350	2	No	**Do**	No	
108.	Abu Taleb	Lengurdi	351	3	No	**Do**	No	
109.	Abdul Awal	Lengurdi	351	1	No	**Do**	No	
110.	Most. Hosneara Begum	engurdi	416	1	No	**Do**	No	
111.	Sarmin Akhter (Under 18)	Kumarbag	83	2	No	**Do**	No	
112.	Ruzmin (Under 18)	Kumarbag	83	2	No	**Do**	No	
113.	Surmin (Under 18)	Kumarbag	83	2	No	**Do**	No	
114.	Parvin Begum (Mother)	Kumarbag	83	3	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
115.	Md. Abu Dien Bhuiyan	Idbardi	75	1	No	**Do**	No	
116.	Saylina Akhter	Idbardi	75	1	No	**Do**	No	
117.	Amena Begum	Idbardi	75	1	No	**Do**	No	
118.	Amina Khatun	Idbardi	75	1	No	**Do**	No	
119.	Sahin Mia	Idbardi	75	1	No	**Do**	No	
120.	Md. Halim	Idbardi	75	1	No	**Do**	No	
121.	Most. Jahanara Begum	Idbardi	75	1	No	**Do**	No	
122.	Shanaz	Idbardi	75	1	No	**Do**	No	
123.	Saiful Islam	Idbardi	75	1	No	**Do**	No	
124.	Al Amin	Idbardi	75	1	No	**Do**	No	
125.	Most. Salma Akhter	Idbardi	75	1	No	**Do**	No	
126.	Md. Alom	Idbardi	75	1	No	**Do**	No	
127.	Rukia Begum	Idbardi	75	1	No	**Do**	No	
128.	Sirajul Haque	Idbardi	643	2	No	**Do**	No	
129.	Md. Ruhul Amin Molla	Idbardi	747	2	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
130.	Abul HasemMolla	Idbardi	747	2	No	**Do**	No	
131.	Md. Al Amin	Baliapara	80	3	No	**Do**	No	
132.	Hazera	Baliapara	80	2	No	**Do**	No	
133.	Yanus Miah	Baliapara	669	2	No	**Do**	No	
134.	Joinal Abedin	Baliapara	1582	1	No	**Do**	No	
135.	Doly Akhter	Kamaldi	2214	1	No	**Vested Propaty**	No	
136.	Asis Kumar Dey	Bijoynagar	2	2	No	Do	No	
137.	Sharafat	Bijoynagar	57	2	No	Do	No	
138.	Firoj Mia	Baliapara	100	2	No	Do	No	
139.	Md. Parul	Ranidi	22	2	No	**Due to small quantity of land and share distribution problems APs are not interested to go to DC office for CCL payment**	No	
140.	Mst. Selina Begum	Ranidi	22	2	No	Do	No	
141.	Md. Kamal Uddin	Aguandi	150	2	No	Do	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
142.	AbdurRouf	Aguandi	232	2	No	Do	No	
143.	Delowar	Aguandi	353	2	No	Do	No	
144.	Md. Ismail	Aguandi	353	2	No	Do	No	
145.	Abdul Wahab	Aguandi	353	2	No	Do	No	
146.	Joni	Kumarbag	85	2	No	Do	No	
147.	Most. Piara Begum	Kumarbag	85	2	No	Do	No	
148.	Sahina Begum	Kumarbag	85	2	No	Do	No	
149.	Md. Romij Uddin	Idbardi	67	2	No	Do	No	
150.	Nosu Mia	Idbardi	480	1	No	Do	No	
151.	Soliman	Idbardi	480	2	No	Do	No	
152.	Jomiruddin	Idbardi	480	1	No	Do	No	
153.	Mohiuddin Bhuiyan	Idbardi	633	3	No	Do	No	
154.	Moslem Miah	Idbardi	633	2	No	Do	No	
155.	Abu Kalam	Kamaldi	2058	2	No	**Khas land (Govt. land).**	No	
156.	Amzad Hossain	Hazishahadi	297	1	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SL.No.	Name of Affected Person	Mouza	Plot No	Number of times contacted within the reporting period	Papers submitted to Deputy Commissioner's Office Yes/ No	Status of case for the reporting period	Payment received Yes/No	Remarks
157.	Ainal Hossain	Hazishahadi	297	1	No	**Do**	No	
158.	Mozibor	Hazishahadi	297, 315	1	No	**Do**	No	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.7 Cow & goat rearing in Section 1

Dhaka Environmentally Sustainable Water Supply Project

Raw Water Transmission Line (Section-1)

Upazila: Araihazar, District: Narayanganj

Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

Name of trade:Cow & Goat Rearing, **Training period: 05.09.2021-09.09.2021**

Sl No	Identity No.	Name of training recipient	Father's/ Husband Name	Mother's Name	Vulnerable Households benefit	Training grant	Total	Replacement of ….	Relationship with Affected Persons	Male/Female	Category of vunerable
1	**11011113877**	**Abdul Halim**	Miah Hossain	MstJoymala	97500	20000	117500	Miah Hossain	**Son**	**Male**	**Elderly**
				TOTAL	97500	20000	117500				

Total trained Affected Persons= 01 (Male-1, Female-0)

Vulnerability criteria:

Elderly =	**01 Affected Persons**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.8 Cow & Goat_3rd Batch

Dhaka Environmentally Sustainable Water Supply Project

Raw Water Transmission Line (Section-2)

Upazila: Araihazar, District: Narayanganj

Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

Name of Trade: Cow & Goat Rearing (Batch-3),							Training period: 05.09.2021-09.09.2021				
Sl No	**ID No.**	**Name of training recipient**	**Father's/ Husband Name**	**Mother's Name**	**Vulnerable Households benefit**	**Training grant**	**Total**	**Replacement of ….**	**Relationship with Affected Persons**	**M/F (M=Male, F=Female)**	**Category of vunerable**
1	**11042110129**	**Md. Hanifa**	LATE ABDUL MANNAN	LATE AYSHA	97500	20000	117500				**BPL (Below poverty line)**
2	**11052113591**	**Abul Kalam**	Md. AB. Rahim	Hosneara Begum	78000	20000	98000	Md. AB. Rahim	Son	**M**	**Elderly**
3	**11021113731**	**Saidul Islam**	Md. Misher Ali	Sarjahan Begum	58500	20000	78500	Md. Misher Ali	Son	**M**	**BPL**
4	**11042113119**	**Rozina Akter**	Abu Hanifa	Mahamuda Begum	78000	20000	98000	Abu Hanifa	Wife	**F**	**BPL**
5	**11062113809**	**Shohidulla**	Md.AfjalBuya	Mabia	136500	20000	156500	Md. Afjal Bhuiyan	Son	**M**	**Elderly**
6	**11042113333**	**Ataur**	Harez Mia	Norjahan Begum	78000	20000	98000	Hares Mia	Son	**M**	**Elderly**
7	**11052113078**	**Md Mamun**	Md Nurul Islam	Amena Begum	117000	20000	137000	Md Nurul Islam	Son	**M**	**Elderly**
8	**11052210923**	**Ranu Begum**	ALAUDDIN	LATE ALATON	19500	20000	39500			**F**	**FHHH**
9	**11062110470**	**Roman**	Zakir	Fuzila	78000	20000	98000	Zakir	Son	**M**	**BPL**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

10	**11062210477**	**JakirHossan**	Late Aman Ullah	Momotaz Begum	117000	20000	137000	Momotaz Begum	Son	**M**	**FHHH (Female headed households)**
11	**11062223059**	**Rofiqul Islam**	Late AbdurRahaman	Azimon	19500	20000	39500	Azimon	Son	**M**	**FHHH**
12	**11062210109**	**Nurul Islam**	Late Abdul Malek	Late AltamunNesa	78000	20000	98000	Majada Begum	Husband	**M**	**FHHH**
13	**11062110369**	**Babu**	Dipty	SofuraBiBi	78000	20000	98000	Dipty	Son	**M**	**BPL**
14	**11062113812**	**Monir Hossain**	LATE SHAMSUDDIN	LATE FUL MEHERUN	78000	20000	98000			**M**	**BPL**
15	**11052113889**	**Jamal**	TOMIJUDDIN	AAJIMUN	97500	20000	117500			**M**	**BPL**
16	**11062113825**	**Abu Talak**	LATE NOUAB ALI	SAHERA BEGUM	78000	20000	98000			**M**	**Elderly**
TOTAL					1287000	320000	1607000				

	Total trained Affected Persons= 16 (M-14, F-2), FHHHs- 1 Affected Person		
	Vulnerability criteria:		
		BPL =	**07 Affected Persons**
		Male from FHHHs	**03 Affected Persons**
		Female from FHHHs =	**01 Affected Person**
		Elderly =	**05 Affected Persons**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.9 Cow & Goat_4th Batch

Dhaka Environmentally Sustainable Water Supply Project
Raw Water Transmission Line (Section-2)
Upazila: Araihazar, District: Narayanganj
Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

Name of Trade: Cow & Goat Rearing (4th batch) **Training period: 28.11.2021 to 02.12.2021**

Sl No	ID No.	Name of training recipient	Father's/ Husband Name	Mother's Name	VH benefit	Training grant	Total	Replacement of ….	Relationship with Affected Persons	M/F (M=Male, F=Female)	Category of vunerable
1	11062113041	ArifurRahaman	SahajaddinBhuyan	Amina Begum	19500	20000	39500	SahajaddinBhuyan	Son	M	Elderly
2	11062113676	Azaharul Islam	Md YesinMolla	Ayasa Begum	117000	20000	137000	Md YesinMolla	Son	M	Elderly
3	11032110058	Md Sojol Mia	Abdul Matin	Sultana Begum	117000	20000	137000	Abdul Matin	Son	M	BPL (Below poverty line)
4	11032110063	Md Nazarul Islam	Late Abdul Latif	Late Mehrun	97500	20000	117500	-	-	M	BPL
5	11052212958	Md Manik Mia	Late Shahajat Hossain	Rehana	78000	20000	98000	BithiAkter	Brother	M	FHHH (Female headed households)
6	11052112882	Parul Miah	Late Najimuddin	Late Amina	78000	20000	98000	-	-	M	BPL
7	11062113638	Md Johirul	Abdul MotinMolla	Saleha Begum	117000	20000	137000	Abdul MotinMolla	Son	M	Elderly
8	11042113756	Foysal	Md Billa; Hossan	Rahima Begum	156000	20000	176000	Md Danu Mia	Grand Son	M	Elderly
9	11042113317	Jakir Hossain	Late Abdul Barek	Mst.Rafiya Bibi	0	20000	20000	-	-	M	Full Loss

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

10	11052113117	Md Omar Chan	Late AbdurRahaman	Halima Begum	0	20000	20000	-	-	**M**	**Full Loss**
11	11012112815	Khaleda Begum	Anar Hossain	Asia Begum	0	20000	20000	Anar Hossain	Wife	**F**	**Full Loss**
12	11032110053	Najarul	Late Aual	Sofia	0	20000	20000	-	-	**M**	**Full Loss**
13	11052113271	Md Akbar Ali	L.MdAbur Hosen	L. Mst.Saharban	0	20000	20000	-	-	**M**	**Full Loss**
14	11042114083	Joynal Uddin	Sahaj Udin	Rohimun Begum	117000	20000	137000	-	-	**M**	**BPL**
15	11042114082	Ieanus Mia	Sahaj Uddin	Rahimun	97500	20000	117500	-	-	**M**	**BPL**
16	11062213832	RumanaAkter	MasudBuyan	Nazma Begum	117000	20000	137000	Amana Begum	Son Wife	**F**	**FHHH**
17	11042213797	TaslimaAktar	Md Golap Hossain	Rezia Begum	97500	20000	117500	-	-	**F**	**FHHH**
18	11062210110	Md Solaiman	Late Ahamed Khan	Amina Khatun	78000	20000	98000	Bithi Khatun	Brother	**M**	**FHHH**

	Total trained Affected Persons= 18 (M-15, F-3), FHHHs- 2 Affected Persons		
	Vulnerability criteria:		
		BPL =	**05 Affected Persons**
		Female headed HHs	**04 Affected Persons**
		Elderly =	**04 Affected Persons**
		Full loss=	**05 Affected Persons**

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.10Small business training (2nd Batch)

Annex-2/B

Dhaka Environmentally Sustainable Water Supply Project

Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

List of LIRP training recipient

Raw Water Transmission Line (Section-2)

Upazila: Araihazar, District: Narayanganj

	Name of trade: Small Business(2nd Bach),				Training period: 12.09.2021 - 16.09.2021 (5 Days)							
	Sl No	ID No.	Name of training recipient	Father's/ Husband Name	Mother's Name	VH benefit	Training grant	Total	Replacement of ….	Relationship with Affected Persons	M/F (M=Male, F=Female)	Category of vulnerable
	1	11062110464	Md Salim Uddin	Late Tomij Uddin	Late roymun	136500	20000	156500	-	-	M	Elderly
	2	11062110298	Fazlul Haque	Late Tomij Uddin	Ayasa Khatun	78000	20000	98000	-	-	M	BPL (Below poverty Line)
	3	11062113700	Md Shahin Mia	LatyeNayeb Ali	Mst Amina Begum	58500	20000	78500	-	-	M	BPL
	4	11062110370	Abdul Awyal	Abed Ali Prodhan	Late Korimunnesa	97500	20000	117500	-	-	M	Elderly
	5	11062110293	Noor Mohammad Mia	Late Ashraf Ali Mia	Late Jarina Begum	78000	20000	98000	-	-	M	Elderly
	6	11062110119	Md Helal Uddin	Late Ohab Ali	Late Peskarunnesa	0	20000	20000	-	-	M	Full Loss

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

	7	11062113823	Jalil	Late Abu Taleb Ali	Moriom	97500	20000	117500	-	-	M	BPL
	8	11062113821	Delower	Md Shahajoddin	Moroum Begum	97,500	20000	117500	Md Shahajoddin	Son	M	Elderly
	9	11062113798	Nazrul Islam	Md Gias Uddin	Asia Akter	97,500	20000	117500	-	-	M	BPL
	10	11062112953	Faruk Hossan	Sona Mia	Anowara Begum	97500	20000	117500	Sona Mia	Son	M	Elderly
	11	11062113775	Shalom	Samsu Mia	Masuda Begum	97500		97500	Masum Mia	Brother	M	BPL
	12	11062113830	Manu Mia	Late Mujaffor Mia	Late Joynob Bibi	117000	20000	137000	-	-	M	BPL
	13	11062110481	Jobayer Hasan	Ashad Miah	Rowsonara Begum	117000	20000	137000	Ashad Miah	Son	M	BPL
	14	11062110436	Shibli	Md Nurul Islam	Ferdusi Begum	97500	20000	117500	Md Nurul Islam	Son	M	BPL
	15	11062110433	Midul	Monir	Naznin Begum	58500	20000	78500	Monir	Son	M	BPL
	16	11062110381	Nasim	Md Halim Sarker	Nasima Begum	117000	20000	137000	Md Halim Sarker	Son	M	BPL
					TOTAL	**1443000**	**300000**	**1743000**				
		Total participants: 16 nos (M-16, F-0), Male Headed Households-16										
		Category of vulnerable: Elderly- 05 nos., BPL-10 nos. , Full loss- 01										

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.11 Small Business (3rd Batch)

Dhaka Environmentally Sustainable Water Supply Project

Upazila: Araihazar, District: Narayanganj

Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

Name of Trade: Small Business(3rd Bach) **Duration: 14-18 November/2021 (05 Days)**

Sl No	ID No.	Name of training recipient	Father's/ Husband Name	Mother's Name	Vulnerable Household benefit	Training grant	Total	Replacement of ….	Relationship with Affected Persons	M/F (M=Male, F=Female)	Category of vulnerable
1	11062113710	Babul Miah	Late Alauddin	Momotaz Begum	58500	20000	78500	-	-	M	BPL (Below poverty line)
2	11062110479	Abdul Awal	Md Amanullah	Momotaz Begum	78000	20000	98000	-	-	M	BPL
3	11062113142	Md Sofiqul Islam	Late Haji Serajol Haque	Late Ful Banu	97500	20000	117500	Md GolumSorowar	Brother	M	BPL
4	11032110268	A B Am Hannan Ramigi	Late Romij Uddin Bhuyain	Late Nurbanu	78000	20000	98000	-	-	M	Elderly
5	11042113455	Md Amdadul Haque	Late Motiul Uddin	Late Alimon	0	20000	20000	-	-	M	Full Loss
6	11042113451	Md Kamal	Aktaruzzaman	Forida Begum	0	20000	20000	-	-	M	Full Loss
7	11062110502	Md Anwar Hossain	Late Sukkur Ali	Late Amena Khatun	0	20000	20000	-	-	M	Full Loss
8	11032110200	Arju Miya	Late Sona Mia	Late Amena Khatun	0	20000	20000	-	-	M	Full Loss
9	11032112853	Mostafa Mia	Late Jobed Ali	Late Ajimun	0	20000	20000	-	-	M	Full Loss

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

10	11062113595	Tota Miah	Late Razzak	Late Saleha	**0**	**20000**	**20000**	-	-	**M**	Full Loss
11	11062113688	AlamHossin	Late Jobed Ali	Late Aysha	**0**	**20000**	**20000**	-	-	**M**	Full Loss
12	11042113646	Md Abdul Karim	Chomir Uddin	Golbahar Begum	**0**	**20000**	**20000**	-	-	**M**	Full Loss
13	11062113592	Md Abul Bashar Molla	Late Gazi Abdul Latif	MehurunNesa	**0**	**20000**	**20000**	-	-	**M**	Full Loss
14	11042110079	KhokanChabdra Mitra	Late Gojendro Mohon Mitro	Mukul Rani Mitro	**0**	**20000**	**20000**	-	-	**M**	Full Loss
15	11042110078	Ranjit Kumar Mitra	Late Gojendro Mohon Mitro	Mukul Rani Mitro	**0**	**20000**	**20000**	-	-	**M**	Full Loss
16	11052114056	Tara Mia	Late Abdul Aziz	Late Rohima	**0**	**20000**	**20000**	-	-	**M**	**Full Loss;CCL is yet to be received but Livelihood and Income Restoration Program (LIRP)provided**
17	11052114055	Bokul Mia	Late Abdul Aziz	Late Rohima	**0**	**20000**	**20000**	-	-	**M**	**CCL is yet to be received but Livelihood and Income Restoration Program (LIRP) provided**
				TOTAL	**312000**	**340000**	**652000**				
	Total trained Affected Persons= 17 (M-17, F-0)										

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

	Vulnerability criteria:										
		BPL =	**03 Affected Persons**								
		Full loss=	**13 Affected Persons**								
		Elderly =	**01 Affected Person**								

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.12 Chicken & Duck Rearing (3rd Batch)

Annex-2/A

Dhaka Environmentally Sustainable Water Supply Project

Upazila: Araihazar, District: Narayanganj

Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

Name of trade: Chicken and Duck Rearing (3rd batch) **Training period : 03-07 October/2021 (5 days)**

SL NO	ID NO.	AFFECTED PERSONS NAME	FATHER'S/HUSBAND NAME	MOTHER'S NAME	Vulnerable Households	LIRP	TOTAL	REPLACEMENT OF	RELATIONSHIP WITH APS	M= Male, F=Female	Category of vulnarability
1	11052110207	Md Al Amin	Abdul Baten	Amina Begum	0	20000	164894	-	-	M	Full Loss
2	11042113570	Md Nobi Hossan	Late. Mohammad	Rahatun	0	20000	130201	-	-	M	Full Loss
3	11052113386	Md Shaiful Islam	Late Md.Billal Hossain	Mst.Shahatun Nesa	0	20000	470787	-	-	M	Full Loss
4	11062113150	HARUN AR RASID	Late Saheb Ali	Late Jaitun	0	20000	207152	-	-	M	Full Loss
5	11052110163	MD DAIMADDIN MOLLA	LATE RABIULLAH	MST AMINA KHATUN	0	20000	20000	-	-	M	Full Loss
6	11052213073	Md Mostafa Molla	Late Sofiullah Mollah	Late Tahrunnesa	0	20000	20000	-	-	M	Full Loss
7	11052212890	KHODEZA AKTER	ABDUL AZIZ	AMBIS AKTAR	0	20000	20000	-	-	F	Full Loss
8	11052112899	MD ABU DAIYAN	LATE MANNAN MOLLAH	LATE SUFIA BEGUM	0	20000	20000	-	-	M	Full Loss
9	11032112913	Rokeya	Roson Mia	Somirun Begum	0	20000	20000	Roson Mia	Wife	F	Full Loss
10	11062212951	SHAHIDA BEGUM	KHOBOR UDDIN	NURJAHAN	0	20000	20000	-	-	F	Full Loss
11	11022114037	Alamgir	Safaz Uddin	Rahima Begum	0	20000	20000	Safaz Uddin	Son	M	Full Loss
12	11062113914	Ismail	Md Shaidullah	LATE KODBANU	97500	20000	117500	Md Shaidullah	Son	M	Elderly
13	11042112800	Md Amdadul Molla	Md Aziz Mollah	Setara Begum	39000	20000	59000	Md Aziz Mollah	Son	M	Elderly
14	11052113162	Md Parvej	Md Wahid Miah	Mst Parvin Begum	78000	20000	98000	Md Wahid Miah	Son	M	BPL
15	11052213743	Mamun Mia	Rokeya Begum	MOHAMMAH ABDUR RAHMAN	39000	20000	59000	Rokeya Begum	Son	M	FHHH (Female headed households)
16	11062113810	Helal Uddin	Md Abdul Mannan Mia	Masuda Begum	58500	20000	78500	Md Abdul Mannan Mia	Son	M	BPL (Below poverty line)
TOTAL AMOUNT						320000	1525034				

Total trained Affected Persons= 16 (M-13, F-03), FHHHs- 1

Vulnerability criteria:

BPL =	02 Affected Persons
Full loss=	11 Affected Persons
Elderly =	02 Affected Persons
FHHHs =	01 Affected Person

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Annex-2/C

Dhaka Environmentally Sustainable Water Supply Project

Raw Water Transmission Line (Section-2)

Upazila: Araihazar, District: Narayanganj

Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

Name of trade:Fish Culture, **Duration: 07-11 November-2021 (05 Days)**

Sl No	ID No.	Name of training recipient	Father's/ Husband Name	Mother's Name	Vulnerable Households benefit	Training grant	Total	Replacement of ….	Relationship with Affected Persons	M/F (M=Male, F=Female)	Category of vunerable
1	11062110429	Nadim Buyan	Md Nazrul Islam	Rokeya Begum	58500	20000	78500	Md Nazrul Islam	Son	M	BPL (Below poverty line)
2	11052110215	Md Sirajul Islam	Late Hasen Ali	Late Somola Bibi	136500	20000	156500	-	-	M	Elderly
3	11042113892	Ali Asgor	LATE DOCTOR ABUL KASEM	AYESHA BEGUM	97500	20000	117500	Omar Faruk	Brother	M	BPL
4	11062110281	Nargis Begum	Md Halim	Renu Begum	78000	20000	98000	Md Halim	Wife	F	BPL
5	11052110164	Md Sanaulla Molla	Late Safiullah Mollah	Late Taherunnesa	97500	20000	117500	-	-	M	Elderly
6	11042113447	Suruz Mia	Late Abus Sobahan	Late Rupban	0	20000	20000	-	-	M	Full loss
				TOTAL	409500	80000	489500				

Total trained Affected Persons= 06 (M-05, F-1)

Vulnerability criteria:

BPL =	03 Affected Persons
Full loss=	01 Affected Person
Elderly =	02 Affected Persons

11.13Fish Culture

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.14 Tailoring

Annex-2/D

Dhaka Environmentally Sustainable Water Supply Project

Raw Water Transmission Line (Section-2)

Upazila: Araihazar, District: Narayanganj

Implemented by: DWASA with the assistance of the Development Organisation of the Rural Poor (DORP)

Name of trade: Tailoring (2nd Bach), **Duration: 19-23 September-2021 (05 Days)**

Sl No	ID No.	Name of training recipient	Father's/ Husband Name	Mother's Name	Vulnerable Household benefit	Training grant	Total	Replacement of	Relationship with Affected Persons	M/F (M=Male, F=Female)	Category of vunerable
1	11042213674	Maheetun	Md Anower Hossain	Mst Afia	78000	20000	98000		-	F	FHHH (Female headed household)
2	11052110160	Shilpi	Md Nannu Mia	Rehana	97500	20000	117500	Md Nannu Mia	Wife	F	BPL (Below poverty line)
3	11062113799	Minara Akter	Jahirul	Firoza Begum	58500	20000	78500	Jahirul	Wife	F	BPL
4	11062213870	Sahanaj	Abul Hossan	Late Fullmehorun	97500	20000	117500		-	F	FHHH
5	11062110406	Zakia Begum	Amir Hossen	Monowara Begum	0	20000	20000	Amir Hossen	Wife	F	Full Loss
6	11062210473	Umme Habiba	Shahajada	Mst Gol Akther Bagum	0	20000	20000	Mst Gol Akther Bagum	Daughter	F	Full Loss
7	11062210457	Halima	Ali ahmad	Safia	0	20000	20000		-	F	Full Loss
8	11062210432	Saleha Begum	Alomgir Buyan	Safia	0	20000	20000		-	F	Full Loss
9	11042111849	Kohinoor Akter	Anowar Hossan	Kokila Begum	0	20000	20000	Md. Anowar Hossain	Wife	F	Full Loss
				TOTAL	331500	180000	511500				

Total trained Affected Persons= 09 (M-0, F-09), FHHHs- 2 Affe

Vulnerability criteria:

BPL =	02 Affected Persons
Female from FHHHs =	02 Affected Persons
Full loss =	05 Affected Persons(2 from Male Headed Households & 3 from FHHHs)

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.15 Pictures on Community Meeting, LIRP & IGA

Pictures on community meeting, Livelihood and Income Restoration Program (LIRP) training and Income Generating Activities (IGA)

Community meeting with affected persons

Community meeting with affected persons

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Vulnerable AP received vulnerable benefit from the project, Section 3

Vulnerable APs received training on livelihood activities, Section 2

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Income generating activities (small business) doing by the male Affected Person, Section 2

Income generating activities (vegetable gardening) doing by the female Affected Person, Section 1

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Income generating activities (chicken rearing)doing by Bilkis Begum, Section 4

Female security guard on duty at intake area, Section 1

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Female security guard on duty at intake area, Section 1

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.16 Microfinance involvement in Section-1

Dhaka Environmentally Sustainable Water Supply Project (DESWSP)

Development Organization of the Rural Poor (DORP)

List of Affected PersonsInvolved with NGO/financial institutions

Section-: 01 Monitoring Month: December /2021 Name of Upazila: Araihazar, Name of District: Narayanganj, Date: 31.12.2021

(AP=Affected Person, M=Male, F=Female, LIRP= Livelihood and Income Restoration Program, IGA= Income Generating Activities)

Total APs eligible for LIRP training: 52 APs. (M-33, F-19)

Total APs received training: 52 APs (M- 31, F- 21)

Total trained APs involved with IGA: 52 APs (M-31, F-21)

APs linked with financial institutions during this reporting period: 14APs (M- 09, F-05)

Total APs linked with financial institutions: 33APs (M- 19, F-14)

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Receive Trade	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
1.	11011110342	Jahanara	Late Nuruzzaman	Sumbupura Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank	01833404646	
2.	11011110548	Hossain Ali	Late Akkal Ali	Sumbupura Mouza	Cow & Goat Rearing	Yes	SIDOR NGO	01869434557	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

3.	11011210347	Minara	Late Taijul Islam	Tatea Mouza	Cow & Goat Rearing	Yes	BRACK NGO	01883364216	
4.	11011110256	Al Amin	Late Abdul Munaf	Sumbupura Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank	01720309661	
5.	11011210004	Sorif	LATE RABIUL	Sumbupura Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank	01949866627	
6.	11011110003	Rup Miah	Late Chan Mia	Sumbupura Mouza	Cow & Goat Rearing	Yes	Agrani Bank	01927383428	
7.	11011110094	Md. Khaliur	Late HaziNeowaz Ali	Sumbupura Mouza	Cow & Goat Rearing	Yes	SIDOR NGO	01827795267	
8.	11011110016	Shohel Miah	Late. Abdul Barek	Sumbupura Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank	01726107209	
9.	11011112798	Mojibor Rahman	Mongol Miah	Sumbupura Mouza	Cow & Goat Rearing	Yes	ASA NGO	01717920834	
10.	11011110091	Jobed Ali	Late Korom Ali	Sumbupura Mouza	Cow & Goat Rearing	Yes	Grameen Bank	01754592743	
11.	11011110001	Abdul Aziz	Late Abdul ohab	Sumbupura Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank		
12.	11011110002	Ayesa	Late Abu hanif	Sumbupura Mouza	Cow & Goat Rearing	Yes	SSS NGO		
13.	11011110103	Md Mostafa	Neyas Ali Hazi	Sumbupura Mouza	Cow & Goat Rearing	Yes	ASA NGO		

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

14.	11011110008	Sub Mia	Late Mojajffor Ali	Sumbupura Mouza	Cow & Goat Rearing	Yes	Sokti Foundation		
15.	11011110232	Md harunurRoshed	Late Lal Mia Beparey	Sumbupura Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank		
16.	11011210261	Ayesa Khatun	Amir ali	Sumbupura Mouza	Cow & Goat Rearing	Yes	ASA NGO		
17.	11011110520	Sahidullah	Late.Afil Uddin	Sumbupura Mouza	Chicken& Duck Rearing	Yes	Grameen Bank	01736936794	
18.	11011210534	Lakiba	Safikul Islam	Sumbupura Mouza	Chicken& Duck Rearing	Yes	BRACK NGO	01831125520	
19.	11011212721	SamsuzzamanLimom	Md. Ismail Mia	Sumbupura Mouza	Chicken& Duck Rearing	Yes	Bangladesh Krishi Bank	01776271440	
20.	11011210557	Fatema	Late Sirajul Islam	Sumbupura Mouza	Chicken& Duck Rearing	Yes	PalliMongalKarmosuchi	01790453308	
21.	11011210100	Sufiya Khatun	Late Joj Mia	Sumbupura Mouza	Chicken& Duck Rearing	Yes	PalliMongalKarmosuchi	01749396835	
22.	11011110241	Hosna	Late Kawsar	Sumbupura Mouza	Chicken& Duck Rearing	Yes	ASA NGO	01754451793	
23.	11011110239	Roshan Ali	Late.Abdul Rahim	Sumbupura Mouza	Chicken& Duck Rearing	Yes	ASA NGO	01726174628 3	
24.	11011212814	Jahanara Begum	Jamal Uddin	Sumbupura Mouza	Chicken& Duck Rearing	Yes	BRACK NGO	01764350258	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

25.	1101112747	Kamal Hossen	Mohiuddin	Sumbupura Mouza	Chicken& Duck Rearing	Yes	Bangladesh Krishi Bank	01817014445	
26.	11011110099	Rohima Begum	Dulal Hossain	Sumbupura Mouza	Chicken& Duck Rearing	Yes	Grameen Bank		
27.	11011210093	Sama Akter	Nurul Amin	Sumbupura Mouza	Chicken& Duck Rearing	Yes	SIDOR NGO		
28.	11011112747	Md. Kamal Hossain	Mohi Uddin	Sumbupura Mouza	Chicken& Duck Rearing	Yes	ASA NGO	01817014446	
29.	11011112788	SHOQUR MOHAMMAD	Late mortobali	Sumbupura Mouza	Chicken& Duck Rearing	Yes	SIDOR NGO	01728160865	
30.	11011210302	MONORA	Sadar Ali	Sumbupura Mouza	Chicken& Duck Rearing	Yes	ASA NGO	01776674381	
31.	11011110105	Md Jomir Ali	Late Mokarrom Ali	Sumbupura Mouza	Chicken& Duck Rearing	Yes	ASA NGO		
32.	**11011213882**	**Rahima Begum**	**Hafijuddin**	**Sumbupura Mouza**	**Tailoring**	**Yes**	**ASA NGO**	**01744681787**	
33.	**11011213880**	**Halima**	**Iman Ali**	**Sumbupura Mouza**	**Tailoring**	**Yes**	**Grameen Bank**	**01770512377**	

Note: During this reporting period 14 APs involved with IGA which is marked in the table and up to 31st December total 33 APs involved with IGA.

Summary of the APs involved with following financial institutions

Bangladesh Krishi Bank = 8 APs (M-7, F-1)

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

SIDOR NGO	= 4 APS (M-3, F-1)
BRAC NGO	= 3 APs (M-0, F-3)
Agrani Bank	= 1 AP (M-1, F-0)
ASA NGO	= 9 APs (M-4, F-5)
Grameen Bank	= 4 APs (M-2, F-2)
Palli Mongal Karmosuchi	=2 APs (M-1, F-1)
SSS NGO	=1 AP (M-0, F-1)
Sokti Foundation	=1 AP (M-1, F-0)

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.17Microfinance involvement in Setion-2

Dhaka Environmentally Sustainable Water Supply Project (DESWSP)

Development Organization of the Rural Poor (DORP)

List of APs involved with NGO/financial institutions

Section-: 02 Monitoring Month: December /2021 Name of Upazila: Araihazar, Name of District: Narayanganj,
Date: 31.12.2021

(AP=Affected Person, M=Male, F=Female, LIRP= Livelihood and Income Restoration Program, IGA= Income Generating Activities)

Total APs eligible for LIRP training: 291 APs (M-216, F-75)
Total APs received training: 243 APs (M- 166, F- 77)

Total trained APs involved with IGA: 235 APs (M- 163, F- 72)

APs linked with financial institutions during this reporting period: 54 APs (M-39, F-15)

Total APs linked with financial institutions: 89 APs (M-60, F-29)

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
1.	11052210206	Masuda Begum	Nurul Haque	Kamaldi Mouza	Cow & Goat Rearing	Yes	Grameen Bank	01796277834	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
2.	11052213027	SalehaAkter	Md Alauddin	Ranidi Mouza	Cow & Goat Rearing	Yes	BRAC NGO	01902218906	
3.	11032213218	Fajila	Late Taizuddin	Auguandi Mouza	Cow & Goat Rearing	Yes	Grameen Bank	01779185115	
4.	11062113679	Dolal Bhuiyan	Late Abdul Ali Bhuiyan	Idbardi Mouza	Cow & Goat Rearing	Yes	BRAC NGO	01812181546	
5.	11062213811	Monuara Begum	Ayet Ali	Baliapara Mouza	Cow & Goat Rearing	Yes	BRAC NGO	01717838224	
6.	11032110051	Alomgir Hossain	Abdul Batan	Auguandi Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank	01793320529	
7.	11042213216	Mst Salma	Late Abdul Motaleb	Atadi Mouza	Cow & Goat Rearing	Yes	PalliMongalKarmosuchi	01845251037	
8.	11042113137	Bilkis	Jalal	Kadirdia Mouza	Cow & Goat Rearing	Yes	Grameen Bank	01991049392	
9.	11062110288	Shahjahan Mia	Late Tufani Miah	Baliapar Mouza	Cow & Goat Rearing	Yes	Bangladesh Krishi Bank	01922961602	
10.	11052110157	Md Babul Miah	Md. RobiulMolla	Atabdi Mouza	Cow & Goat Rearing	Yes	BRAC NGO	01959612627	
11.	11032110044	Md. Babul Hosun	Late Hazrat Ali	Auguandi Mouza	Cow & Goat Rearing	Yes	ASA NGO	01779629055	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
12.	11032210201	Peyara	Helal Uddin	HALIMA	Cow & Goat Rearing	Yes	BRAC NGO	01868293441	
13.	11032111718	Hossain Ali	Late Abdul aziz	Auguandi	Cow & Goat Rearing	Yes	BRAC NGO	01861998451	
14.	11052113254	Md Abed Ali	Late AbdurRahamn	Sripoti	Cow & Goat Rearing	Yes	ASA NGO	01736684537	
15.	11052110154	Md SohidllaMolla	Late OliullahMolla	Atabdi	Cow & Goat Rearing	Yes	ASA NGO	01822551840	
16.	11052113075	Md Abdul BatenMolla	Late AzzillaMomlla	Atabdi	Cow & Goat Rearing	Yes	Grameen Bank	01933488642	
17.	11052113078	Md Mamun	Md Nurul Islam	Auguandi Mouza	Cow & Goat Rearing	Yes	ASA NGO		
18.	11062113041	ArifurRahaman	SahajaddinBhuyan	Lenguardi	Cow & Goat Rearing	Yes	PalliMongalKarmosuchi		
19.	11032110058	Md Sojol Mia	Abdul Matin	Laxmipura	Cow & Goat Rearing	Yes	ASA NGO		
20.	11032110053	Najarul	Late Aual	Auguandi	Cow & Goat Rearing	Yes	BRAC NGO		
21.	11032213249	Fatema	F.Momen	Auguandi Mouza	Tailoring	Yes	Bangladesh Krishi Bank	01989472779	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
22.	11052213241	Joni Akter	H.MdNaym	Tilchandi Mouza	Tailoring	Yes	Grameen Bank	01986794758	
23.	11052213793	Shirin Shila	H. Salim Bhuiyan	Hazishadi Mouza	Tailoring	Yes	ASA NGO	01846790314	
24.	11062110422	Tanvir	Md Abdul Baten Miah	Idbardi Mouza	Tailoring	Yes	Ektee Bari EkteeKhamar	01766302227	
25.	11062210430	Sahera	Mobarak Hossain	Idbardi Mouza	Tailoring	Yes	Bangladesh Krishi Bank	01648187942	
26.	11062110428	JorinaAkter	H. Md Ebrahim Bhuyain	Idbardi Mouza	Tailoring	Yes	Bangladesh Krishi Bank	01965473381	
27.	11062113805	ParulAkter	H. Nobi Hossain	Idbardi Mouza	Tailoring	Yes	SIDOR NGO	01940627441	
28.	11052113219	Israt Jahan	H. Alamin	RanidiMouza	Tailoring	Yes	PalliMongalKarmosuchi	01929572494	
29.	11032110055	SUFIA BEGUM	ABDUL AUAL	AuguandiMouza	Tailoring	Yes	Bangladesh Krishi Bank	01872116871	
30.	11042213528	KHALEDA AKTER	H. FAZLUL HAQUE	Atadi Mouza	Tailoring	Yes	Grameen Bank		
31.	11052112889	Amjad Hosan	Md Serajul Islam	Ranidi Mouza	Small Business	Yes	Grameen Bank	01710666871	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
32.	11052113197	Md Montaz Uddin Mollah	Late Jahor Ali Molla	Ranidi Mouza	Small Business	Yes	BRAC NGO	01711220287	
33.	11062113791	Md Ruhul Amin Molla	Kopil Uddin Molla	Idbardi Mouza	Small Business	Yes	Grameen Bank	01856876374	
34.	11062110442	Md Jaynal	Abu Siddik	Idbardi Mouza	Small Business	Yes	BRAC NGO	01724793954	
35.	11062110392	AkterHosan	Late Nurul Islam	Idbardi Mouza	Small Business	Yes	Bangladesh Krishi Bank	01726197675	
36.	11062113782	Abdus Salam	Md Serajul Islam	Mouza	Small Business	Yes	ASA NGO	01993519185	
37.	11062113630	Md Shahabuddin Molla	Late Hasib Molla	Idbardi Mouza	Small Business	Yes	Grameen Bank	01929155972	
38.	11062110514	Ali Ahmmad	Yousof Ali	Idbardi Mouza	Small Business	Yes	BRAC NGO	01948767443	
39.	11061110107	Md Joynal Abedin	Md Tyob Ulla Miah	Idbardi Mouza	Small Business	Yes	PalliMongalKarmosuchi	01918417018	
40.	11062113792	Md Tota	Late Aziz Rahaman	Eidbardi	Small Business	Yes	ASA NGO	01956772290	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
41.	11062113677	Md Kobir Sarkar	Easin	Eidbardi	Small Business	Yes	Bangladesh Krishi Bank	01799090666	
42.	11062110427	Waliulla	Miraj Uddin	Eidbardi	Small Business	Yes	SIDOR NGO	01928363083	
43.	11062113848	Salem Mia	Late Abdul Malek mia	Eidbardi	Small Business	Yes	PalliMongalKarmosuchi	01724793953	
44.	11062112819	Asraful	Md Osman Molla	Baliapara	Small Business	Yes	Bangladesh Krishi Bank	01720906138	
45.	11062110280	Joj Mia	Late Taijuddin	Baliapara	Small Business	Yes	BRAC NGO	01720906138	
46.	11062113821	Delower	Md Shahajoddin	Baliapara	Small Business	Yes	ASA NGO		
47.	11062112953	Faruk Hossan	Sona Mia	Baliapara	Small Business	Yes	BURI Bangladesh		
48.	11062113775	Shalom	Samsu Mia	Baliapara	Small Business	Yes	GRAMEEN Bank		
49.	11062110481	Jobayer Hasan	Ashad Miah	Eidbardi	Small Business	Yes	Bangladesh Krishi Bank		
50.	11062110436	Shibli	Md Nurul Islam	Eidbardi	Small Business	Yes	ASA NGO		

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
51.	11062110381	Nasim	Md Halim Sarker	Eidbardi	Small Business	Yes	BRAC NGO		
52.	11062113710	Babul Miah	Late Alauddin	Eidobardi	Small Business	Yes	PolliBikas NGO		
53.	11062113142	Md Sofiqul Islam	Late Haji Serajol Haque	Kumarabag	Small Business	Yes	Sokti Foundation		
54.	11042113451	Md Kamal	Aktaruzzaman	Auguandi	Small Business	Yes	BRAC NGO		
55.	11032110200	Arju Miya	Late Sona Mia	Auguandi	Small Business	Yes	GRAMEEN Bank		
56.	11062211562	Jobeda Begum	Late Abdul Mojid	Baliapara Mouza	Chicken& Duck Rearing	Yes	GRAMEEN Bank	01406297443	
57.	11052112884	Rajib	Konak Dar	Ranidi Mouza	Chicken& Duck Rearing	Yes	Grameen Bank	01911704449	
58.	11052110216	Sakib	Babul Mollah	Kamaldi Mouza	Chicken& Duck Rearing	Yes	Pubali Bank Ltd	01746107663	
59.	11042213621	Majeda Begum	Late Munsur Ali	Atadi Mouza	Chicken& Duck Rearing	Yes	PalliMongalKarmosuchi	01744290701	
60.	11052113345	Omar Faruk	Md Ebrahim	Hazishadi Mouza	Chicken& Duck	Yes	BRAC NGO	01726712713	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
			Mia		Rearing				
61.	11062110286	Md Arman Bhuyan	Late Abdul High	Baliapara Mouza	Chicken& Duck Rearing	Yes	BohumukhiSomobayso miti	01720827185	
62.	11062110513	ShoelMolla	Md Mejba Uddin Molla	Baliapara Mouza	Chicken& Duck Rearing	Yes	BohumukhiSomobayso miti	01977265374	
63.	11062112954	Mintu Mia	Shafiqul Islam	Idbardi Mouza	Chicken& Duck Rearing	Yes	Grameen Bank	01989273283	
64.	11062110435	Azzijul Hakim	Ali Ahamed	Eidbardi	Chicken& Duck Rearing	Yes	SIDOR NGO	01766242970	
65.	11032110049	Monir Hossan	Late Hazrat Ali	Auguandi	Chicken& Duck Rearing	Yes	Grameen Bank	01779629056	
66.	11042113751	Faruk	Late Hasem	Atadi	Chicken& Duck Rearing	Yes	ASA NGO	01729747584	
67.	11062110515	Kamal Hossain	Late Alauddin	Eidbardi	Chicken& Duck Rearing	Yes	BRAC NGO	01631813887	
68.	11032113580	Abdul Ohab	Late Madhbor Ali	Auguandi	Chicken& Duck Rearing	Yes	Grameen Bank	01811156938	
69.	11062213906	Shain Mia	Late AbdurRasidBuy	Eidbardi	Chicken& Duck	Yes	BRAC Bank	01716402833	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
			an		Rearing				
70.	11042113785	Khadiza	Md Nurul Islam	Atadi	Chicken& Duck Rearing	Yes	Grameen Bank	01846239440	
71.	11032110251	Rehana	Md RofikBuyan	Auguandi	Chicken& Duck Rearing	Yes	Grameen Bank	01786491776	
72.	11042212976	MST.ASAIFA BEGUM	LATE MULSEM UDDIN	BAZINABOND	Chicken& Duck Rearing	Yes	Grameen Bank		
73.	11022213196	ROWSHANARA BEGUM	LATE. ABDUR RAHMAN	Laxmipur	Chicken& Duck Rearing	Yes	SIDOR NGO		
74.	11062213724	PARVIN BEGUM	HASIBUR	Kumarabag	Chicken& Duck Rearing	Yes	BRAC Bank		
75.	11042213675	AKHLIMA BEGUM	LATE ABDUL HAQUE	Atadi	Chicken& Duck Rearing	Yes	PalliMongalKarmosuchi		
76.	11062210118	MINA HAQUE	SAFOR ALI	Eidobardi	Chicken& Duck Rearing	Yes	Grameen Bank		
77.	11062210384	GIASMIN	KOBIR HOSSAIN	Eidobardi	Chicken& Duck Rearing	Yes	CSS NGO		
78.	11062110434	Parvin	PEAR ALI	Eidobardi	Chicken& Duck	Yes	Grameen Bank		

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
					Rearing				
79.	11052213073	Md Mostafa Molla	Late SofiullahMollah	Atabdi	Chicken& Duck Rearing	Yes	Sokti Foundation		
80.	11062113150	HARUN AR RASID	Late Saheb Ali	Langurdi	Chicken& Duck Rearing	Yes	PalliMongalKarmosuchi		
81.	11042113570	Md Nobi Hossan	Late. Mohammad	Kamaldi	Chicken& Duck Rearing	Yes	ASA NGO		
82.	11052110207	Md Al Amin	Abdul Baten	Kamaldi	Chicken& Duck Rearing	Yes	Grameen Bank		
83.	11052110164	Md SanaullaMolla	Late SafiullahMollah	Atabdi	Fish Culture	Yes	PalliMongalKarmosuchi		
84.	11062110429	Nadim Buyan	Md Nazrul Islam	Eidbardi	Fish Culture	Yes	ASA NGO		
85.	11052110215	Md Sirajul Islam	Late Hasen Ali	Kamaldi	Fish Culture	Yes	Grameen Bank		
86.	11052112880	Taslima	RustumBuya	Auguandi	Vegetable Gardening	Yes	Grameen Bank		
87.	11052112981	Sofikul Islam	Md Nurul	RANIDI	Vegetable Gardening	Yes	ASA NGO		

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Sl #	AP ID No	Name and Address of the Trained Person	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Mobile Number	Remarks
			Haque						
88.	11062110504	Hajerea Begum	Ianus Mia	Baliapara	**Vegetable Gardening**	**Yes**	**PalliMongalKarmosuchi**		
89.	11012113499	Din Islam	Babul Mia	Choitankanda	**Vegetable Gardening**	**Yes**	**Grameen Bank**		

Note: During this reporting period 54 APs involved with IGA which is marked in the table and up to 31st December total 89 APs involved with IGA.

Summary of the APs involved with following financial institutions

Bangladesh Krishi Bank = 10 APs (M-7, F-3)

SIDOR NGO = 4 AP (M-2, F-2)

BRAC NGO = 15 APs (M-12, F-3)

ASA NGO = 14 APs (M-12, F-2)

Grameen Bank = 25 APs (M-13, F-12)

Palli Mongal Karmosuchi =10 APs (M-4, F-6)

Bohumukhi Somobaysomiti = 2 APs (M-2, F-0)

Ektee Bari Ektee Khamar = 1 AP (M-1, F-0)

Pubali Bank LTD. = 1 AP (M-1, F-0)

BRAC Bank = 2 APs (M-1, F-1)

Sokti Foundation = 2 APs (M-2, F-0)

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Polli Bikas NGO = 1 AP (M-1, F-0)
BURI Bangladesh = 1 AP (M-1, F-0)
CSS NGO = 1 AP (M-0, F-1)

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.18 Microfinance involvement in Section-4

Dhaka Environmentally Sustainable Water Supply Project (DESWSP)

Development Organization of the Rural Poor (DORP)

List of APs involved with NGO/financial institutions

Section-: 04 Monitoring period: December/2021 Name of Upazila: Rupgonj, District: Narayanganj, Reporting Date: 31.12.2021

(AP=Affected Person, LIRP= Livelihood and Income Restoration Program, IGA= Income Generating Activities)

Total APs eligible for LIRP training: 89 affected persons (Male-81, Female-08)

Total APs received training: 83 affected persons (Male - 60, Female - 23)

Total trained APs involved with IGA: 78 affected persons (Male - 57, Female - 21)

APs linked with financial institutions during this reporting period: 8 affected persons (Male -05, Female -03)

Total APs linked with financial institutions: 11 affected persons (Male -7, Female -04)

Sl. No.	affected persons' ID No	affected persons' Name	Name of Father/Husband	Name of Mouza	Name of Trade Received training	Involved IGA	Name of NGO/financial institutions	Remarks
01.	12094145005	Md. Aynal Haque	Late- Hazi Shahabuddin	Char-Gandharbpur	Small Business	Yes	Bangladesh Krishi Bank	
02	12094145066	Md. Rabbi	Md. MofijulProdhan	Char-	Chicken & Duck	Yes	Bangladesh Krishi	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

		Prodhan		Gandharbpur	rearing		Bank	
03	12094145051	Solaiman	Md. Waliullah	Char-Gandharbpur	Cow & Goat rearing	Yes	Bangladesh Krishi Bank	
04	12094145085	Ashma	Late Odud Miah	Char-Gandharbpur	Small Business	No	Grameen Bank	
05	12094145150	Roksana	F. Magibur Rahman	Char-Gandharbpur	Tailoring	Yes	Grameen Bank	
06	12094140538	Selina Begum	Habibullah Prodhan	Char-Gandharbpur	Chicken & Duck rearing	Yes	Grameen Bank	
07	12094145006	Jhuma	Alauddin	Char-Gandharbpur	Tailoring	Yes	ASA (NGO)	
08	12094140523	Mizanur Rahman	Abdul Halim	Char-Gandharbpur	Cow & Goat rearing	Yes	ASA (NGO)	
09	12094145120	Md. Arab Ali	Shahabuddin	Char-Gandharbpur	Cow & Goat rearing	Yes	ASA (NGO)	
10	12094145205	Abdul Kadir Bhuiya	Abdul Bhuiyan	Char-Gandharbpur	Chicken & Duck rearing	Yes	Sajeda Foundation	
11	12094145156	Shahidullamia	Late Samsuddin	Char-Gandharbpur	Cow & Goat rearing	Yes	TMSS (NGO)	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Note: During this reporting period 08 affected persons involved with IGA which is marked in the table and up to 31st December total 11 APs involved with IGA.

Summary of the APs involved with following financial institutions

Bangladesh Krishi Bank	= 03 affected persons (Male-03, Female-0)
ASA NGO	= 03 affected persons (Male -02, Female -1)
Grameen Bank	= 03 affected persons (Male -0, Female -03)
Sajeda Foundation	= 01 affected person (Male -01, Female -0)
TMSS	= 01 affected person (Male -01, Female -0)

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.19 Request Letter for COVID Vaccine on Site_Bangla

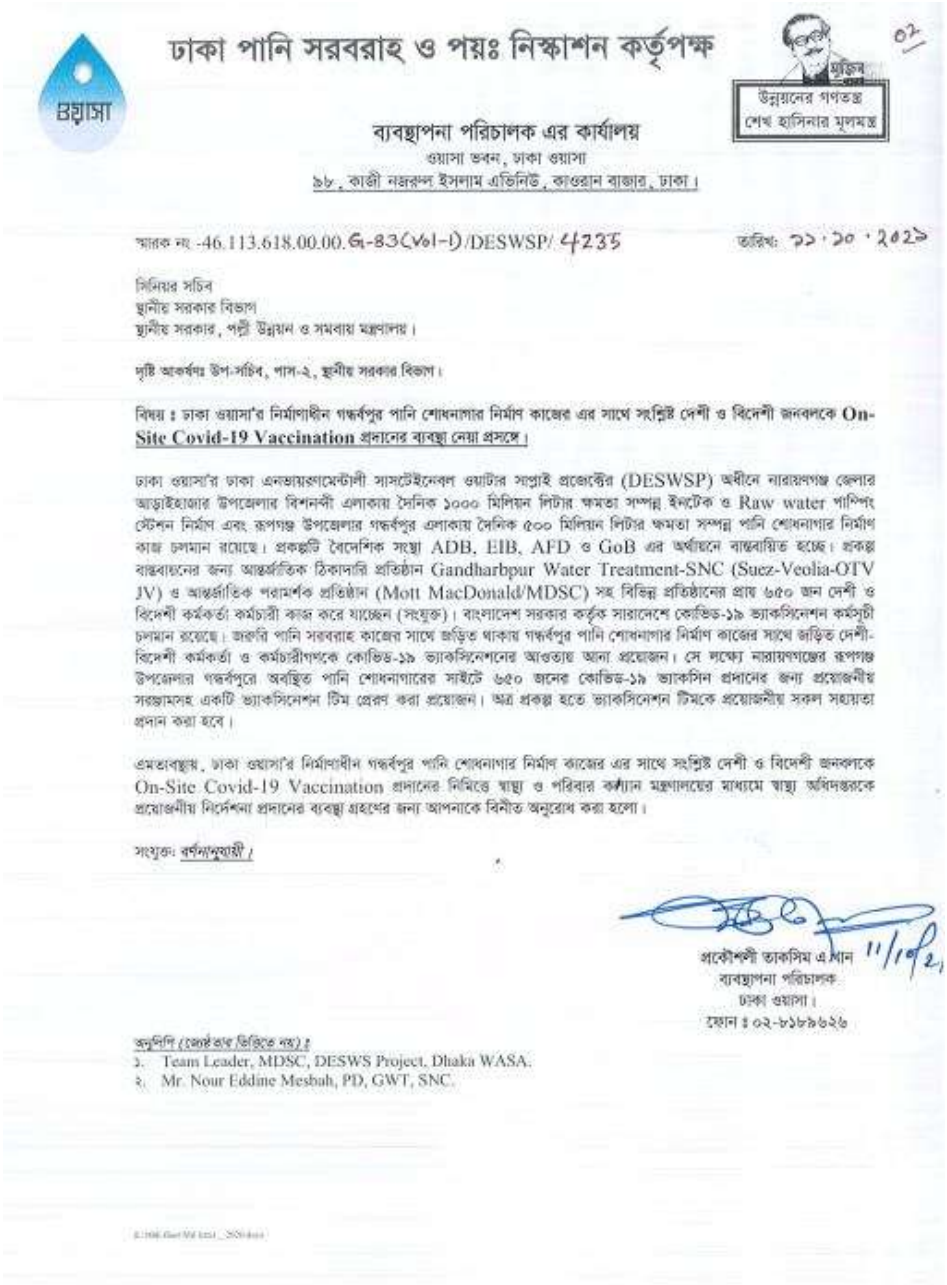

ঢাকা পানি সরবরাহ ও পয়ঃ নিস্কাশন কর্তৃপক্ষ

উন্নয়নের গণতন্ত্র
শেখ হাসিনার মূলমন্ত্র

ব্যবস্থাপনা পরিচালক এর কার্যালয়
ওয়াসা ভবন, ঢাকা ওয়াসা
৯৮, কাজী নজরুল ইসলাম এভিনিউ, কাওরান বাজার, ঢাকা।

স্মারক নং -46.113.618.00.00.৬-83(Vol-1)/DESWSP/ 4235 তারিখ: ২২ · ১০ · ২০২১

সিনিয়র সচিব
স্থানীয় সরকার বিভাগ
স্থানীয় সরকার, পল্লী উন্নয়ন ও সমবায় মন্ত্রণালয়।

দৃষ্টি আকর্ষণ উপ-সচিব, পাস-২, স্থানীয় সরকার বিভাগ।

বিষয় : ঢাকা ওয়াসা'র নির্মাণাধীন গন্ধর্বপুর পানি শোধনাগার নির্মাণ কাজের এর সাথে সংশ্লিষ্ট দেশী ও বিদেশী জনবলকে **On-Site Covid-19 Vaccination** প্রদানের ব্যবস্থা নেয়া প্রসঙ্গে।

ঢাকা ওয়াসা'র ঢাকা এনভায়রণমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্টের (DESWSP) অধীনে নারায়ণগঞ্জ জেলার আড়াইহাজার উপজেলার বিশনন্দী এলাকায় দৈনিক ১০০০ মিলিয়ন লিটার ক্ষমতা সম্পন্ন ইনটেক ও Raw water পাম্পিং স্টেশন নির্মাণ এবং রূপগঞ্জ উপজেলার গন্ধর্বপুর এলাকায় দৈনিক ৫০০ মিলিয়ন লিটার ক্ষমতা সম্পন্ন পানি শোধনাগার নির্মাণ কাজ চলমান রয়েছে। প্রকল্পটি বৈদেশিক সংস্থা ADB, EIB, AFD ও GoB এর অর্থায়নে বাস্তবায়িত হচ্ছে। প্রকল্প বাস্তবায়নের জন্য আন্তর্জাতিক ঠিকাদারি প্রতিষ্ঠান Gandharbpur Water Treatment-SNC (Suez-Veolia-OTV JV) ও আন্তর্জাতিক পরামর্শক প্রতিষ্ঠান (Mott MacDonald/MDSC) সহ বিভিন্ন প্রতিষ্ঠানের প্রায় ৬৫০ জন দেশী ও বিদেশী কর্মকর্তা কর্মচারী কাজ করে যাচ্ছেন (সংযুক্ত)। বাংলাদেশ সরকার কর্তৃক সারাদেশে কোভিড-১৯ ভ্যাকসিনেশন কর্মসূচী চলমান রয়েছে। জরুরি পানি সরবরাহ কাজের সাথে জড়িত থাকায় গন্ধর্বপুর পানি শোধনাগার নির্মাণ কাজের সাথে জড়িত দেশী-বিদেশী কর্মকর্তা ও কর্মচারীগণকে কোভিড-১৯ ভ্যাকসিনেশনের আওতায় আনা প্রয়োজন। সে লক্ষ্যে নারায়ণগঞ্জের রূপগঞ্জ উপজেলার গন্ধর্বপুরে অবস্থিত পানি শোধনাগারের সাইটে ৬৫০ জনের কোভিড-১৯ ভ্যাকসিন প্রদানের জন্য প্রয়োজনীয় সরঞ্জামসহ একটি ভ্যাকসিনেশন টিম প্রেরণ করা প্রয়োজন। অত্র প্রকল্প হতে ভ্যাকসিনেশন টিমকে প্রয়োজনীয় সকল সহায়তা প্রদান করা হবে।

এমতাবস্থায়, ঢাকা ওয়াসা'র নির্মাণাধীন গন্ধর্বপুর পানি শোধনাগার নির্মাণ কাজের এর সাথে সংশ্লিষ্ট দেশী ও বিদেশী জনবলকে On-Site Covid-19 Vaccination প্রদানের নিমিত্তে স্বাস্থ্য ও পরিবার কল্যাণ মন্ত্রণালয়ের মাধ্যমে স্বাস্থ্য অধিদপ্তরকে প্রয়োজনীয় নির্দেশনা প্রদানের ব্যবস্থা গ্রহণের জন্য আপনাকে বিনীত অনুরোধ করা হলো।

সংযুক্ত: বর্ণনানুযায়ী।

প্রকৌশলী তাকসিম এ খান 11/10/21
ব্যবস্থাপনা পরিচালক
ঢাকা ওয়াসা।
ফোন : ০২-৮১৮৯৬২৬

অনুলিপি (জ্যেষ্ঠতার ভিত্তিতে নয়) :
১. Team Leader, MDSC, DESWS Project, Dhaka WASA.
২. Mr. Nour Eddine Meshab, PD, GWT, SNC.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.20 Request Letter for COVID Vaccine on Site_English

Dhaka Water Supply & Sewerage Authority

Office of the Managing Director's

WASA Bhaban, Dhak WASA

98 Kazi Nazrul Islam Avenue, Kaowran Bazar, Dhaka

Memo No.: 46.113.618, 00, 00. G-83 (Vol.-1)/DESWSP/ 4135 Date: 11. 10. 2021

Senior Secretary

Local Government Division

Ministry of Local Government Rural Development and Cooperatives.

Attention: To Deputy Secretary, PAS-2, Local Government Division

Subject: Prayer for taking initiative of 'on Site Covid-19 Vaccination' to the manpower (national and international) engaged in construction work of water treatment plan at Gandharbpur under DWASA.

Under the 'Dhaka Environmentally Sustainable Water Supply Project (DESWSP) construction of a water intake with a capacity of 1000 million litres per day (MLD) raw water from pumping station at Bishnandi area under AraihazarUpazila of Narayanganj district and construction of a water treatment plant (WTP) at Gandharbpur with a capacity of 500 million liters per day (MLD) at Gandharbpur under RupganjUpazila of Narayanganj district is ongoing. The project is being implementing with the financial support of ADB, EIB, AFD and Bangladesh Government. For implementation of the project a large number of native and foreign human resources are working. In this construction work the institution of international contractors are engaged at 'Water Treatment' area named "Gandharbpur Water Treatment- SNC (Suez-Veolia-OTVJV) and international consulting firm (Mott. MacDonald/MDSC). About 650 personnel including officers and workers are working at the Gandharbpur project site. The Covid-19 vaccination program is ongoing throughout the country by the Government of Bangladesh. A number of 650 personnel are engaged in the kind of emergency work for supplying purified water at an urgent basis to the Dhaka city dwellers, under this project. Hence, a vaccination team is needed to send to the project construction area at Gandharbpur area to vaccinate all of the personnel working in the Gandharbpur project site. All sorts of support to the vaccination team will be provided from the project.

Therefore, you are humbly requested to give necessary instructions through the Ministry of Health and Family Planning for providing on-site Covid-19 Vaccination to those native and foreign employees engaged in construction of "Water Treatment Plant" at Gandharbpur, RupganjUpazila.

Engineer Taksim A Khan

Managing Director

Dhaka WASA

Phone: 02-8189626

CC (Not based on Seniority)

1. Team Leader, MDSC, DESWS Project, Dhaka WASA

2. Mr. Nour Eddine, Mesbah, PD, GWT, SNC.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.21 Awareness Campaign Notice to Affected Persons regarding

DHAKA ENVIRONMENTALLY SUSTAINABLE WATER SUPPLY PROJECT
DHAKA WATER SUPPLY & SEWERAGE AUTHORITY
DESWSP, DHAKA WASA

Memo No. : 46.113.618.00.G-243(V-1)/DESWSP/ 4167 Date : 26·09·2021

নোটিশ

আপনারা অবগত আছেন যে, ঢাকা ওয়াসা, বাংলাদেশ সরকার ও বৈদেশিক ঋণ সহায়তায় 'ঢাকা এনভায়রণমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই' প্রকল্পের আওতায় গন্ধর্বপুর পানি শোধনাগার নির্মাণ প্রকল্প বাস্তবায়ন করছে। প্রকল্পটি নারায়ণগঞ্জ জেলার আড়াইহাজার উপজেলার বিশনন্দী এলাকায় মেঘনা নদীর পাড়ে প্রস্তাবিত ইনটেক থেকে অপরিশোধিত পানি উত্তোলন করে পাইপলাইনের মাধ্যমে রূপগঞ্জ উপজেলার গন্ধর্বপুরে ওয়াসার নিজস্ব জমিতে পানি শোধনাগার প্ল্যান্টে নিয়ে তা পরিশোধন করে পরিশোধিত/বিশুদ্ধ পানি ঢাকার উত্তর-পশ্চিমাংশে বসবাসকারী সকল শ্রেণির গ্রাহকদের মাঝে পানি সরবরাহ করবে। উক্ত প্রকল্প বাস্তবায়নে মোট ১০৫ কি.মি. পরিশোধিত ও অপরিশোধিত পানির লাইন স্থাপন করা হবে। এটি বাস্তবায়নের জন্য রূপগঞ্জ উপজেলার যথাক্রমে ৬০.৫৫ একর জমি অধিগ্রহণ করা হচ্ছে। স্থাবর সম্পত্তি অধিগ্রহণ ও হুকুম-দখল অধ্যাদেশ ২০১৭ মোতাবেক জেলা প্রশাসন অধিগৃহীত জমি, অবকাঠামো ও গাছ পালার ক্ষতিপূরণ প্রদান করা হবে।

ইতোমধ্যে জেলা প্রশাসনের ভূমি অধিগ্রহণ সংশ্লিষ্ট কার্যালয় থেকে সকল ক্ষতিগ্রস্ত পরিবারকে ৪ ধারা, ৭ ধারা ও ৮ ধারা নোটিশ প্রদান করা হয়েছে। এই নোটিশ মোতাবেক আপনারা জেলা প্রশাসনের ভূমি অধিগ্রহণ সংশ্লিষ্ট কার্যালয় থেকে আপনাদের ক্ষতিপূরণ গ্রহনের জন্য আপনার ভূমি ও অবকাঠামোর যাবতীয় ডকুমেন্ট, ছবি ও প্রয়োজনীয় কাগজপত্র জেলা জেলা প্রশাসনের ভূমি অধিগ্রহণ সংশ্লিষ্ট কার্যালয়ে জমা করবেন এবং একই সাথে এর এক সেট ফটোকপি ঢাকা ওয়াসা এনজিও ডব্লপ এর এরিয়া অফিসে জমা দিবেন। এ ছাড়াও অতিরিক্ত ক্ষতিপূরণ গ্রহণ করার জন্য জেলা প্রশাসনের ভূমি অধিগ্রহণ সংশ্লিষ্ট কার্যালয় থেকে ক্ষতিপূরণ প্রাপ্তির চেক উভয় পৃষ্ঠা ফটোকপি করে ডব্লপ এরিয়া অফিসের (ডব্লপ এরিয়া অফিস, আমিনপ্লাজা, ২য় তলা, মুড়াপাড়া বাজার, রূপগঞ্জ, নারায়ণগঞ্জ) জমা দেওয়ার জন্য অনুরোধ করা হল।

উল্লেখ্য যে, অতিরিক্ত ক্ষতিপূরণ প্রাপ্তির জন্য অথবা অর্থ প্রাপ্তি ত্বরান্বিত করার জন্য কোন ধরণের অর্থ লেনদেন না করার জন্য অনুরোধ জানানো হল। আপনার ক্ষতিপূরনের অর্থ যথাযথ কাগজপত্র প্রাপ্তির সাপেক্ষে যথাসময়ে ওয়াসা হতে প্রদানের নিশ্চয়তা দেয়া হল।

প্রকল্পের কাজে সহযোগিতা করার জন্য সকলকে ধন্যবাদ।

মোঃ মাহবুবুল ইসলাম
প্রকল্প পরিচালক
ঢাকা ওয়াসা।

যোগাযোগ ঃ
এরিয়া ম্যানেজার
DORP
আমিনপ্লাজা, ২য় তলা, মুড়াপাড়া বাজার, রূপগঞ্জ, নারায়ণগঞ্জ।
মোবাইল ঃ ০১৭১৬-১০৪৬০৪

WASA Bhaban (9th floor), 98, Kazi Nazrul Islam Avenue, Kawran Bazar, Dhaka-1215, Bangladesh
Tel : 88-02-8189095. www.deswsp-dwasa.com, e-mail: pddeswspgwtpc@gmail.com

DHAKA WASA

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

CCL and Resettlement Assistance_Bangla)

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.22 Awareness Campaign Notice to APs regarding CCL and Resettlement Assistance English

Dhaka Environmentally Sustainable Water Supply Project

Dhaka Water Supply & Sewerage Authority

DESWSP, Dhaka WASA

Memo No.: 46.113.618, 00, G-243 (Vol.-1)/DESWSP/ 4167 Date: 026. 09. 2021

All are well informed that the Bangladesh Government with the support of foreign loan the 'Dhaka Environmentally Sustainable Water Supply Project (DESWSP) is implementing to construct a water treatment plant (WTP) at Gandharbpur with a capacity of 500 million liters water per day (MLD). The project will pump raw water at intake point from Meghna River at Bishkhali union under AraihazarUpazila of Narayanganj District and send it to the water treatment plant (DWASA own land) for purification at Gandharbpur of RupganjUpazila through laying raw water pipeline. The treated (purified) water will then be distributed to the city dwellers of north and west part of Dhaka city. For implementing of this project, a 102 km raw and treated water transmission pipeline to be installed. For implementation purpose of the project 60.55 acres of land has been acquired only from RupganjUpazila. According to the ARIPA 2017, the Deputy Commissioner will pay compensation for the acquired land, affected structures, trees, crops, fish stocks.

By this time the land acquisition section of Deputy Commissioner's office has issued notice under section 4(1), 7(1) and 8(3) ka to all of the affected persons. So, according to the instructions of notice under section 8(3) ka all concerned affected persons are requested to submit their necessary relevant documents in support of ownership to the land acquisition office for receiving compensation on affected land, structures etc. At the same time the affected persons are requested to submit one set of those papers along with a photocopy (both side) of compensation received cheque to DORP (INGO) Area office 1st floor at Amin bazar, Murapara, Rupganj, Narayanganj for processing additional/other resettlement assistances payment from the project (DWASA).

It is to be mentioned here and to request all that for receiving additional/other resettlement assistances or to accelerate the payment financial transaction to any person/persons is quite prohibited. WASA is giving assurance to everybody to provide the additional/other resettlement assistances on time subject to submission of the proper documents to DORP area office as early as possible after CCL payment.

Thanks in advance to everybody for rendering necessary supports for smooth operation of the project activities.

Md. Mahmudul Islam

Superintending Engineer and project Director

DESWSP, Dhaka WASA

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.23 Summary of Community Meetings (July to December 2021)

Acronyms:

ADB: Asian Development Bank
AP: Affected Person
CCL: Cash Compensation under Law
DESWSP: Dhaka Environmentally Sustainable Water Supply Project
DORP: Development Organisation of the Rural Poor
ID: Identity
DC: Deputy Commissioner
NGO: Non- Government Organization
NID: National Identity
INGO: Implementing Non-Government Organization
RP: Resettlement Plan
SPS: Safeguard Policy Statement.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Dhaka Environmentally Sustainable Water Supply Project (DESWSP) Quarterly summary of the community meetings discussion issues Conducted by DORP Period: July to December- 2021		
Key Issues of Discussion	**Participants Responses**	**Project Response**
	From October to December- 2021 a total number of **92** community meetings with a total of **923** participants (M-359, F-564) were held in the project site of Araihazar and Rupganj Area. The above **92** meetings were held in all of the 6 sections during the reporting quarter. The section-wise distribution of meetings and meeting participants are given below:- a. In the section-1 total meeting held **12** with a total of 114 participants (Male-49, Female-65); b. In the section-2 total meeting held 24 with a total of 224 participants (Male-79, Female-145); c. In a section-3 total meeting held 17 with a total of 185 participants (Male-68, Female-117); d. In a section-4 total meeting was held13 with a total of 141 participants (Male-46, Female-95); e. In the section-5 total meeting held 14 with a total of 148 participants (Male-63, Female-85); f. In the section-6 total meeting was held 12 with a total of 111 participants (Male-54, Female-57); 12. In this reporting period 5 FGD meetings have been held with non-paid CCL APs. for External Monitoring Report in section-2. The following questions/queries were raised by the participants in the meetings: -	In reply to the query made by the meeting participants in the meeting, the following responses were made from the project: -
1.Discussed non-paid CCL APs payment.	Affected persons who are yet receive CCL want to know how to get money if it takes a long time to resolve their land issues.	. The project informed them that the CCL money is deposited in the Deputy commissioner's office according to the amount of their land. The money that they will receive from Dhaka WASA as

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

		resettlement assistance has been deposited in a dedicated account. The Affected persons should try to resolve their problems. INGO is always there to help them.
2.Discussion on how unpaid CCL affected persons can get money if there is no NGO.	*A*ffected persons who are yet to receive CCL wants to know how to get money by submitting papers if there is no INGO since their resolution of problems may take longer time. Who will collect their documents and submit them to Dhaka WASA?	It was mentioned thatthat if there is no NGO, they will get their dues by contacting Dhaka WASA directly. DWASA will have an operational unit in Rupganj and they will be responsible for payment.
3. Discussion about not getting CCL money for land yet	Affected persons want to know why they are not getting money from the Deputy Commissioner's office despite they have submitted the necessary paper to the DC office.	On behalf of the project, it is said that INGO is to help before submitting the document to the Deputy Commissioner's office. Such as whether all the documents are in order, what type of documents are required, etc. Even, PMU is trying its best so that the Deputy Commissioner's office pays this payment immediately. In addition,tha affected persons may contact the land office and arrange to take the money. If theyneed any cooperation from the land office or anywhere else, then the PMU and DORP will assist in every way possible.
4. Court Case related problem discussed	Affected persons wants to know - what to do to get money if there is a case for land or infrastructure	In was informedthataccording to the project, if there is a court case onthe acquired land, it has to be settled.They will not receive any money until a settlement has been reached between the two parties.They will get the money if they can socially resolve the matter.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

5. The market value of the land of Section-5 is discussed	Affected persons want to know the price of land that the Deputy Commissioner's office will pay is much less. It is not possible to buy land elsewhere with this money. So how do we buy land instead of this land? So how do we buy land instead of our accusation land?	In reply, on behalf of the project – everyone will get three times more than their mouza rate. In addition, the project will pay top up is the market rate is not covered by the Deputy Commissioner's rate. Property valuation advisory committee (PVAC) will decide the market rate of the land and structures, trees, standing crops, etc.
6. Serving notice under sections 7(1) and 8 (3) (ka) and commencement of payment.	In the meeting serving notice under section-7(1) and 8(3) (ka) were discussed for section-3 and 5. After serving notice under dhara 8(3) (ka) the affected persons will be identifiedand the payment process in the DC office will be started.	The meeting participants were informed that through serving the notice under dhara 8(3) (ka) in sections 3 and 5 the project affected persons will be identified and after that payment process will be started, for payment they will be notified by the DC office to receive compensation subject to submission of necessary documents against their ownership.
7. Papers required inreceiving compensation from the DC office and additional payment/ resettlement benefits from DWASA.	The meeting participants wanted to know how they will receive their compensation money from the DC office and additional payment/other resettlement benefits from DWASA. They also wanted to know the kind of papers they will need to submit to the DC office for compensation and papers to be submitted to INGO DORP for receiving additional payment/other resettlement benefits. the participant wants to know what benefits theywill get if theybuy land elsewhere after getting 8 dhara notice.	The participants were informed in the meeting that the kind of papers they needed for receiving compensation from DC's office is, Ownership document of the land, updated mutation, and land tax receipt, national ID card, bank account number, etc. DORP will try its utmost so that payments are made fair and transparent. The INGO personnel assured the participants that they will guide them in collecting papers accordingly. In response to the query about papers to be collected for receiving additional paymentand other resettlement benefits, the meeting participants were informed that they will receive additional payment according to the current market value and according to the project entitlement matrix. INGO DORP will assist/guide them in preparing/collecting necessary papers to be submitted to

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

		DWASA for receiving additional payment and other resettlement benefits. In this regard, they need to open an individual bank account. In response to the participant's question, they were informed that those have already been received CCL from the DC office, all those papers along with the affected person ID card, Photocopy of NID/SMART card, citizenship certificate from Union Parishad Chairman or Pauroshava Chairman, account number, share sheet, etc. death certificate in case of death, the stamp of Rs. 300, etc. will be required. to be submitted to DORP local office for payment of additional/resettlement benefits. After receiving the Section 7 notice, if they purchase the land elsewhere, theywill get the money for the stamp cost of registering the land.
8. Discussing employees of Rupganj Dockyard who will lose their job.	Dockyard Employees stated that if Dhaka WASA acquired d this land, they will lose our jobs. What will be the compensation system and how much they will get?	On behalf of the project, it is ensured that all of their entitled compensation will be given from the project. It has been also suggested that since they are experienced, they may look for other opportunities to be employed anywhere else. Because the land has been acquired for government work, it must be encumbrance free.
9. Discuss training and borrowing.	Participants want to know if the project can provide a loan for the business after the training. If you take a loan from somewhere else, you have to pay a lot of interest.	Participants were informed that those who were harmed by the project were compensated in the same way. Those who are very poor are given grants from this project, training is provided and training allowance of tk. 20,000 is given at the end of the training. With this money, they will be able to start a business. Even

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

		then, if the business needs more money, they will be linked with the micro-credit or financial institution. So that they can take loans. There is no opportunity to give a loan in this project.
10. Investment of compensation, additional and other resettlement benefits inincome-generating activities;	In the meeting using compensation money and other benefits by the project affected persons were discussed. They have been informed that the compensation from the DC office and additional/resettlement benefits from DWASA made intending to invest the money in income-generating activities so that they can improve their economic status better off compared to their present status. The participants showed theirinterestto use the money in productive sectors. They committed to using their compensation money and resettlement benefits to re-start or re-establish their livelihoods activities at the previous level or better off compared to their previous life. The meeting participants requested DORP to guide them regarding spending the compensation money and other resettlement benefits properly.	In this regard the participants were informed that the money which they have received and yet to be received as compensation and resettlement benefits will have to be used to re-establish and restart their livelihood so that they can bring a positive change in their lives or at least at the level of pre-project status. Affected persons were advised by the project personnel that due to the intervention of the project they have lost land, residential and business structures, crops, trees, and employment. So, these amounts of money are to be used in purchasing land, constructing structures, re-start business, and re-establishes livelihoods. They should not be using the compensation money/ resettlement benefits in unproductive ways,
11. Discuss the necessary paper required to obtain CCL and WTP Job opportunities.	Affected Persons stated that they can't talk to the people in the Deputy Commissioner's office about their problem, they are not well behaved with them. How do they can submit papers to Deputy Commissioner's office? Affected Persons want job in WTP. How cantheyget?	On behalf of the project, it is said that after receiving the 8 dhara notice, they will be able to submit all necessary documents to the Deputy Commissioner's office. INGO will help in submitting documents. The job facilities in WTP is very limited since most of the work is mechanized. Despite PMU has requested GWT to deploy project affected persons as per competency. PMU has submitted a list of willing people to the contractor with affected persons mobile numbers. If there is any

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

		opportunity the contractor will contact.
12. Income generating work is being hampered due to Covid-19 - many people have taken loans. How to repay the loan is the topic of discussion.	The participants want to know, how they will be able to keep the business afloat during the increase in Covid-19, which has been shutting down from time to time started income-generating activities.	Participants are advised to wear face masks when outdoors at all times, to keep soap in their place of business to wash themselves and the customer's hands so that everyone is germ-free, and to have a social distance of at least three feet at the time of sale. They are also told to keep their homes and workplaces clean with a little Dettol or soapy water if necessary. Because it will take a long time or even may be 2/3 years for the infection of COVID-19 to be eradicated from our country, it will not work if we do not work for this long time So everyone should follow the rules and continue their work from a safe distance.
13. Investment of compensation, additional and other resettlement benefits inincome-generating activities;	**In** the meeting using compensation money and other benefits by the project affected persons were discussed. They have been informed that the compensation from the DC office and additional/resettlement benefits from DWASA made intending to invest the money in income-generating activities so that they can improve their economic status better off compared to their present status. The participants showed their positivity to use the money in productive sectors. They committed to using	In this regard the participants were informed that the money which they have received and yet to be received as compensation and resettlement benefits will have to be used to re-establish and restart their livelihood so that they can bring a positive change in their lives or at least at the level of pre-project status. Affected persons were advised by the project personnel that due to

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

.	their compensation money and resettlement benefits to re-start or re-establish their livelihoods activities at the previous level or better off compared to their previous life. The meeting participants requested DORP to guide them regarding spending the compensation money and other resettlement benefits properly.	the intervention of the project they have lost land, residential and business structures, crops, trees, and employment. So, these amounts of money are to be used in purchasing land, constructing structures, re-start businesses, and re-establishes livelihoods. They should not be using the compensation money/ resettlement benefits in unproductive ways,
14. Providing support to the ongoing/ensuing project construction work by the APs.	In the meeting, participants were requested to cooperatewiththe contractors during project construction work, especially by making free of the project acquired land. irrespective of those who have received resettlement benefits and those did not receive yet due to problems with papers, ownership, shareholders, land record/mutation and court cases. The participants raised questions that they have been not yet compensated for their lost properties, whether they will receive their payment earlier?	Regarding assisting in the project construction work the participants were informed that those have received payment and those did not receive payment yet, both the groups have been notified several times and requested verbally to let the land make free by making land for the smooth construction work as their land has already been acquired by the Government for pipeline installation purposes. Those who did not receive payment yet, payment delayed mostly due to legal problems and lack of mutation according to RS record, etc. So, as long as their problems will remain unsettled the compensation money will be kept safe in a separate account (Dedicated) opened for them and as soon as their problems will be solved, they could receive their payments. Ultimate the participants agreed to cooperatewith the contractors during project construction work, especially by making free of the project acquired land.
15. Take away or remove the structures from the project-acquired land.	Based on discussions, the participants who have been paid fully and did not remove the structures were asked to remove the structures. On this ground, non-paid participants raised questions that whether they will be paid their compensation before	In the meeting the participants were informed that those who have already fully paid have been notified several times (verbally and written) but did not remove structures yet and those did not

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

	shifting their structures. Unless they fully paid up, they will not shift their structures and will not make the project area free for project construction work. The participants conditioned that they must be cleared up of their dues and notified and allow them a reasonable time for shifting, otherwise they will not hand over their land or remove their structures, etc.	receive compensation yet from the DC office and resettlement benefits from DWASA due to legal issues and mutation problems their amount will be safely deposited to the DC office and DWASA as well in an account (Dedicated) opened separately for them. Being assured from the project side they agreed to shift their structures and to make the project area free for project construction work.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.248th GRC Meeting Minutes_14-10-2021_Bangla

ঢাকা এনভায়রণমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্ট-ডিইএসডব্লিউএসপি, ঢাকা ওয়াসা

গণপ্রজাতন্ত্রী বাংলাদেশ সরকারের স্থানীয় সরকার পল্লী উন্নয়ন ও সমবায় মন্ত্রণালয়ের স্থানীয় সরকার বিভাগের অধীনে
ঢাকা পানি সরবরাহ ও পয়ঃনিষ্কাশন কর্তৃপক্ষ কর্তৃক
প্রজ্ঞাপন নং ঃ ৪৬.০৮৫.০১৪.০১.০০.০০৬.২০১৩ (অংশ) ৮৮৮ তাং ১১.১১.২০১৫ এর মাধ্যমে গঠিত

ক্ষোভ নিরসন সভার কার্যবিবরণী (সেকশন-৪)

তারিখ ঃ ১৪/১০/২০২১ইং।
সময় ঃ ১১:০৫ মিনিট।

সভার স্থানঃ ডিইএসডব্লিউএস প্রকল্পের সভাকক্ষ ,ওয়াসা ভবন, ঢাকা।

আলোচ্য বিষয় ঃ

ক) ক্ষোভ নিরসন কমিটি বরাবর আবেদনকারীর অভিযোগ সমূহের পর্যালোচনা/ শুনানী।
খ) আবেদনকারীর মৎস্য চাষের ক্ষতিপূরণের বিষয়ে আলোচনা এবং সিদ্ধান্ত গ্রহণ।
গ) গৃহীত পদক্ষেপ।

সভায় উপস্থিত কমিটির সদস্য ও অন্যান্যদের নাম ও পদবী ঃ

১. জনাব মোঃ মাহমুদুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
২. জনাব বাহরুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক, আহ্বায়ক জিআরসি, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
৩. জনাব মোস্তাফিজুর রহমান,নির্বাহী প্রকৌশলী, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
৪. ড. রাফেজা আক্তার, রিসেটেলমেন্ট এক্সপার্ট (ন্যাশনাল) এমডিএসসি ও সদস্য জিআরসি, ডিইএসডব্লিউএস প্রকল্প ।
৫. জনাব রোকসানা বেগম (সোসাল এ্যান্ড জেন্ডার স্পেশালিস্ট), এমডিএসসি, ডিইএসডব্লিউএস প্রকল্প।
৬. তোফাজ্জল হোসেন, সেইফগার্ড অফিসার (সোসাল এ্যান্ড জেন্ডার), ডিইএসডব্লিউএস প্রকল্প , ঢাকা ওয়াসা।
৭. জনাব আশরাফ আলী , উপ-সহকারী প্রকৌশলী, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
৮. জনাব মোঃ শাহ্ আলম, এরিয়া ম্যানেজার ও সদস্য সচিব, জিআরসি, ভরপ- ডিইএসডব্লিউএস প্রকল্প ,রূপগঞ্জ, নারায়ণগঞ্জ।
৯. জনাব মোঃ ইকবাল হোসেন, এরিয়া ম্যানেজার, ভরপ- ডিইএসডব্লিউএস প্রকল্প ,আড়াইহাজার, নারায়ণগঞ্জ।
১০. সাইয়্যিদুর রহমান, রিসেটেলমেন্ট অর্গানাইজার, ভরপ- ডিইএসডব্লিউএস প্রকল্প, রূপগঞ্জ, নারায়ণগঞ্জ।
১১. জনাব মোঃ ফারুক প্রধান, মৎস্য চাষী, (আবেদনকারী)।

1

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

সূচনা বক্তব্য ঃ

জনাব মোঃ মাহমুদুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা। জিআরসি সভায় উপস্থিত সকলকে শুভেচ্ছা এবং ধন্যবাদ জানিয়ে সভার কার্যক্রম শুরু করেন। তিনি সকলকে নিজ নিজ পরিচয় দেওয়ার জন্য অনুরোধ করেন।

পরিচয় পর্ব ঃ সভাপতির আহ্বানে সভায় অংশগ্রহণকারী সকলে নিজ নিজ পরিচয় প্রদান করেন।

পরিচয় পর্ব শেষে প্রকল্প পরিচালক মহোদয় বলেন, আপনারা অবগত আছেন যে, ঢাকা ওয়াসা তথা গণপ্রজাতন্ত্রী বাংলাদেশ সরকার, Dhaka Environmentally Sustainable Water Supply Project (DESWSP) নামে একটি মেগা প্রকল্প বাস্তবায়ন করছে। এমতাবস্থায় সেকশন-৪ চরগন্ধর্বপুর মৌজায় ওয়াটার ট্রিটমেন্ট প্লান্টের কাজ চলমান রয়েছে। জনাব মোঃ ফারুক প্রধান মৎস্য চাষী হিসাবে মৎস্য চাষের ক্ষতিপূরণের জন্য আবেদন করেছেন তার আবেদনের প্রেক্ষিতে মৎস্য চাষের আরো কাগজ পত্র দাখিল করা প্রয়োজন। আবেদনকারী জনাব মোঃ ফারুক প্রধান মৎস্য চাষী হিসাবে মৎস্য চাষের ক্ষতিপূরণের জন্য "তারাব পৌরসভার" মৎস্য চাষের ট্রেড লাইসেন্স ডরূপ এরিয়া অফিসে জমা করেছেন, আরো কিছু মৎস্য ক্রয়-বিক্রয়ের কাগজ পত্র দাখিল করতে প্রকল্প পরিচালক মহোদয় অনুরোধ করেন।

জনাব বাহরুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক, আহবায়ক জিআরসি, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা, জনাব মোঃ ফারুক প্রধানকে উদ্দেশ্য করে বলেন যে, ১৯৭১ সালে বাংলাদেশ স্বাধীন হয়েছে, অনেক মুক্তিযোদ্ধা যুদ্ধ করেছেন, তার মধ্যে ক'জন মুক্তিযোদ্ধার আসল সনদ আছে। আপনি মৎস্য খামার করেছেন ঠিকই যথাযথ প্রয়োজনীয় কাগজপত্র জমা দিতে পারেননি। আপনি মৎস্য চাষী হিসেবে প্রমাণিত হতে হলে আপনাকে আরো কিছু মৎস্য ক্রয়-বিক্রয়ের কাগজ পত্র জমা দিতে হবে। এই প্রকল্পের কাজ বর্তমান সরকারের আমলেই শেষ হবে বলে আশাবাদ ব্যক্ত করেন।

জনাব মোঃ শাহ্ আলম, এরিয়া ম্যানেজার, প্রকল্প পরিচালক মহোদয়ের অনুরোধে মোঃ ফারুক প্রধানের মৎস্য চাষ সম্পর্কে কি তথ্য আছে তা উপস্থাপন করেন। জনাব মোঃ ফারুক প্রধান পূর্বে ওয়াটার ট্রিটমেন্ট প্লান্টের জলাশয়ে মৎস্য চাষ করেছেন। এলাকার গণ্যমান্য ব্যক্তি, দরিদ্র ও নিরীহ এলাকাবাসীর কাছে তদন্ত সাপেক্ষে জানা যায় যে, প্রকৃত পক্ষে মোঃ ফারুক প্রধান পূর্বে মৎস্য খামার পরিচালনা করেছেন।

ড. রাফেজা আক্তার, রিসেটেলমেন্ট এক্সপার্ট (ন্যশনাল) এমডিএসসি ও সদস্য জিআরসি, ডিইএসডব্লিএস প্রকল্প বলেন, জনাব মোঃ ফারুক প্রধান আপনি আমাদের পূর্ব পরিচিত। এ প্রকল্প বাস্তবায়নে আপনার সহযোগিতা অনেক পেয়েছি, তা বলে আপনাকে তুষ্ট করতে চাইনা। আপনার মৎস্য খামারের নিরপেক্ষ তদন্তে মাছ চাষের সত্যতা পাওয়া গেছে। আমরা জানি, আপনার অনেক সম্পদ আছে। আজকের সভায় আপনাকে আমরা সামান্য কিছু একটা দিয়ে সম্মান করতে চাই। আপনাকে মৎস্য চাষী হিসাবে ক্ষতিপূরন বাবদ (১.৫) এক দশমিক পাঁচ একর জমির মাছ চাষের ক্ষতিপূরণ দেয়ার মতামত পোষন করেছি। যা আপনার সম্পদের কাছে খুবই সামান্য। আপনি আমাদের প্রকল্পের কাজে সাহায্য ও সহযোগিতা করবেন বলে আমি আশা করি।

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

ক্ষোভ নিরসন সভার সিদ্ধান্ত ঃ

ক্রমিক নং	অভিযোগ কারীর নাম ও ঠিকানা	অভিযোগের বিষয়	আলোচনা ও পর্যালোচনা	গৃহীত দলিলপত্র	সিদ্ধান্ত
০১	নামঃ ফারুক প্রধান পিতাঃ আনোয়ার আলী, সাং- গন্ধর্বপুর, ২নং ওয়ার্ড, তারাব পৌরসভা, রূপগঞ্জ, নারায়ণগঞ্জ।	মৎস্য চাষের ক্ষতিপূরণ মৌজা ঃ চন্দ্রগন্ধর্বপুর	আবেদনকারী জনাব মোঃ ফারুক প্রধান মৎস্য চাষী হিসাবে ক্ষতিপূরন পাওয়ার জন্য সভায় উপস্থিত ছিলেন। তার মাছের খামারের মাছ চাষের ক্রয়-বিক্রয়ের আরো কাগজ পত্র নিয়ে তাকে মৎস্য খামারের মাছ চাষের ক্ষতিপূরণ দেয়া যেতে পারে বলে সভায় আলোচনা হয়েছে।	আবেদনকারী সংশ্লিষ্ট জলাশয়ে মৎস্য খামার করেছেন ভরুপ এরিয়া ম্যানেজার এর তদন্তে তা প্রমানীত হয়েছে। তাই জনাব মোঃ ফারুক প্রধান কে তার মাছ চাষের আরো কাগজ পত্র নিয়ে তাকে (১.৫) এক দশমিক পাঁচ একর জমির মাছ চাষের ক্ষতিপূরণ দেয়া হবে।	জনাব মোঃ ফারুক প্রধানকে মৎস্য চাষী হিসেবে মাছ চাষের ক্ষতিপূরণ বাবদ তাকে (১.৫) এক দশমিক পাঁচ একর জমির মৎস্য খামারের মাছ চাষের ক্ষতিপূরণ দেয়া হবে বলে জিআরসি সভায় সিদ্ধান্ত গৃহীত হয়েছে।

উক্ত সভায় আর কোনো আলোচনা না থাকায় প্রকল্প পরিচালক মহোদয় সবাইকে ধন্যবাদ জ্ঞাপন করে জিআরসি সভার সমাপ্তি ঘোষণা করেন।

মোঃ শাহ্ আলম
এরিয়া ম্যানেজার, ভরুপ,
ডিইএসডব্লিউএস প্রকল্প
ও সদস্য সচিব জিআরসি।

ড. রাফেজা আক্তার
রিসেটেলমেন্ট এক্সপার্ট (ন্যাশনাল),
এমডিএসসি,ডিইএসডব্লিউএস প্রকল্প
ও সদস্য জিআরসি।

বাহরুল ইসলাম
তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক
ডিইএসডব্লিউএস প্রকল্প,
ঢাকা ওয়াসা ও আহ্বায়ক জিআরসি।

মোঃ মাহবুবুল ইসলাম
তত্ত্বাবধায়ক প্রকৌশলী ও প্রকল্প পরিচালক
ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।

3

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Office of the Project Director
Dhaka Environmentally Sustainable Water Supply Project (DESWSP)
Dhaka Water Supply and Sewerage Authority (WASA)
WASA Bhaban, 98, Kazi Nazrul Islam Avenue (9th Floor)
Kawran Bazar, Dhaka-1215
Email: pddeswsppgwtp@gamil.com

Attendance Sheet

Subject: Grievance Redress Committee (GRC) meeting on Section-4 of DESWSP, Dhaka WASA.

Date of Meeting: 14 October, 2021

Venue : DESWSP, conference room.

SL No.	Name	ORG & Designation	Mobile No.	Signature
01	MD. MAHMUDUL	PD / DESWSP. DWASA.	01922198190	
02	BAHRUL ISLAM	DPD / DESWSP DWASA.	01715848493	14.10.21
03	Dr. Rafeza Nekhe	NRE / MDSC MM DESWSP	01718219041	Rafeza
04	Ruksana Begum	GD-EGS / MDSC MM DESWSP	01711-824537	RBegum
05	Md. Rakibul Alam.	Database Manager - DORP	01712597049	
06	Tofazzal Hossen	Safeguard officer (GRC), DESWSP Dhaka WASA.	01745421948	14.10.21
07	Md. Iqbal Hossain	Area Manager - DORP	01716104604	14.10.2021
08	Md. Shah Alam	Area Manager DORP	01721095525	14.10.21
09	Md. Saidur Rahman	RO, DORP	01611397674	
10	Md. Ashraf Ali	SAE, DESWSP DWASA	01920-725455	
11	[illegible]	Fish cultivator	01910866098	
12	Mostafijur Rahman	EE, DESWSP	01716-285008	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.259th GRC meeting minute_23.12.2021_Bangla

ঢাকা এনভায়রণমেন্টালী সাসটেইনেবল ওয়াটার সাপ্লাই প্রজেক্ট-ডিইএসডব্লিউএসপি,

ঢাকা ওয়াসা।

গণপ্রজাতন্ত্রী বাংলাদেশ সরকারের স্থানীয় সরকার পল্লী উন্নয়ন ও সমবায় মন্ত্রণালয়ের স্থানীয় সরকার বিভাগের অধীনে
ঢাকা পানি সরবরাহ ও পয়ঃনিষ্কাশন কর্তৃপক্ষ কর্তৃক
প্রজ্ঞাপন নং ঃ ৪৬.০৮৫.০১৪.০১.০০.০০৬.২০১৩ (অংশ) ৮৮৮ তাং ১১.১১.২০১৫ এর মাধ্যমে গঠিত
ক্ষোভ নিরসন সভার কার্যবিবরণী (সেকশন-৪)

তারিখ ঃ ২৩/১২/২০২১ইং
সময় ঃ সকাল ১১:০০ ঘটিকা।

সভার স্থানঃ ডিইএসডব্লিউএস প্রকল্পের সভাকক্ষ,ওয়াসা ভবন, ঢাকা।

আলোচ্য বিষয় ঃ

ক) আবেদনকারীর মৎস্য চাষের ক্ষতিপূরণের বিষয়ে আলোচনা এবং সিদ্ধান্ত গ্রহণ।

সভায় উপস্থিত কমিটির সদস্য ও অন্যান্যদের নাম ও পদবী ঃ

১. জনাব বাহরুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক, আহ্বায়ক জিআরসি, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
২. জেসমিন সাহানা, টিম লিডার (ভারপ্রাপ্ত), ডব্লূপ, ডিইএসডব্লিএস প্রকল্প।
৩. ড. রাফেজা আক্তার, মনোনীত প্রতিনিধি, এমডিএসসি, রিসেটেলমেন্ট এক্সপার্ট (ন্যাশনাল) ও সদস্য জিআরসি।
৪. জনাব মোস্তাফিজুর রহমান, নির্বাহী প্রকৌশলী, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
৫. তোফাজ্জল হোসেন, সেইফগার্ড অফিসার (সোসাল এ্যান্ড জেন্ডার) ডিইএসডব্লিউএস প্রকল্প,ও সদস্য জিআরসি, ঢাকা ওয়াসা।
৬. জনাব আশরাফ আলী, উপ-সহকারী প্রকৌশলী, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা।
৭. জনাব মোঃ রাকিবুল ইসলাম, ডাটাবেজ ম্যানেজার, ডব্লূপ, ডিইএসডব্লিএস প্রকল্প।
৮. মোঃ শাহ্ আলম, এরিয়া ম্যানেজার, ও সদস্য সচিব, জিআরসি, ডব্লূপ।
৯. জনাব মোঃ হোসেন আহম্মেদ রাজিব (আবেদনকারী) রূপগঞ্জ, নারায়নগঞ্জ।
১০. জনাব মোঃ আলীনুর ভূইয়া, এলাকাবাসি, রূপগঞ্জ, নারায়নগঞ্জ।
১১. শহিদুল ইসলাম, এলাকাবাসি, রূপগঞ্জ, নারায়নগঞ্জ।

সভার সূচনা বক্তব্য ঃ

জনাব বাহরুল ইসলাম, তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক, আহ্বায়ক জিআরসি, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা। তিনি সকলকে নিজ নিজ পরিচয় দেওয়ার জন্য অনুরোধ করেন। উপস্থিত সকলে নিজ নিজ পরিচয় প্রদান করেন।

পরিচয় পর্ব শেষে উপ-প্রকল্প পরিচালক মহোদয় বলেন, আপনারা অবগত আছেন যে, ঢাকা ওয়াসা তথা বাংলাদেশ সরকার, Dhaka Environmentally Sustainable Water Supply Project (DESWSP) নামে একটি মেগা প্রকল্প বাস্তবায়ন করছে। এমতাবস্থায় সেকশন-৪ চরগন্ধর্বপুর মৌজায় ওয়াটার ট্রিটমেন্ট প্লান্টের কাজ চলমান রয়েছে। জনাব মোঃ হোসেন আহমেদ রাজিব মৎস্য চাষের ক্ষতিপূরণের জন্য আবেদন করেছেন। তার আবেদনের প্রেক্ষিতে মৎস্য চাষের কাগজ পত্র সঠিক ভাবে যাচাই-বাছাই করা হয়েছে।

ড. রাফেজা আক্তার রিসেটেলমেন্ট এক্সপার্ট (এমডিএসসি) মোঃ হোসেন আহমেদ রাজিব সাহেবকে প্রশ্ন করেন যে, তিনি কেন এতদিন জিআরসি মিটিংয়ে উপস্থিত হননি? জনাব আশরাফ আলী, উপ-সহকারী প্রকৌশলী, ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা- তিনি বলেন আপনি বিগত জিআরসি মিটিংয়ে চিঠি গ্রহণ করেও উপস্থিত হননি।

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

আপনাকে মোবাইলে ফোন করা হয়েছিল, মোবাইলে মেসেজ প্রদান করা হয়েছিল, কিন্তু আপনি আমাদের কথায় কোন সাড়া দেননি। জনাব হোসেন আহম্মেদ রাজিব কোনো সদুত্তর দিতে পারেন নাই।

জনাব বাহারুল ইসলাম বলেন, আপনি যেহেতু এতদিন মিটিংয়ে উপস্থিত হন নাই এবং মাছ চাষের স্বপক্ষে কোনো প্রমানাদি উপস্থাপন করেন নাই সেহেতু আমরা বুঝে নিয়েছি,আপনি ট্রিটমেন্ট প্লান্টের সামনের জলাশয়ে মাছ চাষ করেন নাই। বর্তমানে আপনার প্রদত্ত মৎস্য চাষের কাগজ পত্র সঠিক ভাবে যাচাই-বাছাই করা হয়েছে। আজকের সভায় যা সিদ্ধান্ত হবে তা আপনি খুশি মনে গ্রহণ করবেন বলে আমি আশা করি। উপ-প্রকল্প পরিচালক এবং আহবায়ক জিআরসি বলেন, আপনার ক্ষতির বিবেচনায় প্রকল্পের পক্ষ থেকে সর্বোপরি আপনাকে ১,০০,০০০/- (এক লক্ষ) টাকা ক্ষতিপূরন প্রদান করা যেতে পারে।

ক্ষোভ নিরসন সভার সিদ্ধান্ত ঃ

ক্রমিক নং	অভিযোগকারীর নাম ও ঠিকানা	অভিযোগের বিষয়	আলোচনা ও পর্যালোচনা	গৃহীত পদক্ষেপ	সিদ্ধান্ত
০১	মোঃ হোসেন আহম্মেদ (রাজিব) পিতা- মোঃ রফিক হোসেন ২নং ওয়ার্ড, সাং-গন্ধর্বপুর, তারাব পৌরসভা, রূপগঞ্জ, নারায়ণগঞ্জ।	মৎস্য চাষের ক্ষতিপূরণ মৌজা ঃ চরগন্ধর্বপুর	জনাব মোঃ হোসেন আহম্মেদ (রাজিব) পূর্বে আলোচ্য জলাশয়ে মাছের চাষ করে ছিলেন বলে সভায় আলোচনা করা হয়েছে ঃ তার মাছ চাষের কাগজপত্র জমা দিয়েছেন।	জনাব মোঃ হোসেন আহম্মেদ (রাজিব) কে তার মাছ চাষের কাগজপত্র যাচাই-বাছাই করে ৪৩.৪৮ (তেতাল্লিশ দশমিক আটচল্লিশ) শতাংশ জমির জলাশয়ের ক্ষতিপূরণ প্রদান করার জন্য সভায় উপস্থিত সকলে একমত পোষণ করেন। মোঃ হোসেন আহম্মেদ (রাজিব) সকলের সাথে সহমত পোষণ করেন।	জনাব, মোঃ হোসেন আহম্মেদ (রাজিব) কে ৪৩.৪৮ (তেতাল্লিশ দশমিক আটচল্লিশ) শতাংশ জমির জলাশয়ের ক্ষতিপূরণ বাবদ ১,০০,০০০/- (এক লক্ষ) টাকা প্রদানের সিদ্ধান্ত গৃহীত হয়েছে।

উক্ত সভায় আর কোন আলোচনা না থাকায়, সভার আহবায়ক সবাইকে ধন্যবাদ জ্ঞাপন করে জিআরসি সভার সমাপ্তি ঘোষণা করেন।

মোঃ শরিফ আলম
এরিয়া ম্যানেজার,
ডব্লিউ, ডিইএসডব্লিউএস
এবং সদস্য সচিব জিআরসি।

তোফাজ্জল হোসেন,
সেইফগার্ড অফিসার (সোসাল এন্ড জেন্ডার),ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা ও সদস্য জিআরসি।

ড. রাফেজা আক্তার
রিসেটেলমেন্ট এক্সপার্ট (ন্যাশনাল),
এমডিএসসি, ডিইএসডব্লিউএস প্রকল্প
এবং সদস্য জিআরসি।

বাহারুল ইসলাম
তত্ত্বাবধায়ক প্রকৌশলী ও উপ-প্রকল্প পরিচালক ডিইএসডব্লিউএস প্রকল্প, ঢাকা ওয়াসা এবং আহ্বায়ক জিআরসি।

2

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Office of the Project Director
Dhaka Environmentally Sustainable Water Supply Project (DESWSP)
Dhaka Water Supply and Sewerage Authority
WASA Bhaban, 98, KaziNazrul Islam Avenue (8th Floor)
Kawran Bazar, Dhaka-1215
Email: pddeswsppetp@gmail.com

Attendance Sheet

Subject: Grievance Redress Committee Meeting on Sel: 04

Date of Meeting: 23.12.2021, PMU, DESWSP conference room.

SL	Name	ORG & Designation	E-mail/Mobile No.	Signature
1.	BAHRUL ISLAM	DPD DESWSP DWASA	01713-84273	
2.	Mostafijur Rahman	E.E. DESWSP	01716-355648	
3.	Dr. Rafiq Alam	NRE MM MDSC DESWSP	01718217941	Rafiq
4.	M. Rakibul Islam	Database Manager DESWSP	01750769157	
5.	Jasmin Shultana	DPE = DORP. DESWSP	01713154818	
6.	Tarannum Hoss	Safeguard Officer (S&R), DWASA.	01715421946	23.12.2021
7.	[illegible]	DORP, Nawabganj	01879114666	
8.	Md. Aslam Ali	SAE, DWASA	01920-725453	23.12.21
9.	[illegible]	[illegible]	0183-6512691	
10.	[illegible]	[illegible]	01946-563430	
11.	SHAHIDUL ISLAM	"	01771954965	23.12.21
12.				

3

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.26 8th GRC Meeting Minutes_14-10-2021_English

Dhaka Environmentally Sustainable water Supply Project (DESWSP), DWASA
Under the Ministry of Local Government rural Development and Cooperatives (MLGRDC) of Bangladesh Government and by the Dhaka Water Supply and Sewerage Authority the Committee is constituted through an issued Memo
Memo No. 46.085.014.01.00.006.2013 (part) 888 Date: 11.11.2015
GRC Meeting Proceedings

Date: 14 October 2021 Time: 11.05 AM
Meeting Venue: Meeting room of DESWSP, WASA Bhaban, Dhaka.

Agenda

1. Review and hearing on complaint filed by the complainant to GRC;
2. Discussion and decision on the application for compensation payment for the loss of fish stock by complainant;
3. Step undertaken.

Name and designation of the meeting attendees:-

1. Md. Mahmudul Islam, Superintending Engineer, and Project Director, DESWSP, DWASA;
2. Mr. Bahrul Islam, Superintending Engineer, DPD-1. DESWSP, DWASA and Convener of the Committee;
3. Md. Mostafizur Rahman, Executive Engineer, DESWSP, DWASA;
4. Dr. RafezaAkter, National Resettlement Expert, MDSC, Member of the Committee;
5. Ms. Ruksana Begum, Social and Gender Specialist, MDSC, DESWSP;
6. Md. TofazzalHossen, Safeguard officer (Social & Gender), DESWSP, DWASA;
7. Md. Aahraf Ali, Sub Assistant Engineer, DESWSP, DWASA;
8. Md. Shah Alam, Area Manager, DORP, Rupganj and Member Secretary of the Committee;
9. Md. Iqbal Hossan, Area Manager, DORP, Araihazar, DESWSP;
10. Md. Saidur Rahman, Resettlement Organizer, DORP, Rupganj, DESWSP;
11. Md. FaruqueProdhan, Fish cultivator (Applicant).

Introductory speech of Convener: Mr. Bahrul Islam, Superintending Engineer, Deputy Project Director, DESWSP and the Convener of the GRC welcomed and requested the participants attended in the GRC meeting to introduce themselves. Accordingly the meeting participants introduced themselves (Name, occupation and address etc.). As the honorable project Director was present in the meeting the convener requested him to chair the meeting.

In response to the request of the Convener of the meeting Project Director described the project in brief. He addressed to the participants and informed them that they are well aware about that the Dhaka WASA is implementing a mega project "DhakaEnvironmentally Sustainable Water Supply Project (DESWSP) of Peoples Republic of Bangladesh Government. The construction work of "Water Treatment Plant" is ongoing on the WASA own land at Ghandharbpur under Rupganjupazila of Narayanganj district. The complainant Mr. Md. Faruque Pradhan claims compensation for loss of fish stock cultivated in the project land. In support of his claim he has submitted a trade license from "TaraboPauroshava" to DORP Rupganj area office. The trade license is not the only document as proof, to show him as a fish cultivator, hence, the chair of the meeting requested him to submit some more papers on sale of fish and purchase of fingerlings.

Md. Bahrul Islam, Superintending Engineer, Deputy Project Director and convener of the GRC meeting pointed out to MrFarque that he has operated a fish farm in the WASA own land but could not submit all necessary papers in support of his claim. So, the convener re-enforced the same word as was told by the project director that he (Mr. Faruque) needs to submit some more papers on fish sale and fingerling

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

purchase in support of his fish farming. The convener strongly affirmed that the project work will be completed during the period of this Government of Bangladesh.

With the request of Project Director Md. Shah Alam, Area Manager, Rupganj presented some information in support of fish farming by Mr. Faruque Pradhan. Mr. Shah Alam collected opinion from the local elites, poor people and general public. It revealed from their opinion that Mr. Faruque Pradhan has operated the fish farm in the DWASA owned water body of the project.

Dr. RafezaAkter, National Resettlement Expert, MDSC, DESWSP and member of the GRC added that Mr. Faruque Pradhan is a familiar person to the project personnel for a long time. He has cooperated in implementing the project in many ways. Further she mentioned that through a neutral enquiry it transpired that he (Mr. Faruque) has cultivated fish in the project water body. Dr. Rafeza told to Mr. Faruque that from the project side he will be compensated for the loss of fish stock of an area of 1.5 acres of water body as per entitlement matrix. She requested Mr. Faruque to provide his cooperation for success and smooth operation of the project activities.

Discussions and decisions:

Sl. No.	Name of Complainant	Subject matter of complaint	Discussion (s)	Decision (s)
1	Name: Md. Faruque Pradhan, Father's Name: Anowar Ali, Address: Gandharbpur, Ward # 2, TaraboPauroshava, Rupganj	Compensation for loss of fish stock, Mouza: Char Gandharbpur	Md. Faruque Pradhan was present in the GRC meeting to receive compensation for loss of fish stock cultivated in the project alignment of DWASA owned land	It was decided in the meeting that the affected person will be entitled to receive compensation for the loss of fish stock for cultivating fish on 1.5 acres of land. Subject to submit fish sale and fingerling purchase documents.

Having no any other matter for discussions the Project Director and chair of the meeting gave thanks to the participants and closed the meeting proceedings.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

Office of the Project Director
Dhaka Environmentally Sustainable Water Supply Project (DESWSP)
Dhaka Water Supply and Sewerage Authority (WASA)
WASA Bhaban, 98, Kazi Nazrul Islam Avenue (9th Floor)
Kawran Bazar, Dhaka-1215
Email: pddeswspgwtp@gamil.com

Attendance Sheet

Subject: Grievance Redress Committee (GRC) meeting on Section-4 of DESWSP, Dhaka WASA.

Date of Meeting: 14 October, 2021

Venue : DESWSP, conference room.

SL No.	Name	ORG & Designation	Mobile No.	Signature
01	MD. MAHMUDUL Islam	PD / DESWSP. DWASA.	01922198140	
02	BAHRUL ISLAM	DPD / DESWSP DWASA.	01711584893	14.10.21
03	Dr. Rafeza Akter	NRE / MDSC MM DESWSP	01718217041	Rafeza
04	Ruksana Begum	SD&GS / MDSC MM DESWSP	0171I-824537	RBegum
05	Md. Rakibul Alm.	Database Manager - DORP	01712597649	
06	Tofazzal Hossen	Safeguard officer (GRG), DESWSP Dhaka WASA.	01745421948	14.10.21
07	Md. Iqbal Hossain	Area Manager - DORP	01716104604	14.10.2021
08	Md. Shah Alam	Area Manager DORP	01721095535	14.10.21
09	Md. Saidur Rahman	R.O, DORP	01611397674	
10	Md. Ashraf Ali	SAE, DESWSP DWASA	01920-725455	
11	[illegible]	Fish cultivator	01940866098	
12	Mostafijur Rahman	EE, DESWSP	01710-785008	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.27 9th GRC Meeting Minutes_23.12.2021_English

Dhaka Environmentally Sustainable Water Supply Project (DESWSP), DWASA
Under the Ministry of Local Government Rural Development and Cooperatives (MLGRDC) of Bangladesh Government and by the Dhaka Water Supply and Sewerage Authority the Committee is constituted through an issued Memo
Memo No. 46.085.014.01.00.006.2013 (part) 888 Date: 11.11.2015
GRC Meeting Proceedings (Section-4)

Date: 23 December 2021 Time: 11.00 AM

Meeting Venue: Meeting room of DESWSP, WASA Bhaban, Dhaka.

Agenda

1. Discussion and decision on the complainant's application for compensation payment for loss of fish stock;

Name and designation of the meeting attendees:-
1. Mr. Bahrul Islam, Superintending Engineer, DPD-1. DESWSP, DWASA and Convener of the Committee;
2. JesminAkterShahana, Deputy Team Leader, DORP, DESWSP;
3. Dr. RafezaAkter, National Resettlement Expert, MDSC, member of the Committee;
4. Md. Mustafijur Rahman, Executive Engineer, DESWSP, DWASA;
5. Md. TofazzalHossen, Safeguard officer (Social & Gender), DESWSP, DWASA;
6. Md. Ashraf Ali, Sub Assistant Engineer, DESWSP, DWASA;
7. Md. Rakibul Islam, Database Manager, DORP, DESWSP;
8. Md. Shah Alam, Area Manager, DORP, Rupganj and Member Secretary of the Committee;
9. Md. Hossain Ahmed Rajib (Complainant), Rupganj, Narayanganj;
10. Md. Alinur Bhuiyan, local people, Rupganj, Narayanganj;
11. Md. Shahidul Islam, local people, Rupganj, Narayanganj.

Introductory speech of Convener: Mr. Bahrul Islam, Superintending Engineer, Deputy Project Director 1, DESWSP and the Convener of the GRC welcomed and requested the attendees to introduce themselves. Accordingly, the attendees introduced themselves. As the honorable Project Director was present in the meeting, the convener requested him to chair the meeting

After completion of introducing session, Md. Baharul Islam, Superintending Engineer, Deputy Project Director 1 and convener of the GRC meeting informed the participants that they might have been aware about that Dhaka WASA is implementing a mega project "DhakaEnvironmentally Sustainable Water Supply Project (DESWSP). As a consequence, the construction work of "Water Treatment Plant" is ongoing at Char Ghandharbpur*mouza*, under Rupganjupazila of Narayanganj district. The applicant Mr. Md. Hossain Ahmed (Rajib) prayed for compensation for loss of fish stock which he claimed that he cultivated on the project land. In support of his claim he submitted supporting documents. The documents have been verified by the committee members.

Dr.RafezaAkter, National Resettlement Expert, MDSC, DESWSP and member of the GRC enquired after Mr. Rajib why was he not present in the previous GRC meetings. Mr. Ashraf Ali, Sub Assistant Engineer, DESWS Project, Dhaka WASA added that in spite of receiving meeting letter, mobile message and phone call Mr. Rajib did not attend in the meetings held previously . But Mr. Rajib failed to give any acceptable reply on the queries made in the meeting.

Based on the discussions Mr. Bahrul Islam the convener of the meeting concluded that as Mr. Rajib did not attend in the meeting held previously and even previously could not submit any supporting documents in

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

favor of his fish cultivation on the project land, so, he believed that based on social recognition and after scrutiny of his newly submitted documents whatever decisions are taken by the committee members, Mr. Rajib should accept whole heartedly. Considering extent of loss, GRC advised DWASA to pay BDT 1, 00,000 to Mr. Hossain Ahmed (Rajib) for the loss of fish cultivation. Mr. Rajib has consented with the decision of the GRC.

Discussions and decisions:

Sl. No.	Name of Complainant	Subject matter of complaint	Review and discussion (s)	Steps taken	Decision (s)
1	Name: Md. Hossain Ahmed (Rajib), Father's Name: Md. Rafique Hossain, Address: Ward # 2, Gandharbpur, TaraboPauroshava, Rupganj	Compensation for loss of fish stock, Mouza: Char Gandharbpur	It was discussed in the GRC meeting that Md. Hossain Ahmed (Rajib), previously cultivated fish on the project land. He has submitted the documents in support of fish cultivation.	All participants of the meeting unanimously consented and decided to provide compensation an amount of BDT 1, 00,000 for fish cultivation of an area of 43.48 decimals of water body. Md. Hossain Ahmed (Rajib) agreed to the meeting decision.	It was decided in the meeting that the affected person will be entitled to receive compensation for the loss of fish stock for cultivating fish on 43.48 decimals of water body of an amount of BDT 1, 00,000.

Having no any other discussions in the meeting the chair of the meeting gave thanks to the participants and close the meeting.

Md. Shah Alam
Area Manager, DORP
DESWSP

Md. Tofazzal Hossen
Safeguard officer (Social & Gender),
DESWSP, DWASA

Dr. Rafeza Akter,
Resettlement Expert (National),
MDSC

Bahrul Islam
Superintending Engineer,
Deputy Project Director and
Convener of the Meeting,
DESWSP, DWASA

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

11.28 Summary of GRC meetings in English

Summary of GRC meetings in English (section-wise)									
Name of Meeting	**Date of Meeting**	**RP Sections**	**Total Nos. of Cases**	**Name and mobile no. of APs**	**Fathers/ Husbands Name**	**Mouza**	**Application Details: Land/ Structures/ Trees/Others**	**Decisions/ Comments**	**Remarks**
8th	14.10.2021	04	01	Name: Md. Faruque Pradhan Address: Ward # 2, Gandharbpur, TaraboPauroshava, Rupganj	Father: Anowar Ali,	Char Gandharbpur	Compensation for loss of fish stock, Mouza: Char Gandharbpur	It was decided in the meeting that the affected person will be entitled to receive compensation for the loss of fish stock for cultivating fish on 1.5 acres of land. Subject to submit fish sale and fingerling purchase documents.	
9th GRC	23.12.2021	04	01	Name: Md. Hossain Ahmed (Rajib), Address: Ward # 2, Gandharbpur, TaraboPauroshava, Rupganj	Father: Md. Rafique Hossain,	Char Gandharbpur	Compensation for loss of fish stock, Mouza: Char Gandharbpur	It was decided in the meeting that the affected person will be entitled to receive compensation for the loss of fish stock for cultivating fish on 43.48 decimals of water body of an amount of BDT 1, 00,000.	

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.

INTERNAL. This information is accessible to ADB Management and staff. It may be shared outside ADB with appropriate permission.
